

# RAMPART POWER SYSTEM UPGRADE PROJECT

## MODULAR POWER PLANT ASSEMBLY

### MODULAR POWER PLANT ASSEMBLY – MECHANICAL DRAWINGS

- M1.1 MECHANICAL LEGENDS & SCHEDULES
- M1.2 WARNING SIGN & FIRE EXTINGUISHER PLAN, SIGN & VALVE TAG SCHEDULES
- M1.3 SYSTEM START UP & SEQUENCE OF OPERATIONS
- M2.1 MECHANICAL PENETRATIONS PLAN, ELEVATIONS & DETAILS
- M2.2 MECHANICAL PENETRATION DETAILS
- M2.3 MECHANICAL SUPPORT PLANS & DETAILS
- M2.4 MECHANICAL SUPPORT HORIZONTAL WALL STRUT INSTALLATION
- M2.5 MECHANICAL SUPPORT VERTICAL WALL STRUT INSTALLATION
- M3.1 EQUIPMENT LAYOUT PLAN, SECTION, & DETAILS
- M3.2 WALL ELEVATIONS & PIPING DETAILS
- M3.3 MECHANICAL DETAILS
- M3.4 GENERATOR FABRICATION DETAILS
- M4.1 COOLANT & HEAT RECOVERY PIPING PLAN & DETAILS
- M4.2 COOLANT & HEAT RECOVERY ISOMETRICS & DETAILS
- M4.3 ENGINE COOLANT & HEAT RECOVERY PIPING DETAILS
- M4.4 GLYCOL STORAGE & EXPANSION TANKS FABRICATION
- M5.1 DIESEL FUEL & USED OIL PIPING PLAN, DIAGRAM, & DETAILS
- M5.2 DIESEL FUEL & USED OIL PIPING ELEVATIONS & DETAILS
- M5.3 USED OIL HOPPER & BLENDER INSTALLATION DETAILS
- M5.4 200 GALLON DAY TANK FABRICATION
- M5.5 USED OIL BLENDER FILTER BANK LAYOUT & CONFIGURATION
- M5.6 USED OIL BLENDER TYPICAL FILTER HOUSING DETAILS
- M5.7 USED OIL BLENDER 25 GALLON HOPPER FABRICATION
- M6 EXHAUST & CRANK VENT PLAN & DETAILS
- M7.1 VENTILATION PLAN & DETAILS
- M7.2 SHEET METAL FABRICATION DETAILS
- FS1 FIRE SUPPRESSION SYSTEM PLAN, SECTION, LEGEND, & NOTES

### MODULAR POWER PLANT ASSEMBLY – ELECTRICAL

- E1.1 ELECTRICAL LEGENDS & SCHEDULES
- E2 GROUNDING PLAN & DETAILS
- E3.1 WIREWAY PLAN, BUILDING SECTION, & DETAILS
- E3.2 ELEVATIONS & DETAILS
- E3.3 ELEVATIONS & DETAILS
- E4.1 RECEPTACLE & LIGHTING PLANS & PANELBOARD
- E4.2 STATION SERVICE PLAN, DETAILS, & PANELBOARD
- E5 INSTRUMENTATION & DATA PLAN & DETAILS
- E6.1 SWITCHGEAR ENCLOSURE LAYOUT, SETTING TABLE, & DETAILS
- E6.2 SWITCHGEAR ONE-LINE & SCHEMATICS
- E6.3 24VDC ENGINE WIRING JUNCTION BOX
- E7.1 DAY TANK CONTROL PANEL LOGIC DIAGRAM & BILL OF MATERIALS
- E7.2 DAY TANK CONTROL PANEL LAYOUT & TERMINAL STRIPS
- E7.3 DAY TANK CONTROL PANEL NOTES, SEQUENCE OF OPERATIONS & INTERCONNECT DETAILS
- E7.4 DAY TANK FILTER WATER INDICATION PANEL

### MODULAR POWER PLANT ASSEMBLY – ARCHITECTURAL DOORS & WINDOWS

- A1 FLOOR PLAN, REFLECTED CEILING PLAN, CODE ANALYSIS, & GENERAL NOTES
- A2 INTERIOR ELEVATIONS & DOOR/WINDOW DETAILS & SCHEDULE

### OWNER FURNISHED MODULE STRUCTURE REFERENCE DRAWINGS


- A3 EXTERIOR ELEVATIONS & ROOFING NOTES & TRIM DETAILS
- A4 BUILDING SECTIONS & DETAILS
- S1.1 FOUNDATION PLAN, CODE ANALYSIS, & STRUCTURAL NOTES
- S2 MODULE FRAMING PLANS & DETAILS
- S3 MODULE SECTIONS DETAILS
- S4 ROOF FRAMING PLAN & DETAILS
- S5.1 STAIRS, LANDINGS, LOADING DOCK, & RADIATOR SUPPORT PLAN
- S5.2 STAIRS/LANDINGS FABRICATION DETAILS
- S5.3 LOADING DOCK FABRICATION DETAILS
- S5.4 RADIATOR SUPPORT FABRICATION DETAILS
- V105 MODULE SHOP DRAWING ISOMETRIC FRONT VIEW
- V107 MODULE SHOP DRAWING ISOMETRIC BACK VIEW

ALL WORK SHOWN ON THE FOLLOWING PAGES IS INCLUDED IN THE MODULE ASSEMBLY SCOPE EXCEPT WHERE SPECIFICALLY NOTED OTHERWISE.

ON SOME OF THE MECHANICAL AND ELECTRICAL SHEETS THERE ARE SHOP/ON SITE NOTES THAT CLARIFY THE EXTENT OF WORK THAT IS INCLUDED IN THE MODULE ASSEMBLY SCOPE (SHOP) FOR ITEMS THAT WILL ULTIMATELY BE FIELD INSTALLED OR CONNECTED BY OTHERS (ON SITE).

ISSUED FOR  
CONSTRUCTION  
JULY 2022



 ALASKA ENERGY AUTHORITY		
PROJECT: RAMPART POWER SYSTEM UPGRADE		
TITLE: MODULAR POWER PLANT ASSEMBLY SCHEDULE OF DRAWINGS		
DRAWN BY: BCG	SCALE: NO SCALE	
DESIGNED BY: BCG	DATE: 7/15/22	
FILE NAME: RAM PP G1	SHEET:	G1
PROJECT NUMBER:		



P.O. 111405, Anchorage, AK 99511 (907)349-0100

PIPING LEGEND	
	BUTTERFLY VALVE
	BALL VALVE
	CHECK VALVE
	HOSE END DRAIN VALVE
	GAUGE COCK
	Y-STRAINER
	AUTOMATIC AIR VENT
	FLEXIBLE CONNECTOR
	FLANGED JOINT
	UNION
	ELBOW TURNED UP
	ELBOW TURNED DOWN
	PIPING CONNECTION (TEE)
	PIPING REDUCER
	DIRECTION OF FLOW
INSTRUMENT/CONTROL LEGEND	
	PRESSURE GAUGE
	ANALOG THERMOMETER
	DIGITAL THERMOMETER
	TEMPERATURE TRANSMITTER
	PRESSURE TRANSMITTER
	DIFFERENTIAL PRES GAUGE
	FLOW METER
	FLOAT SWITCH
	LOW COOLANT SWITCH
	TANK LEVEL MONITOR
	LEVEL SENSOR PROBE
	GLYCOL LEVEL SENSOR
NOTE: SEE ELECTRICAL FOR ADDITIONAL DETAIL ON CONTROL & INSTRUMENTATION DEVICES	
ABBREVIATIONS	
Ø	DIAMETER (PHASE)
A	AMPS
AFF	ABOVE FINISHED FLOOR
BTU	BRITISH THERMAL UNIT
DFR	DIESEL FUEL RETURN
DFS	DIESEL FUEL SUPPLY
ECR	ENGINE COOLANT RETURN
ECS	ENGINE COOLANT SUPPLY
EWT	ENTERING WATER TEMPERATURE
EXIST	EXISTING
FPT	FEMALE PIPE THREAD
GA	GAUGE
GALV	GALVANIZED
GPM	GALLONS PER MINUTE
GRC	GALVANIZED RIGID CONDUIT
HP	HORSEPOWER
HYR	HYDRONIC RETURN
HYS	HYDRONIC SUPPLY
ID	INSIDE DIAMETER
KW	KILOWATT
LT	LIQUID TIGHT
LWT	LEAVING WATER TEMPERATURE
MAX	MAXIMUM
MBH	THOUSAND BTU PER HOUR
MIN	MINIMUM
MPT	MALE PIPE THREAD
NC	NORMALLY CLOSED
NO	NORMALLY OPEN
OC	ON CENTER
OD	OUTSIDE DIAMETER
PRV	PRESSURE RELIEF VALVE
PSI	POUNDS/PER SQUARE INCH
PSID	PSI DIFFERENTIAL
PSIG	PSI GAUGE
SCH	SCHEDULE
TDH	TOTAL DEVELOPED HEAD
TYP	TYPICAL
UOR	USED OIL RETURN
V	VOLTS
W	WATTS
WG	WATER GAUGE

ENGINE COOLING SYSTEM EQUIPMENT SCHEDULE			
SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
R-1 R-2	GLYCOL RADIATOR	SINGLE PASS, 4 ROW, VERTICAL CORE, 3" FLANGED CONNECTIONS, GALVANIZED COATING, EXPANDED METAL GUARD, 6,000 BTU/MIN AT 77°F AMBIENT, 50 GPM 50% ETHYLENE GLYCOL AT 192F IN, 0.22 PSI MAX GLYCOL PRESSURE DROP, 3 HP, 460 V, 3 PH, MOTOR SUITABLE FOR VFD OPERATION AT 10:1 TURNDOWN RATIO.	DIESEL RADIATOR PART NO. DR3490
TV-1	COOLANT THERMOSTATIC VALVE	3" ANSI 125# FLAT FACED FLANGES, CAST IRON BODY, FACTORY SET NON-ADJUSTABLE FIELD REPLACEABLE THERMOSTATIC ELEMENTS, 175F NOMINAL TEMPERATURE	FPE PART NO. A3010-175
ET-1	GEN COOLANT EXPANSION TANK	24 GALLON CAPACITY TANK, 12.75" O.D x 48" LONG FABRICATED STEEL TANK, SEE FABRICATION DETAIL	CUSTOM FABRICATION
HP-EC	ENGINE COOLANT FILL HAND PUMP	DOUBLE ACTION PISTON HAND PUMP, ALUM HOUSING, SS PISTON SHAFT & LINER, BUNA-N SEALS, ANTI-SIPHONING VALVE.	GPI MODEL HP-100
G-EC	ENGINE COOLANT GLYCOL TANK LEVEL GAUGE	MAGNETIC OPERATED SPIRAL GAUGE FOR #1 DIESEL, 25 PSIG MAX OPERATING PRESSURE, 35" LIQUID COLUMN PLUS 4" RISER.	ROCHESTER MODEL 8660
GT-1	ENGINE COOLANT GLYCOL STORAGE TANK	60 GALLON CAPACITY, 36"x10"x44" HIGH FABRICATED RECTANGULAR STEEL TANK, SEE FABRICATION DETAIL	CUSTOM FABRICATION

HEAT RECOVERY & PLANT HEATING EQUIPMENT SCHEDULE:			
SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
HX-1	POWER PLANT HEAT EXCHANGER	316 SS PLATES, BRAZED CONST. 2" SOLDER CUP PORTS, 290 MBH MIN CAPACITY. PRIMARY: 35 GPM 195F EWT (50% ETHYLENE) 2.0 PSI MAX WPD, SECONDARY: 28 GPM 185F LWT (50% PROPYLENE) 1.3 PSI MAX WPD	SWEP INTERNATIONAL AB B120THx60/1P
P-CUH1	CONTROL ROOM HEAT	1 GPM AT 18' TDH, 1/25HP, 115V, 1Ø. PROVIDE WITH 3/4" SOLDER COMPANION SHUT OFF FLANGES, GASKETS, & BOLTS.	GRUNDFOS UPS 15-58FC SPEED 3
P-HR1A	HEAT RECOV. PRIMARY	35 GPM AT 8' TDH, 1/6HP, 115V, 1Ø. PROVIDE WITH 2" NPT COMPANION FLANGES, GASKETS, & BOLTS.	GRUNDFOS UPS 50-44F SPEED 3
P-HR1B	HEAT RECOV. SECONDARY	22 GPM AT 23' TDH (PRESENT ON CP-2) 28 GPM AT 30' TDH (FUTURE ON CP-3) 1/2HP, 115V, 1Ø. WITH 2" NPT FLANGES	GRUNDFOS MAGNA1 40-120 F CONSTANT PRESSURE
CUH-1	CONTROL ROOM HEAT	WALL MOUNTED HOT WATER CABINET UNIT HEATER, 18 MBH AT 1 GPM 180F EWT & 60F EAT.	TOYOTOMI HC-20 WITH WALL MOUNT BRACKET
ET-2	HEAT RECOV. EXP. TANK	BLADDER TYPE EXPANSION TANK, 44 GALLON TANK, 22 GALLON ACCEPTANCE VOL, 125 PSIG WORKING PRESSURE, 12 PSIG PRE-CHARGE.	AMTROL AX-80
<del>HX-2</del>	<del>WASHTERIA HEAT EXCHANGER</del>	<del>316 SS PLATES, BRAZED CONST. 2" SOLDER CUP PORTS, 225 MBH MIN CAPACITY. PRIMARY: 22 GPM 195F EWT (50% ETHYLENE) 1.0 PSI MAX WPD, SECONDARY: 25 GPM 185F LWT (50% PROPYLENE) 1.1 PSI MAX WPD</del>	<del>SWEP INTERNATIONAL AB B120THx60/1P ON SITE</del>
<del>P-HR2</del>	<del>WASHTERIA HEAT RECOVERY PUMP</del>	<del>27 GPM AT 7' TDH, 1/6HP, 115V, 1Ø. PROVIDE WITH 1-1/2" SOLDER SHUT OFF COMPANION FLANGES, GASKETS, &amp; BOLTS.</del>	<del>GRUNDFOS UPS 50-44F SPEED 2 ON SITE</del>

PIPE/TUBING STRUT CLAMP SCHEDULE				
PIPE/TUBE	CLAMP #	PIPE/TUBE	CLAMP #	NOTES:
1/2" COPPER	BVT062	1/2" STEEL	B2008	1) ALL CLAMP NUMBERS ARE B-LINE. EQUIVALENT EQUALS ACCEPTABLE. 2) ALL COPPER TUBE CLAMPS TO BE CUSHIONED, VIBRA-CLAMP. 3) ALL STEEL PIPE CLAMPS NOT CUSHIONED. USE FOR ALL STEEL PIPE AND RIGID CONDUIT. 4) SEE PLANS, ELEVATIONS, ISOMETRICS, AND DETAILS FOR ACTUAL PIPE SIZES.
3/4" COPPER	BVT087	3/4" STEEL	B2009	
1" COPPER	BVT112	1" STEEL	B2010	
1-1/4" COPPER	BVT125	1-1/4" STEEL	B2011	
1-1/2" COPPER	BVT162	1-1/2" STEEL	B2012	
2" COPPER	BVT212	2" STEEL	B2013	
2-1/2" COPPER	BVT262	2-1/2" STEEL	B2014	
3" COPPER	BVT312	3" STEEL	B2015	

VENTILATION EQUIPMENT SCHEDULE:			
SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
EF-1 EF-2	GENERATION ROOM EXHAUST FANS	DIRECT DRIVE 14"Ø PROPELLER SIDEWALL EXHAUST FAN, 2,100 CFM AT 0.375" SP, 1,750 RPM. FURNISH WITH SPECIAL 1/2 HP, 115 V, 1 PH VARIGREEN MOTOR WITH OPTIONAL 0-10V LEADS AND OPTIONAL TRANSFORMER	GREENHECK SE1-14-436-VG (1/2 HP)
EF-1 EF-2 COMB.	FAN & INTAKE DAMPERS	OPPOSED BLADE LOW-LEAKAGE CONTROL DAMPER, AIRFOIL BLADES, GALVANIZED STEEL CONSTRUCTION, ACETAL BEARINGS, STAINLESS STEEL JAMB SEALS, TPE BLADE SEALS.	GREENHECK VCD-33
MD	MOTORIZED DAMPER ACTUATOR	MULTI-VOLTAGE SPRING RETURN ACTUATOR	BELIMO AF-BUP

FUEL SYSTEM EQUIPMENT SCHEDULE			
SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
P-DF1	DAY TANK FILL PUMP	ROTARY GEAR PUMP, 5 GPM @ 25 PSID, C-FRAME MOUNT, 1" FPT INLET AND OUTLET, IRON CONSTRUCTION, STEEL SHAFT, CARBON GRAPHITE BUSHINGS, BUNA-N LIP SEAL, WITH 75 PSID INTERNAL PRV. DIRECT MOUNT TO FOOT MOUNT 56C FRAME MOTOR, 1,200 RPM, 1/2 HP, 115VAC.	GORMAN RUPP GMC1DC3-B-40C PUMP AND CENTURY #C827 MOTOR FOR FIELD ASSEMBLY
P-DF2	DIESEL CIRC. PUMP		
P-UO1	USED OIL DRAIN PUMP		
P-UO2	USED OIL INJECTION PUMP	ROTARY GEAR PUMP GEAR PUMP - 1.2 GPH @ 15 PSID, 1/8" FPT INLET AND OUTLET, PEEK GEARS, PTFE SEALS, MAGNETICALLY COUPLED TO FOOT MOUNT 56C FRAME MOTOR, 1,725 RPM, 1/2 HP, 115VAC.	MICROPUMP GA-V21.J8F.S.A PUMP WITH #81518 ADAPTER & CENTURY #C826V1 MOTOR
HP-DI	DAY TANK FILL HAND PUMP	DOUBLE ACTION PISTON HAND PUMP, ALUM HOUSING, SS PISTON SHAFT & LINER, BUNA-N SEALS, ANTI-SIPHONING VALVE.	GPI MODEL HP-100
G-DI	DAY TANK LEVEL GAUGE	MAGNETIC OPERATED SPIRAL GAUGE FOR #1 DIESEL, 25 PSIG MAX OPERATING PRESSURE, 35" LIQUID COLUMN PLUS 4" RISER.	ROCHESTER MODEL 8660
M-DI	DAY TANK METER	STEEL BODY, 1" ANSI 150# FLANGED ENDS, 20-800 GPH FLOW RANGE, O-RINGS AND SEALS COMPATIBLE WITH #1 DIESEL, DIRECT READ 6-DIGIT REGISTER TO 0.1 GAL, DRY CONTACT PULSER.	ISTEC CONTOIL 9226-F
F-DI	DAY TANK FILTER	THREE FILTER BANK WITH INDIVIDUAL FILTER ISOLATION VALVES, IMPACT RESISTANT "SEE-THRU" BOWLS, 15 PSIG WORKING PRESSURE. WITH 1/2" WATER PROBE PORT & 3 EACH WATER-IN-FUEL DETECTION KITS. INSTALL 3 EACH 10 MICRON AQUABLOC FILTER ELEMENTS & FURNISH 3 SPARES.	RACOR TURBINE 791000FV10-P WATER-IN-FUEL RR30880E ELEMENTS 2020V10
F-GEN	GENSET FILTER	SINGLE FILTER, IMPACT RESISTANT "SEE-THRU" BOWL, 15 PSIG WORKING PRESSURE. INSTALL 10 MICRON AQUABLOC FILTER ELEMENTS & FURNISH 1 SPARE.	RACOR TURBINE 1000FV-10 ELEMENT 2020V10
F-UOB	USED OIL BLENDER FILTER	CUSTOM FABRICATED FILTER BANK. FURNISH WITH TWO STAGE ELEMENTS: 10 MICRON HYDROSORB II FILTER 2 MICRON PARTICULATE FILTER PROVIDE 3 OF EACH ELEMENT TYPE	CIM-TEK #30034 (HYDROSORB) CIM-TEK #30066 (2 MICRON)
<del>ABV-1</del>	<del>1" ACTUATED BALL VALVE</del>	<del>ACTUATED BALL VALVE ASSEMBLY RATED TO -50F. TYPE 304 STAINLESS STEEL FABRICATED COUPLING BRACKET, SHAFT, AND FASTENERS CONFIGURED TO ALLOW WRENCH ACCESS FOR MANUAL OPERATION OF VALVE WITHOUT REMOVING ACTUATOR. LOW TEMP BALL VALVE, 150# RF FLANGED ENDS. ELECTRIC ACTUATOR WITH OPERATING VOLTAGE, NEMA RATING, AND TORQUE AS INDICATED. CONFIGURE WITHOUT MANUAL OVERRIDE SHAFT EXTENSION. FURNISH WITH PTC SELF REGULATING HEATER, AUXILIARY SWITCH SET (AUXILIARY SWITCHES 3 &amp; 4), AND EXXON BEACON 325 SEVERE COLD LUBRICANT.</del>	<del>ON SITE VALVE ASSEMBLY: DG VALVE (780) 413-1760 1" BALL VALVE - 151 IN-LB OPERATING TORQUE @ -50F NUTRON MODEL T3-R10R01LZ NEMA 7 ACTUATOR - 600 IN-LBS TORQUE, 10 SECOND STROKE TIME, 0.50 LOCKED ROTOR AMPS. RCS MODEL SXR-1023</del>

INSTRUMENTATION SCHEDULE			
SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
TT	TEMPERATURE TRANSMITTER	RTD, 20-240°F RANGE, 4-20mA OUTPUT, 1/2" NPT PIPING CONNECTION, 6mm DIAMETER BY 2.5" LONG STEM, HIRSCHMANN ELECTRICAL CONNECTION	NOSHOK 800-20/240-1-1-8-8-025-6
PT	PRESSURE TRANSMITTER	0-60 PSIG RANGE, 4-20mA OUTPUT, 1/4" NPT PIPING CONNECTION, HIRSCHMANN ELECTRICAL CONNECTION	NOSHOK 100-60-1-1-2-7
FM	HEAT RECOVERY FLOW METER	150# ANSI FLANGED CONNECTION, SIZE AS INDICATED, PTFE LINER, HASTELLOY C ELECTRODES, RATED FOR 210F OPERATION. FURNISH WITH TRANSMITTER FOR DIRECT AND REMOTE MOUNTING, 115/230 VAC, 50/60 HZ, AND NEMA 4X BODY.	SIEMENS SITRANS METER: FM MAGFLO MAG 3100 TRANSMITTER: F M MAGFLO MAG 5000, CODE NO. FDK: 7ME6910, OPTION 1AA10-1AA0
LCA	GLYCOL TANK LOW COOLANT ALARM	LOW COOLANT LEVEL ALARM FLOAT SWITCH, SEE MECHANICAL FOR INSTALLATION DETAILS	MURPHY EL-150-K1
GLS	GLYCOL TANK LEVEL SENSOR PROBE	12" PROBE, 2" NPT TANK CONNECTION, SS FLOAT, 1/4" RESOLUTION, NEMA 4 ENCLOSURE WITH SIGNAL CONDITIONER AND 1/2" NPT CONDUIT CONNECTION	INNOVATIVE COMPONENTS CLM-2012-SS
FS	DAY TANK/HOPPER FLOW SWITCH	VERTICAL ACTION FLOAT SWITCH, REVERSIBLE 70VSPST NC/NO SWITCH, 1/8" NPT, 1" MAX Ø BUNA-N FLOAT FOR S.G.=.47, MINIMUM 60" LONG PVC COATED #20 AWG LEAD WIRES	INNOVATIVE COMPONENTS LS-12-111/2
TLM	TANK LEVEL MONITOR PANEL	TANK LEVEL MONITOR CONSOLE FOR UP TO SIX TANKS, COLOR LCD SCREEN, ETHERNET CONNECTION WITH WEB INTERFACE, PROGRAMMABLE VOLUME CALCULATIONS WITH TEMPERATURE COMPENSATION	FRANKLIN/INCON EVO 200
LSP	DAY TANK/HOPPER TANK LEVEL SENSOR PROBE (SHOP FAB.)	TOP-MOUNT TANK PROBE WITH INSTALLATION KIT FOR 2" NPT RISER, WATER TIGHT COMPRESSION GLAND FITTING FOR CABLE ENTRANCE, FRANKLIN FUEL SYSTEMS, NO SUBSTITUTES. PROBE AND RISER LENGTH AS INDICATED ON INSTALLATION DETAILS.	4' TANK PROBE: FMP-LL3-53-1 2' TANK PROBE: FMP-LL3-29-1 FLOAT: TSP-IDF 2" FOR DIESEL INSTALLATION KIT: TSP-C2A
LSP	<del>INTERMEDIATE TANK LEVEL SENSOR PROBE (ON SITE)</del>	<del>TOP-MOUNT TANK PROBE WITH INSTALLATION KIT FOR 2" NPT RISER, WATER TIGHT COMPRESSION GLAND FITTING FOR CABLE ENTRANCE, FRANKLIN FUEL SYSTEMS, NO SUBSTITUTES. PROBE AND RISER LENGTH AS INDICATED ON INSTALLATION DETAILS.</del>	<del>10' TANK PROBE: FMP-LL3-125-1 FLOAT: TSP-IDF 2" FOR DIESEL INSTALLATION KIT: TSP-C2A</del> <b>ON SITE</b>

EQUIPMENT REQUIREMENTS FOR APPROVED EQUALS (APPLIES TO ALL SCHEDULES): SPECIFIC PARTS MANUFACTURER AND MODEL SELECTED NOT ONLY TO MEET PERFORMANCE FUNCTION BUT ALSO TO COORDINATE AND INTERFACE WITH OTHER DEVICES AND SYSTEMS. APPROVED EQUAL SUBSTITUTIONS WILL BE ALLOWED ONLY BY ENGINEER'S APPROVAL. TO OBTAIN APPROVAL, SUBMITTALS MUST CLEARLY DEMONSTRATE HOW SUBSTITUTE ITEM MEETS OR EXCEEDS SPECIFIED ITEM QUALITY AND PERFORMANCE CHARACTERISTICS AND ALSO COMPLIES WITH MECHANICAL AND/OR ELECTRICAL CONNECTIONS AND PHYSICAL LAYOUT REQUIREMENTS.


AS PART OF THE MODULE ASSEMBLY WORK FURNISH AND INSTALL ALL MATERIALS AND EQUIPMENT ON THE SCHEDULES THIS SHEET EXCEPT FOR THOSE ITEMS SPECIFICALLY NOTED "ON SITE".

ITEMS SPECIFICALLY NOTED AS ON-SITE WILL BE FURNISHED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT.

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: MECHANICAL LEGENDS & SCHEDULES			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M1		SHEET:	
PROJECT NUMBER:		<b>M1.1</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

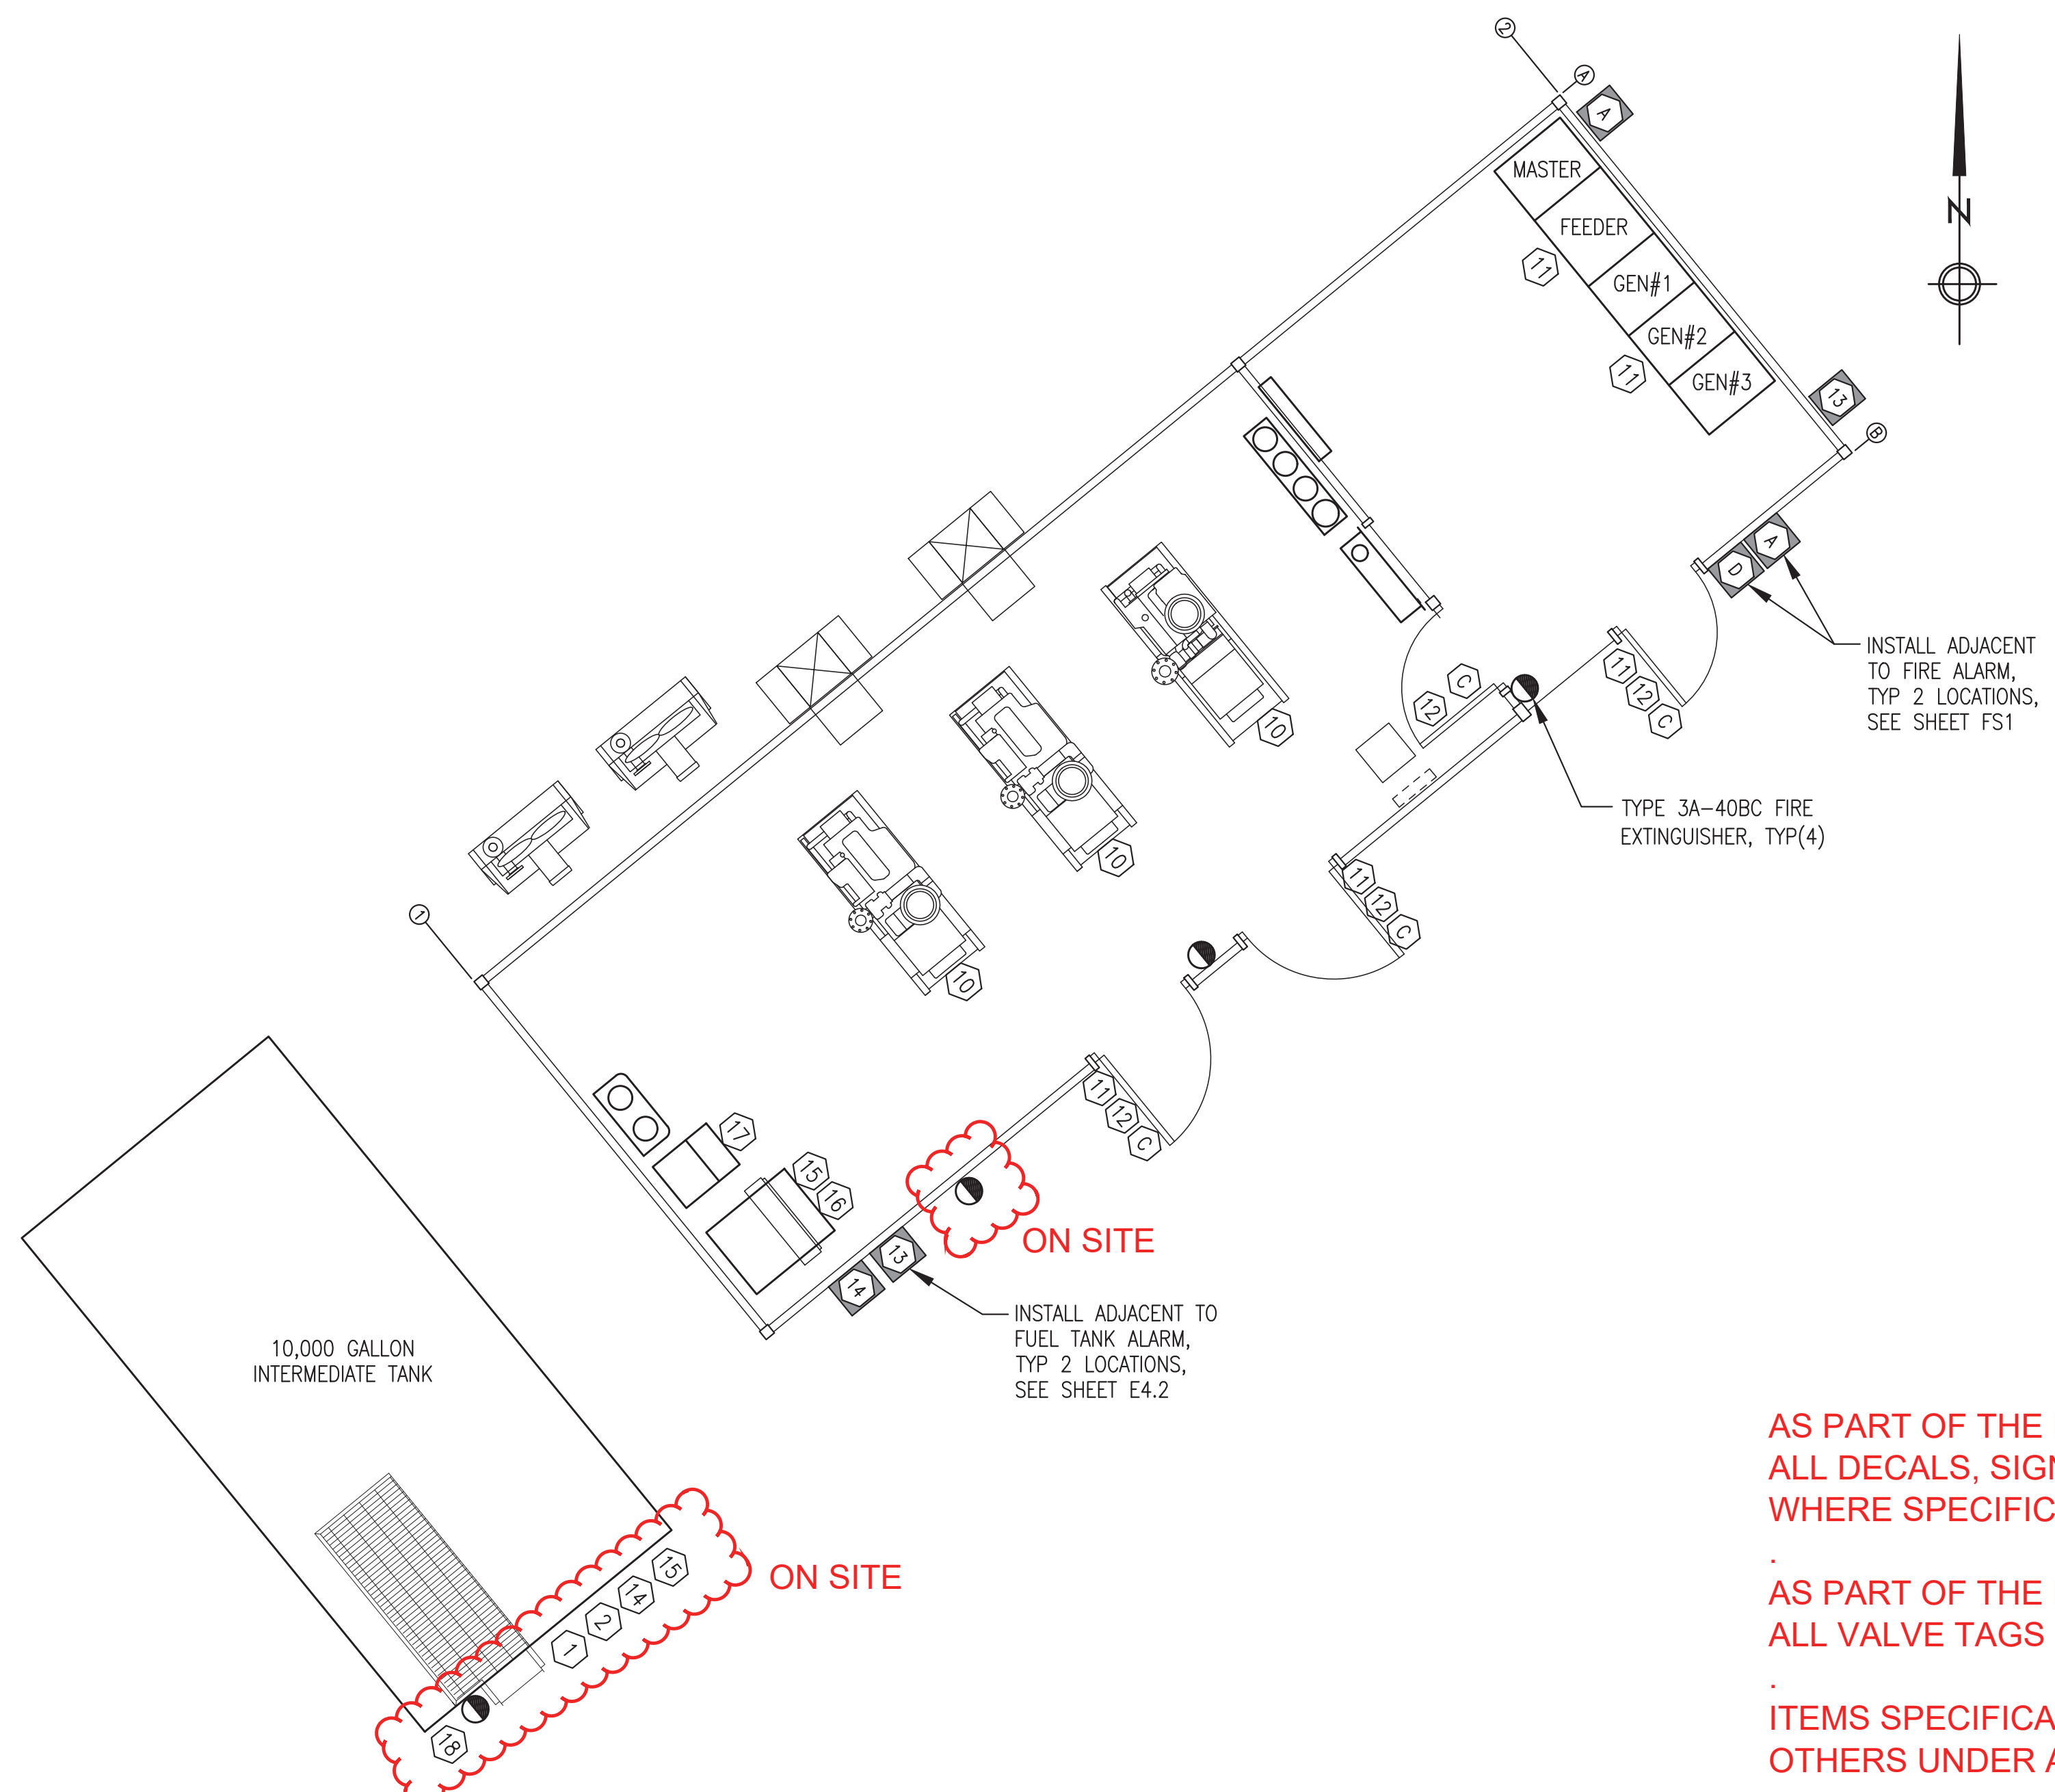

AS PART OF THE MODULE ASSEMBLY WORK FURNISH AND INSTALL ALL DECALS, SIGN BOARDS, AND FIRE EXTINGUISHERS EXCEPT WHERE SPECIFICALLY NOTED "ON SITE".

AS PART OF THE MODULE ASSEMBLY WORK FURNISH AND INSTALL ALL VALVE TAGS EXCEPT WHERE SPECIFICALLY NOTED "ON SITE".

ITEMS SPECIFICALLY NOTED AS ON-SITE WILL BE FURNISHED BY OTHERS UNDER A SEPARATE FUTURE ON SITE CONTRACT.

**WARNING SIGN & INFORMATIONAL PLACARD SCHEDULE:**

PROVIDE DECALS AND SIGN BOARDS AS SPECIFIED BELOW IN ACCORDANCE WITH THE SCHEDULE. INSTALL WHERE SHOWN ON THE WARNING SIGN/PLACARD PLAN THIS SHEET AND OTHER REFERENCED SHEETS.

**DECALS**  
 # DECALS TO BE WHITE NON-REFLECTIVE VINYL BACKGROUND, 3M 3650-10, WITH 3M SERIES 225 HIGH PERFORMANCE VINYL LETTERS, ONE SIDE ONLY, SELF ADHESIVE BACK. NOMINAL 10"x14" SIZE UNLESS INDICATED OTHERWISE OR REQUIRED TO BE LARGER FOR SPECIFIED LETTER SIZE. WARNING LITES OR EQUAL. INSTALL ON FACE OF DOORS OR ELECTRICAL ENCLOSURES WHERE INDICATED. CLEAN SURFACES AND APPLY IN ACCORDANCE WITH MANUFACTURER'S INSTRUCTIONS.

**BOARDS**  
 # SIGN BOARDS TO BE EQUAL TO DECALS EXCEPT MOUNTED ON 0.08" ALUMINUM PLATE. PROVIDE 3/16" HOLES IN ALL FOUR CORNERS. ATTACH TO CHAIN LINK FENCING WITH HOG RINGS OR STAINLESS STEEL TIES. ATTACH TO WALLS OR STRUCTURES WITH STAINLESS STEEL SCREWS OR BOLTS.


- WARNING SIGNS - RED LETTERING ON WHITE BACKGROUND.**
- A "FIRE ALARM"
  - C "CAUTION, ROOM PROTECTED BY WATER MIST FIRE PROTECTION SYSTEM, IN CASE OF FIRE KEEP DOOR CLOSED AND DO NOT ENTER"
  - D "FLASHING LIGHT MEANS FIRE SUPPRESSION AGENT HAS DISCHARGED"
  - 1 "DANGER FLAMMABLE, NO SMOKING OR OPEN FLAMES"
  - 2 "ATTACH STATIC WIRE, & VERIFY TANK CAPACITY PRIOR TO FILLING TANKS"
  - 10 "CAUTION: THIS UNIT STARTS AUTOMATICALLY, LOCK & TAG OUT PRIOR TO SERVICE"
  - 11 "DANGER HIGH VOLTAGE, AUTHORIZED PERSONNEL ONLY"
  - 12 "CAUTION HEARING & EYE PROTECTION REQUIRED"
  - 13 "FUEL OIL DAY TANK ALARM"
  - 14 "IN CASE OF SPILL CALL DEC 1-800-478-9300"

- INFORMATIONAL PLACARDS - BLACK LETTERING ON WHITE BACKGROUND.**
- 15 15 "CHECK INTERMEDIATE TANK LEVEL DAILY, FILL WHEN BELOW 4'-8"
  - 16 "TO MANUALLY FILL DAY TANK IN CASE OF EMERGENCY:  
 1) TURN OFF POWER TO THE DAY TANK CONTROL PANEL  
 2) MANUALLY OPEN ACTUATOR VALVE AT INTERMEDIATE TANK USING A WRENCH  
 3) OPEN NORMALLY CLOSED VALVE BY HAND PUMP  
 4) OPERATE HAND PUMP WHILE MONITORING LEVEL GAUGE"
  - 17 "TO CHANGE ENGINE OIL:  
 1) VERIFY ENGINE OIL HAS NOT BEEN CONTAMINATED WITH GLYCOL OR OTHER FLUIDS.  
 2) LOCK & TAG GENERATOR OUT OF SERVICE  
 3) OPEN NORMALLY CLOSED DRAIN VALVE AT GEN  
 4) TURN ON PUMP TIMER & PUMP OUT ENGINE OIL  
 5) CHANGE FILTER & PLACE OLD ONE IN HOPPER  
 6) CLOSE DRAIN VALVE & REFILL ENGINE  
 7) RUN ENGINE, SHUT OFF, & CHECK DIPSTICK  
 8) TOP OFF & PLACE ENGINE BACK IN SERVICE"
  - 18 "INTERMEDIATE TANK MAX FILL LEVEL 8'-0" (90% TANK CAPACITY)"

**1** POWER PLANT WARNING SIGN & FIRE EXTINGUISHER PLAN  
 M1.2 1"=4'

VALVE TAG SCHEDULE:		SPECIFICATIONS:
GREEN (DIESEL FUEL)	PINK (COOLING/ETHYLENE GLYCOL)	VALVE TAGS - 3"x5"x.08" ALUMINUM, 3/16" HOLES IN ALL FOUR CORNERS, BLACK GERBER THERMAL TRANSFER FILM PRINTED LETTERS ON GERBER 220 HIGH PERFORMANCE VINYL BACKGROUND, COLOR AS INDICATED, ONE SIDE ONLY. WARNING LITES OR APPROVED EQUAL.
(21) "NORMALLY OPEN, CLOSE ONLY FOR EMERGENCIES & TEMPORARY MAINTENANCE OF DAY TANK & DEVICES" (22) "NORMALLY CLOSED, OPEN ONLY FOR HAND PRIMING DAY TANK" (23) "NORMALLY OPEN, CLOSE ONLY FOR TEMPORARY MAINTENANCE OF BLENDER" (24) "NORMALLY OPEN, CLOSE ONLY FOR TEMPORARY MAINTENANCE OF ENGINE" (25) not used <del>(26) "NORMALLY CLOSED, OPEN ONLY FOR FUEL DELIVERY" ON SITE</del>	(51) "NORMALLY CLOSED, OPEN ONLY FOR ADDING COOLANT - ETHYLENE GLYCOL ONLY" (52) "NORMALLY CLOSED, OPEN ONLY ON HIGH COOLANT TEMPERATURE ALARM" (53) "NORMALLY OPEN, CLOSE ONLY ON HIGH COOLANT TEMPERATURE ALARM" (54) "NORMALLY OPEN, HEAT RECOVERY SUPPLY" (55) "NORMALLY OPEN, HEAT RECOVERY RETURN"	DECALS - WHERE NOTED AS DECALS PROVIDE WITHOUT ALUMINUM BACKING PLATE.  INSTALLATION NOTES: 1) SEE DRAWINGS THAT FOLLOW FOR LOCATIONS OF ALL SPECIFIC FUNCTION TAGS. 2) SECURE EACH METAL TAG TIGHT TO VALVE, PIPE, OR DEVICE WITH STAINLESS STEEL SAFETY WIRE THROUGH ALL FOUR CORNERS OR FASTEN TO ADJACENT WALL OR SECTION OF STRUT WITH SCREWS. 3) APPLY DECALS TO CLEAN SMOOTH SURFACES OF EQUIPMENT OR ON ADJACENT WALL. 4) FOR ALL VALVES NOT INDICATED WITH A SPECIFIC FUNCTION TAG PROVIDE 1-1/2" ROUND BRASS TAG LABELED "N.O." FOR NORMALLY OPEN VALVES AND 1-1/2" SQUARE BRASS TAG LABELED "N.C." FOR NORMALLY CLOSED VALVES. SECURE TAGS TO VALVE OR ADJACENT PIPE WITH BEADED BRASS CHAIN.
BROWN (USED OIL) (41) "NORMALLY CLOSED, OPEN ONLY FOR ENGINE OIL CHANGE" (42) "BLENDER FILTER #1, 10 MICRON HYDROSORB" (DECAL) (43) "BLENDER FILTER #2, 2 MICRON PARTICULATE" (DECAL)	YELLOW (HEAT RECOVERY/PROPYLENE GLYCOL) (61) "NORMALLY CLOSED, OPEN ONLY FOR ADDING FLUID - PROPYLENE GLYCOL ONLY" (62) "NORMALLY OPEN, HEAT RECOVERY SUPPLY" (63) "NORMALLY OPEN, HEAT RECOVERY RETURN" <del>(64) "NORMALLY OPEN, BOILER RETURN TO HW" ON SITE</del> <del>(65) "NORMALLY OPEN, HW TO BOILER" ON SITE</del> (66) "NORMALLY OPEN, CLOSE ONLY FOR TEMPORARY MAINTENANCE"	

REVISION #1  
 ISSUED FOR  
 CONSTRUCTION  
 JULY 2022



1	UPDATED TO COORDINATE WITH ON SITE DESIGN & NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: WARNING SIGN & FIRE EXTINGUISHER PLAN, SIGN & VALVE TAG SCHEDULES			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M1		SHEET: M1.2	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

Demand Control Table (PLC)				
Demand Control	Generator(s) On Line	On-line kW (Overload)	Level Increase	Level Decrease
Level 1	#3	65	55	---
Level 2	#1 or #2	100	90	45
Level 3	#3 & #1 or #2	165	145	80
Level 4	All	265	---	125
Note : Gen #1 & #2 are equal capacity. Manually select lead unit.				
Engine-Generator Alarm Settings (Easygen - EZGN)				
Function	Normal Range	Alarm	Shut Down	
Overspeed	1795-1805	----	1900 RPM	
Oil Pressure	30-50 PSI	14.5 PSI	10 PSI	
Air Filter Vacuum	1-10" H2O	15" H2O	20" H2O	
Coolant Temp.	180-200°F	210°F	215°F	
Exhaust Temp.	500-850°F	900°F	-----	
Under Frequency	59.5-60.5 Hz	----	58.2 Hz	
Over Frequency	59.5-60.5 Hz	----	61.8 Hz	
Under Voltage	470-490 V	----	432 V	
Over Voltage	470-490 V	----	528 V	
Reverse Power	0	----	10%	
Generator Breaker Settings (Easygen - EZGN)				
Function	Setting			
Gen #1 Breaker Trip Setpoint (EZGN Rated Current)	200 A			
Gen #2 Breaker Trip Setpoint (EZGN Rated Current)	200 A			
Gen #3 Breaker Trip Setpoint (EZGN Rated Current)	150 A			
Gen Breaker Level 1 (100%) Time Over Current	3 sec.			
Gen Breaker Level 2 (120%) Time Over Current	1 sec.			
Gen Breaker Level 3 (250%) Time Over Current	0.4 sec.			
Feeder Breaker Settings (Feeder Protection Relay - FPR)				
Function (Note: Element 1 is the only active element)	Setting			
T.O.C. Trip Pickup (amps) Note: 5A = 100% of CT rating	5.0			
T.O.C. Curve Selection	U4			
T.O.C. Time Dial	5.00			
E.M Reset delay (Y/N)	N			
Constant Time Adder (seconds)	0.00			
Minimum Response Time (seconds)	0.00			
Maximum Phase T.O.C. Torque Control	1			
Radiator VFD Settings				
Function	Setting			
Min PID Feedback	20			
Max PID Feedback	240			
rSL (Wake UP Threshold)	1			
PID Reference Temperature	175°F			
Proportional Gain	0.93			
Integral Gain	0.3			
Derivative	0			
Minimum Speed	10 Hz.			
Low Speed Timeout	10 sec.			
Loss of Phase	Ignore			

**POWER PLANT GENERATION SWITCHGEAR OPERATION**

THIS POWER PLANT IS DESIGNED TO OPERATE IN AUTOMATIC MODE UNDER CONTROL OF THE PROGRAMMABLE LOGIC CONTROLLER (PLC). MONITORING AND CONTROL IS PRIMARILY DONE THROUGH THE OPERATOR INTERFACE UNIT (OIU). IN AN EMERGENCY SUCH AS A FAILURE OF THE PLC IT CAN ALSO BE OPERATED IN MANUAL MODE. EACH ENGINE IS CONTROLLED BY AN INDIVIDUAL EASYGEN (EZGN) GENSET CONTROLLER LOCATED IN EACH GENERATOR SECTION. FOLLOWING ARE INSTRUCTIONS FOR OPERATING THE SYSTEM. SEE SECTION 3.1 OF THE O&M MANUAL FOR DETAILED SEQUENCES.

**AUTOMATIC OPERATION:**

- VERIFY THAT THE "SYSTEM MODE" SWITCH ON THE MASTER SECTION IS SET TO AUTO.
- CHECK THE MASTER SECTION FOR ANY FAULTS AS INDICATED BY THE ALARM LAMPS. CORRECT THE CAUSE OF THE FAULT (EMERGENCY STOP, LOW COOLANT LEVEL, FEEDER BREAKER TRIPPED, ETC.). PRESS THE ALARM RESET BUTTON ON THE MASTER SECTION AND VERIFY THAT THE ALARMS CLEAR.
- CHECK EACH GENERATOR SECTION FOR ANY FAULTS. FOR ENGINE-GENERATOR RELATED FAULTS CORRECT THE CAUSE OF THE FAULT (LOW OIL LEVEL, HIGH TEMPERATURE, CIRCUIT BREAKER TRIPPED, ETC.). TO CLEAR ANY ALARMS PRESS THE "ALARM RESET" BUTTON ON THE GENERATOR SECTION.
- PLACE EACH AVAILABLE GENERATOR IN SERVICE BY PRESSING THE "AUTO" BUTTON. IF A GENERATOR IS OUT OF SERVICE FOR REPAIR, VERIFY THE STOP BUTTON IS ILLUMINATED.
- THE PLC WILL AUTOMATICALLY START ALL GENERATORS IN AUTO AND PARALLEL THEM TO THE BUS, AS SOON AS THE BUS IS ENERGIZED THE STATION SERVICE POWER WILL TURN ON.
- AFTER THE AVAILABLE GENERATORS ARE ON LINE, THE PLC WILL WAIT FOR A BRIEF INTERVAL (USUALLY 15 SECONDS) AND CLOSE THE FEEDER BREAKER TO ENERGIZE THE COMMUNITY. THE RED BREAKER CLOSED LAMP WILL ILLUMINATE.

**DEMAND CONTROL OPERATION (AUTO MODE):**

- GENERATORS ARE CONSIDERED AVAILABLE FOR DEMAND CONTROL ONLY WHEN THEIR EZGN IS IN THE AUTO MODE AND THERE ARE NO ALARMS. THE DEMAND CONTROL SYSTEM WILL UTILIZE ALL AVAILABLE GENERATORS AS REQUIRED TO MEET THE LOAD ON THE SYSTEM.
- ON INITIAL STARTUP THE DEMAND CONTROL IS ACTIVATED AFTER THE FEEDER BREAKER HAS BEEN CLOSED FOR ONE MINUTE. THIS ALLOWS THE PLC TIME TO DETERMINE THE POWER DEMAND ON THE SYSTEM. THE PLC MONITORS THE LOAD ON THE SYSTEM AND COMPARES IT TO THE CONNECTED GENERATING CAPACITY.
- THE DEMAND CONTROL PROVIDES TWO TYPES OF CONTROL FOR INCREASING LOAD - INCREASE AND OVERLOAD. THE OVERLOAD SETPOINT IS TYPICALLY THE PRIME RATING OF THE GENSET AND THE INCREASE SETPOINT IS TYPICALLY 90% OF THE OVERLOAD SETPOINT. WHEN THE LOAD EXCEEDS THE INCREASE SETPOINT FOR A PRE-SET TIME DELAY (USUALLY 30 SECONDS) THE DEMAND CONTROL WILL SWITCH TO THE NEXT HIGHER LEVEL OF GENERATING CAPACITY. WHEN THE LOAD EXCEEDS THE OVERLOAD SETPOINT THE DEMAND CONTROL WILL IMMEDIATELY SWITCH TO THE NEXT HIGHER LEVEL OF GENERATING CAPACITY (NO TIME DELAY).
- THE DEMAND CONTROL PROVIDES ONE TYPE OF CONTROL FOR DECREASING LOAD. THE DECREASE SETPOINT IS TYPICALLY 80% OF THE OVERLOAD SETPOINT. WHEN THE LOAD DROPS BELOW THE DECREASE SETPOINT FOR A PRE-SET TIME DELAY (USUALLY 2 MINUTES) THE DEMAND CONTROL WILL SWITCH TO THE NEXT LOWER LEVEL OF GENERATING CAPACITY.
- NOTE THAT GENERATORS #1 & #2 ARE EQUAL CAPACITY AND THE OPERATOR MUST SELECT A LEAD GENERATOR USING THE SCADA SYSTEM.
- SEE THE DEMAND CONTROL TABLE THIS SHEET FOR DEMAND LEVEL SETPOINTS AT THE TIME OF COMMISSIONING. ON THE SCADA SYSTEM GO TO THE DEMAND TAB TO VERIFY THE PRESENT SETPOINTS.

**MANUAL OPERATION:**

- PLACE THE MASTER CONTROL "SYSTEM MODE" SWITCH IN THE MANUAL POSITION.
- CHECK THE MASTER AND GENERATOR SECTIONS FOR ANY FAULTS AND CLEAR AS DESCRIBED UNDER AUTOMATIC OPERATION STEPS 2 AND 3.
- TO PLACE A GENERATOR IN SERVICE, PRESS THE EZGN MAN BUTTON, THEN PRESS THE "I" (START) BUTTON. AFTER THE ENGINE STARTS AND STABILIZES, PRESS THE CONTACTOR CLOSE BUTTON ON THE EZGN. THE RED BREAKER CLOSED LAMP WILL ILLUMINATE.
- REPEAT THIS PROCESS FOR AT LEAST ONE MORE GENERATOR.
- WITH TWO GENERATORS ON LINE ROTATE THE FEEDER BREAKER CONTROL KNOB FOR THE MAIN FEEDER BREAKER TO THE CLOSE POSITION TO ENERGIZE THE COMMUNITY. MONITOR THE LOAD ON THE SYSTEM FOR ONE MINUTE THEN SELECT THE APPROPRIATE GENERATOR(S) TO MATCH THE LOAD.
- TAKE ANY GENERATOR(S) NOT NEEDED OFF LINE BY PRESSING THE RED EZGN STOP BUTTON. THE ENGINE WILL COOL DOWN FOR THREE MINUTES THEN SHUT OFF. NOTE THAT PRESSING THE RED STOP BUTTON TWICE WILL IMMEDIATELY SHUT DOWN THE GENERATOR.
- TO MANUALLY SWITCH TO A DIFFERENT GENERATOR AS THE LOAD CHANGES REPEAT STEPS 3 AND 6.

**SERVICE DUE / OIL CHANGE PROCEDURE:**

NOTE THAT UNDER AUTOMATIC OPERATION, WHENEVER THE SERVICE TIME HAS BEEN EXCEEDED THE GENERATOR WILL AUTOMATICALLY BE TAKEN OFF LINE AS LONG AS ANOTHER GENERATOR IS AVAILABLE IN AUTO. AN "ENGINE SERVICE" MESSAGE WILL DISPLAY ON THE EZGN AND THE RED "ENGINE ALARM" LAMP WILL ILLUMINATE.

- IF THE SWITCHGEAR IS IN MANUAL MODE, PERFORM MANUAL OPERATION STEPS 3 AND 6 ABOVE THEN CONTINUE AT STEP 3 BELOW (LOCK OUT).

- IF THE SWITCHGEAR IS IN AUTOMATIC MODE, PRESS THE EZGN MAN BUTTON ON THE GENERATOR TO BE SERVICED. THE PLC WILL START ANOTHER GENERATOR. ONCE THE OTHER GENERATOR IS ON LINE, PRESS THE EZGN STOP BUTTON ON THE GENERATOR TO BE SERVICED. NOTE THAT IF THE STOP BUTTON IS PRESSED BEFORE ANOTHER UNIT IS ONLINE, AN OUTAGE WILL OCCUR.
- LOCK THE UNIT OUT USING THE KEY SWITCH AND TAG OUT OF SERVICE.
- SERVICE ENGINE (OIL CHANGE, FUEL FILTER, AIR FILTER, ETC.).
- REMOVE TAG AND TURN THE GENERATOR LOCKOUT SWITCH TO RUN.
- PRESS THE "SERVICE HOURS RESET" BUTTON AND HOLD FOR 10 SECONDS.
- PRESS THE "ALARM RESET" BUTTON.
- AFTER ALL ALARMS HAVE BEEN CLEARED PRESS THE "HOME" BUTTON.
- START THE ENGINE BY PRESSING THE MAN BUTTON AND THEN "I" (START) BUTTON.
  - AFTER THE ENGINE COMES UP TO SPEED VERIFY THAT THE ENGINE OIL PRESSURE IS IN THE NORMAL RANGE.
  - CHECK THE OIL FILTER FOR LEAKS.
- AFTER THE ENGINE RUNS FOR ONE MINUTE PRESS THE STOP BUTTON.
- CHECK THE OIL LEVEL USING THE DIPSTICK AND ADD OIL AS REQUIRED.
- PLACE THE GENERATOR BACK IN SERVICE BY PRESSING THE AUTO BUTTON ON THE EZGN.

**ENGINE-GENERATOR PROTECTION ALARMS:**

SEE THE TABLES THIS SHEET FOR ALARM LEVEL SETPOINTS AND BREAKER TRIP SETTINGS AT THE TIME OF COMMISSIONING. SEE SECTION 3.1 OF THE O&M MANUAL FOR DETAILED DESCRIPTIONS OF WARNING ALARM AND PROTECTION SEQUENCES.

**FUEL/OIL SYSTEM**

AUTOMATIC DAY TANK FILL - THE 200 GALLON DAY TANK IS FILLED FROM THE 10,000 GALLON INTERMEDIATE TANK. IT HAS AUTOMATIC FILL CONTROLS WITH REDUNDANT HIGH AND LOW LEVEL ALARMS AND TIMERS. SEE FUEL SYSTEM CONTROL PANEL DRAWING SHEET E7.3 FOR DETAILED SEQUENCE OF OPERATION.

DAY TANK FILTER - THE DAY FILTER HAS WATER DETECTION PROBES. AN ALARM LAMP WILL ILLUMINATE WHEN WATER IS PRESENT IN THE FUEL. SEE WATER INDICATION PANEL DRAWING SHEET E7.4.

MANUAL USED ENGINE OIL DRAIN - USED OIL PUMP P-U01 IS USED TO PUMP USED ENGINE OIL FROM THE ENGINE OIL PANS TO THE USED OIL HOPPER. P-U01 RUNS THROUGH A MANUAL 0-5 MINUTE TIMER SWITCH.

AUTOMATIC USED ENGINE OIL BLENDING SYSTEM - THE USED ENGINE OIL BLENDING SYSTEM FILTERS USED OIL AND MIXES IT WITH DIESEL FUEL IN THE DAY TANK TO BE BURNED BY THE ENGINES. THE PUMPING RATES ARE SET TO BLEND APPROXIMATELY 0.5% USED OIL TO 99.5% DIESEL FUEL. NOTE THAT WHEN THERE IS NO USED OIL IN THE HOPPER THE DIESEL PUMP STILL RUNS TO USE THE BLENDER AS A FUEL "POLISHING" FILTER. SEE FUEL SYSTEM CONTROL PANEL DRAWING SHEET E7.3 FOR DETAILED SEQUENCE OF OPERATION.

MANUAL INTERMEDIATE TANK FILL - THE INTERMEDIATE TANK IS LOCATED ADJACENT TO THE POWER PLANT. IT NEEDS TO BE FILLED WHENEVER IT DROPS BELOW THE 50% FULL LEVEL. THE INTERMEDIATE TANK IS FILLED BY TRUCK.

**ENGINE COOLING SYSTEM**

RADIATORS - RADIATOR FAN MOTORS WILL OPERATE UNDER VARIABLE FREQUENCY DRIVE (VFD) CONTROL. WHEN THE COOLANT RETURN TEMP REACHES THE PID REFERENCE SETPOINT THE MOTOR WILL START AT MINIMUM SPEED AND RAMP UP TO THE REQUIRED SPEED. USING PID CONTROL THE VFD WILL MODULATE THE FAN SPEED AS REQUIRED TO MAINTAIN COOLANT RETURN TEMP AT THE PID REFERENCE SETPOINT. AS THE COOLANT RETURN TEMP RISES, THE VFD WILL INCREASE THE SPEED OF THE FAN MOTOR UP TO 100%. ONCE THE FAN REACHES THE MINIMUM SPEED, THE VFD WILL MAINTAIN THAT SPEED UNTIL THE LOW SPEED TIME OUT EXPIRES. WHEN THE LOW SPEED TIME OUT EXPIRES THE MOTOR WILL STOP. THE MOTOR WILL REMAIN OFF UNTIL THE COOLANT RETURN TEMP RISES TO THE PID REFERENCE SETPOINT. SEE THE RADIATOR VFD SETTINGS TABLE THIS SHEET FOR SETPOINTS AT THE TIME OF COMMISSIONING.

THERMOSTATIC VALVE TV-1 WILL MIX HOT COOLANT FROM THE ENGINE DISCHARGE PIPE WITH COLD COOLANT FROM THE RADIATOR RETURN PIPE TO MAINTAIN 175°F +/- TEMPERATURE COOLANT RETURN TO THE ENGINES.

ENGINE COOLANT RETURN HIGH TEMPERATURE ALARM. WHEN THE ENGINE COOLANT RETURN TEMPERATURE RISES ABOVE 190°F FOR A MINIMUM OF 2 MINUTES, THE "HIGH COOLANT RETURN TEMPERATURE" LAMP SHALL ILLUMINATE. LAMP SHALL REMAIN ON UNTIL MASTER RESET BUTTON IS PRESSED.

**POWER PLANT HEATING AND VENTILATION SYSTEM**

GENERATION ROOM - THE OPERATING AND OFF LINE GENERATORS REJECT MORE HEAT TO THE GENERATION ROOM THAN IS REQUIRED SO EXHAUST FANS WITH INTAKE AIR DUCTS ARE INSTALLED TO PROVIDE COOLING.

GENERATION ROOM VENTILATION - THERE ARE THREE AIR INTAKES IN THE GENERATION ROOM CEILING. ONE OF THE AIR INTAKES IS USED FOR COMBUSTION AIR AND THE DAMPER IS OPEN ANY TIME THE STATION SERVICE POWER IS ON. THE OTHER TWO AIR INTAKES ARE LABELED "EF-1" AND "EF-2". THESE DAMPERS OPEN WHENEVER THE ASSOCIATED EXHAUST FAN RUNS. THE INTAKES ARE EQUIPPED WITH A MOTORIZED DAMPER THAT OPENS EACH TIME THE ASSOCIATED EXHAUST FAN RUNS.

EXHAUST FANS - THERE ARE TWO EXHAUST FANS ON THE WALL ABOVE THE FRONT OF THE GENERATORS, EF-1 AND EF-2. EACH FAN IS EQUIPPED WITH A MOTORIZED DAMPER THAT OPENS WHENEVER THE FAN RUNS ON A CALL FOR COOLING THROUGH A 24VAC DIGITAL MODULATING THERMOSTAT. THE THERMOSTAT WILL PROVIDE A 0-10V SIGNAL TO MODULATE THE FAN SPEED AS REQUIRED TO MAINTAIN GENERATING ROOM TEMP, 80F, ADJUSTABLE.

MOTOR OPERATED DAMPERS - ALL DAMPER MOTORS WILL BE NORMALLY CLOSED SPRING RETURN AND WILL CLOSE ON LOSS OF POWER (FIRE ALARM) IN LESS THAN 30 SECONDS. VENTILATION AIR INTAKE AND EXHAUST MOTORIZED DAMPERS WILL OPEN ANY TIME THE ASSOCIATED EXHAUST FAN OPERATES. THE COMBUSTION AIR INTAKE MOTORIZED DAMPER WILL BE OPEN ANY TIME PLANT OPERATES (STATION SERVICE POWER ON).

CONTROL ROOM VENTILATION - COOLING AND VENTILATION FOR THE CONTROL ROOM IS PROVIDED BY AN OPERABLE WINDOW.

CONTROL ROOM HEATING - THE CONTROL ROOM IS HEATED BY A CABINET UNIT HEATER. PUMP P-CUH1 CIRCULATES ENGINE COOLANT FROM THE PIPING MAINS THROUGH THE CABINET UNIT HEATER IN THE CONTROL ROOM. THE TEMPERATURE CONTROLLER ON THE HEATER CYCLES THE PUMP AND THE HEATER FAN ON AND OFF AS REQUIRED TO MAINTAIN TEMPERATURE IN THE CONTROL ROOM, 65 F, ADJUSTABLE.

**HEAT RECOVERY SYSTEM**

THE POWER PLANT HEAT EXCHANGER (HX-1), THE PRIMARY (HOT SIDE) ENGINE COOLANT CIRCULATING PUMP (P-HR1A), AND THE SECONDARY (COLD SIDE) HEAT RECOVERY FLUID MAIN CIRCULATING PUMP (P-HR1B) ARE LOCATED IN THE POWER PLANT. BOTH PUMPS OPERATE CONTINUOUSLY UNDER MANUAL CONTROL.

HEAT RECOVERY LOSS OF PRESSURE - WHEN THE SYSTEM PRESSURE IN THE HEAT RECOVERY PIPING DROPS BELOW 15 PSIG FOR 15 MINUTES, A RED LAMP "HEAT RECOVERY LOSS OF PRESSURE" LOCATED IN THE SWITCHGEAR MASTER SECTION WILL ILLUMINATE.

NO LOAD ON HEAT RECOVERY SYSTEM - WHEN THE HEAT RECOVERY RETURN TEMP. IS EQUAL TO OR GREATER THAN THE HEAT RECOVERY SUPPLY TEMP. FOR 60 MINUTES, AN AMBER LAMP "NO LOAD ON HEAT RECOVERY" LOCATED IN THE SWITCHGEAR MASTER SECTION WILL ILLUMINATE. WHEN THE HEAT RECOVERY SUPPLY TEMP. IS A MIN. OF 1°F GREATER THAN THE HEAT RECOVERY RETURN TEMP. THE LAMP WILL TURN OFF.

HEAT RECOVERY LOSS OF FLOW - WHEN THE FLOW RATE IN THE HEAT RECOVERY PIPING FALLS BELOW 10 GPM FOR 15 MINUTES, A RED LAMP "HEAT RECOVERY LOSS OF FLOW" LOCATED IN THE SWITCHGEAR MASTER SECTION WILL ILLUMINATE.

THE HEAT RECOVERY SYSTEM PROVIDES INTERRUPTIBLE HEAT TO THE WASHETERIA AS SHOWN ON SHEET M8.1. A HEAT EXCHANGER IS USED TO CONNECT TO THE BUILDING BOILER SYSTEM AND THE HEAT RECOVERY SYSTEM PRE-HEATS THE BOILER RETURN. WHEN AVAILABLE RECOVERED HEAT EQUALS OR EXCEEDS BUILDING HEAT DEMAND, THE BOILERS WILL NOT FIRE. AS HEAT LOAD INCREASES THE BUILDING HEATING GLYCOL TEMPERATURE WILL DROP UNTIL BOILERS FIRE. BOILERS MUST BE SET AT 160F-180F OPERATING TEMPERATURE. A HEAT RECOVERY PANEL PREVENTS THE BUILDING HEATING SYSTEM FROM BACKFEEDING INTO THE HEAT RECOVERY SYSTEM OR FROM DEPRESSING THE HEAT RECOVERY LOOP TEMPERATURE. SEE SHEET E8.2 FOR DETAILED SEQUENCE OF OPERATIONS.

**SYSTEM STARTUP**

FUEL OIL PUMPS - PRIOR TO STARTING FUEL AND OIL PUMPS PRIME CAVITIES WITH LUBE OIL AND RUN MOMENTARILY TO VERIFY CORRECT ROTATION.

FUEL OIL PIPING - AFTER PRESSURE TESTING FILL ALL FILTER BODIES, PRIME ALL PIPING, AND BLEED OFF AIR.

VERIFY OPERATION OF ALL FUEL SYSTEM CONTROLS IN ACCORDANCE WITH SEQUENCES OF OPERATION ON THE CONTROL PANEL DRAWINGS.

ENGINE COOLANT PIPING - AFTER PRESSURE TESTING, FLUSHING, AND BLEEDING, FILL SYSTEM WITH ETHYLENE GLYCOL SOLUTION. SEE HYDRONIC PIPING SPECIFICATION 23 21 13.

HEAT RECOVERY PIPING - AFTER PRESSURE TESTING, FLUSHING, AND BLEEDING, FILL SYSTEM WITH PROPYLENE GLYCOL SOLUTION. SEE HYDRONIC PIPING SPECIFICATION 23 21 13.

VERIFY OPERATION AND CALIBRATION OF ENGINE COOLANT SYSTEM THERMOSTATIC VALVE.



VERIFY PROPER OPERATION OF THERMOMETERS, PRESSURE GAUGES, AND ELECTRICAL INSTRUMENTATION DEVICES. SET SWITCHES ON DIFFERENTIAL PRESSURE GAUGES TO SETPOINTS INDICATED. CALIBRATE THERMOMETERS AND ALL ELECTRICAL INSTRUMENTATION DEVICES INCLUDING TEMPERATURE TRANSMITTERS, PRESSURE TRANSMITTERS, DIFFERENTIAL PRESSURE SWITCHES, FLOW METERS, ENERGY METERS, LEVEL GAUGES, ETC. SEE INSTRUMENTATION AND CONTROL DEVICES SPECIFICATION 23 09 00.


CLEAN ALL PIPING STRAINERS AFTER FIRST 48 HOURS OR MORE OF OPERATION. MONITOR SYSTEM OPERATION FOR ONE WEEK MINIMUM BEFORE LEAVING SITE. CHANGE GLYCOL FILTER ELEMENTS AT TIME OF FIRST OIL CHANGE ON EACH ENGINE.

**INITIAL SYSTEM STARTUP, TESTING, AND COMMISSIONING IS INCLUDED IN THE MODULE ASSEMBLY SCOPE. FINAL MODULE TESTING AND COMMISSIONING AND ALL EXTERIOR HEAT RECOVERY SYSTEM STARTUP, TESTING, AND COMMISSIONING WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE ON SITE CONTRACT.**


**REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022**




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT:		<b>RAMPART POWER SYSTEM UPGRADE</b>	
TITLE:		<b>SYSTEM START UP &amp; SEQUENCE OF OPERATIONS</b>	
		DRAWN BY: JTD	SCALE: AS NOTED
P.O. 111405, Anchorage, AK 99511 (907)349-0100		DESIGNED BY: BCG	DATE: 3/15/22
		FILE NAME: RAM PP M1	SHEET:
		PROJECT NUMBER:	<b>M1.3</b>

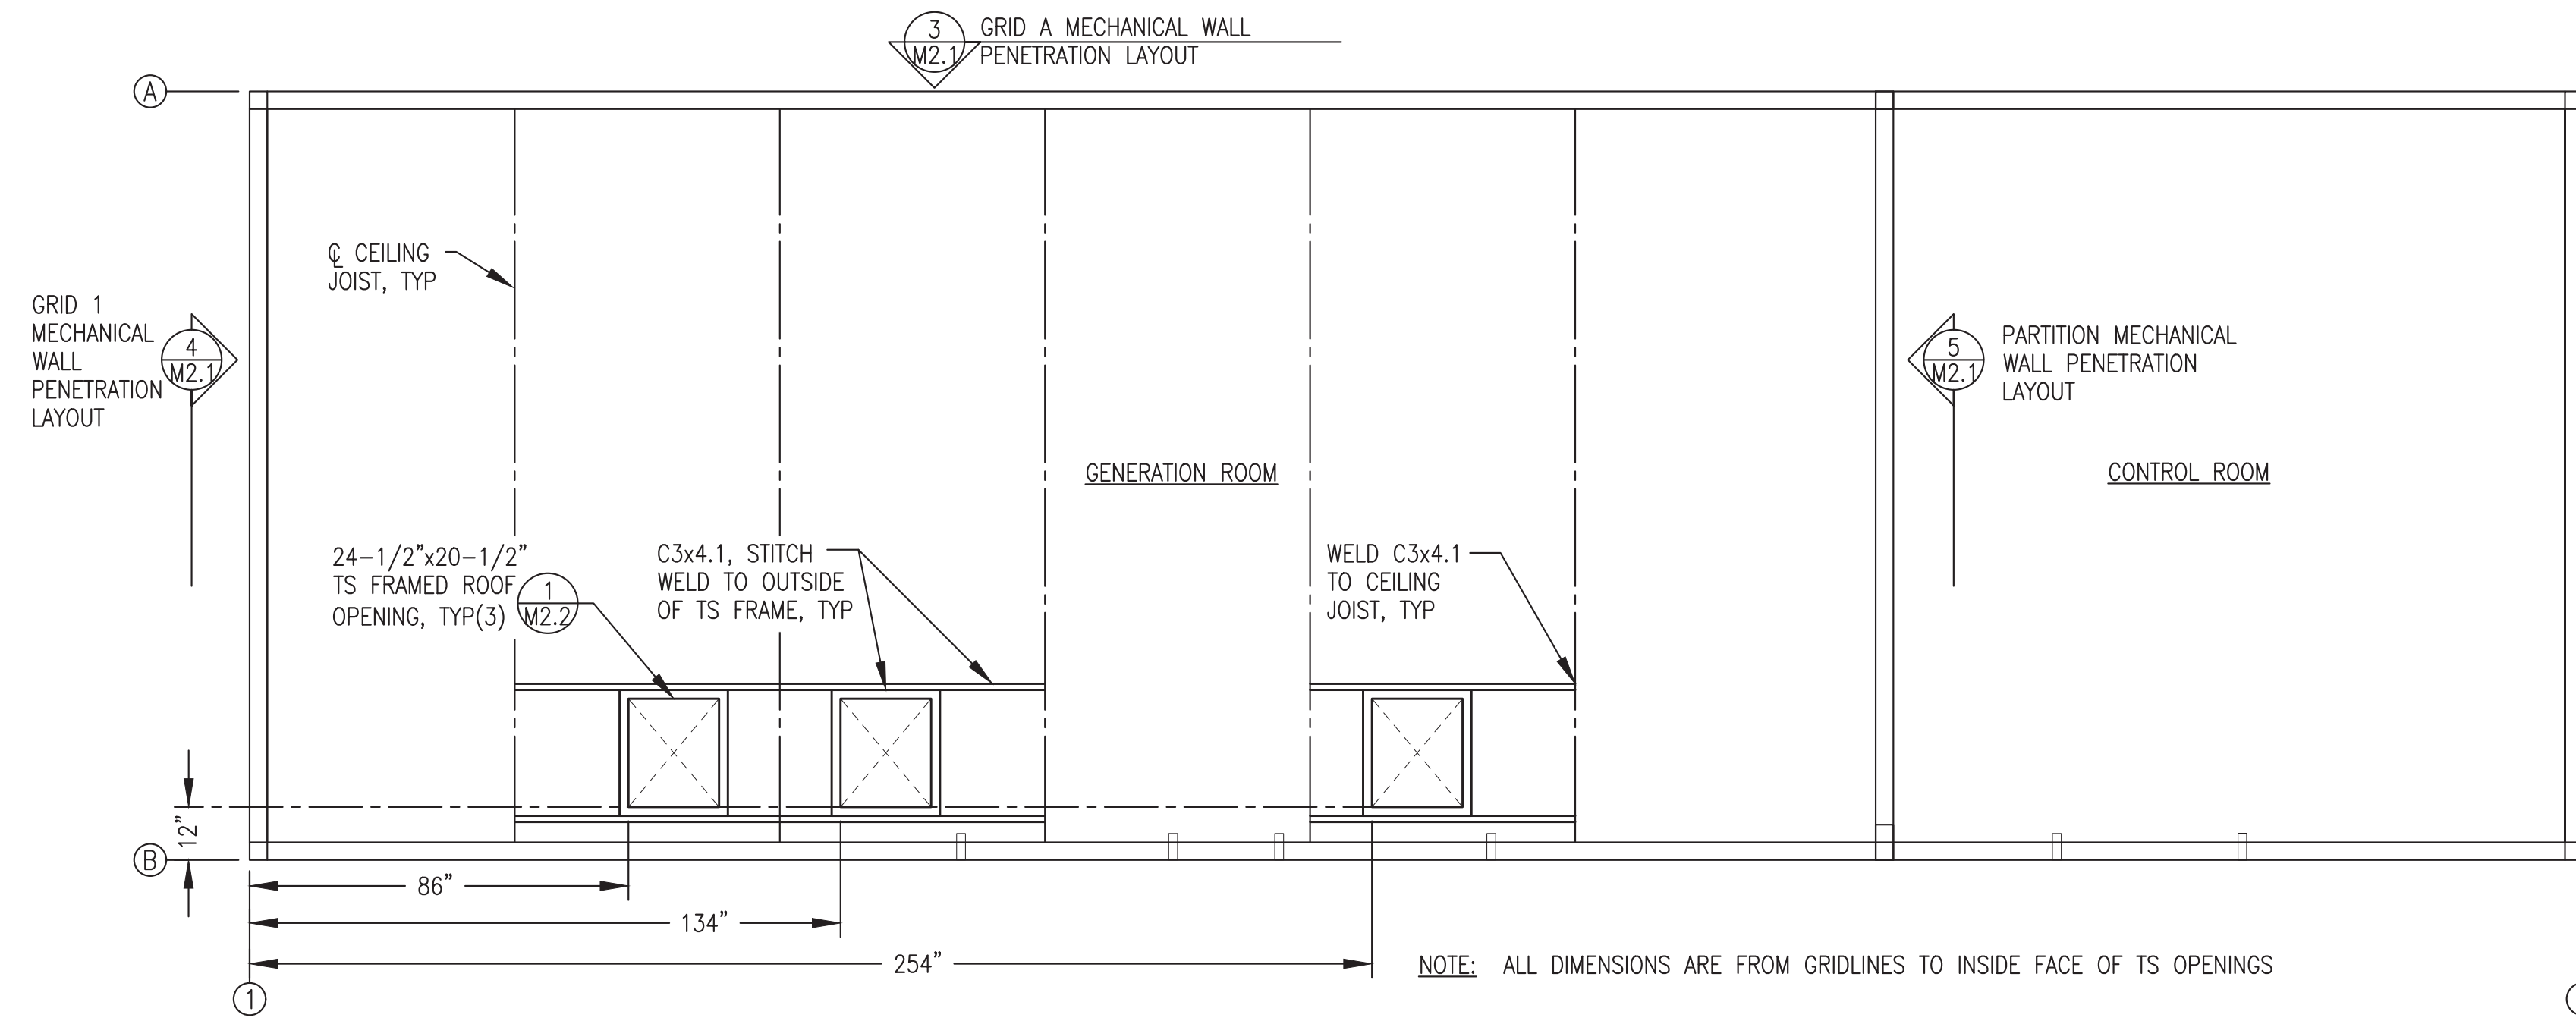


1 MECHANICAL PENETRATION LAYOUT & ROOF PLAN  
M2.1 3/8"=1'-0"

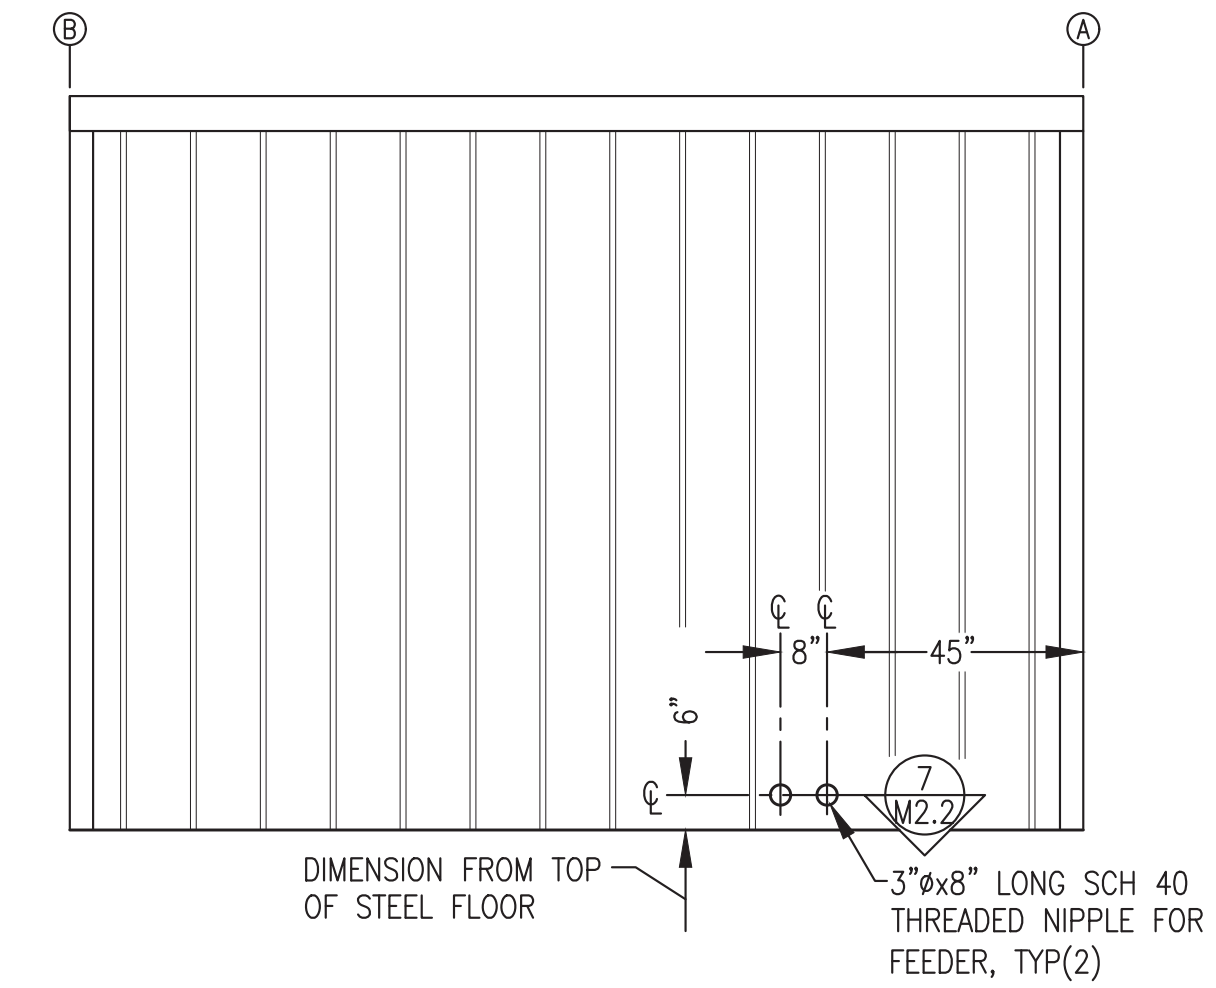

2 GRID 2 MECHANICAL WALL PENETRATION LAYOUT - EXTERIOR ELEVATION  
M2.1 3/8"=1'-0"

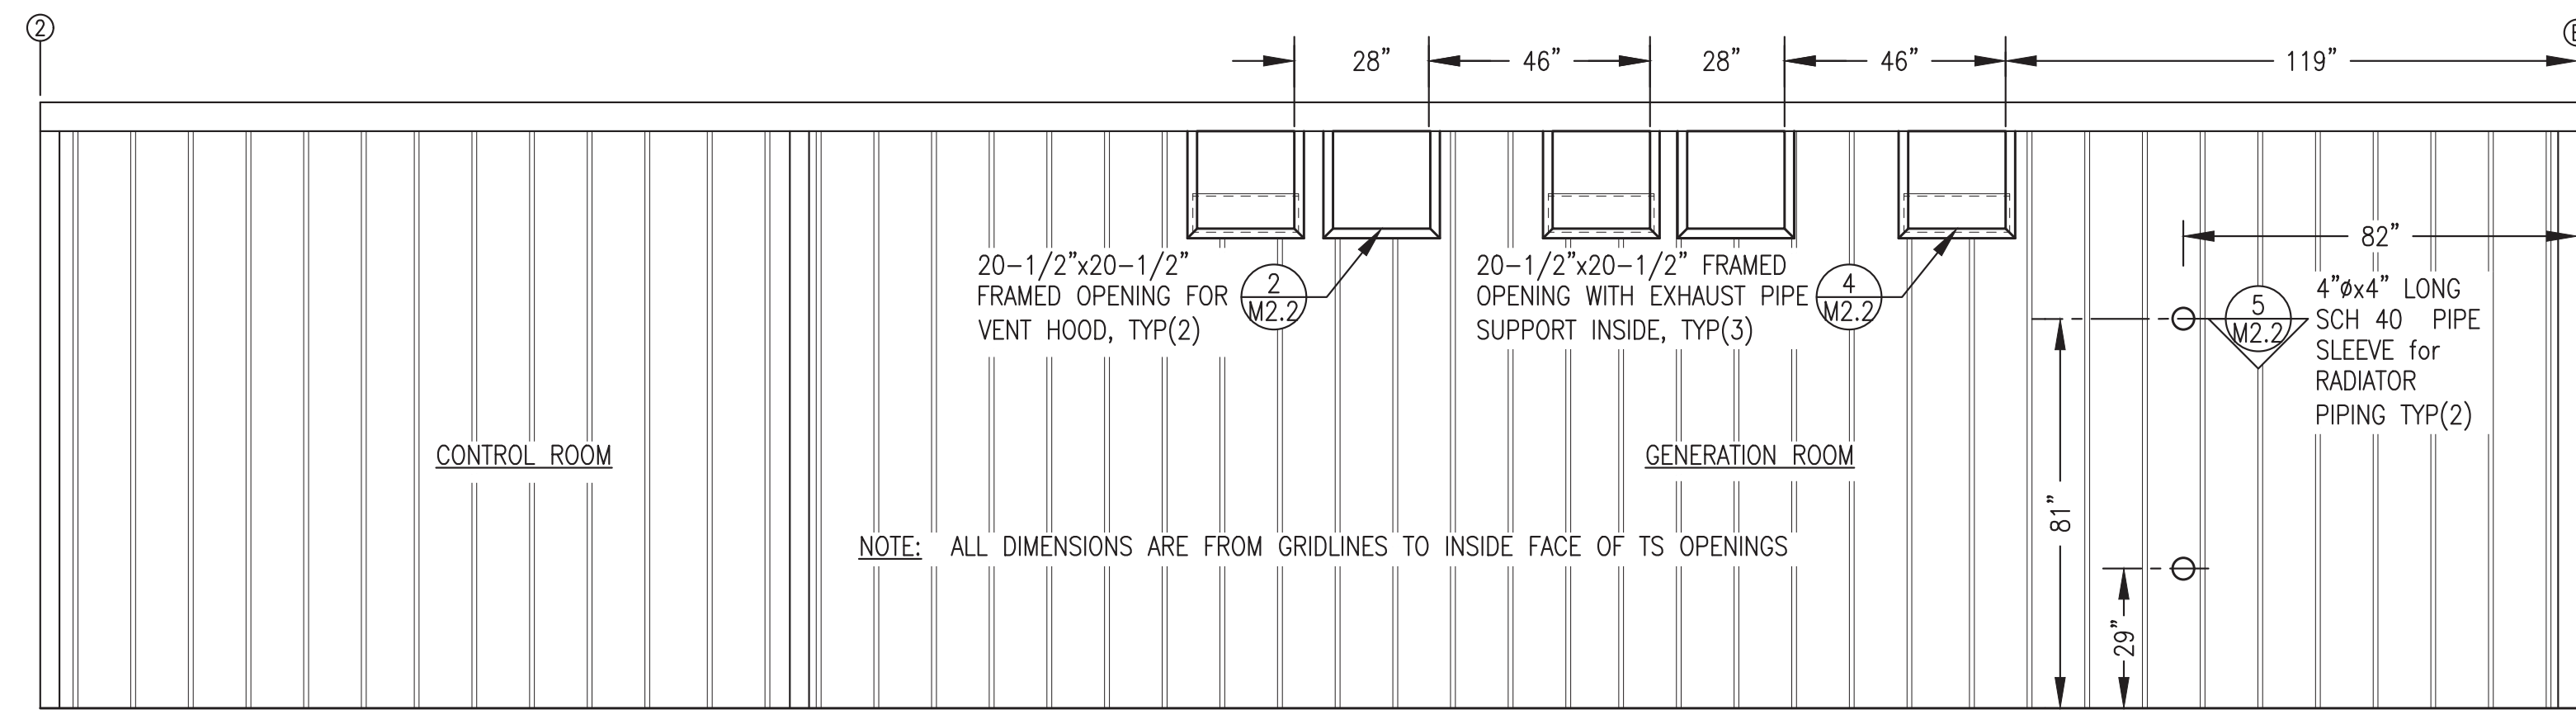


3 GRID A MECHANICAL WALL PENETRATION LAYOUT - EXTERIOR ELEVATION  
M2.1 3/8"=1'-0"

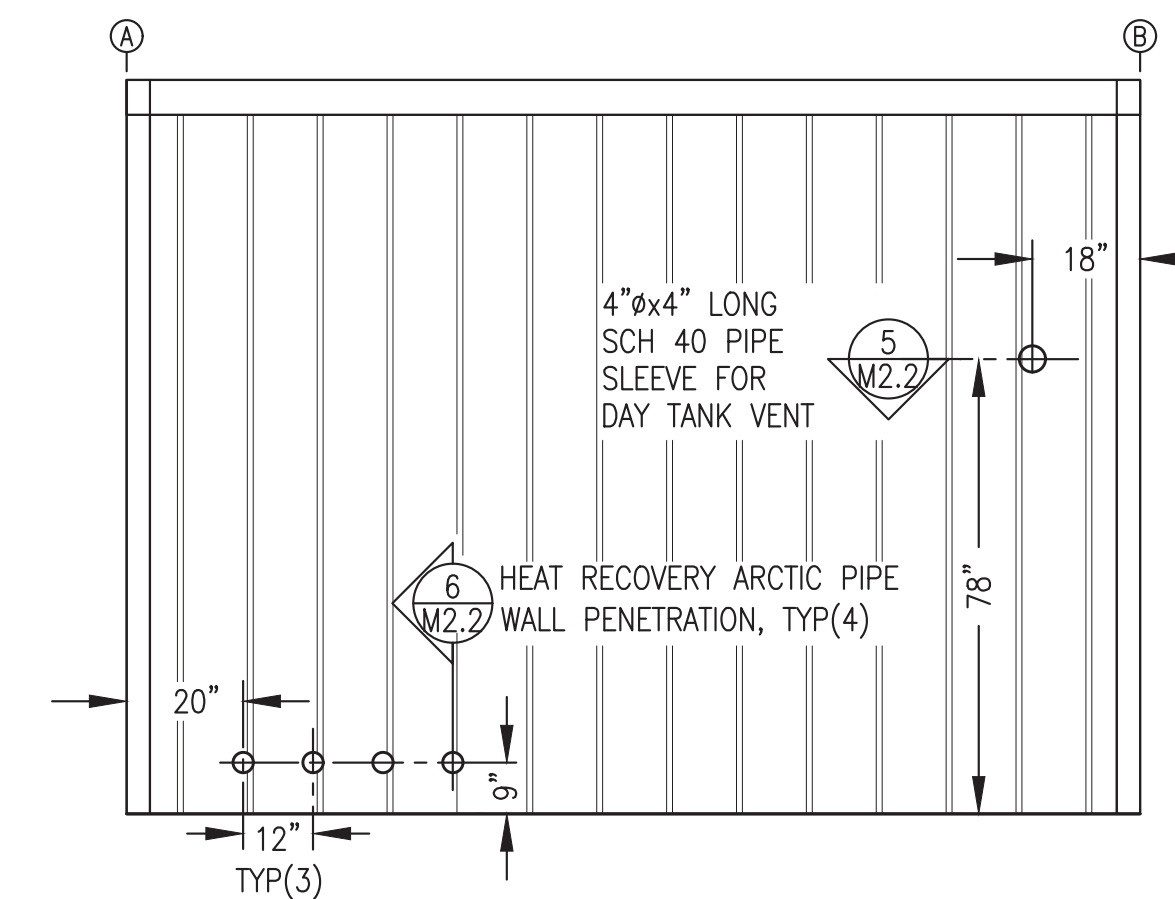

4 GRID 1 MECHANICAL WALL PENETRATION LAYOUT - EXTERIOR ELEVATION  
M2.1 3/8"=1'-0"

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE FABRICATION OF THE OWNER FURNISHED MODULE STRUCTURE AND IS PROVIDED FOR REFERENCE ONLY. SEE OWNER FURNISHED MODULE STRUCTURE REFERENCE DRAWINGS FOR ADDITIONAL DETAIL.

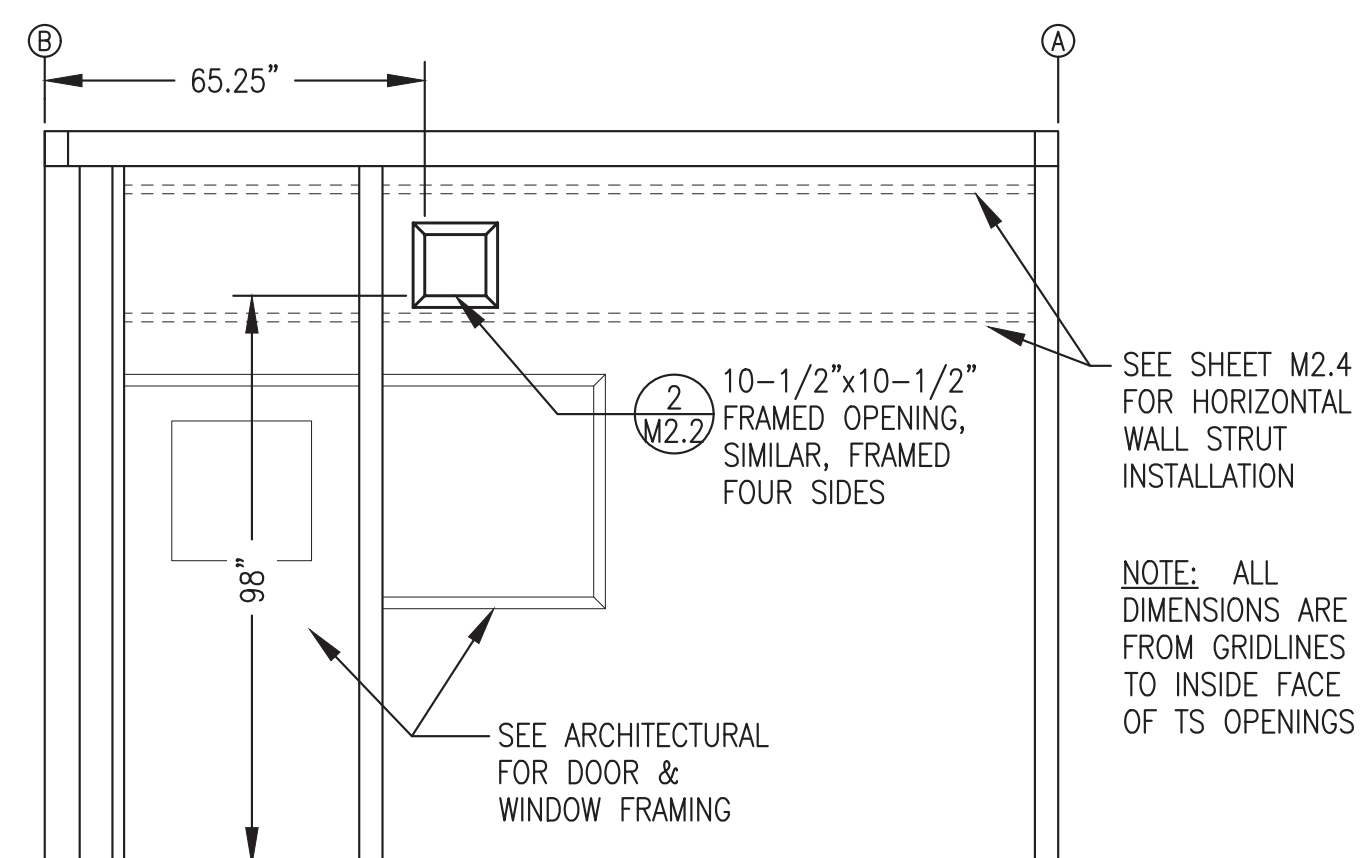



5 PARTITION MECHANICAL WALL PENETRATION LAYOUT - INTERIOR ELEVATION  
M2.1 3/8"=1'-0"

ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022




ALASKA ENERGY AUTHORITY	
PROJECT:	RAMPART POWER SYSTEM UPGRADE
TITLE:	MECHANICAL PENETRATIONS PLAN, ELEVATIONS & DETAILS
DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP M2-M7	SHEET:
PROJECT NUMBER:	<b>M2.1</b>
P.O. 111405, Anchorage, AK 99511 (907)349-0100	



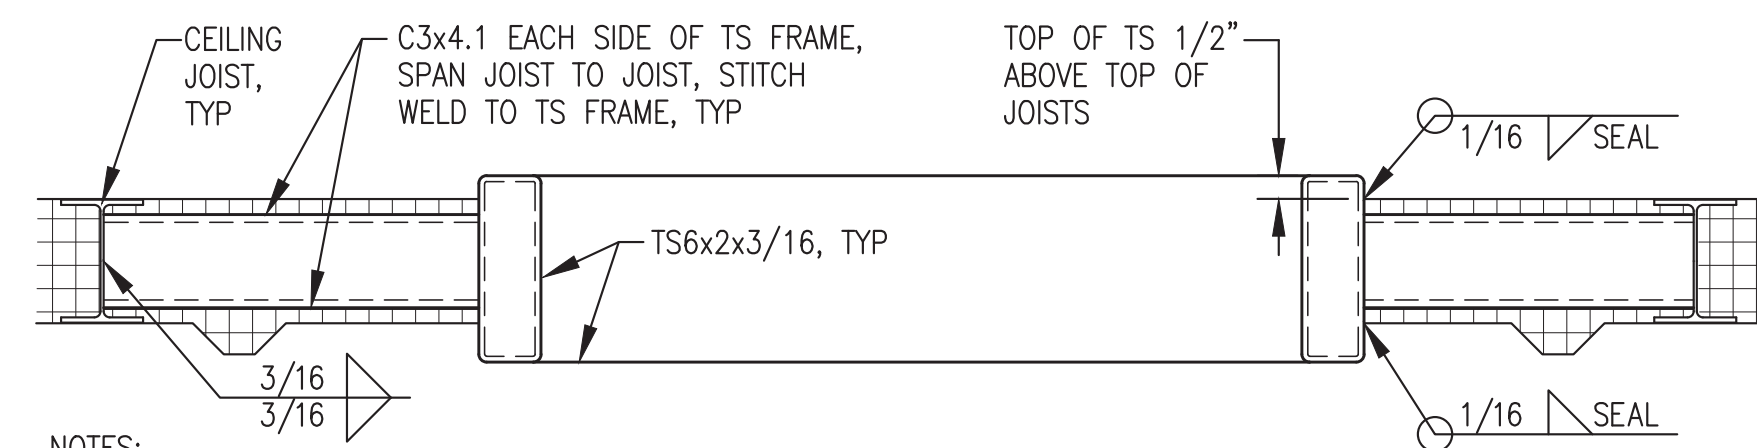


- NOTES:
- 1) FABRICATE FRAMED OPENING WITH MITERED CORNERS AND FULL PENETRATION GROOVE WELDS.
  - 2) FABRICATE TO FINISHED INSIDE (CLEAR) DIMENSIONS INDICATED ON PLANS.
  - 3) GRIND OUT INSIDE OF MITERED CORNERS TO PROVIDE FULL CLEAR OPENING.

**1** TYPICAL ROOF OPENING DETAIL  
M2.2 2'-1'-0"

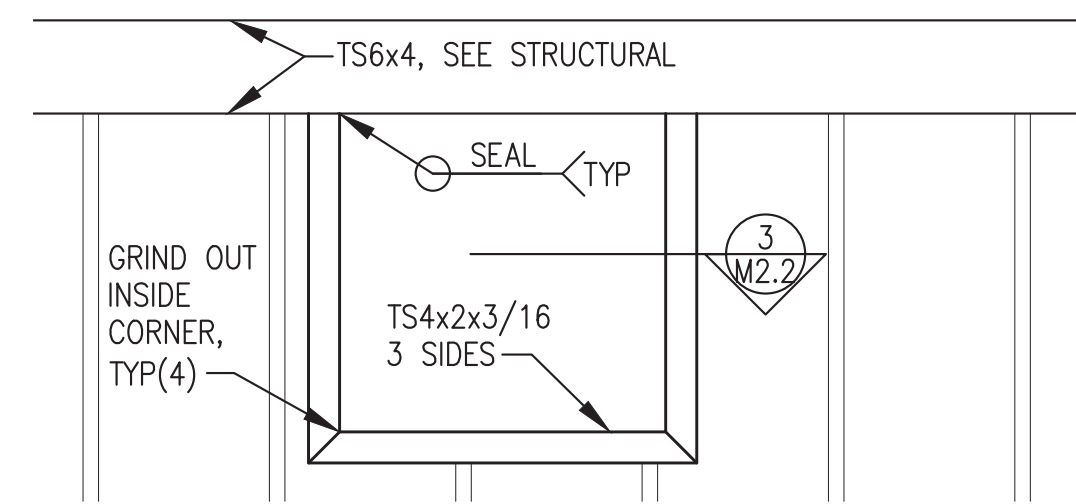


NOTE: SEE ELEVATION FOR INSIDE CLEAR OPENING SIZE.

**2** TYPICAL WALL OPENING - ELEVATION  
M2.2 1'-1'-0"

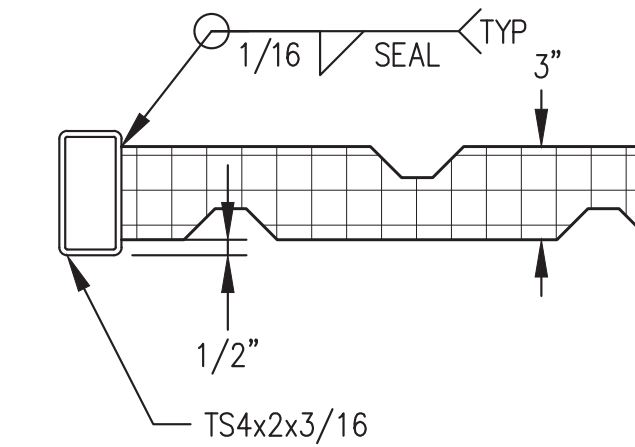


- NOTES:
- 1) FABRICATE FRAMED OPENING WITH MITERED CORNERS AND FULL PENETRATION GROOVE WELDS.
  - 2) FABRICATE TO FINISHED INSIDE (CLEAR) DIMENSIONS INDICATED ON ELEVATIONS.
  - 3) GRIND OUT INSIDE OF MITERED CORNERS TO PROVIDE FULL CLEAR OPENING.

**3** TYPICAL SECTION THROUGH WALL OPENING  
M2.2 2'-1'-0"

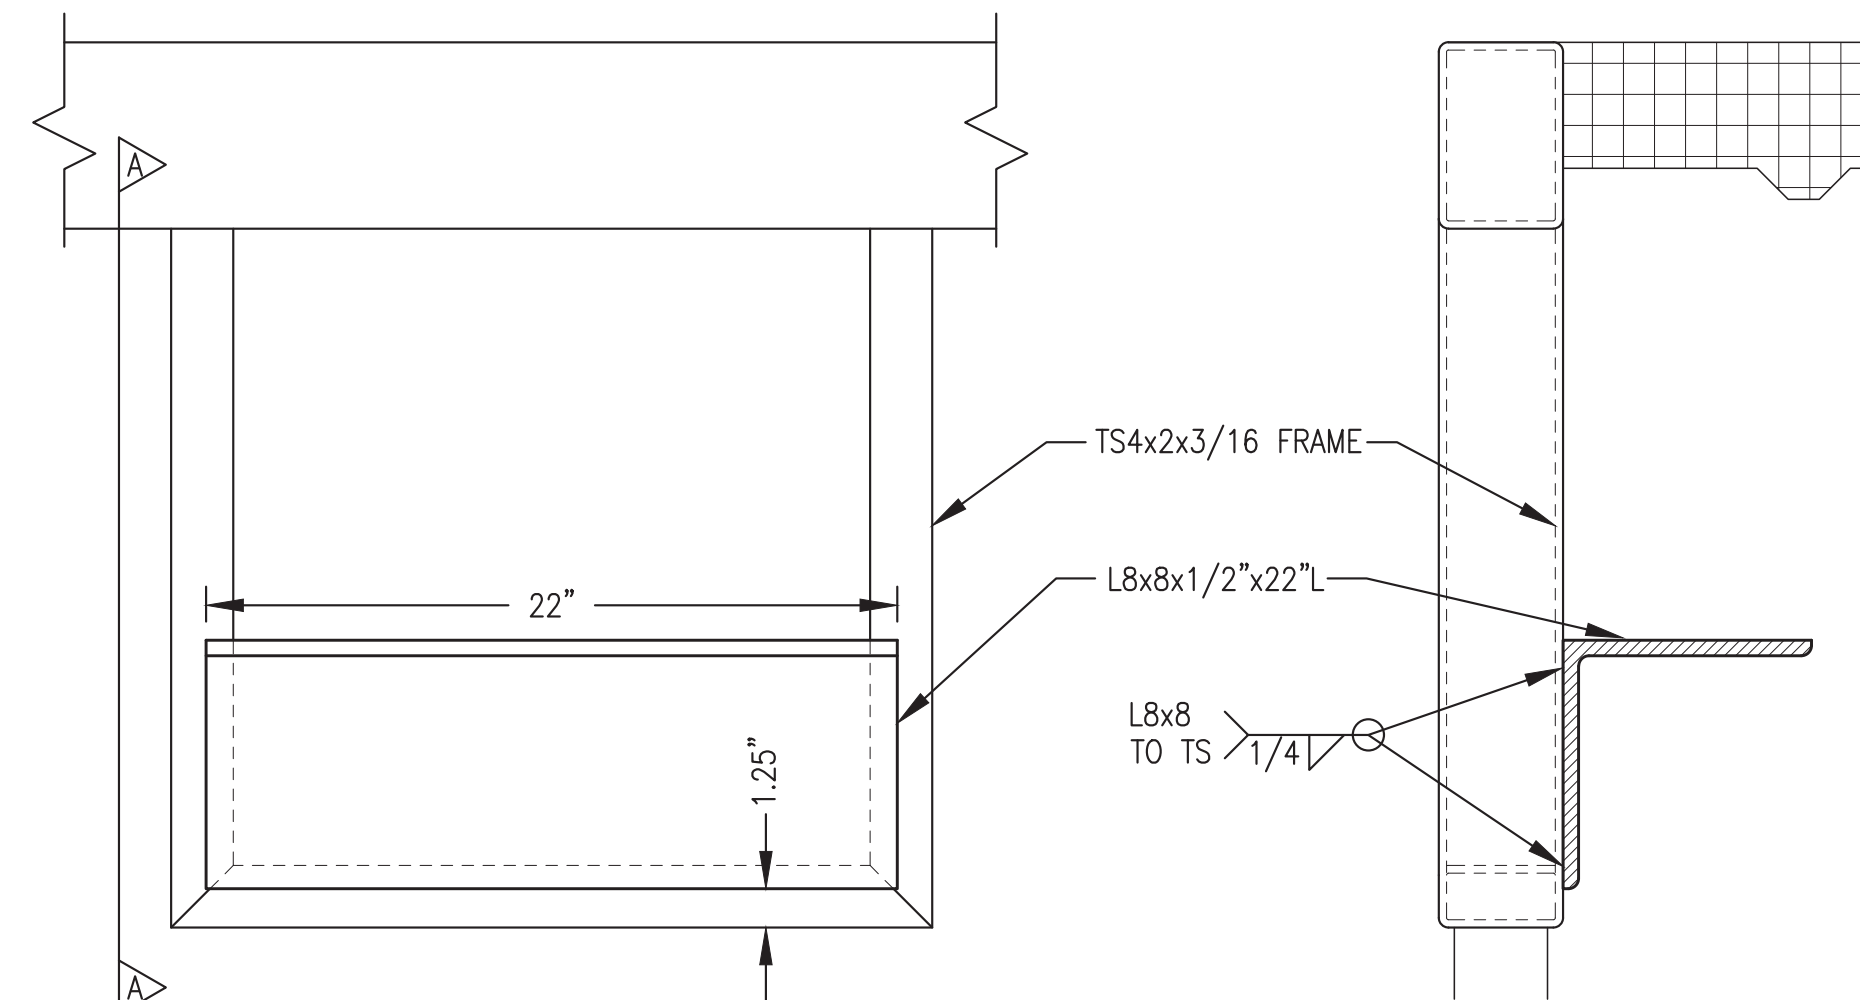


**4** EXHAUST PIPE SUPPORT AT FRAMED OPENING  
M2.2 2'-1'-0"

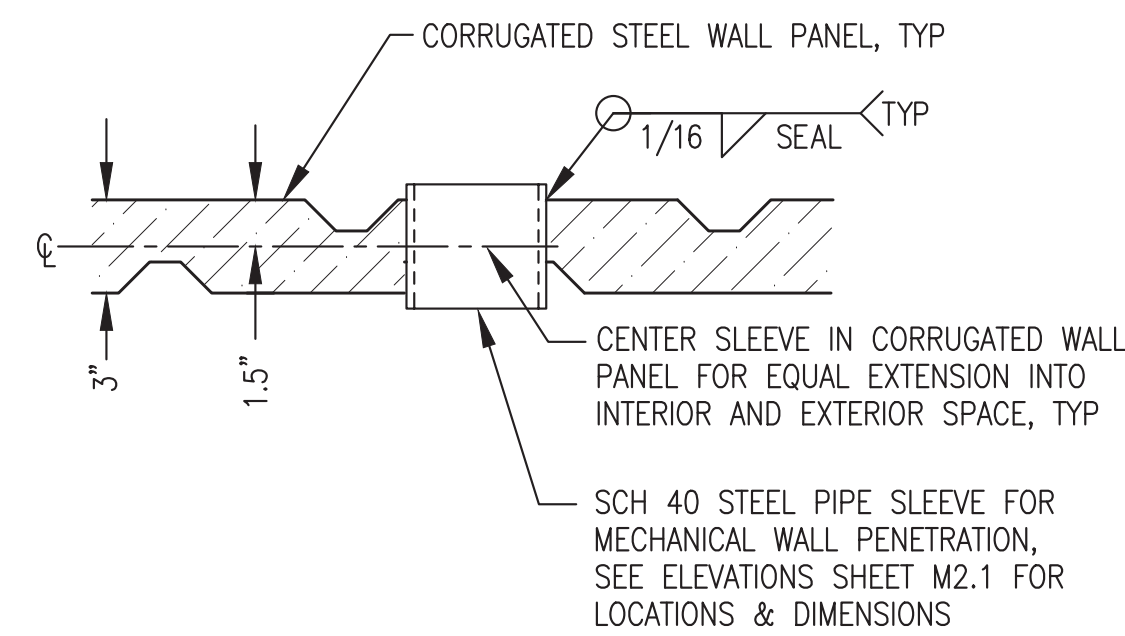


PLAN VIEW

**5** TYPICAL WALL PENETRATION PIPE SLEEVE  
M2.2 2'-1'-0"

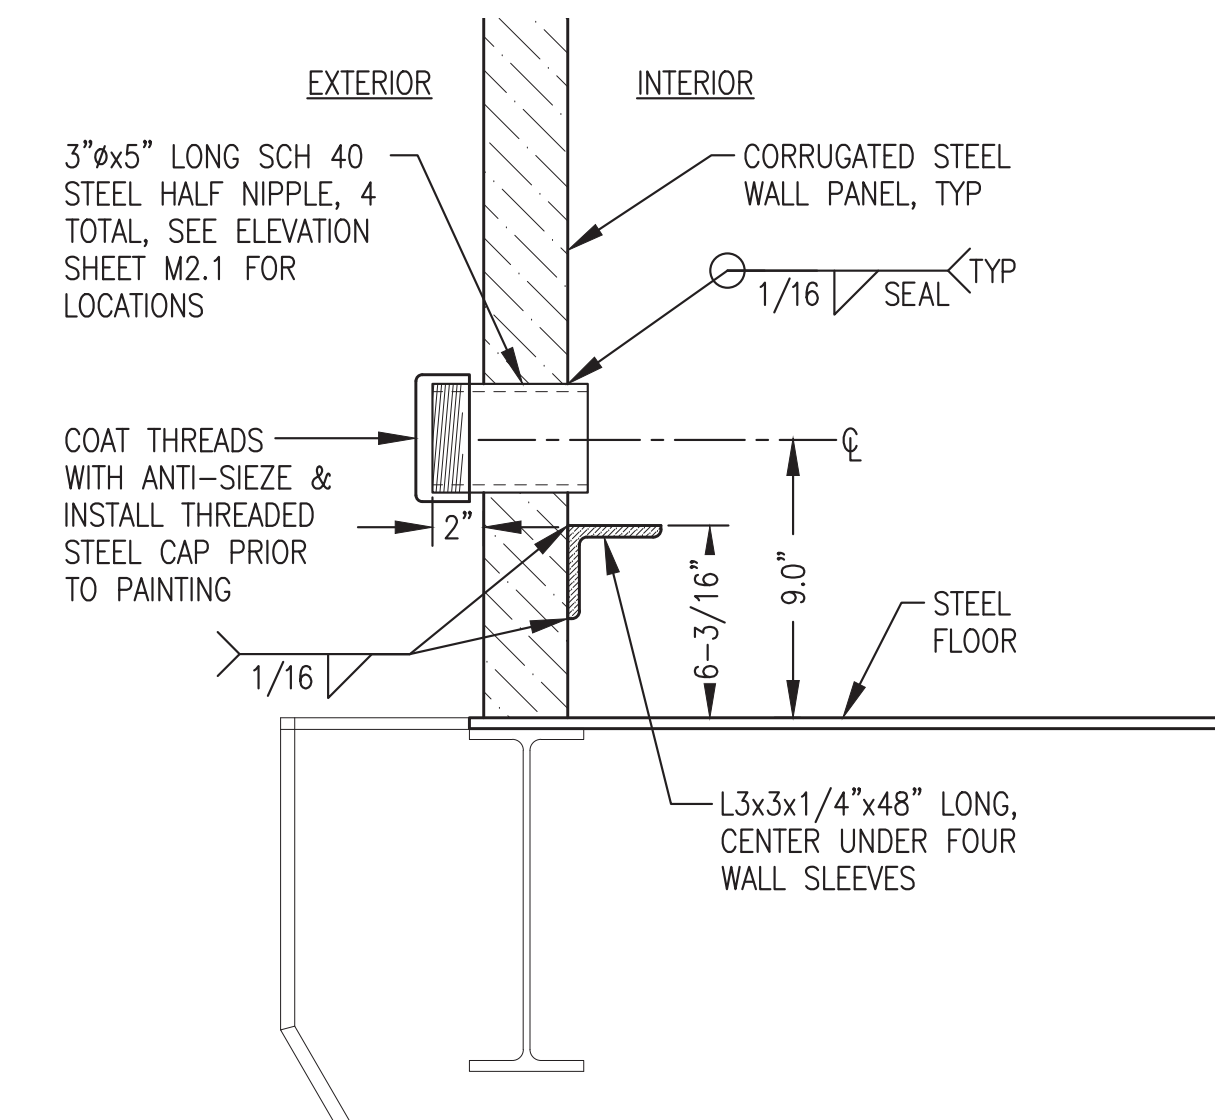

**6** TYPICAL HEAT RECOVERY ARCTIC PIPE WALL PENETRATION  
M2.2 2'-1'-0"

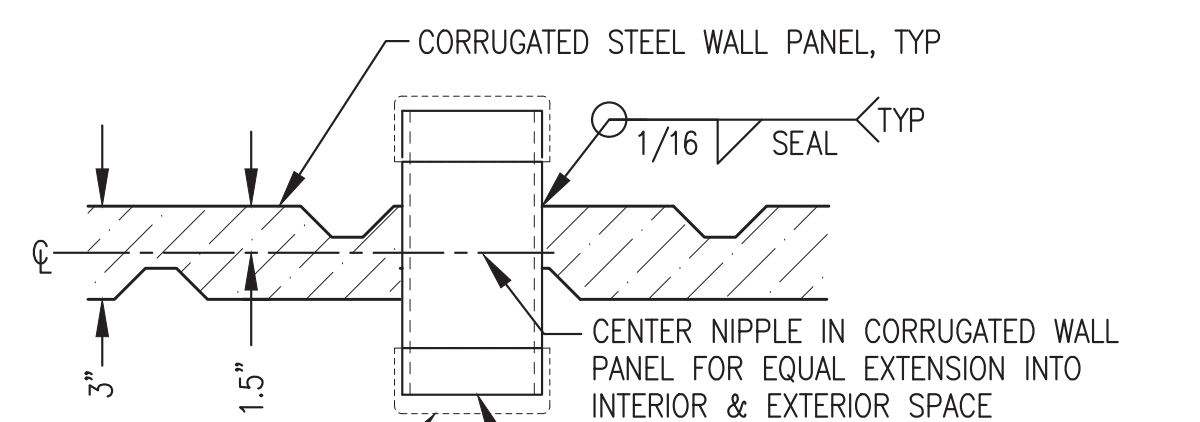

- COAT THREADS WITH ANTI-SIEZE & INSTALL THREADED CAP BOTH ENDS PRIOR TO PAINTING
- 3" x 8" LONG SCH 40 THREADED STEEL NIPPLE FOR ELECTRICAL WALL PENETRATION, SEE ELEVATIONS SHEET M2.1 FOR LOCATIONS

PLAN VIEW

**7** TYPICAL ELECTRIC POWER FEEDER CONDUCTOR WALL PENETRATION  
M2.2 2'-1'-0"

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE FABRICATION OF THE OWNER FURNISHED MODULE STRUCTURE AND IS PROVIDED FOR REFERENCE ONLY. SEE OWNER FURNISHED MODULE STRUCTURE REFERENCE DRAWINGS FOR ADDITIONAL DETAIL.

ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022




PROJECT: RAMPART POWER SYSTEM UPGRADE

TITLE: MECHANICAL PENETRATION DETAILS

DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP_M2-M7	SHEET: M2.2
PROJECT NUMBER:	




P.O. 111405, Anchorage, AK 99511 (907)349-0100

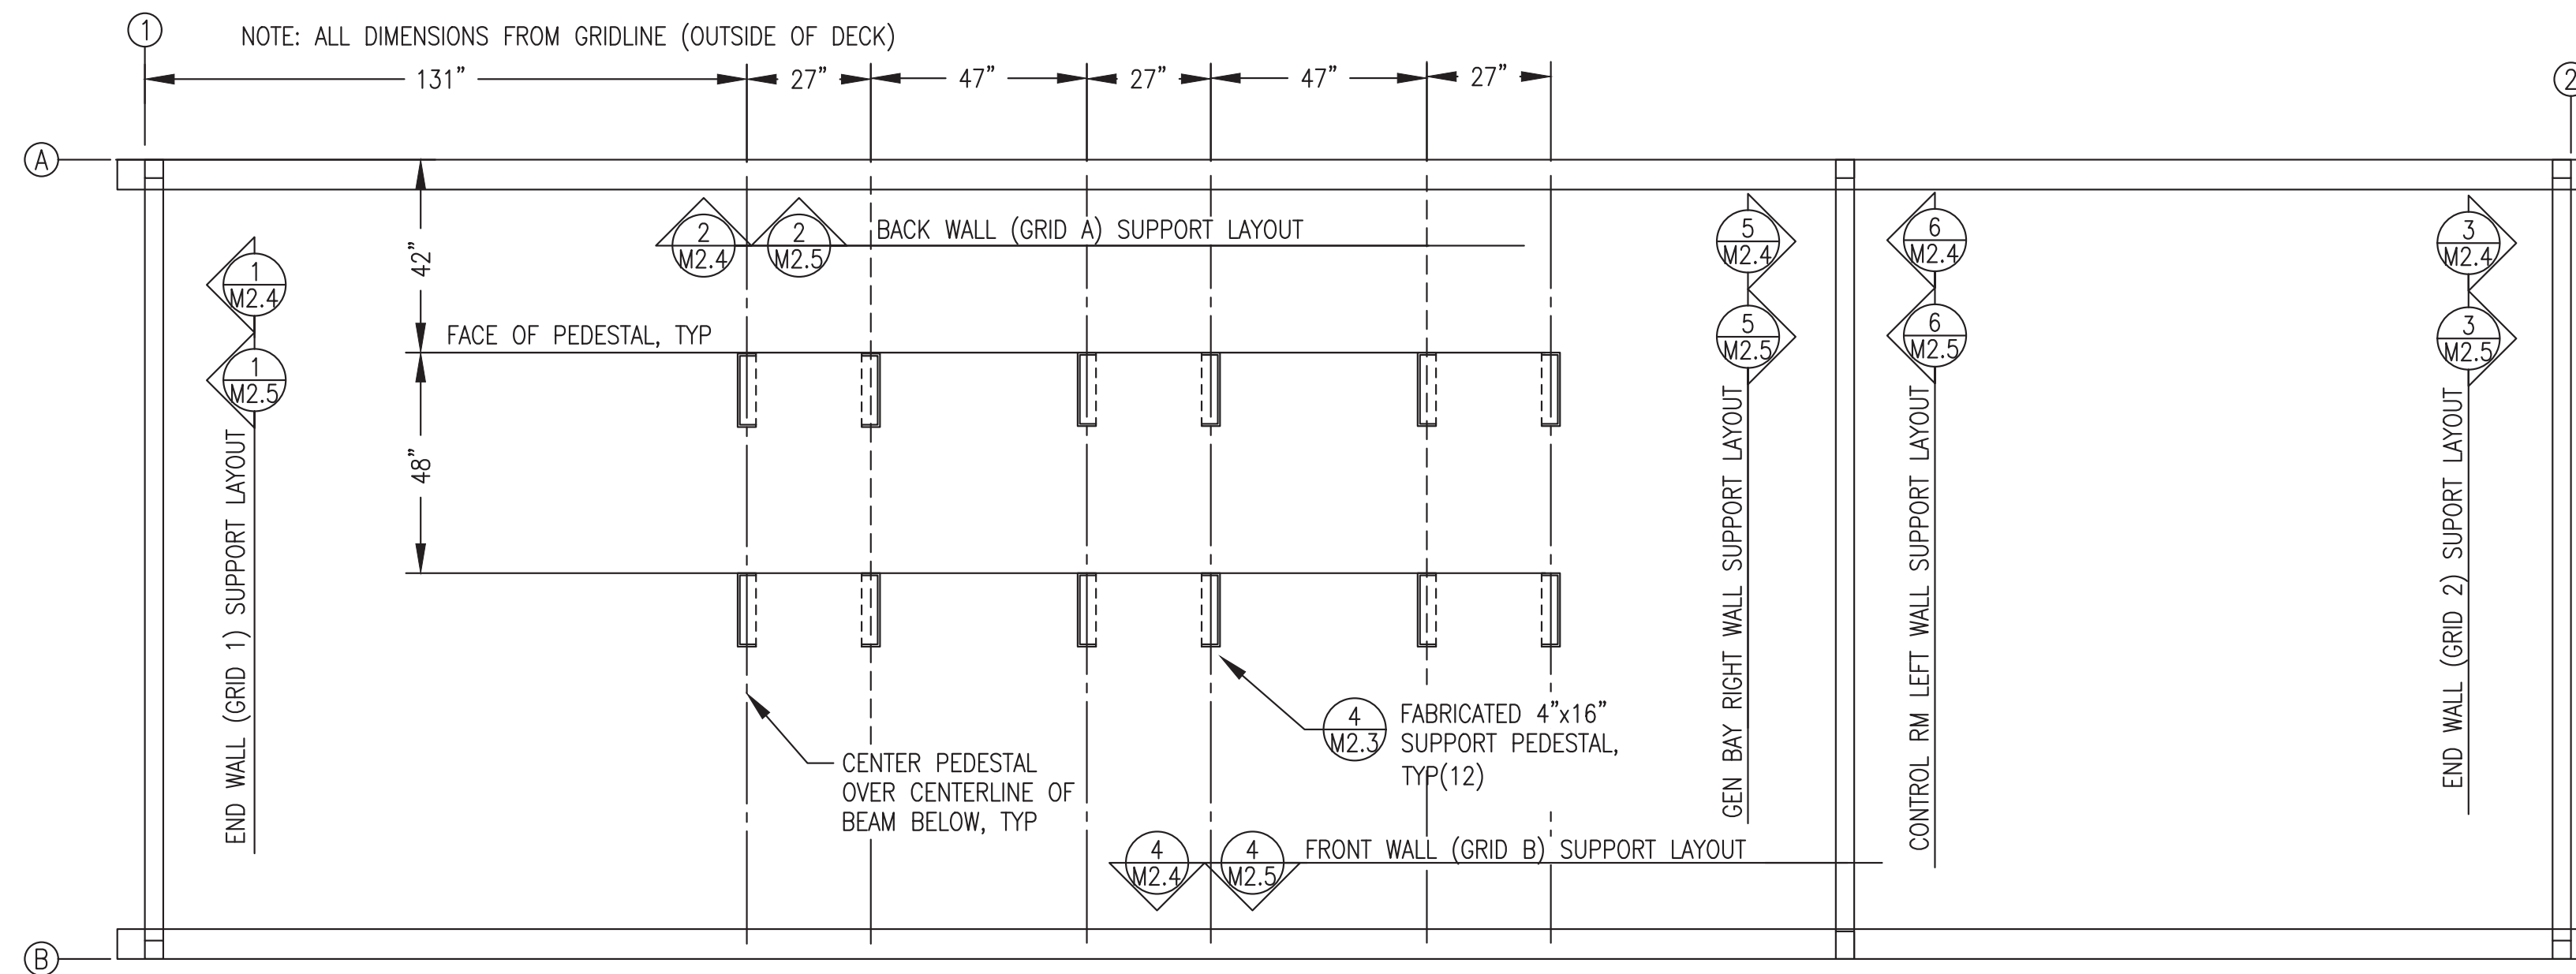


**1** MODULE MECHANICAL SUPPORT PLAN

M2.3 3/8"=1'-0"

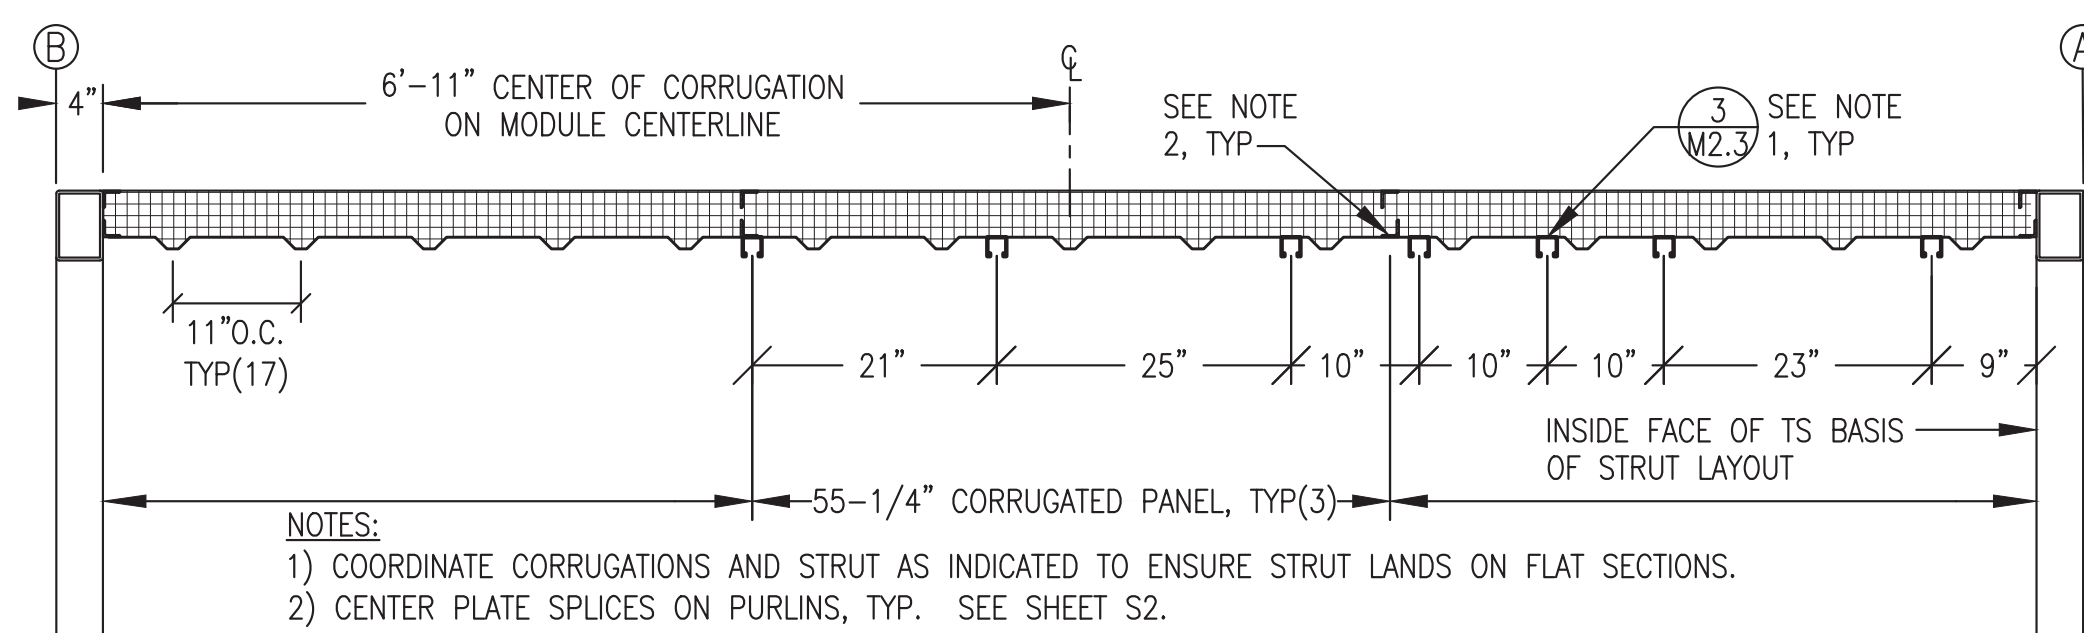

**2** SECTION THROUGH CEILING - CORRUGATION & STRUT LAYOUT


M2.3 3/4"=1'-0"

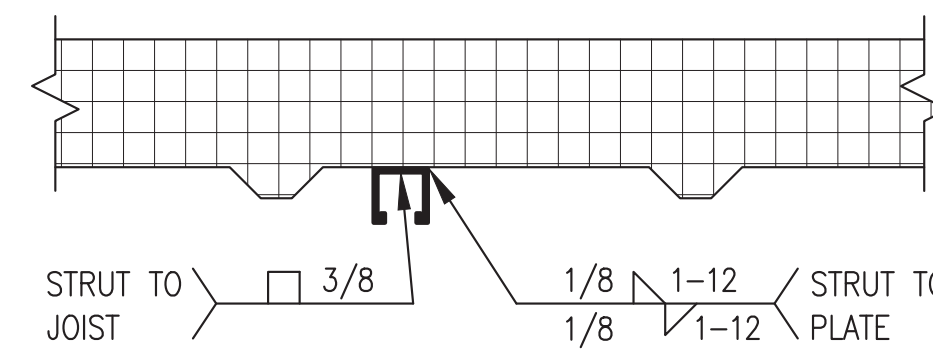

**3** STRUT ATTACHMENT TO CEILING

M2.3 NO SCALE


- GENERAL NOTES:**
- 1) FABRICATE PEDESTALS FROM ASTM A36 ANGLE AND PLATES AS SHOWN.
  - 2) ALL STRUT 12 GAUGE 1-5/8"x1-5/8" SOLID BACK PLAIN (UNFINISHED). B-LINE B22-PLN OR EQUAL. PURCHASE IN 20' LENGTHS TO MINIMIZE SPLICES.
  - 3) INSTALL ALL SUPPORTS INDICATED AND GRIND SMOOTH PRIOR TO SANDBLASTING MODULE. SANDBLAST AND PAINT ALL SUPPORTS THIS SHEET EQUIVALENT TO MODULE INTERIOR. SEE SHEET A1 FOR PAINTING SPECIFICATIONS.

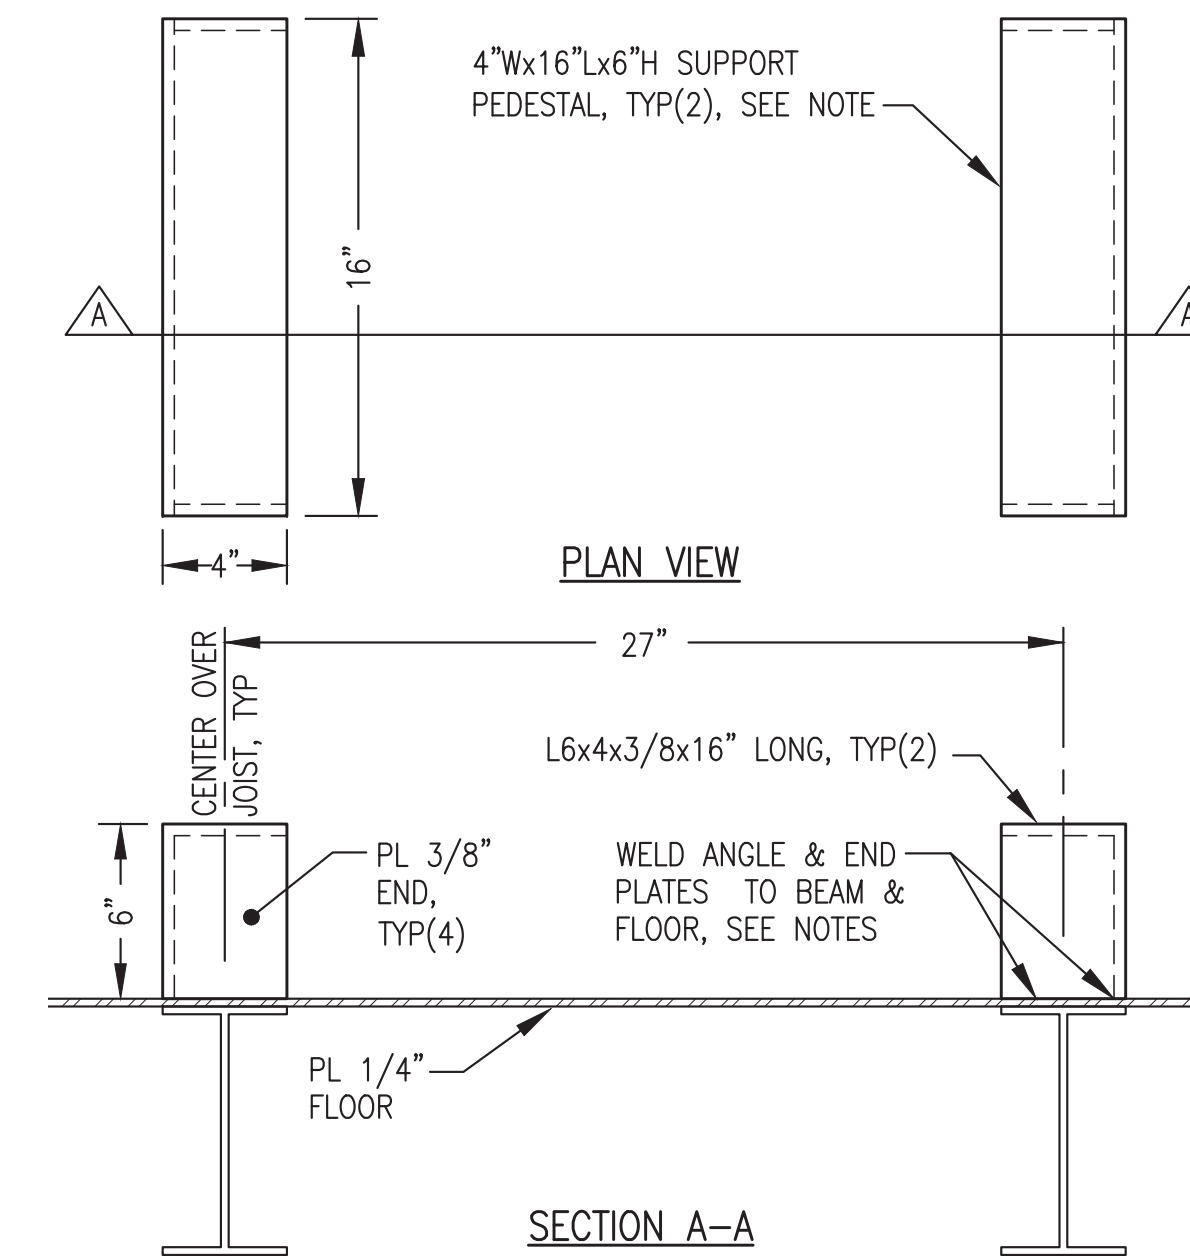

- NOTES:**
- 1) MAKE ALL JOINTS WITH CONTINUOUS GROOVE OR FILLET WELDS.
  - 2) SLOT FLOOR PLATE 3 SIDES, WELD PEDESTAL TO TOP OF BEAM, THEN SEAL WELD TO FLOOR PLATE ALL AROUND INSIDE & OUT.


**4** SUPPORT PEDESTAL FABRICATION

M2.3 2"=1'-0"

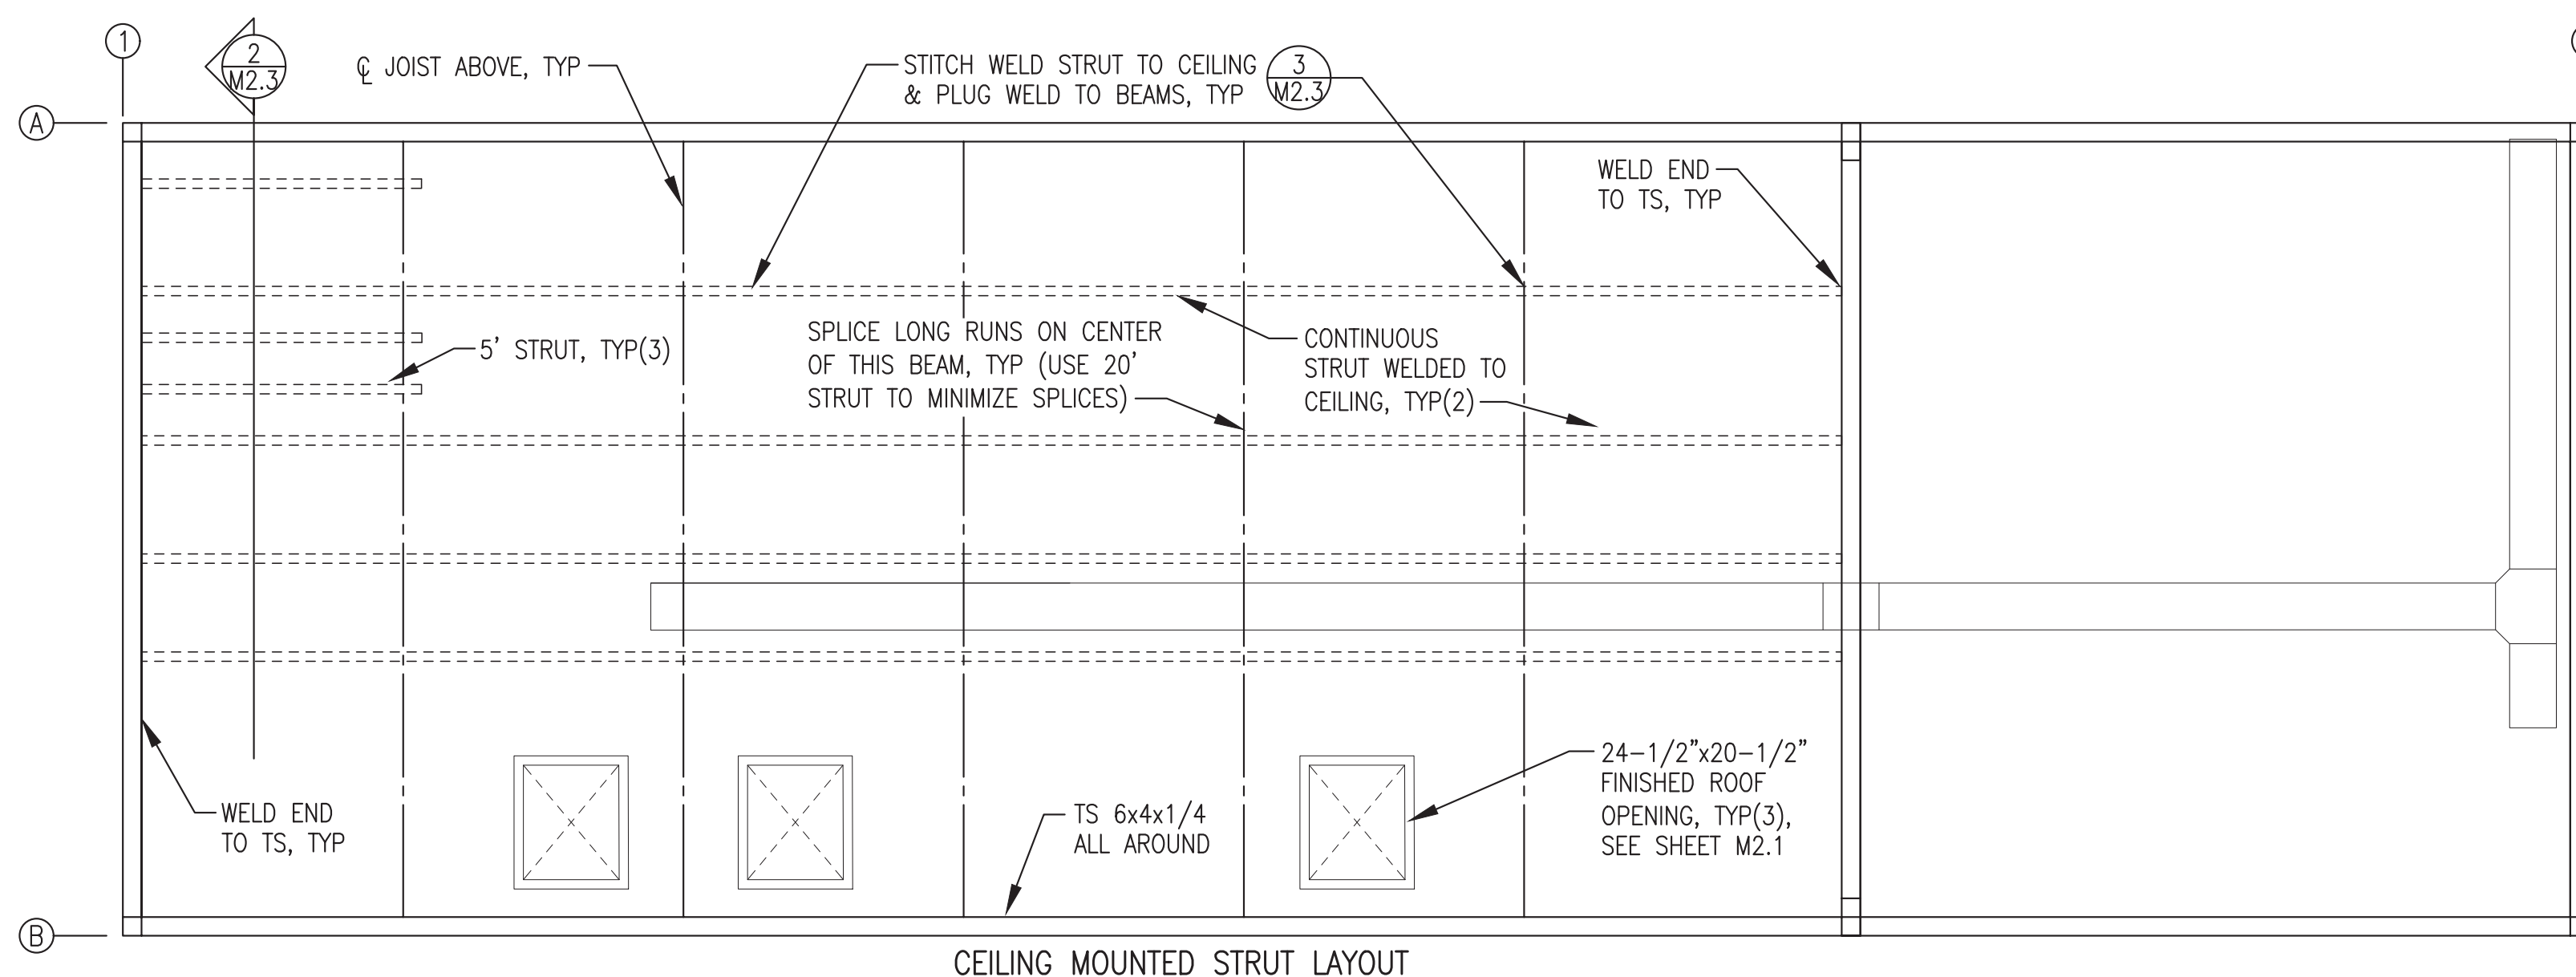

**5** CEILING STRUT SUPPORT LAYOUT PLAN


M2.3 3/8"=1'-0"

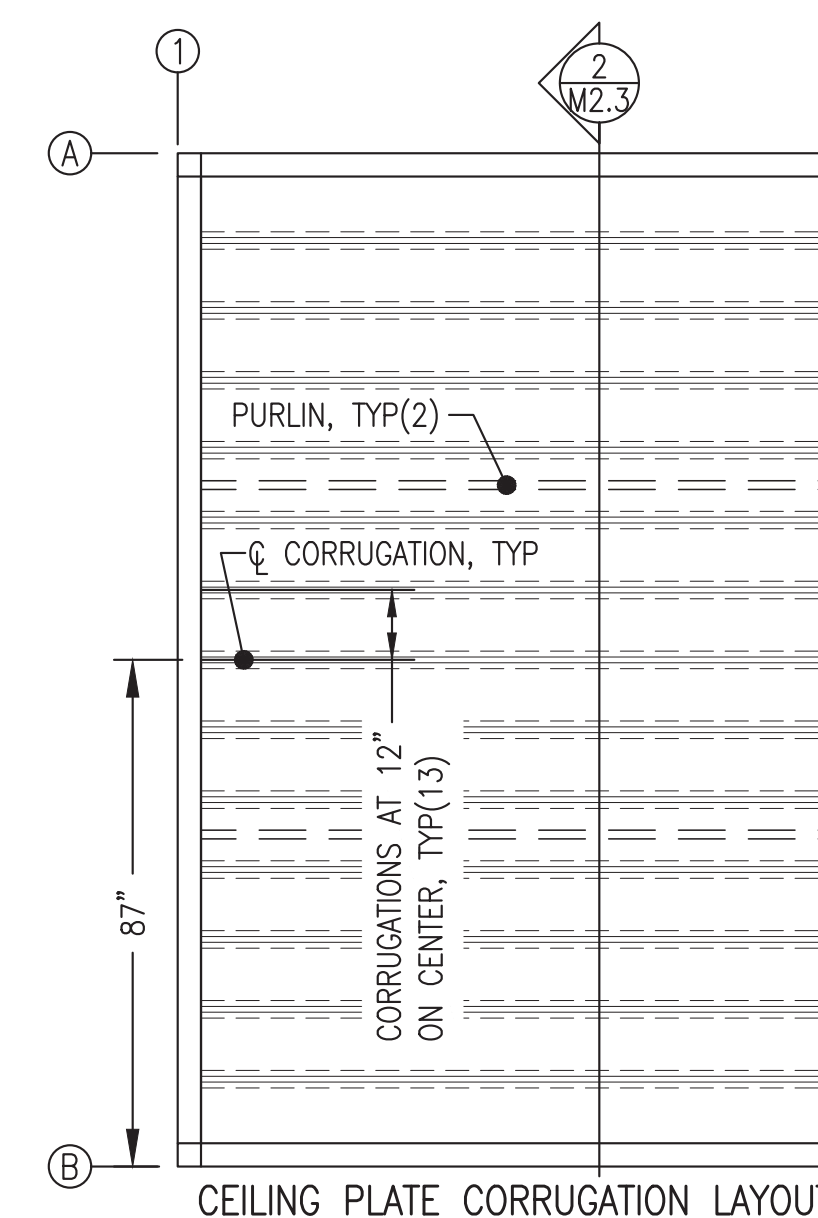


CEILING PLATE CORRUGATION LAYOUT

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE FABRICATION OF THE OWNER FURNISHED MODULE STRUCTURE AND IS PROVIDED FOR REFERENCE ONLY. SEE OWNER FURNISHED MODULE STRUCTURE REFERENCE DRAWINGS FOR ADDITIONAL DETAIL.


REVISION #1  
ISSUED JUNE  
2022




1	CHANGED INTERIOR PLATE CORRUGATIONS TO 11" O.C. & MOVED STRUT TO ALIGN	6/2/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: MECHANICAL SUPPORT PLANS & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET: M2.3	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

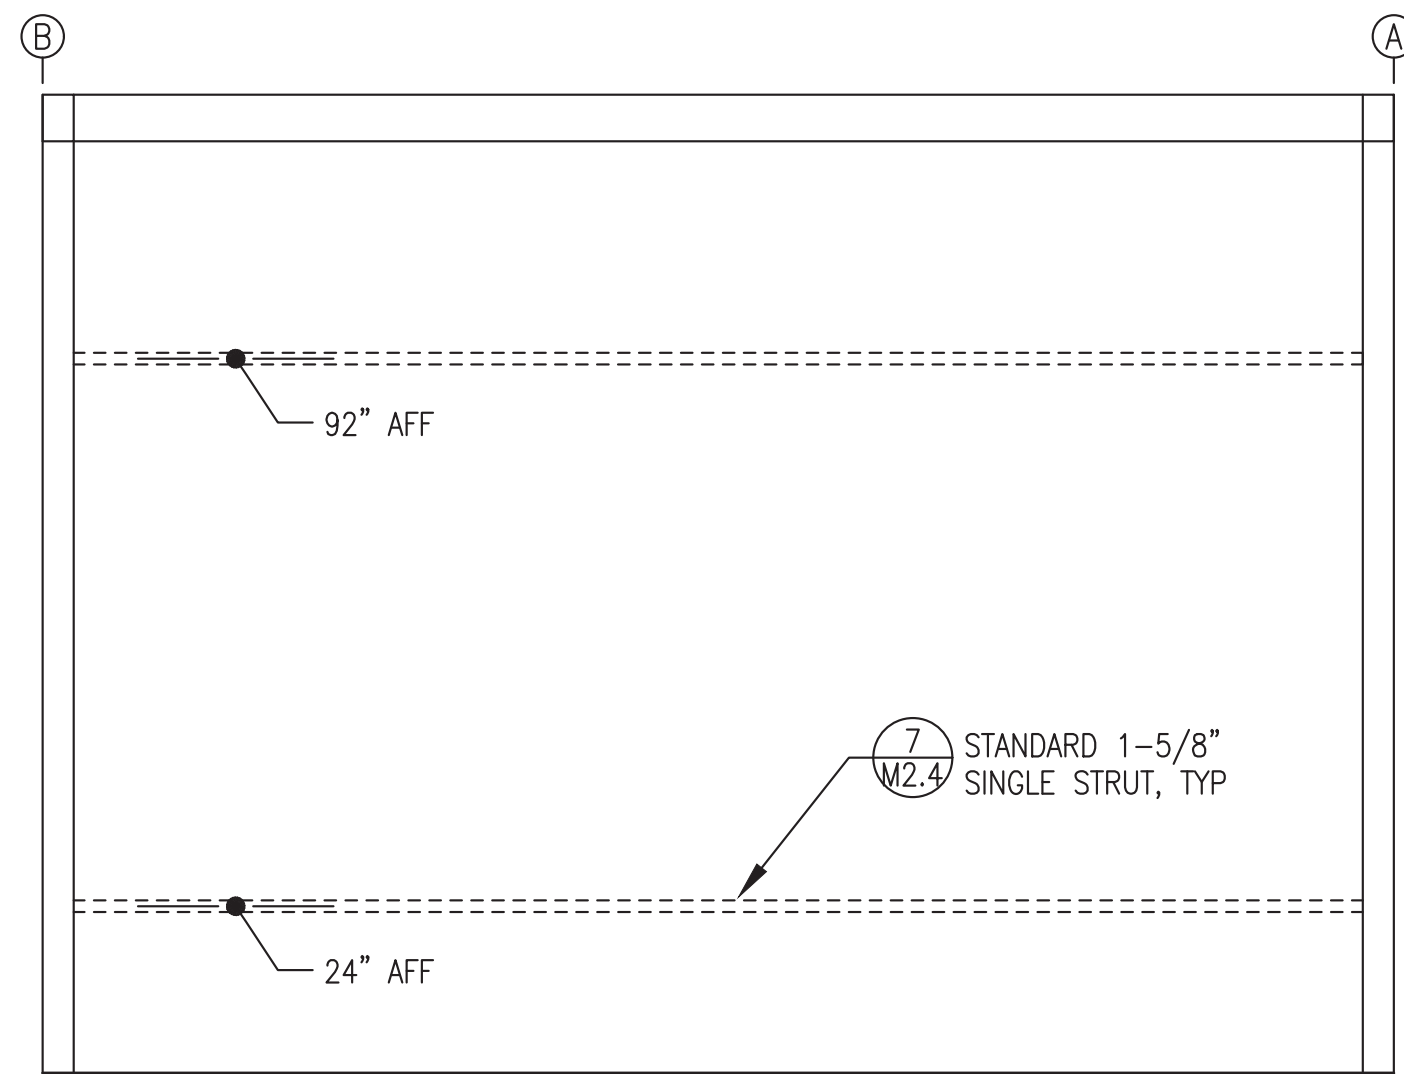


1 END WALL (GRID 1) HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

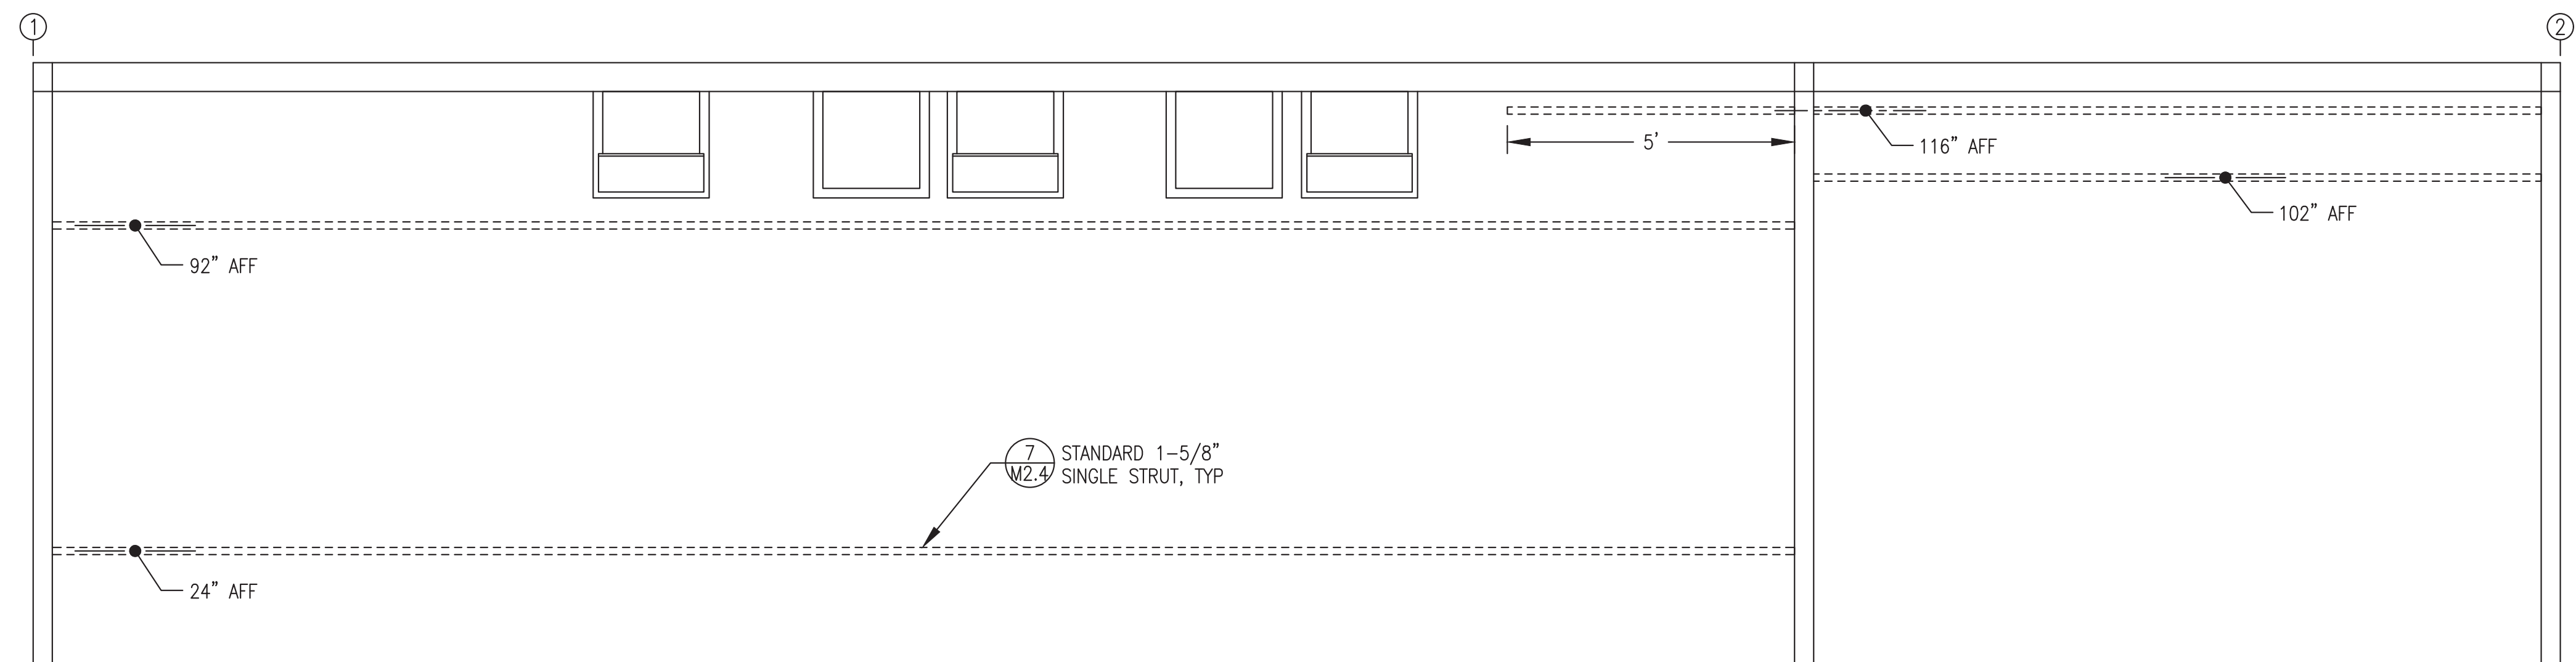


2 BACK WALL (GRID A) HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

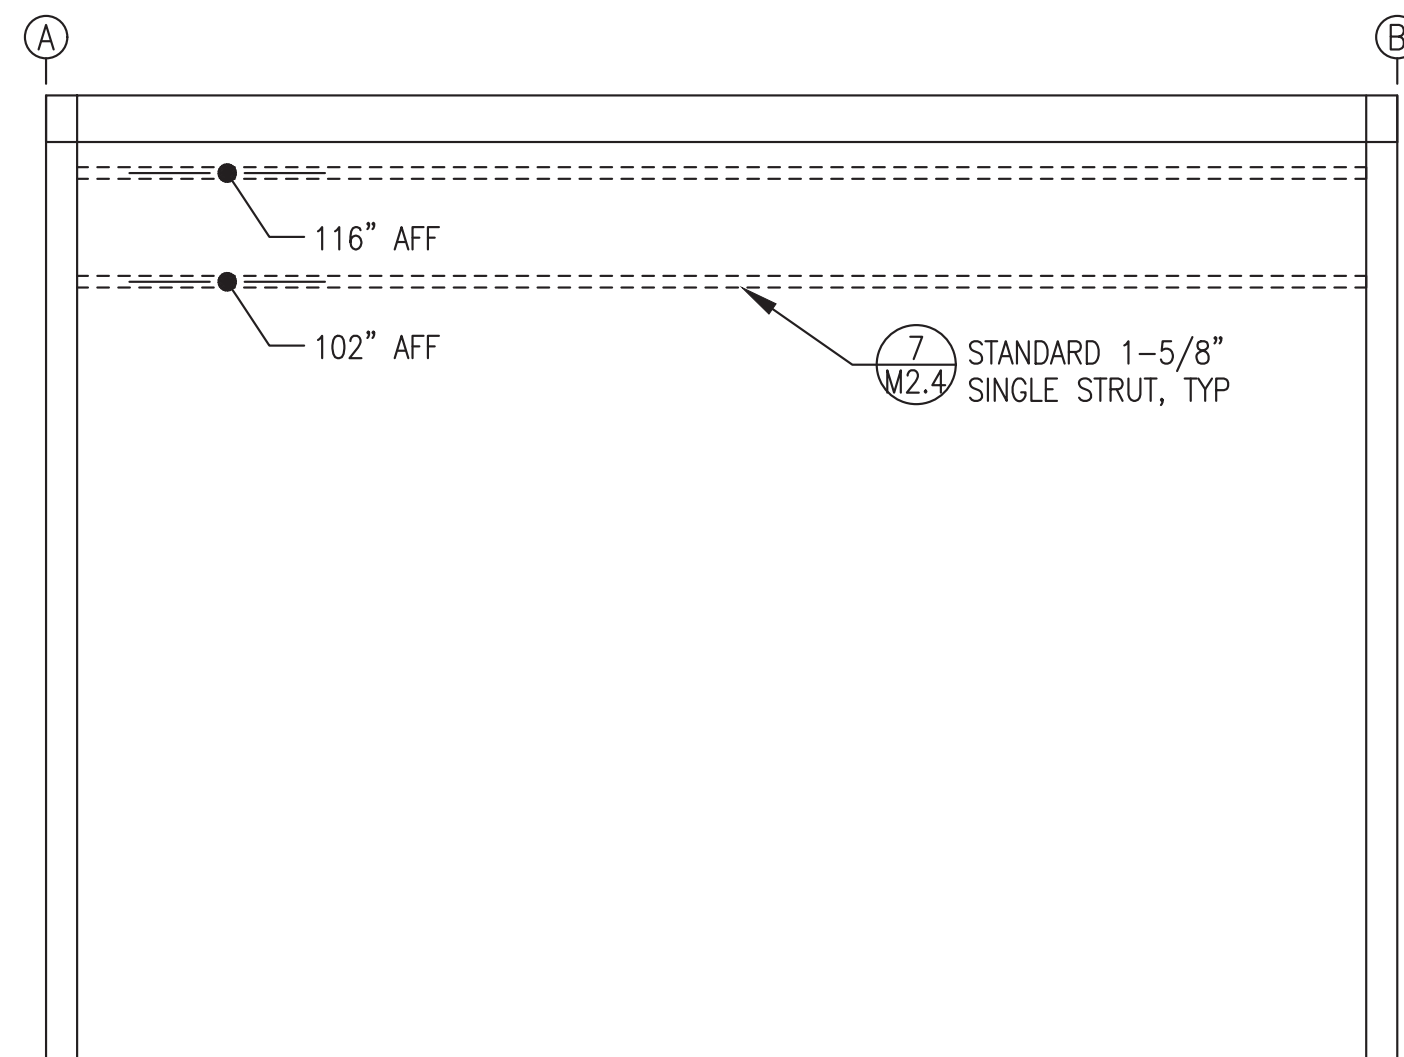


3 END WALL (GRID 2) HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

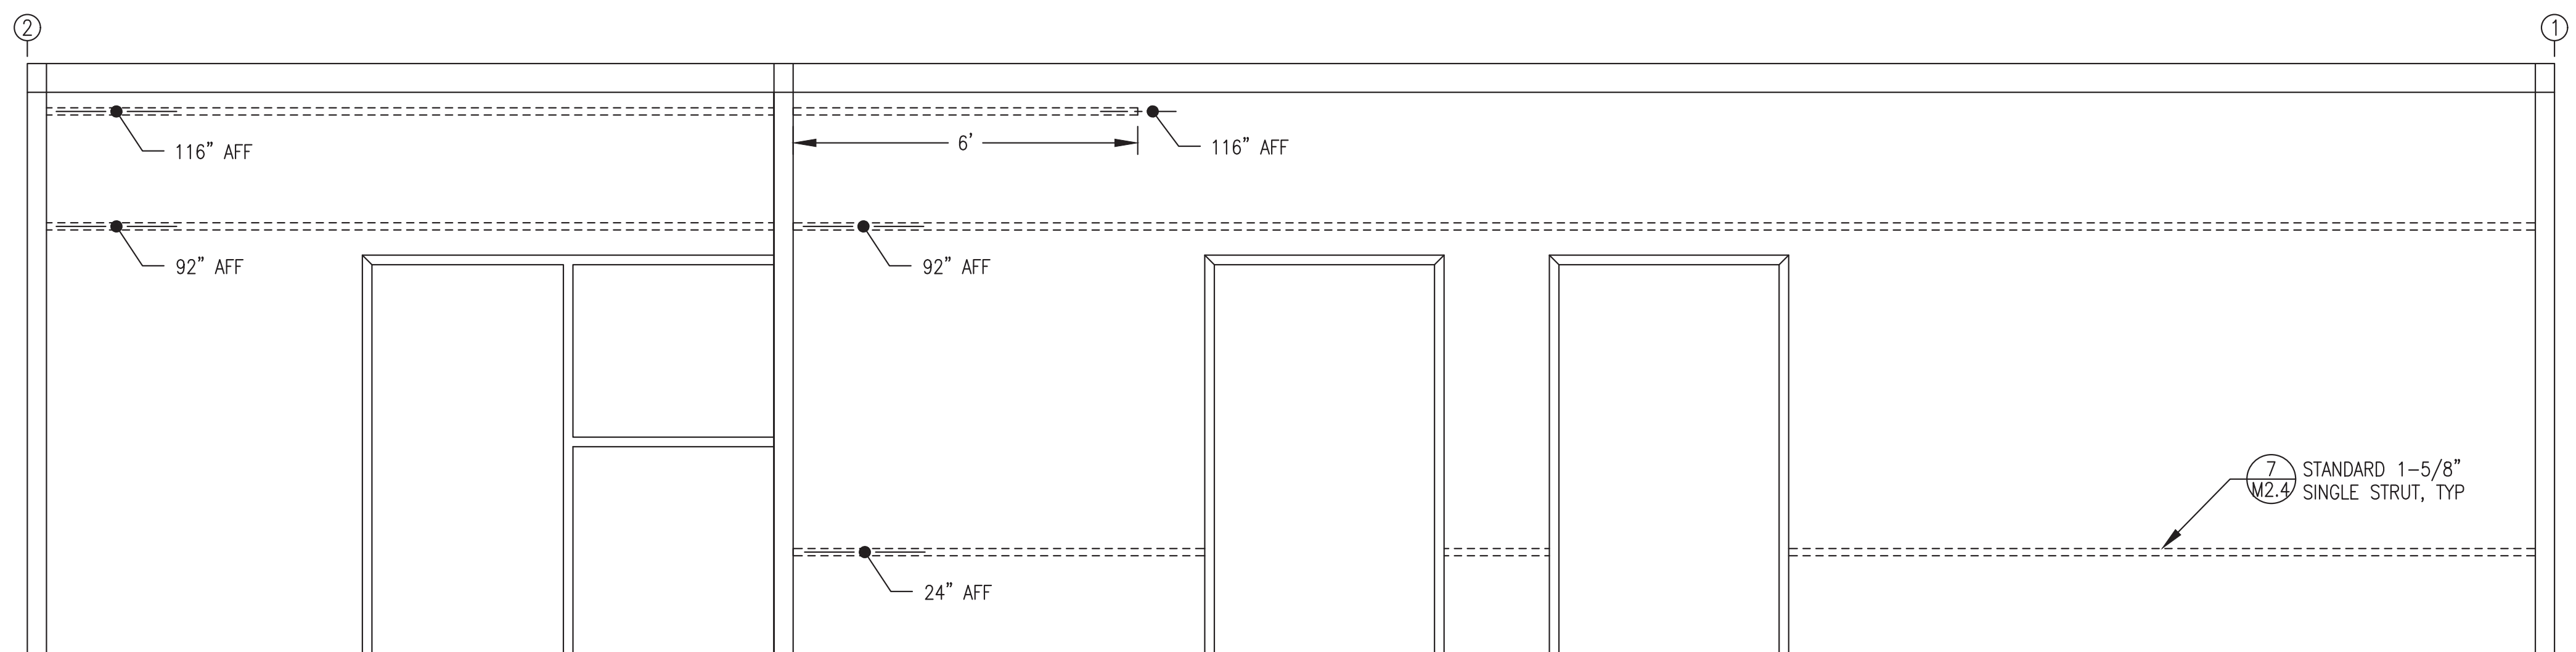

4 FRONT WALL (GRID B) HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

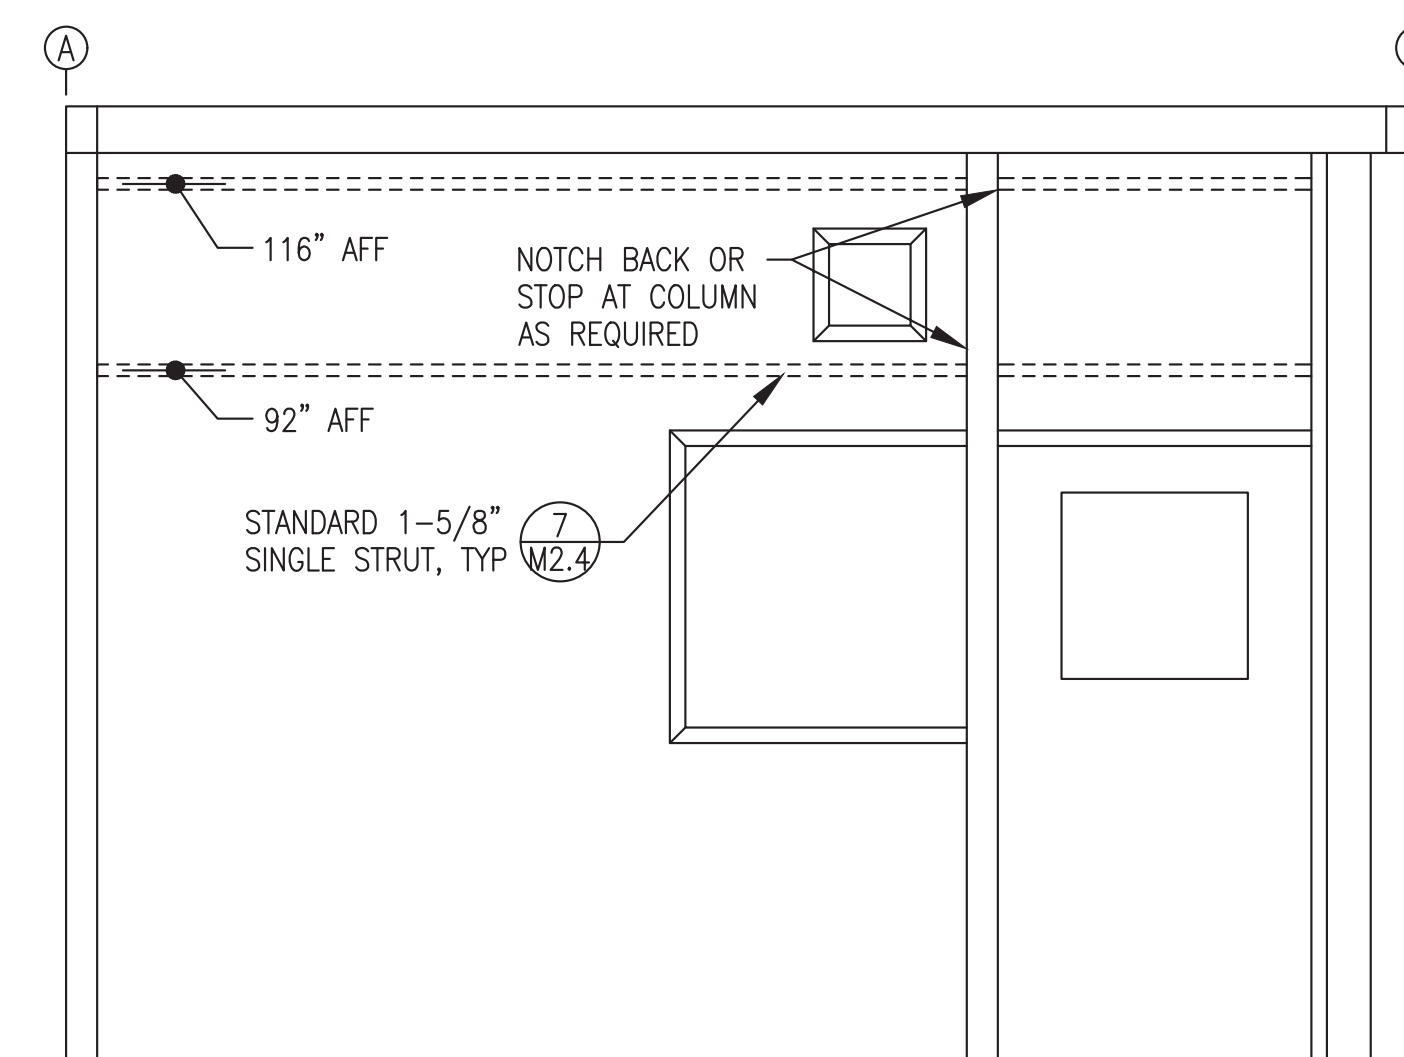


5 GEN BAY RIGHT WALL HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

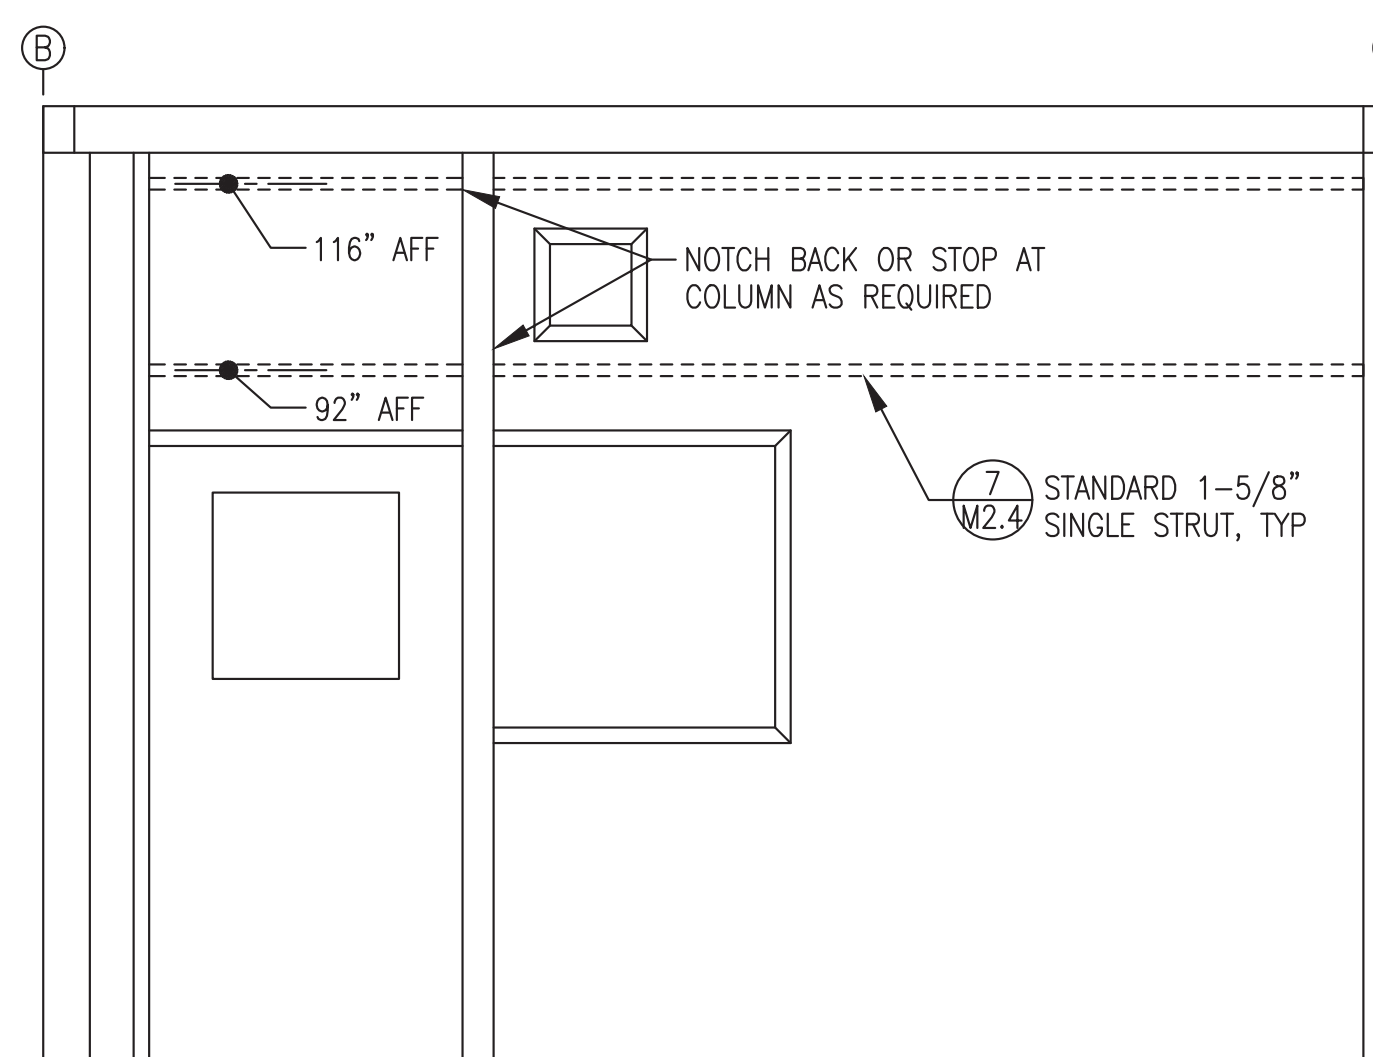

6 CONTROL ROOM LEFT WALL HORIZONTAL WALL STRUT LAYOUT  
M2.4 1/2"=1'-0"

- HORIZONTAL WALL STRUT INSTALLATION NOTES:**
- 1) ALL LOCATIONS ARE CENTERLINE OF STRUT ABOVE FINISHED FLOOR (AFF).
  - 2) ALL STRUT SHALL BE 12 GAUGE, 1-5/8" x 1-5/8", PLAIN (UN-FINISHED BLACK) WITH SOLID BACK, B-LINE B22-PLN OR EQUAL.
  - 3) PRIOR TO PAINTING MODULE, WELD ALL HORIZONTAL STRUT SECTIONS TO WALLS AS SHOWN. SANDBLAST AND PAINT STRUT WITH MODULE INTERIOR WALLS. SEE SHEET A1 FOR PAINTING SPECIFICATIONS.

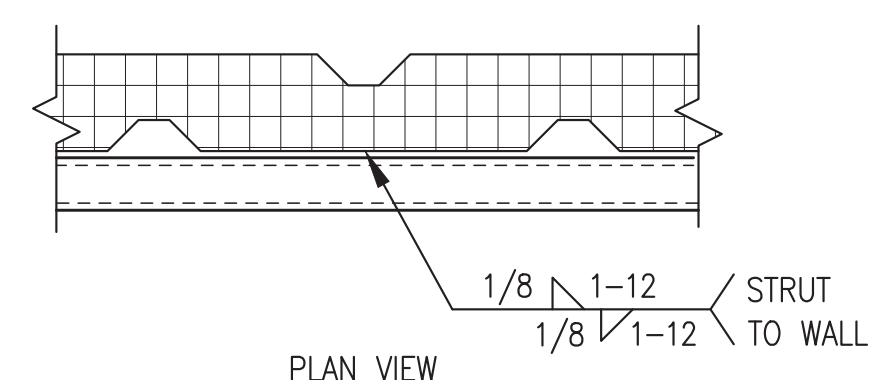

7 HORIZONTAL WALL STRUT ATTACHMENT  
M2.4 NO SCALE


THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE FABRICATION OF THE OWNER FURNISHED MODULE STRUCTURE AND IS PROVIDED FOR REFERENCE ONLY. SEE OWNER FURNISHED MODULE STRUCTURE REFERENCE DRAWINGS FOR ADDITIONAL DETAIL.

ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022




ALASKA ENERGY AUTHORITY	
PROJECT:	RAMPART POWER SYSTEM UPGRADE
TITLE:	MECHANICAL SUPPORT HORIZONTAL WALL STRUT INSTALLATION
DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP_M2-M7	SHEET:
PROJECT NUMBER:	<b>M2.4</b>
P.O. 111405, Anchorage, AK 99511 (907)349-0100	




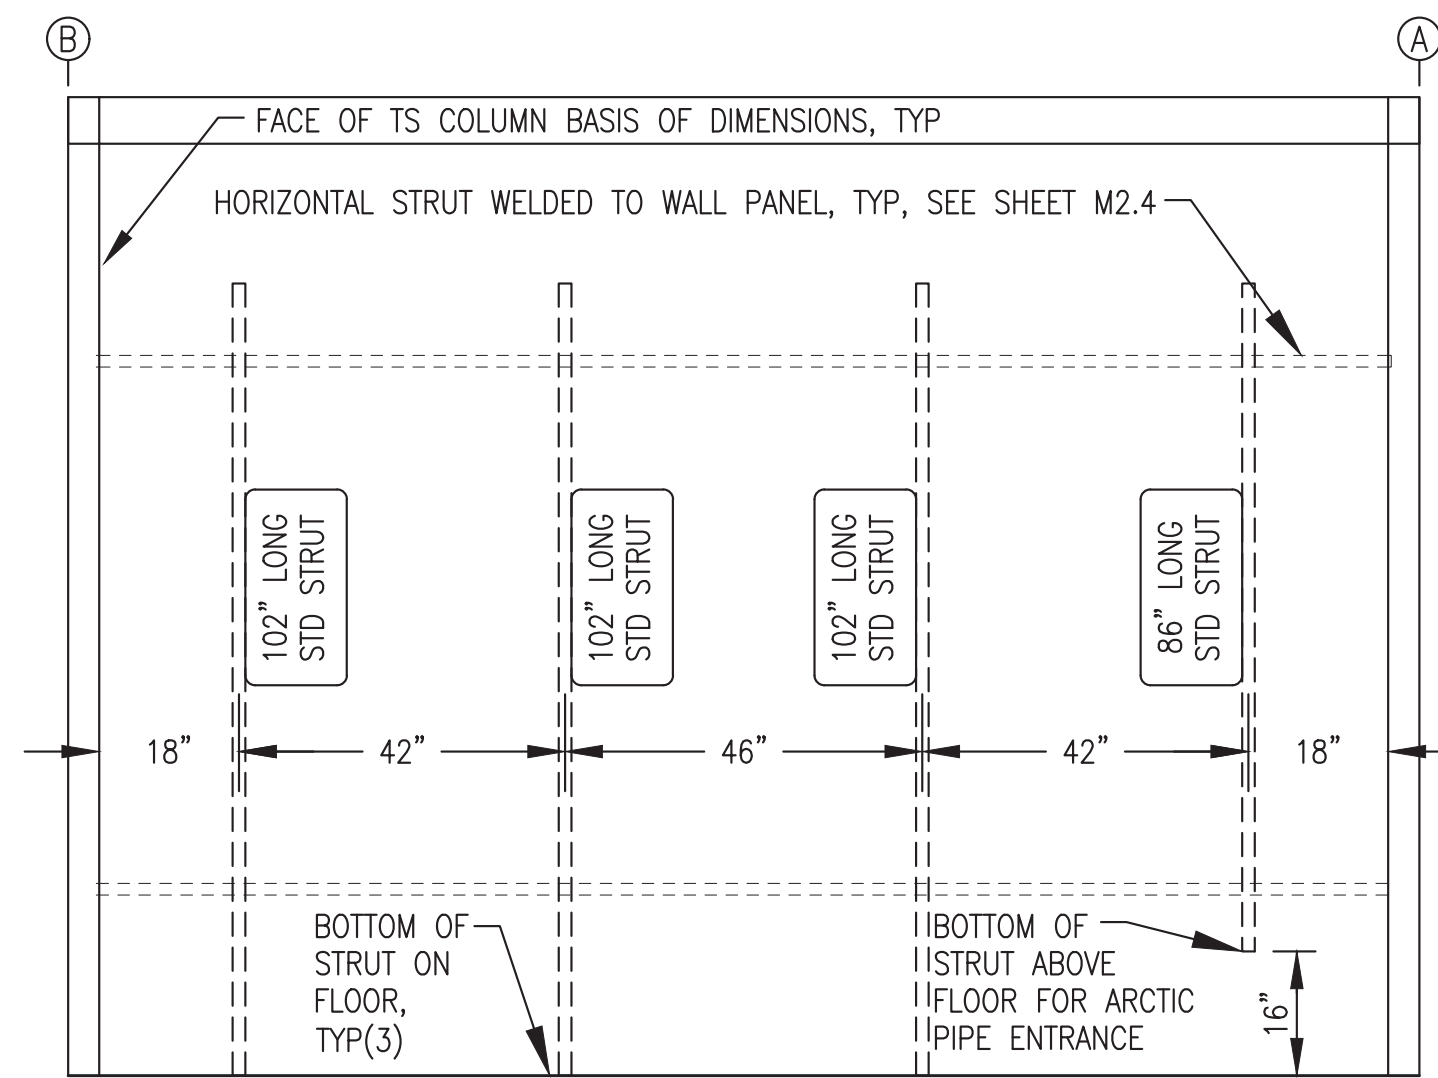


**1** END WALL (GRID 1) VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

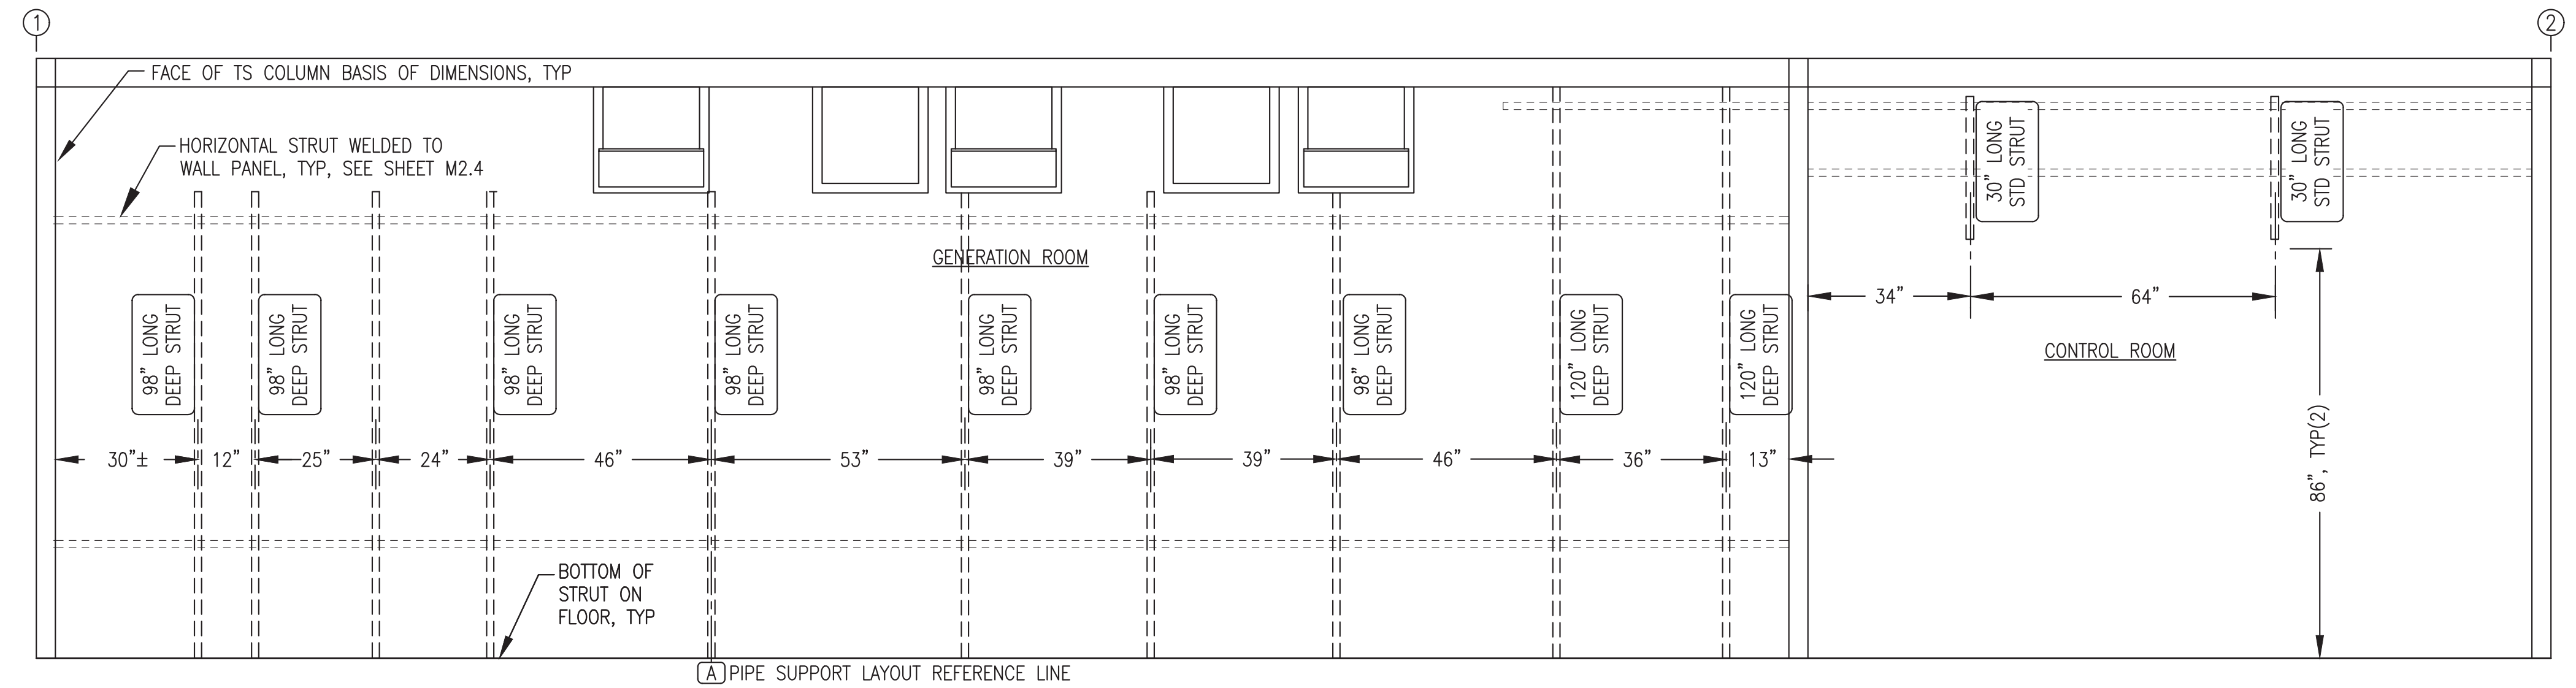


**2** BACK WALL (GRID A) VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

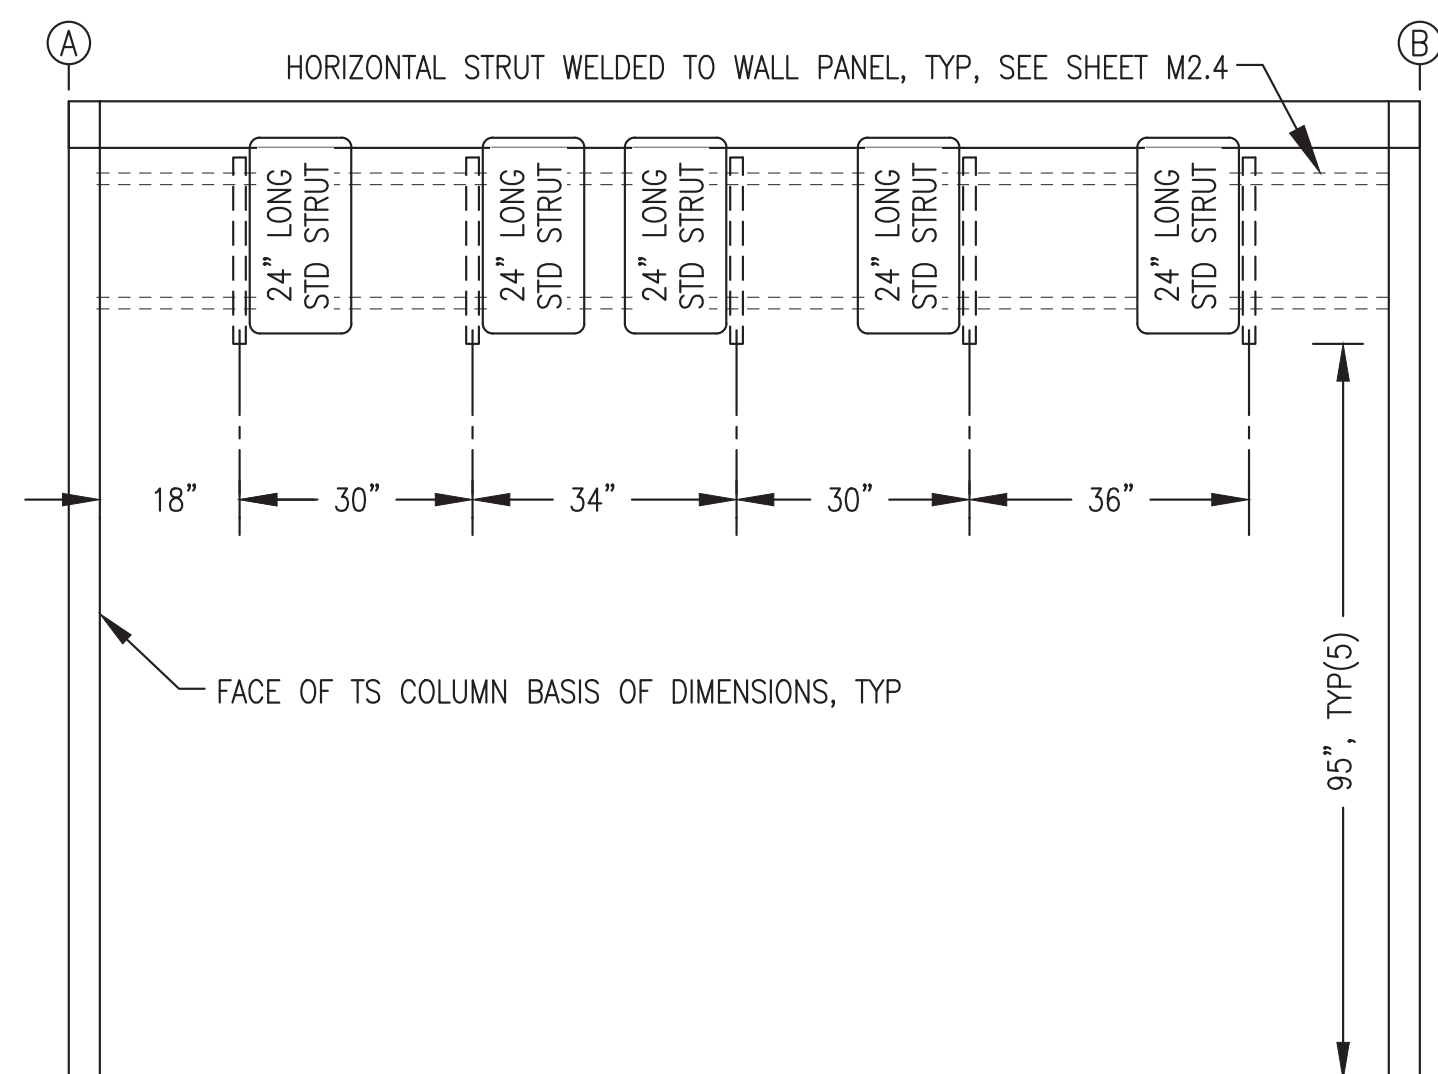


**3** END WALL (GRID 2) VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

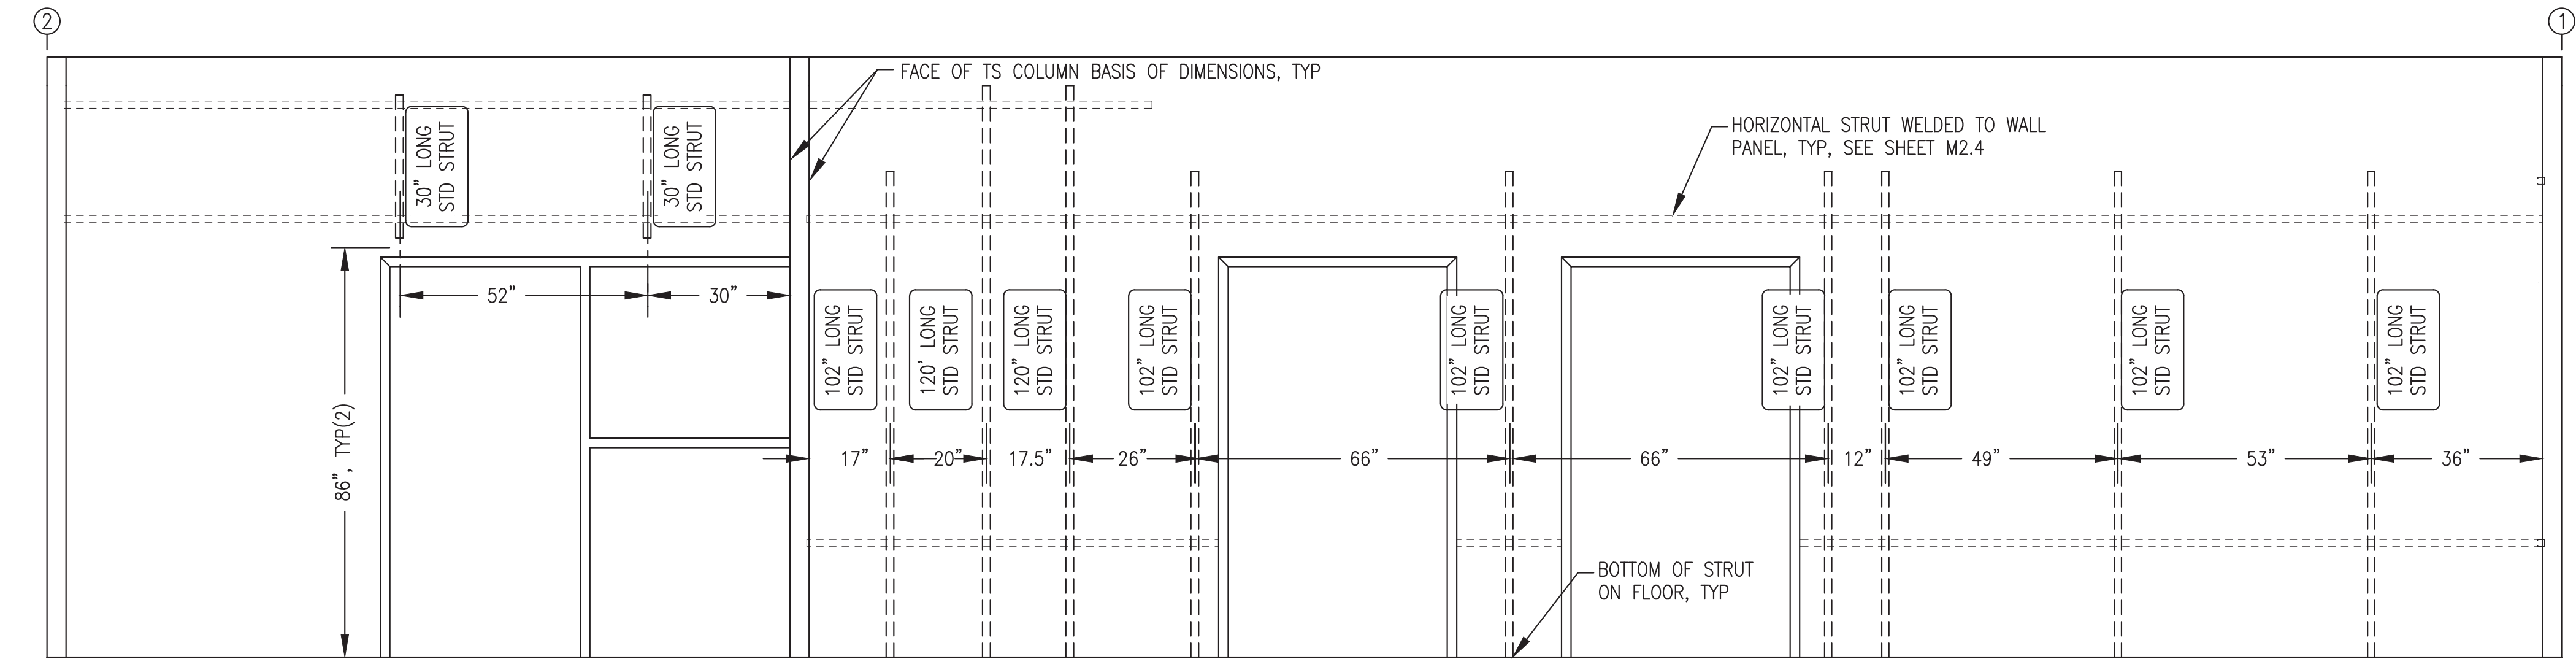

**4** FRONT WALL (GRID B) VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

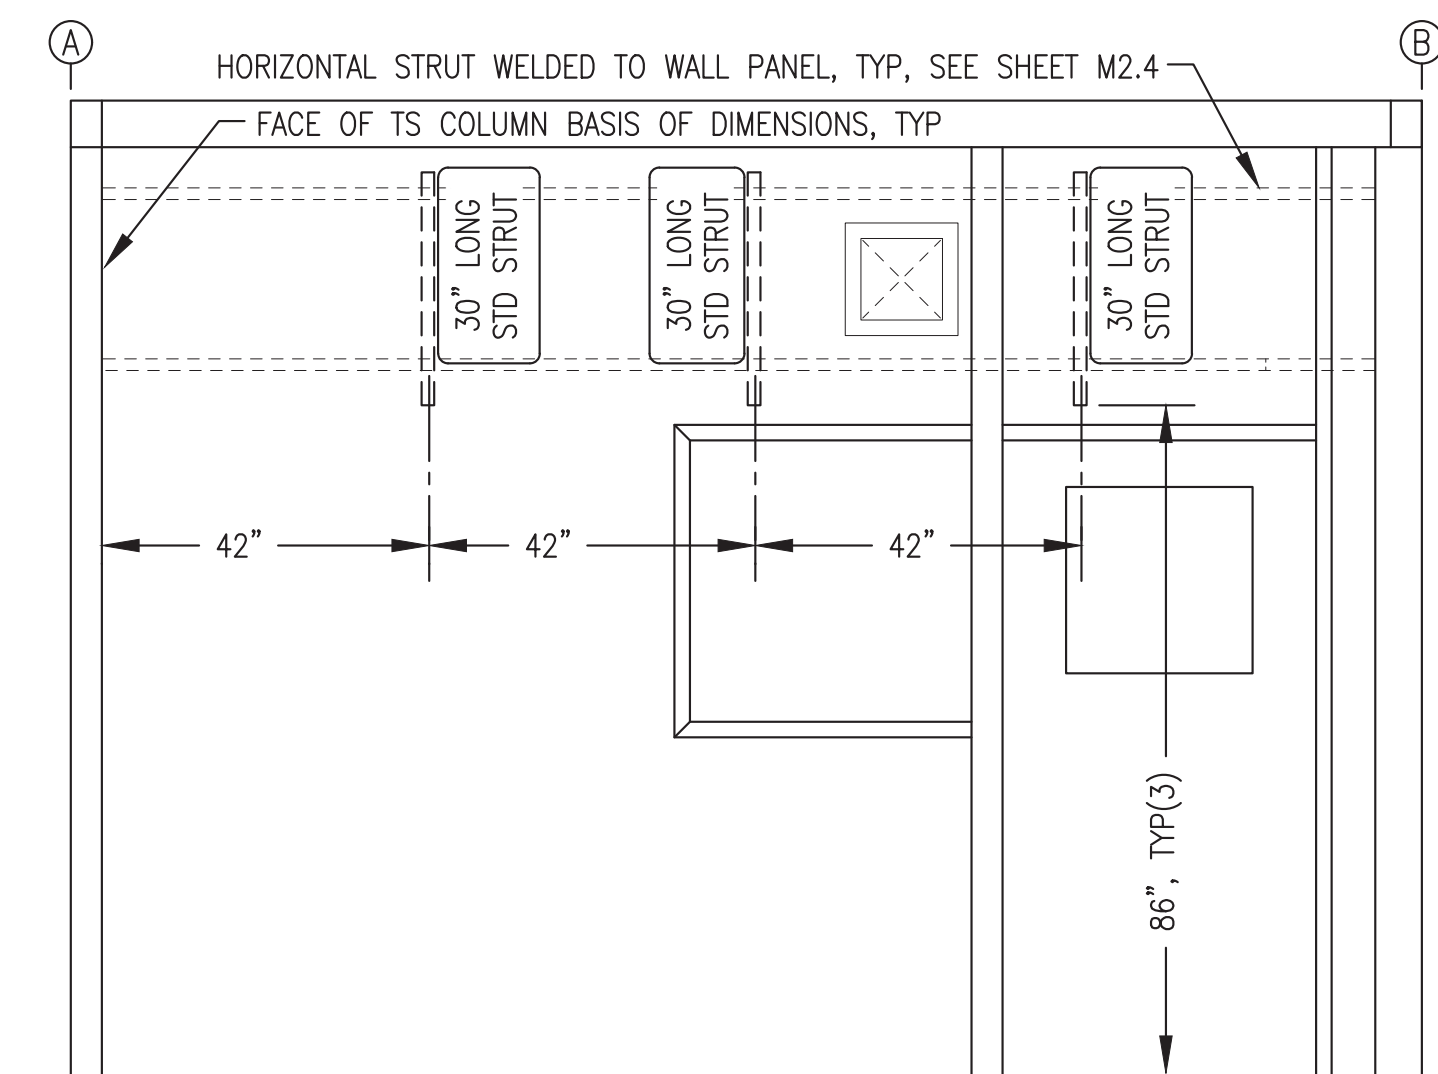

**5** GEN BAY RIGHT WALL VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

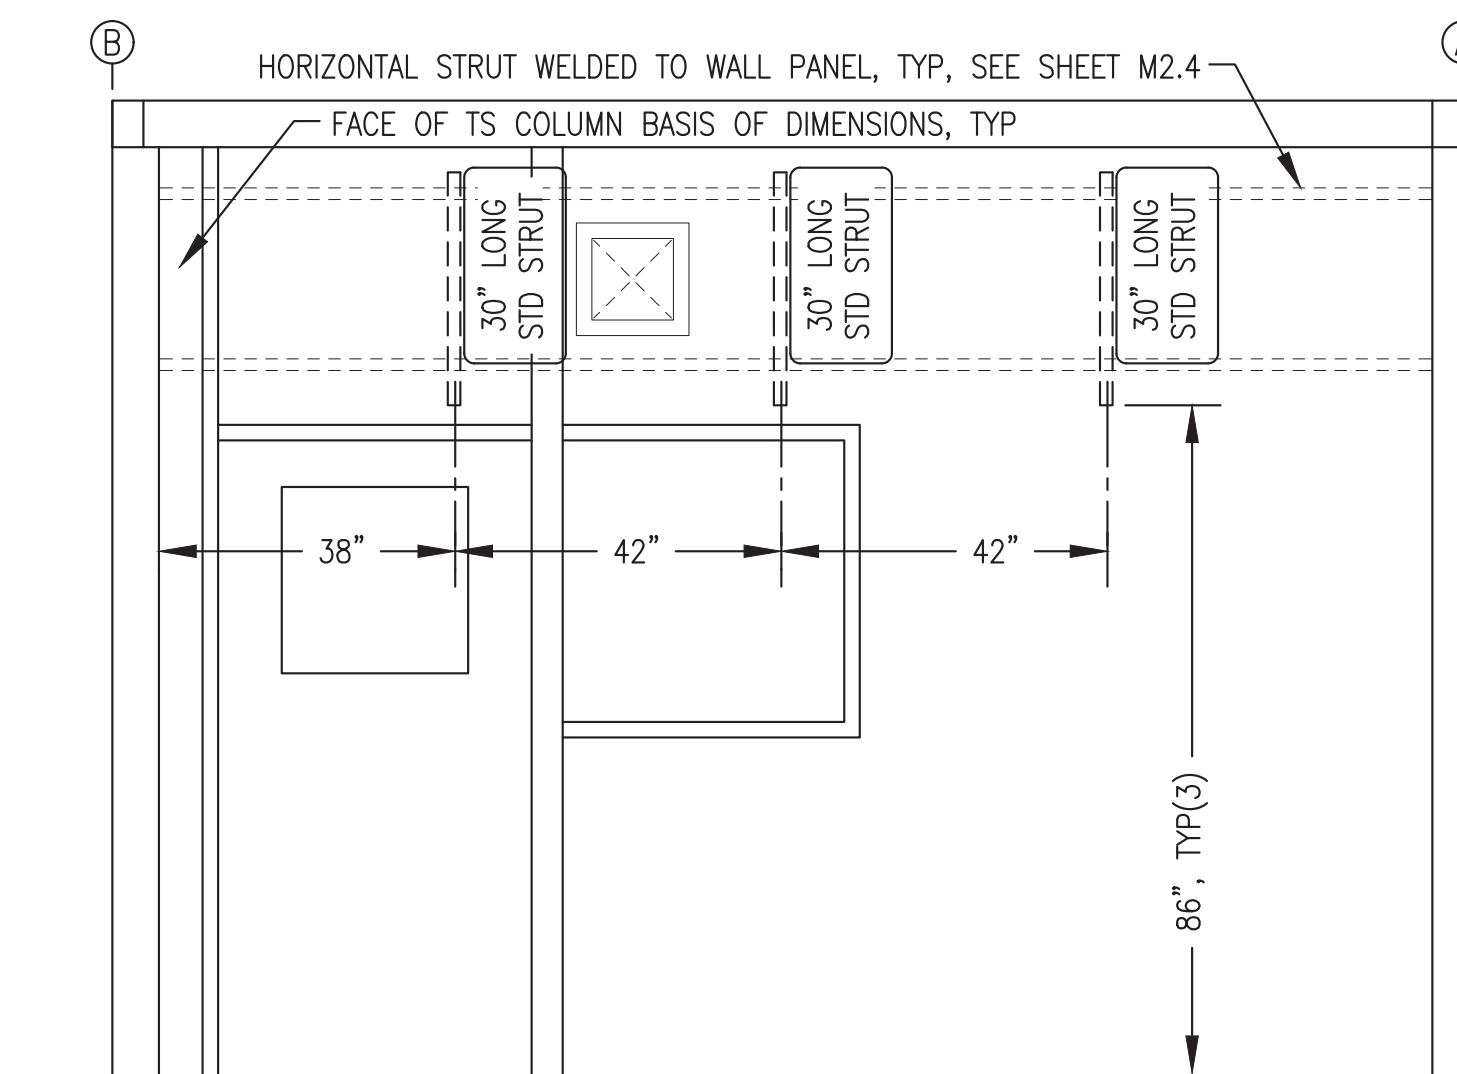


**6** CONTROL ROOM LEFT WALL VERTICAL WALL STRUT LAYOUT  
**M2.5** 1/2"=1'-0"

- VERTICAL WALL STRUT INSTALLATION NOTES:**
- 1) ALL HORIZONTAL LOCATIONS ARE CENTERLINE OF STRUT FROM FACE OF TS COLUMNS. ALL VERTICAL LOCATIONS ARE END OF STRUT ABOVE FINISHED FLOOR.
  - 2) ALL STRUT SHALL BE 12 GAUGE, PRE-GALVANIZED FINISH WITH SLOTTED BACK. "STD" DESIGNATES STANDARD 1-5/8" x 1-5/8" SINGLE STRUT, B-LINE B22-SH-GALV OR EQUAL. "DEEP" DESIGNATES 3-1/4" x 1-5/8" SINGLE STRUT, B-LINE B11-SH-GALV OR EQUAL.
  - 3) FASTEN ALL VERTICAL STRUT SECTIONS TO HORIZONTAL STRUT WITH 1/2"x1" ALLEN HEAD CAP SCREWS & STRUT NUTS.
  - 4) ONLY MAJOR WALL MOUNTED EQUIPMENT SUPPORT STRUT SHOWN THIS SHEET. SEE MECHANICAL AND ELECTRICAL DRAWINGS FOR OTHER EQUIPMENT, PIPING, AND WIREWAY STRUT SUPPORT DETAILS.


**REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022**




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
<p><b>ALASKA ENERGY AUTHORITY</b></p>			
PROJECT:		<b>RAMPART POWER SYSTEM UPGRADE</b>	
TITLE:		<b>MECHANICAL SUPPORT VERTICAL WALL STRUT INSTALLATION</b>	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		<b>M2.5</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

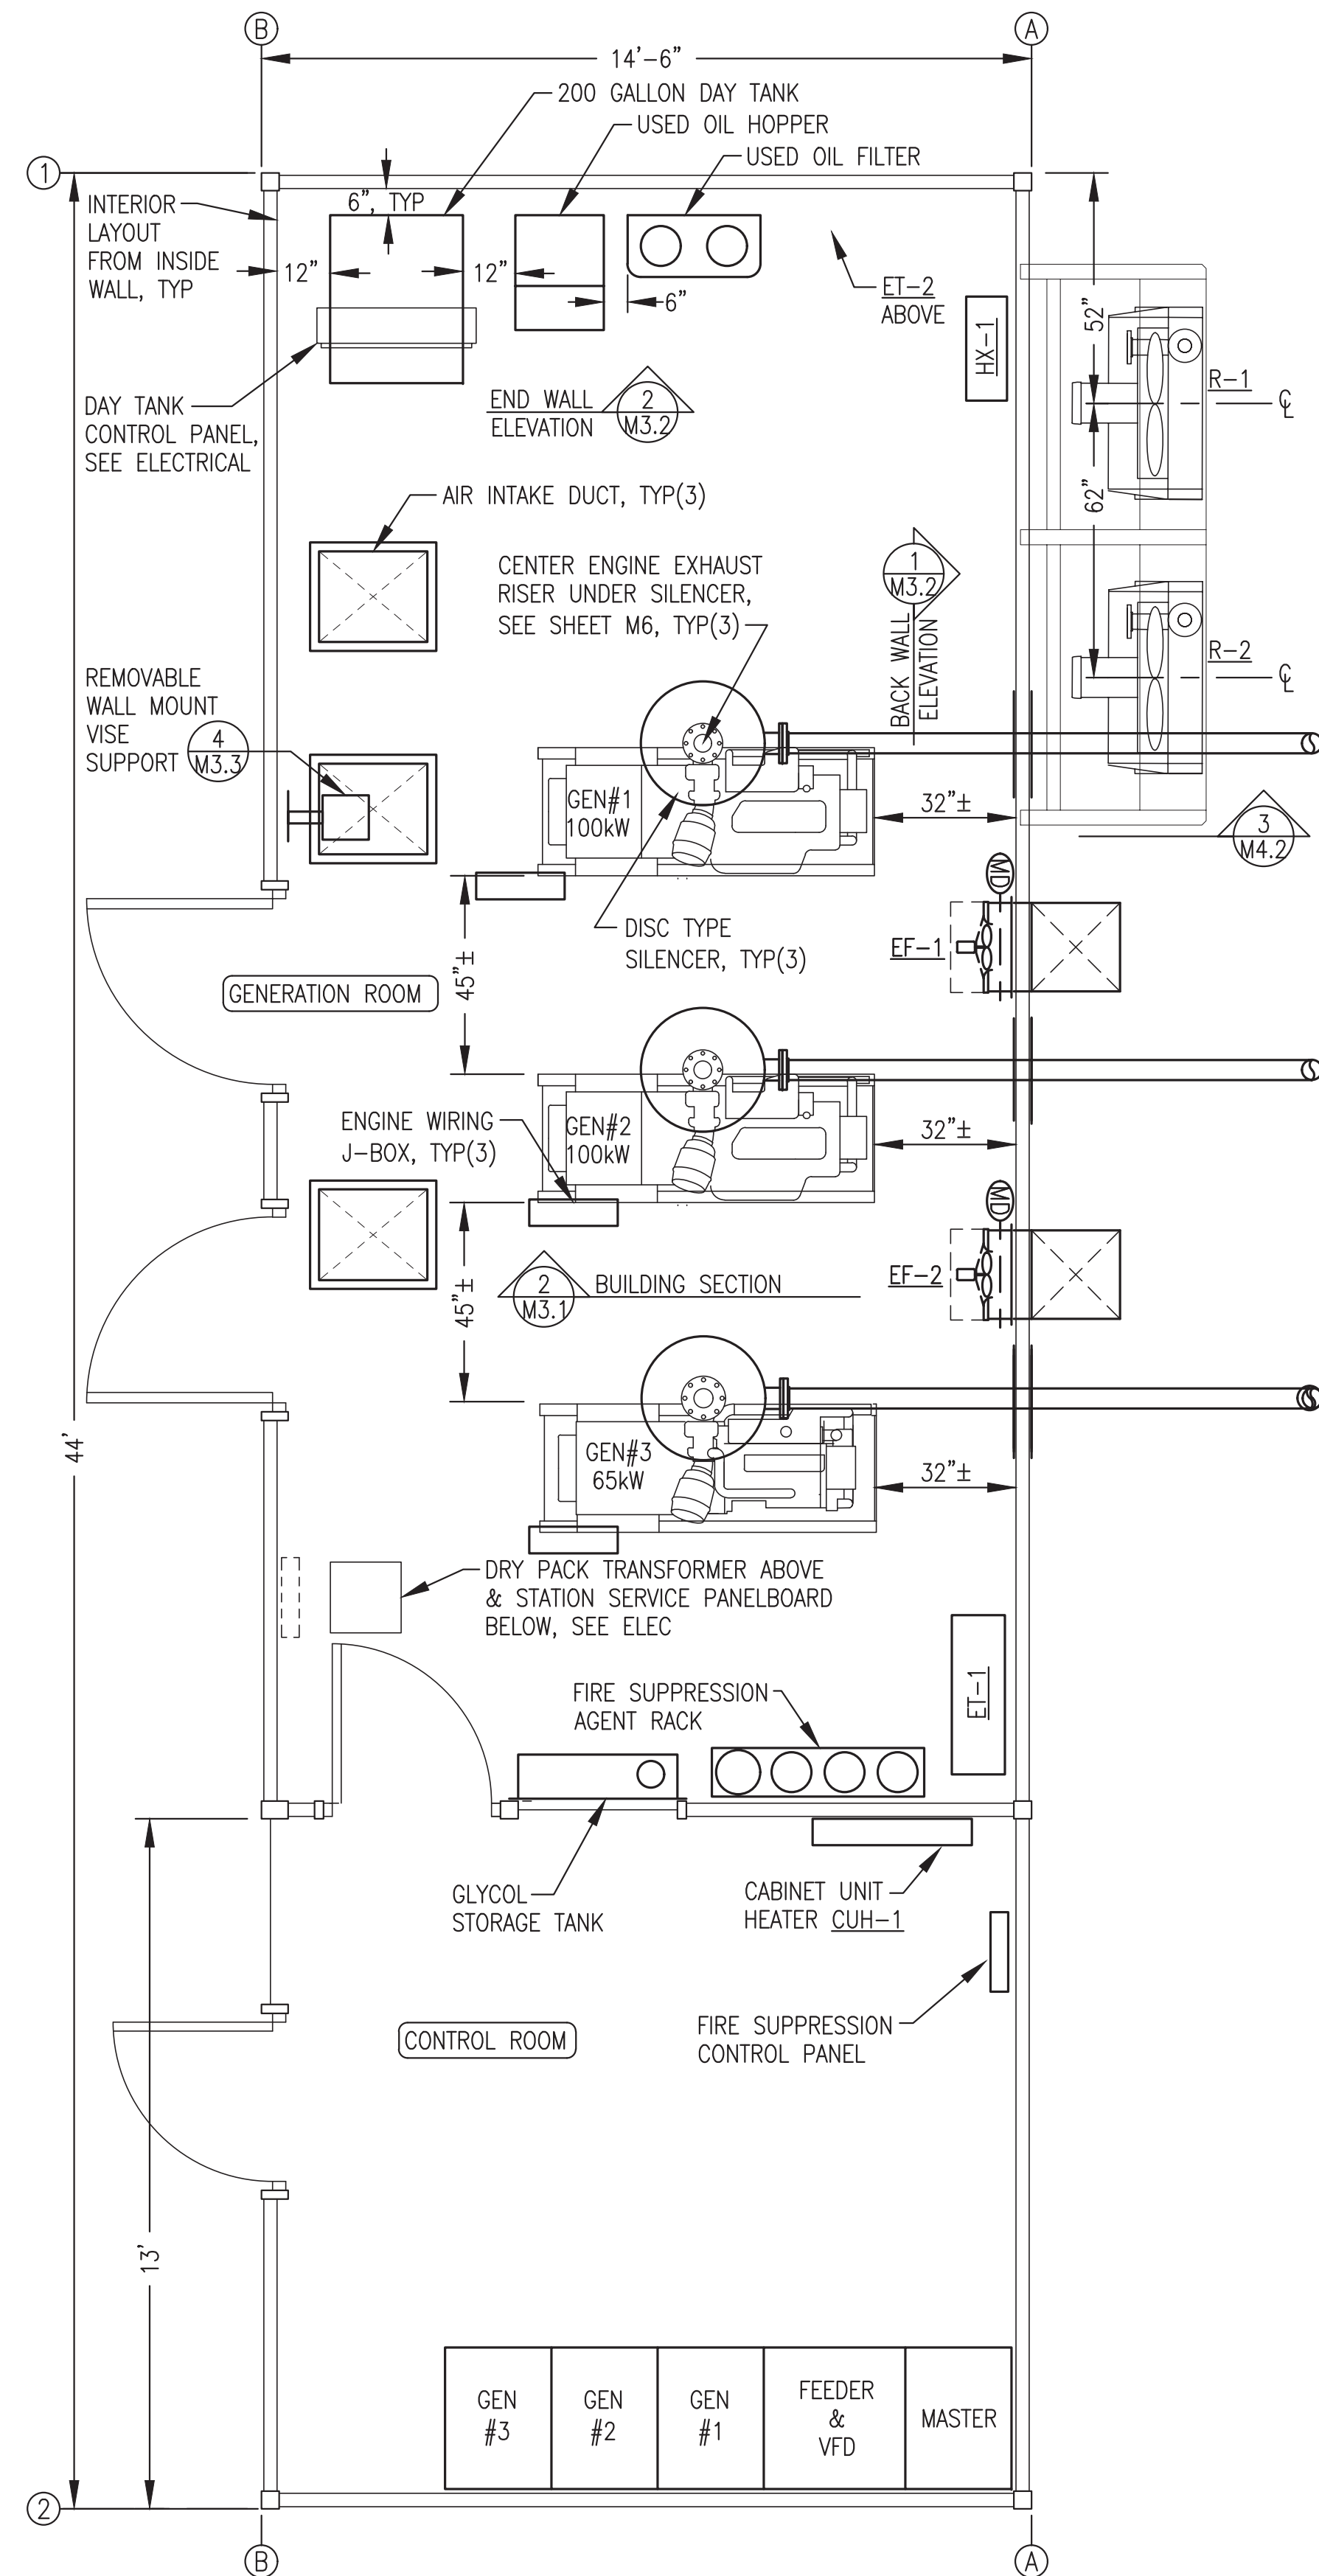

1 EQUIPMENT LAYOUT PLAN  
M3.1 3/8"=1'-0"

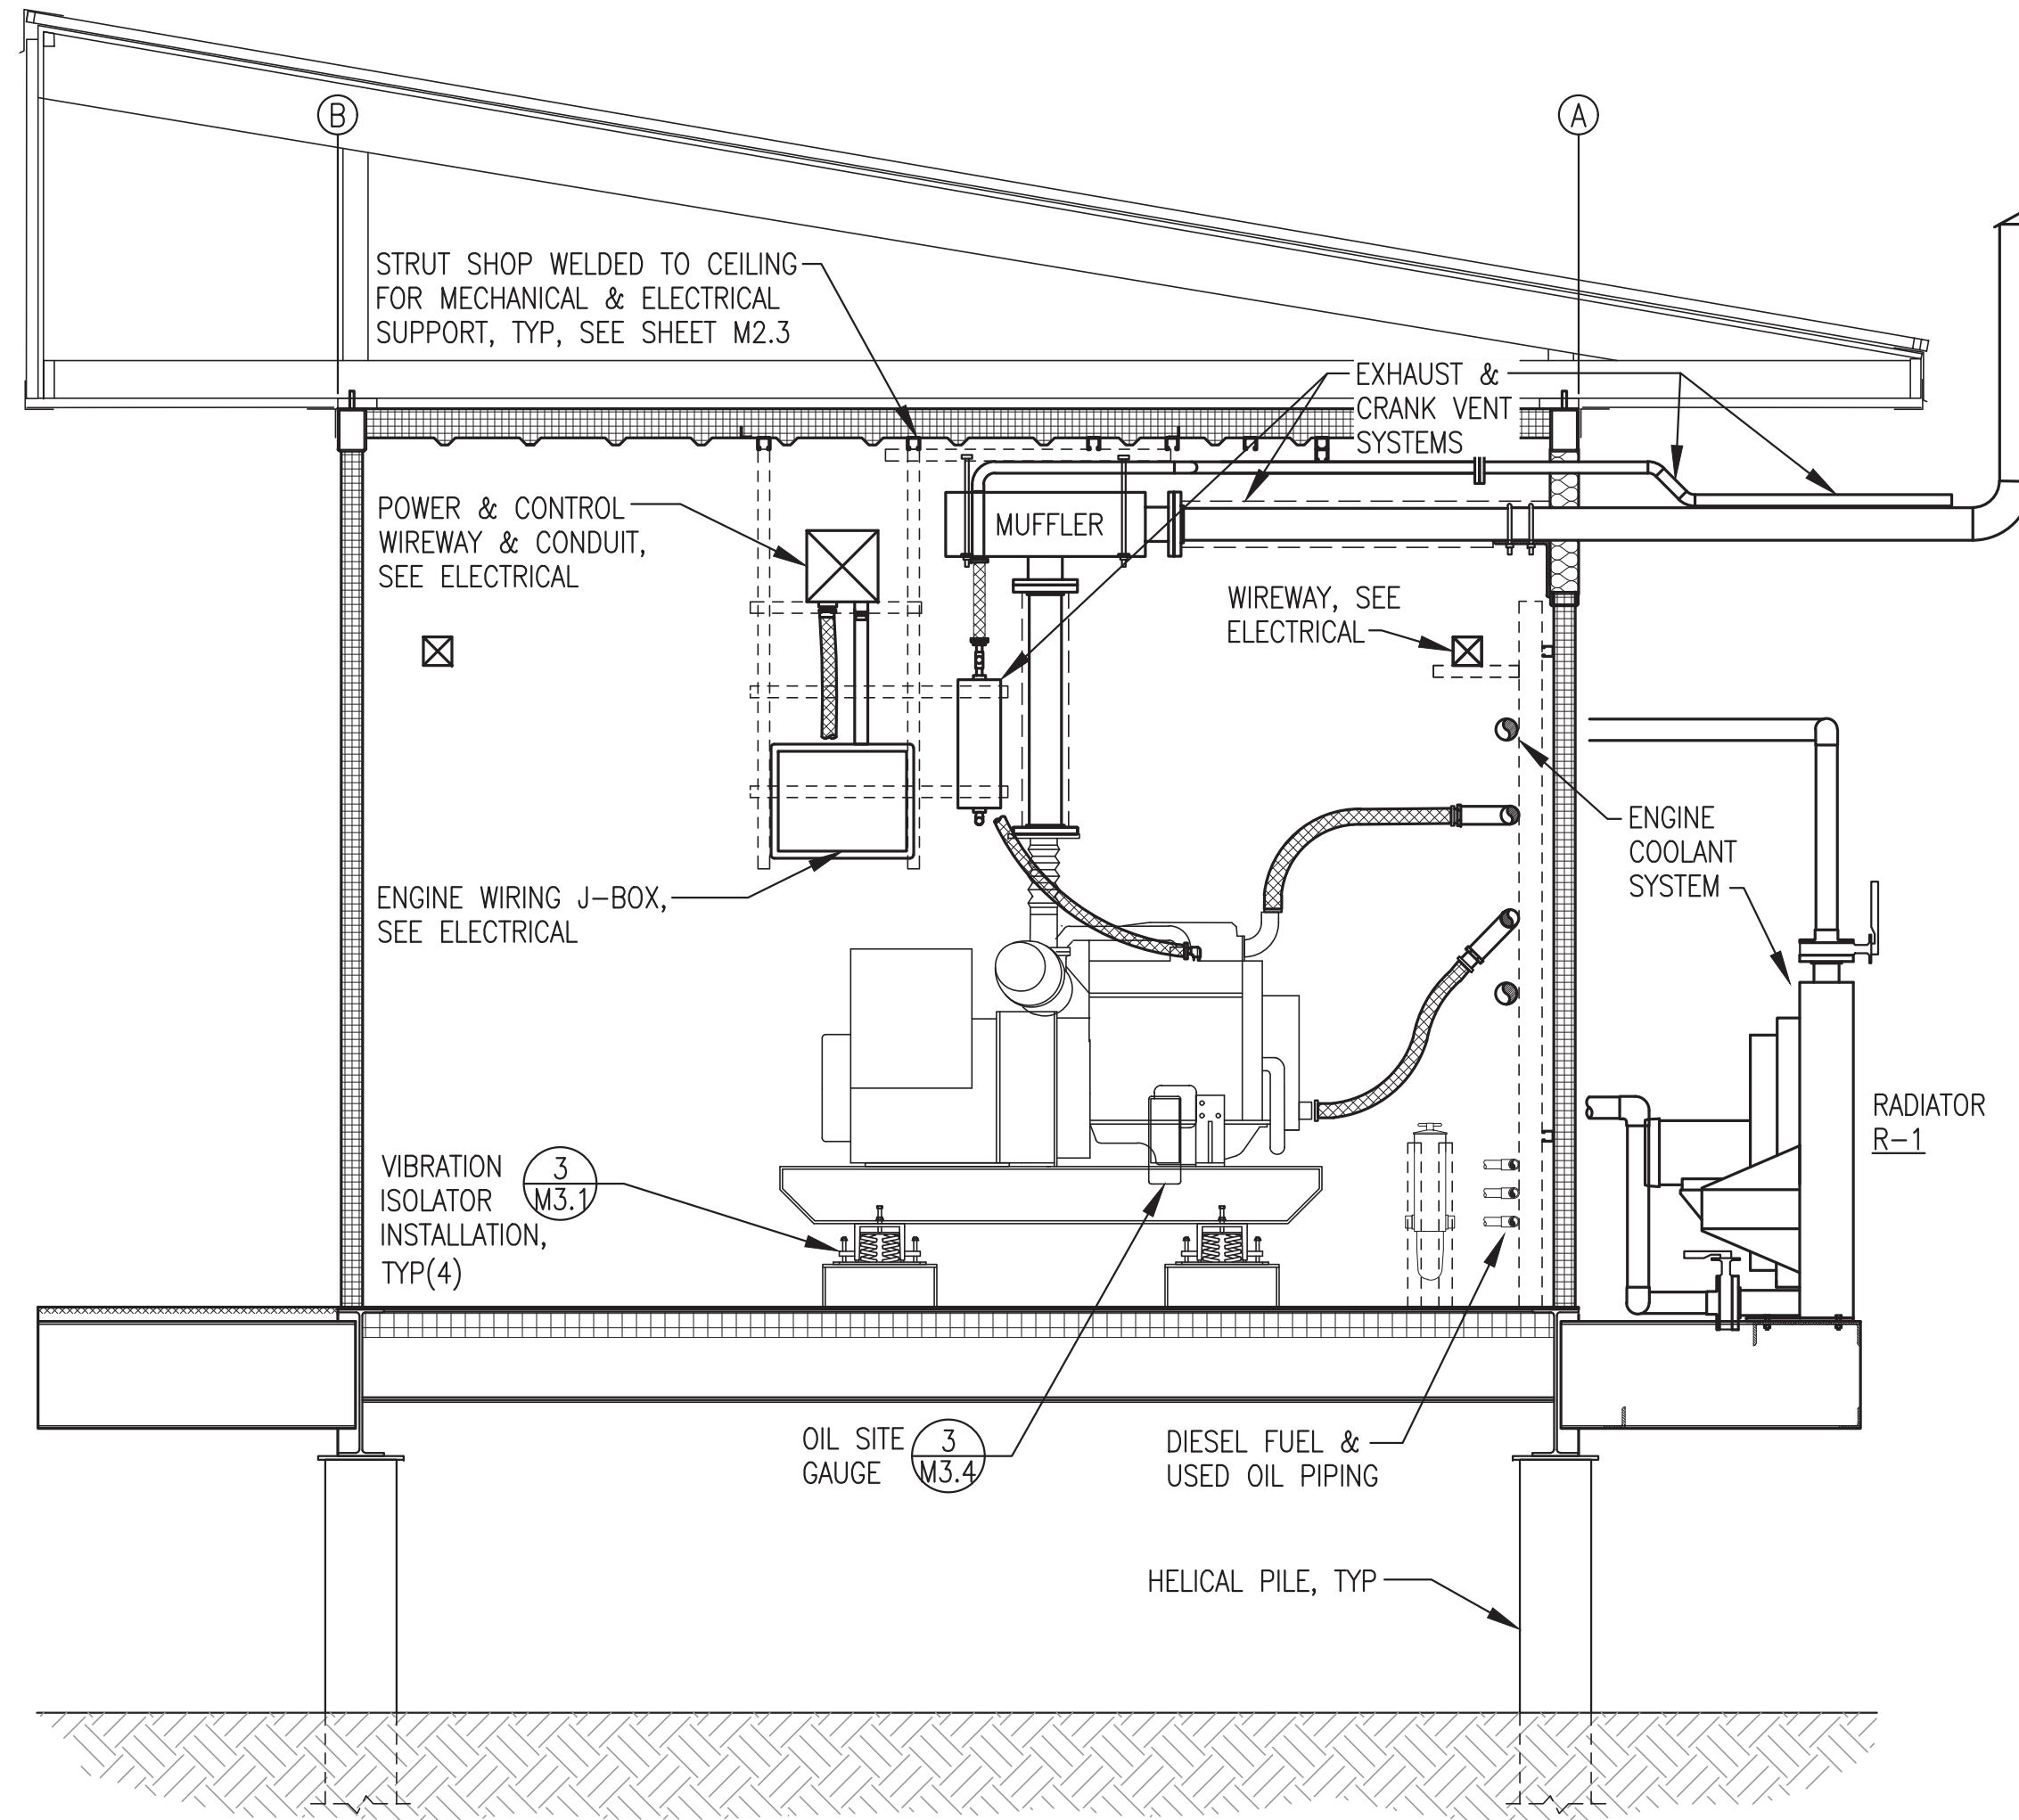

2 TYPICAL MODULE SECTION/GENERATOR INSTALLATION  
M3.1 1/2"=1'-0"

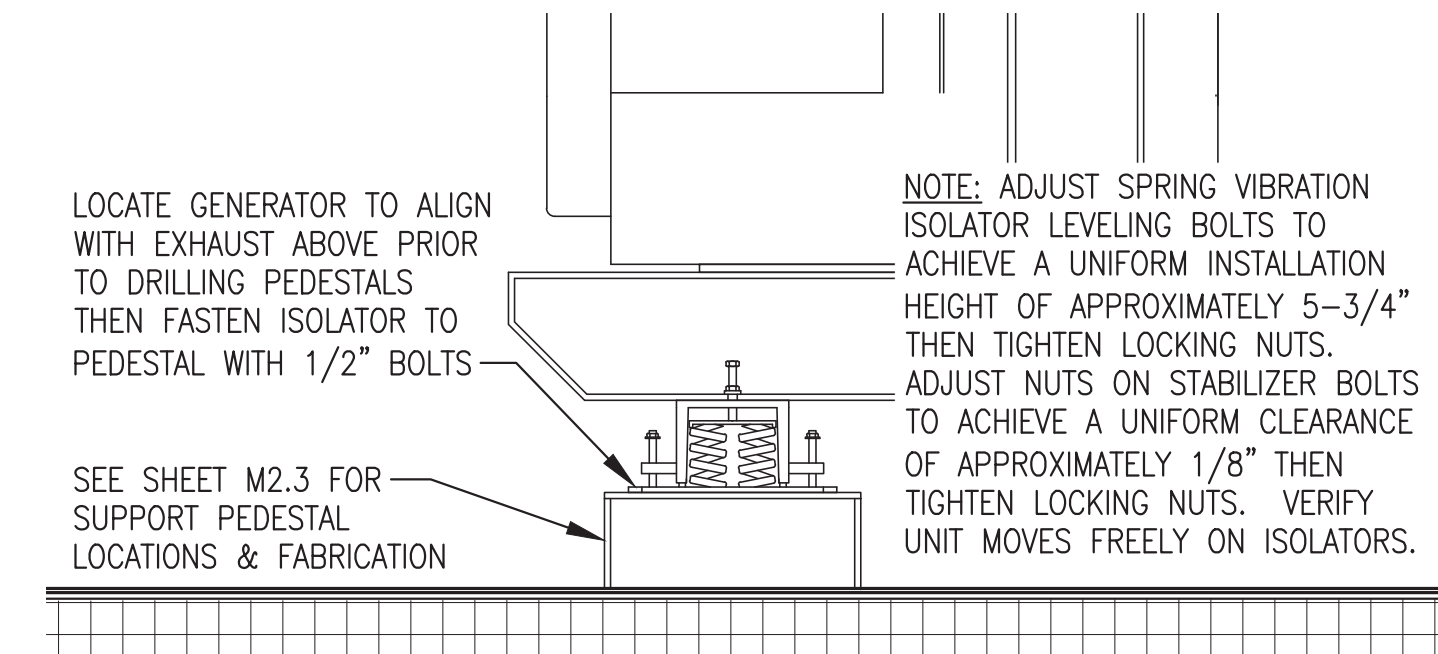

3 VIBRATION ISOLATOR INSTALLATION  
M3.1 1"=1'-0"

EQUIPMENT LAYOUT GENERAL NOTES:

- 1) SEE M2 SHEETS FOR MECHANICAL AND ELECTRICAL SUPPORTS AND PENETRATIONS
- 2) SEE M3 SHEETS FOR GENERAL EQUIPMENT LAYOUT, BASE SUPPORT, FABRICATIONS, AND GENERATOR ASSEMBLY DETAILS.
- 3) SEE M4 SHEETS FOR ENGINE COOLANT SYSTEM AND HEAT RECOVERY SYSTEM PLANS, ISOMETRICS, AND DETAILS.
- 4) SEE M5 SHEETS FOR DIESEL FUEL AND USED OIL SYSTEM PLANS AND DETAILS.
- 5) SEE SHEET M6 FOR EXHAUST AND CRANK CASE VENTILATION PLANS AND DETAILS.
- 6) SEE M7 SHEETS FOR VENTILATION SYSTEM PLANS AND SHEET METAL FABRICATIONS.


ENGINE-GENERATOR SCHEDULE

GENSET	DESCRIPTION
GEN #1	ENGINE - 148 HP, 100 EKW PRIME, JOHN DEERE 4045AFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 125 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UC1274E.
GEN #2	ENGINE - 148 HP, 100 EKW PRIME, JOHN DEERE 4045AFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 125 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UC1274E.
GEN #3	ENGINE - 99 HP, 65 EKW PRIME, JOHN DEERE 4045TFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 90 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UC1274E.


ENGINE-GENERATOR CODE COMPLIANCE NOTES

- 1) PER IMC 915.1 THE ENGINE-GENERATORS AND ASSOCIATED MECHANICAL SYSTEMS SHALL BE INSTALLED IN COMPLIANCE WITH NFPA 37. SEE THE ABOVE REFERENCED DRAWINGS FOR ADDITIONAL DETAIL.
- 2) PER IMC 915.1 THE ENGINE-GENERATORS SHALL BE FABRICATED AND ASSEMBLED IN ACCORDANCE WITH U.L. 2200. SEE ENGINE-GENERATOR SPECIFICATIONS FOR ADDITIONAL DETAIL.


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
<p>ALASKA ENERGY AUTHORITY</p>			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: EQUIPMENT LAYOUT PLAN, SECTION, & DETAILS			
<p>Gray Stassel Engineering, Inc.</p>		DRAWN BY: JTD DESIGNED BY: BCG FILE NAME: RAM_PP_M2-M7 PROJECT NUMBER:	SCALE: AS NOTED DATE: 3/15/22 SHEET: <b>M3.1</b>
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

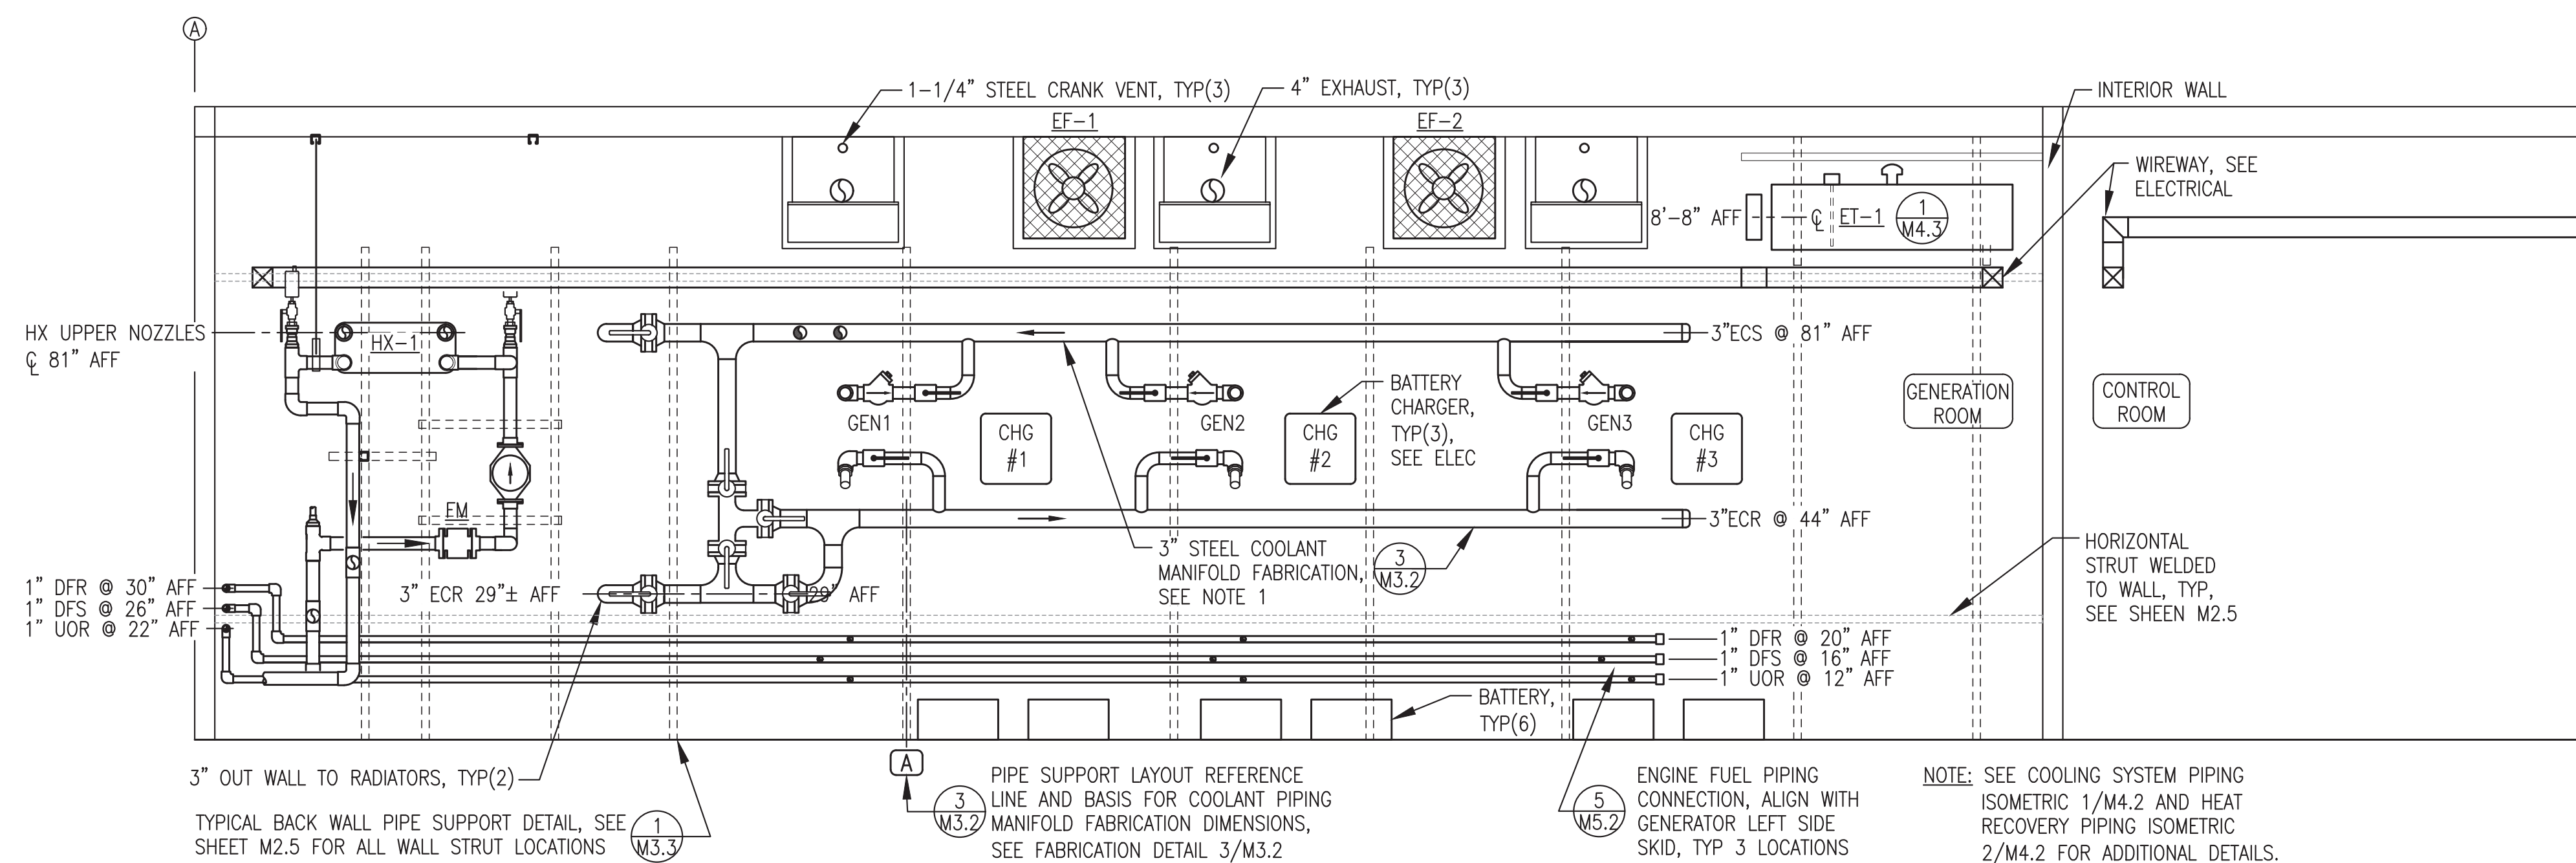


**1** BACK WALL ELEVATION  
M3.2 1/2"=1'-0"

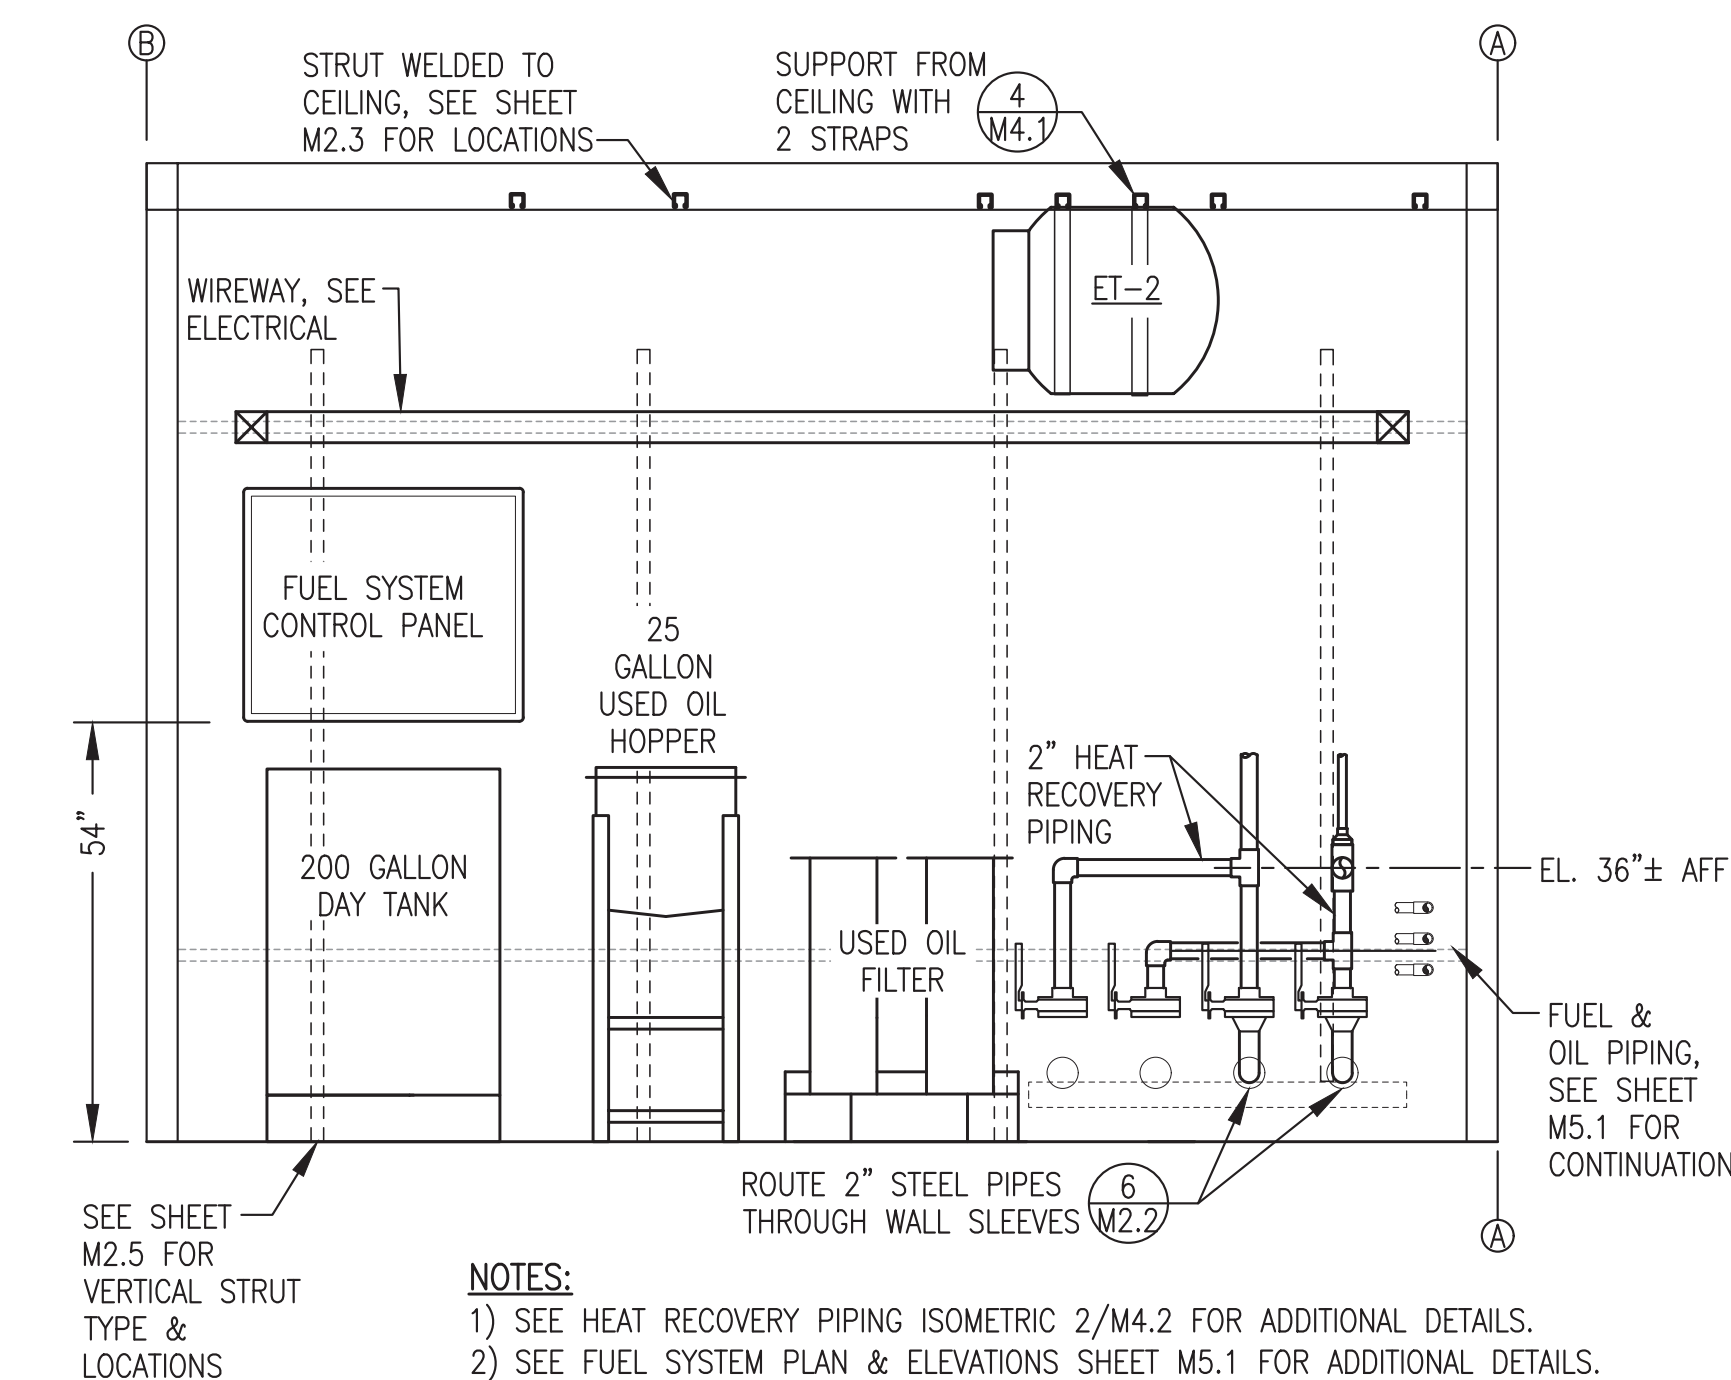

**2** END WALL ELEVATION  
M3.2 1/2"=1'-0"

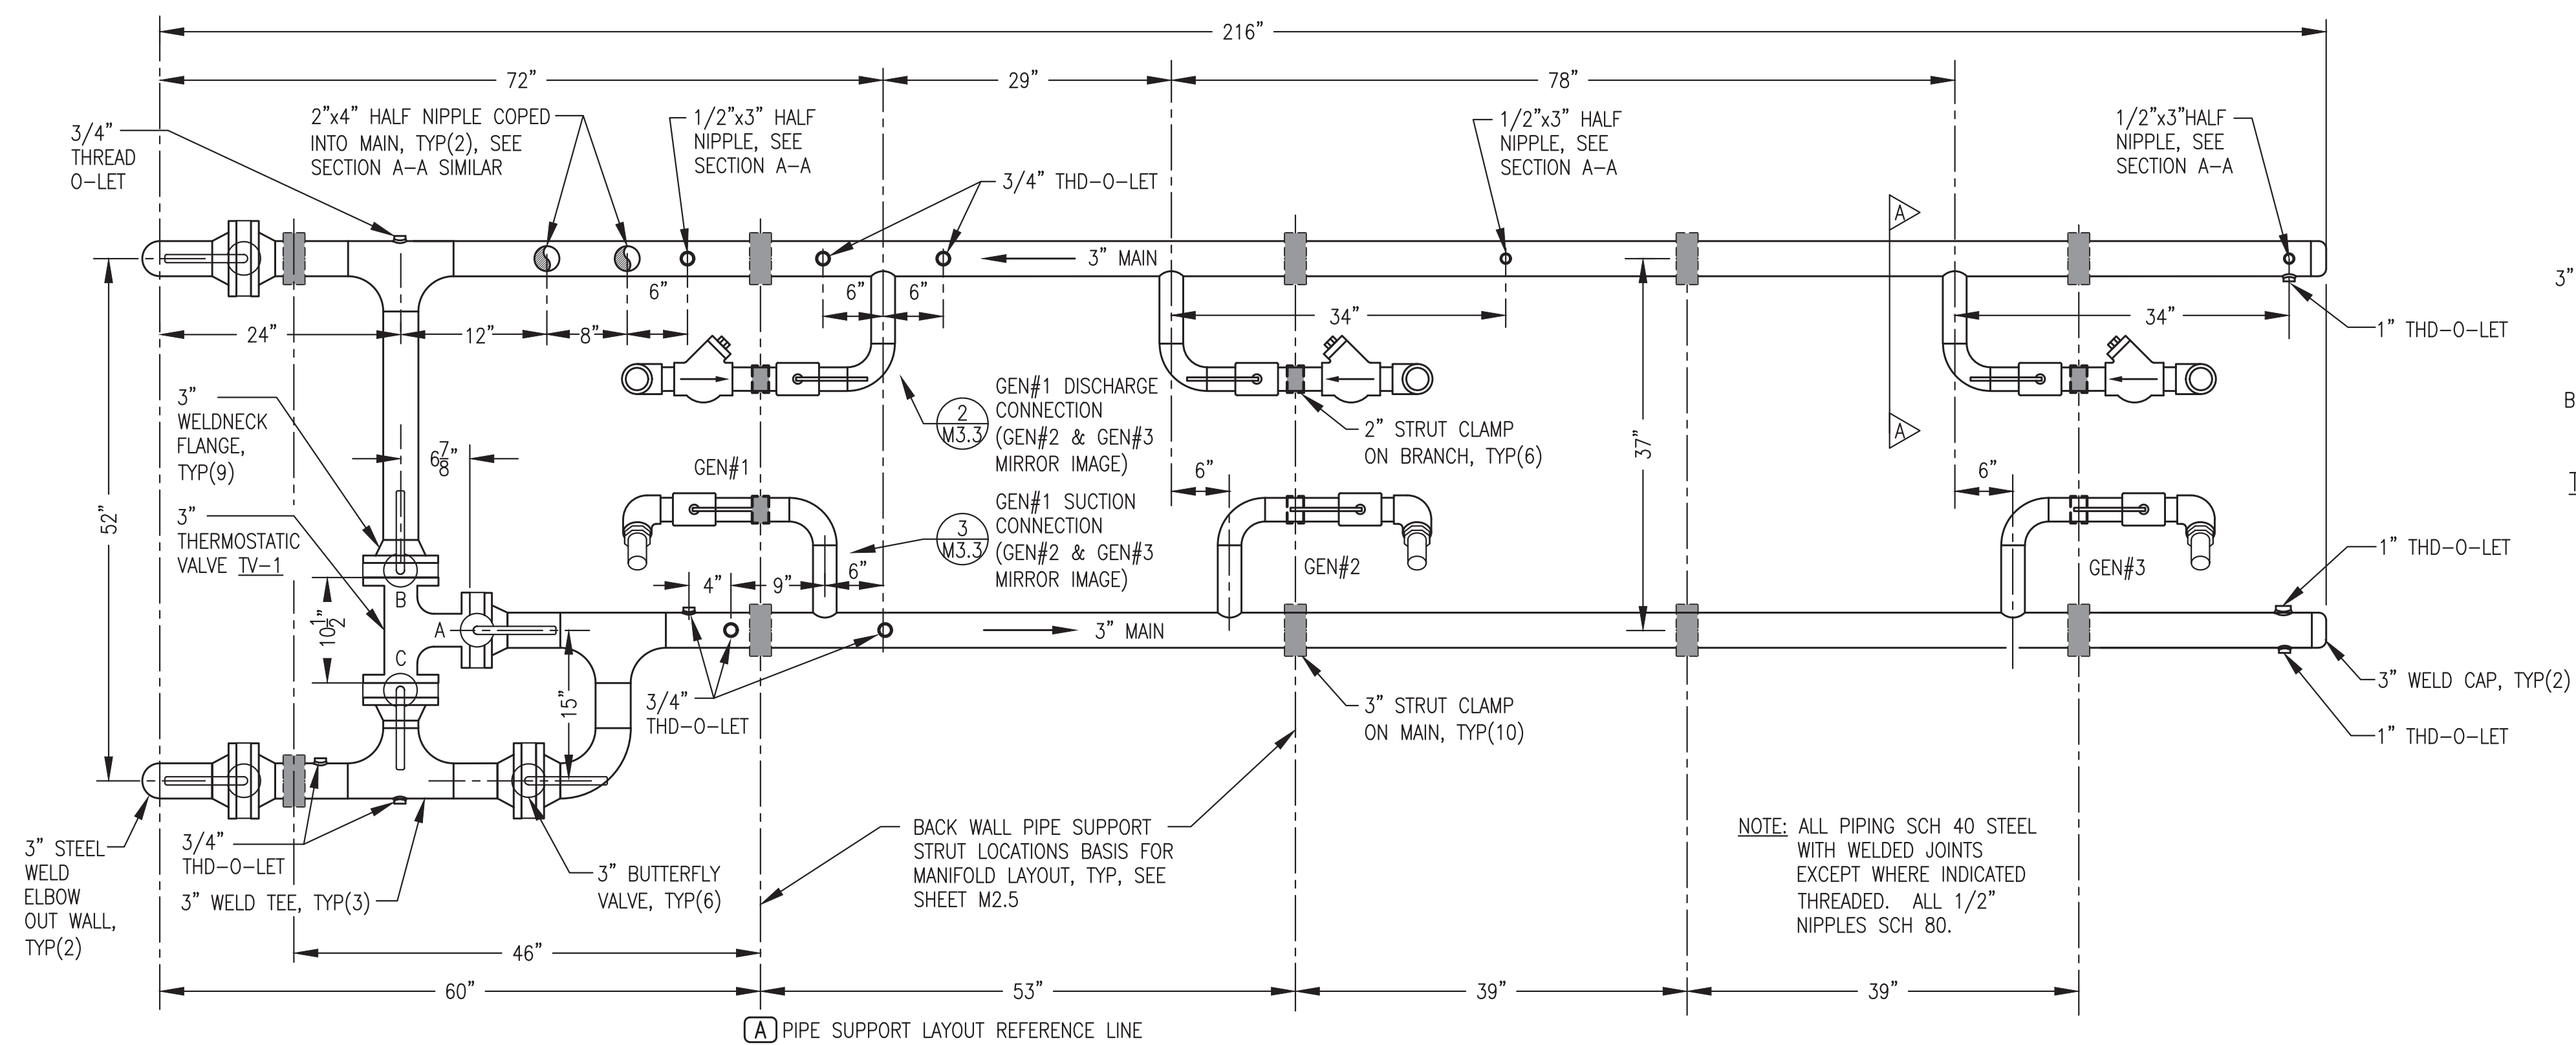

**3** COOLANT MANIFOLD ENLARGED FABRICATION DETAIL  
M3.2 1"=1'-0"

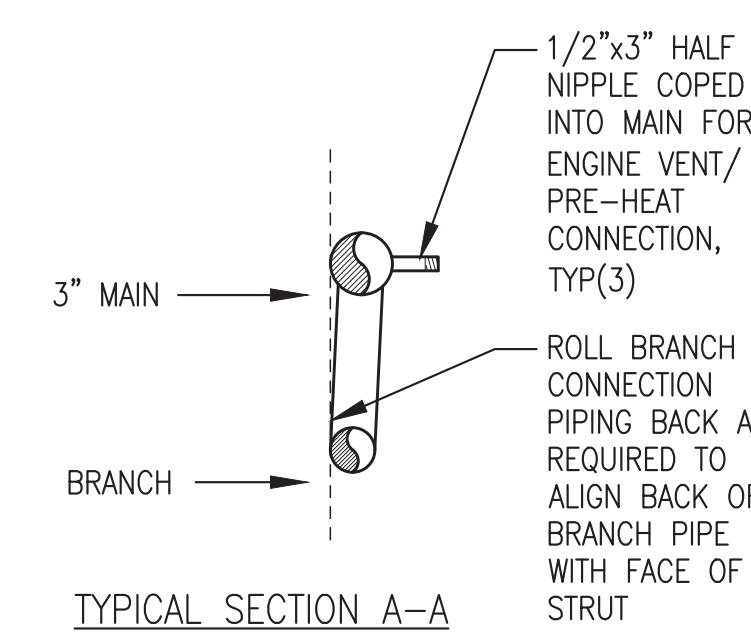


TYPICAL SECTION A-A

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: WALL ELEVATIONS & PIPING DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		<b>M3.2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

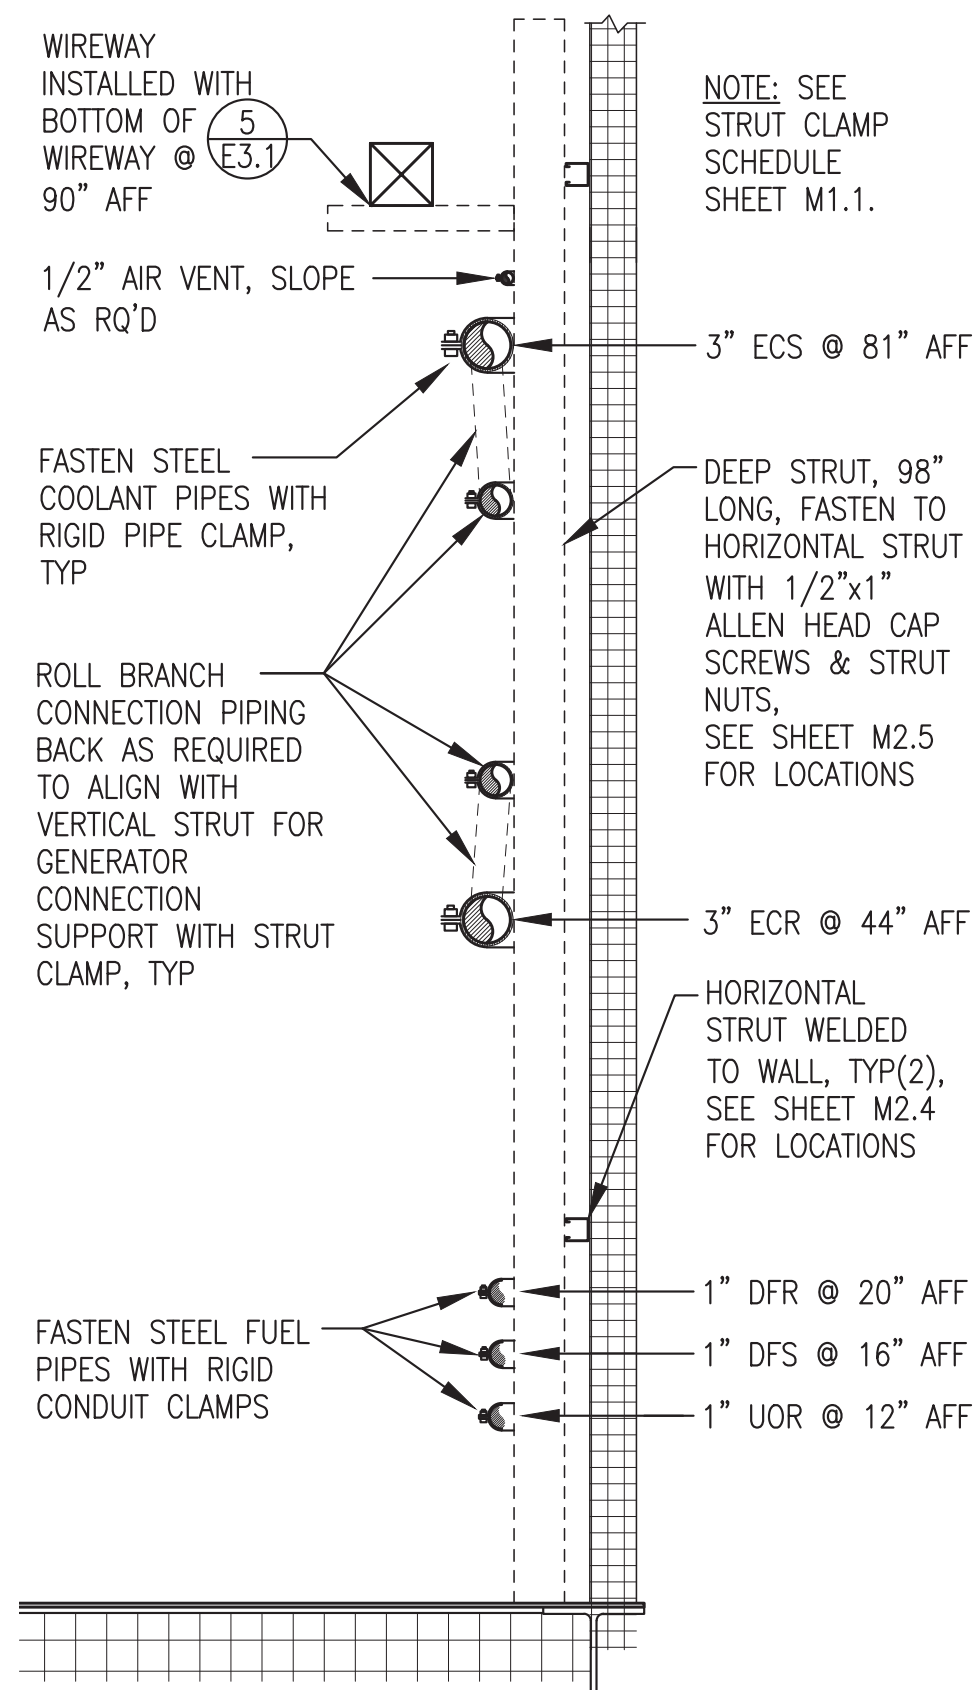

**1** TYPICAL PIPE SUPPORT AT BACK WALL  
**M3.3** 1"=1'-0"


NOTE: SEE STRUT CLAMP SCHEDULE SHEET M1.1.

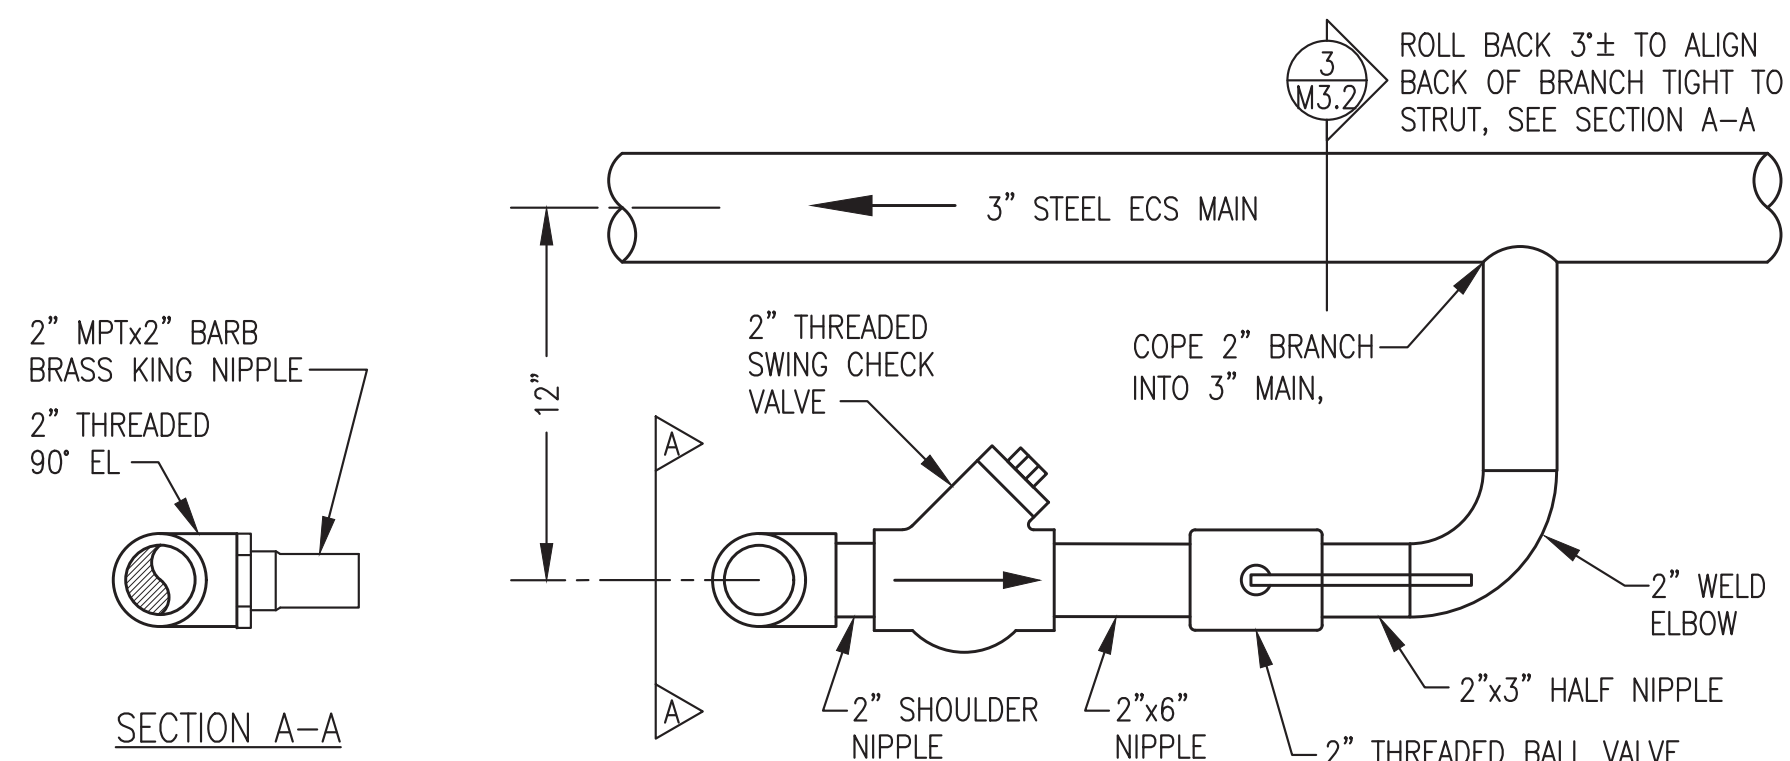

**2** GEN#1 DISCHARGE CONNECTION (GEN#2 & GEN#3 MIRROR IMAGE)  
**M3.3** NO SCALE

NOTES:


- 1) GEN#1 DISCHARGE CONNECTION SHOWN, GEN#2 & GEN#3 MIRROR IMAGE
- 2) MAIN PIPING 3" STEEL WITH 1" INSULATION. ALL BRANCH PIPING NOT INSULATED.
- 3) ALL PIPING SCHEDULE 40 STEEL.

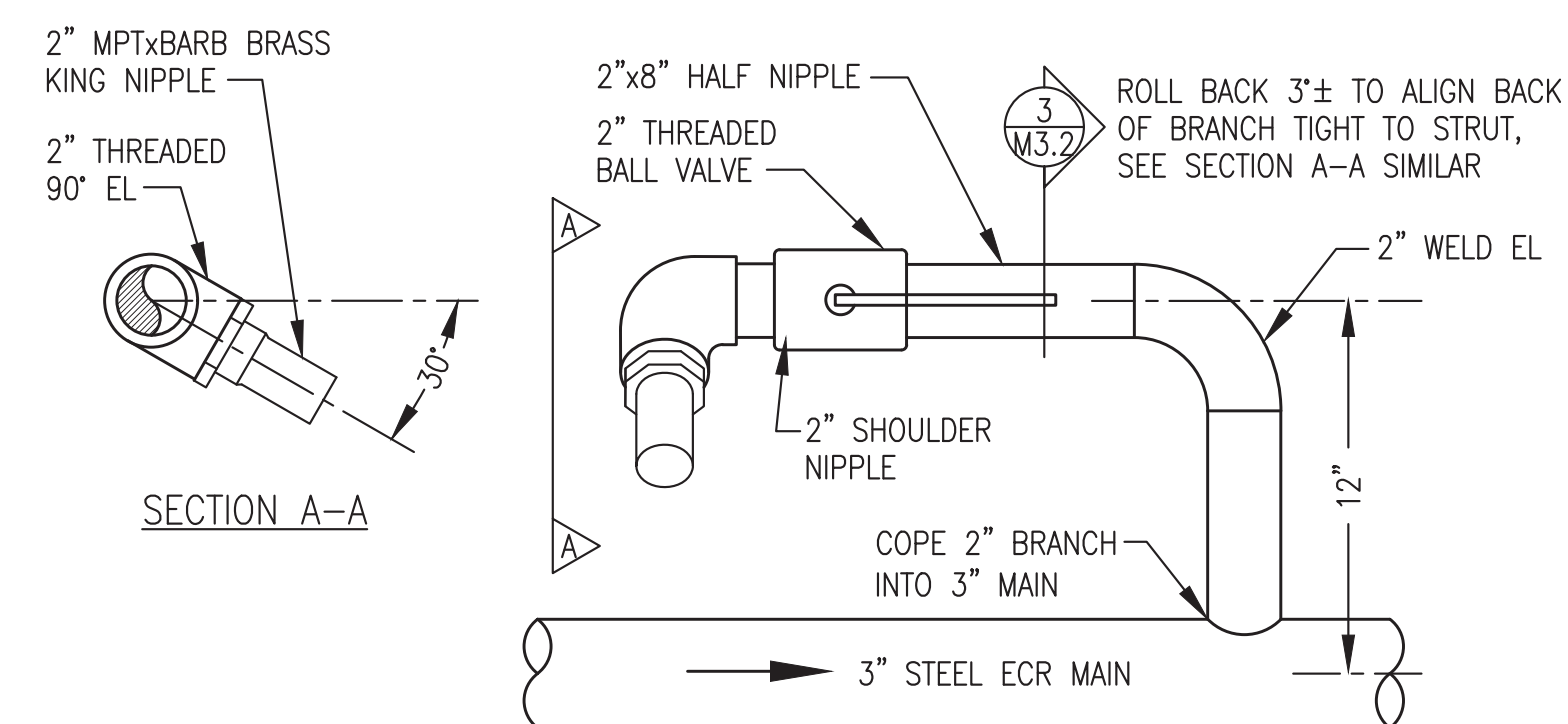

**3** GEN#1 SUCTION CONNECTION (GEN#2 & GEN#3 MIRROR IMAGE)  
**M3.3** NO SCALE


NOTES:


- 1) GEN#1 SUCTION CONNECTION SHOWN, GEN#2 & GEN#3 MIRROR IMAGE
- 2) MAIN PIPING 3" STEEL WITH 1" INSULATION. ALL BRANCH PIPING NOT INSULATED.
- 3) ALL PIPING SCHEDULE 40 STEEL.

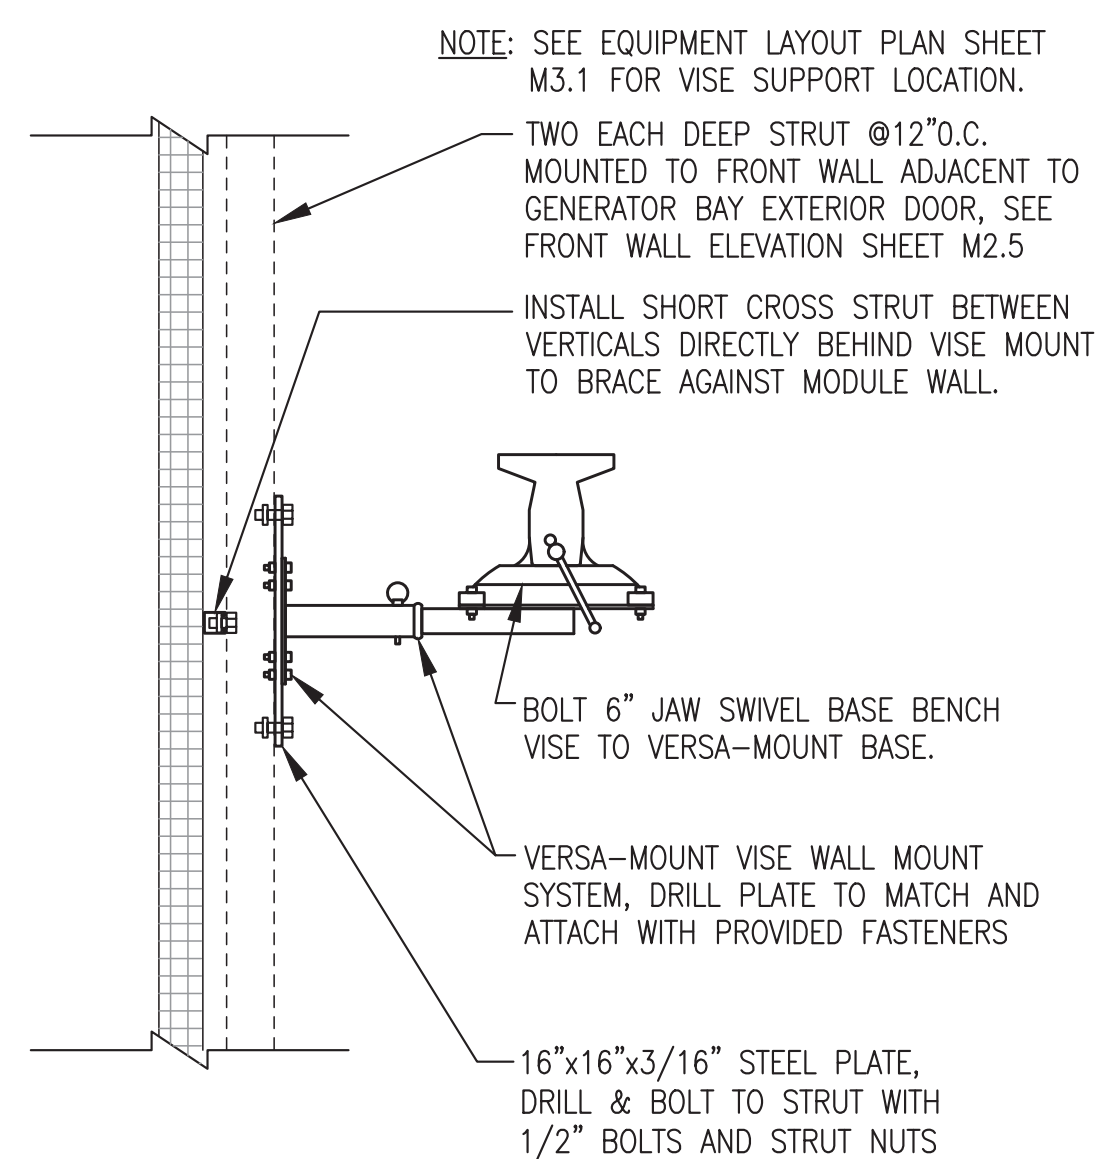


**4** REMOVABLE BENCH VISE INSTALLATION  
**M3.3** NO SCALE


REVISION #1  
 ISSUED FOR  
 CONSTRUCTION  
 JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		MECHANICAL DETAILS	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		<b>M3.3</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

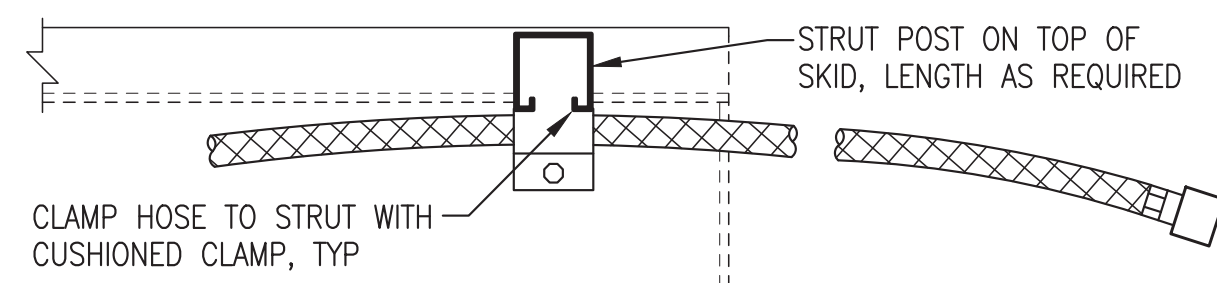

LEFT SKID PLAN (TOP) VIEW

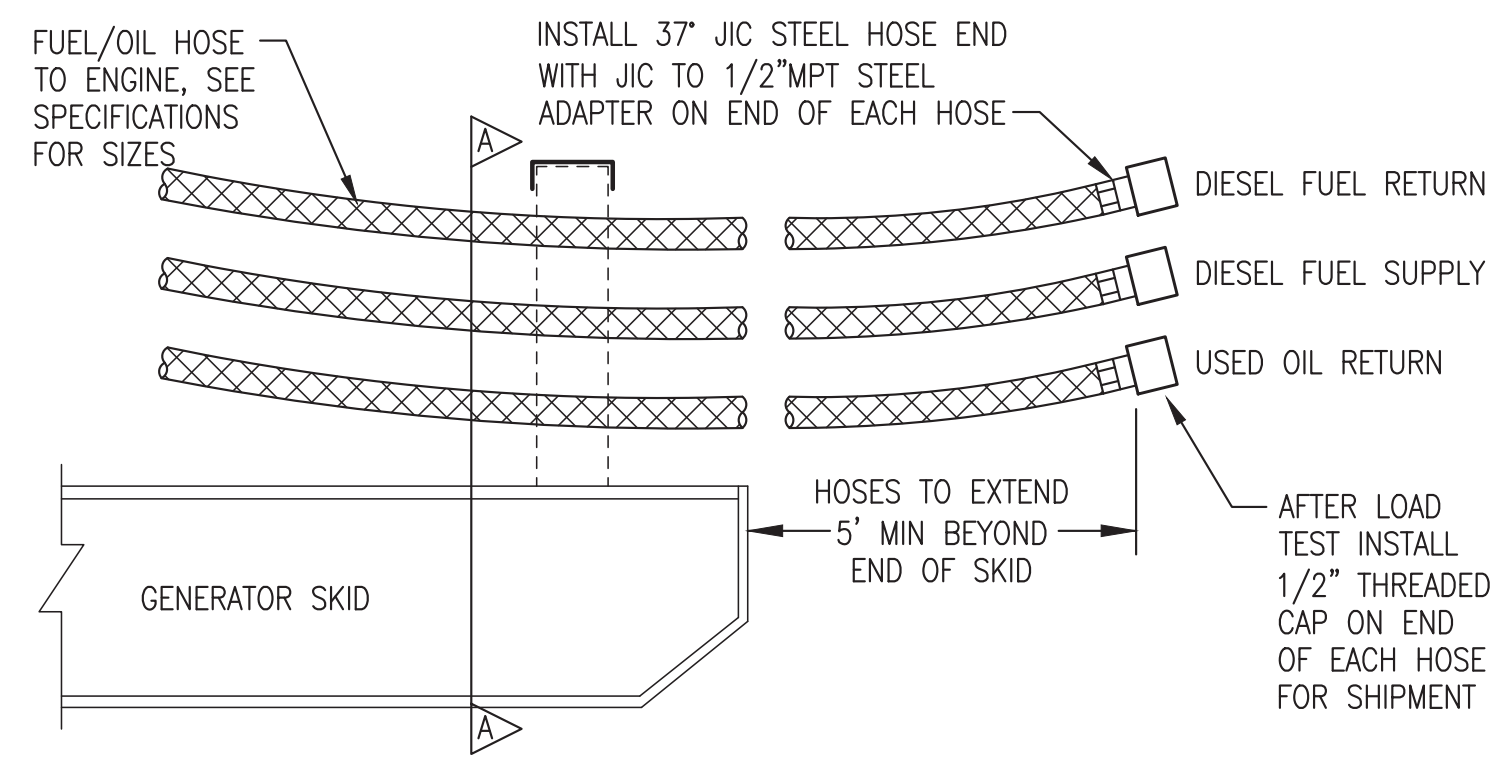


ELEVATION (SIDE) VIEW

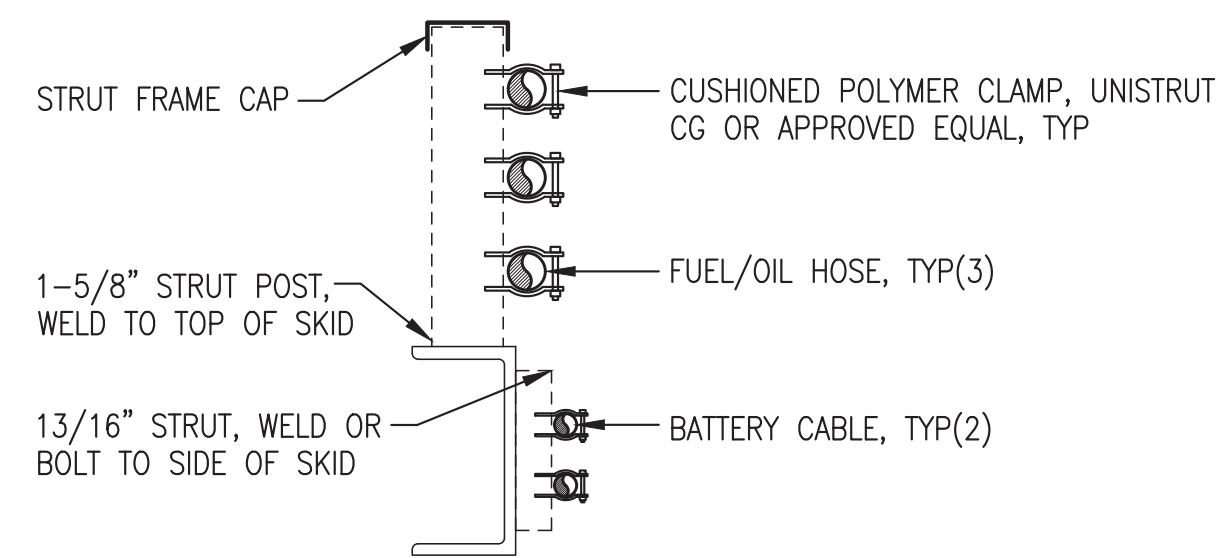


SECTION A-A

NOTE:  
GROUP HOSES ON LEFT SKID AS SHOWN TO COORDINATE WITH COOLANT HOSES ABOVE.


**1** FUEL/OIL HOSE & BATTERY CABLE INSTALLATION  
M3.4 NO SCALE

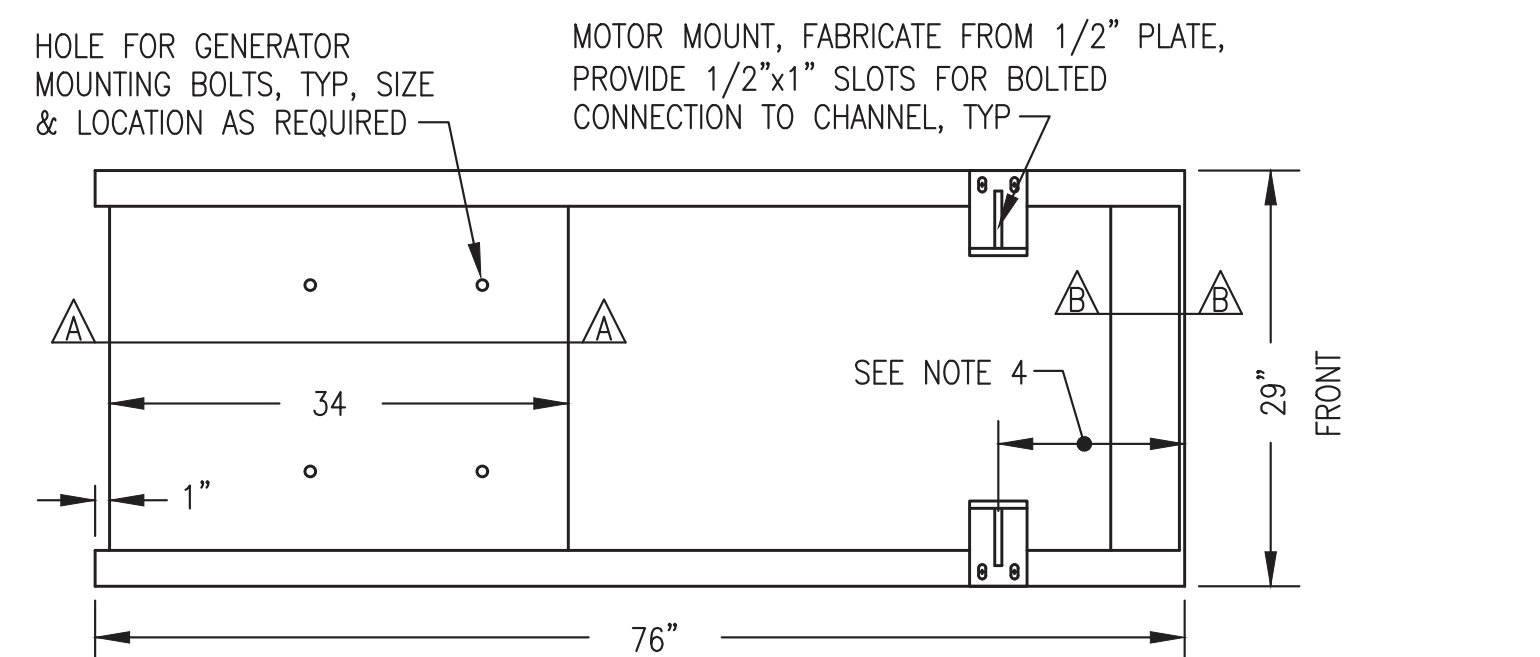


PLAN (TOP) VIEW

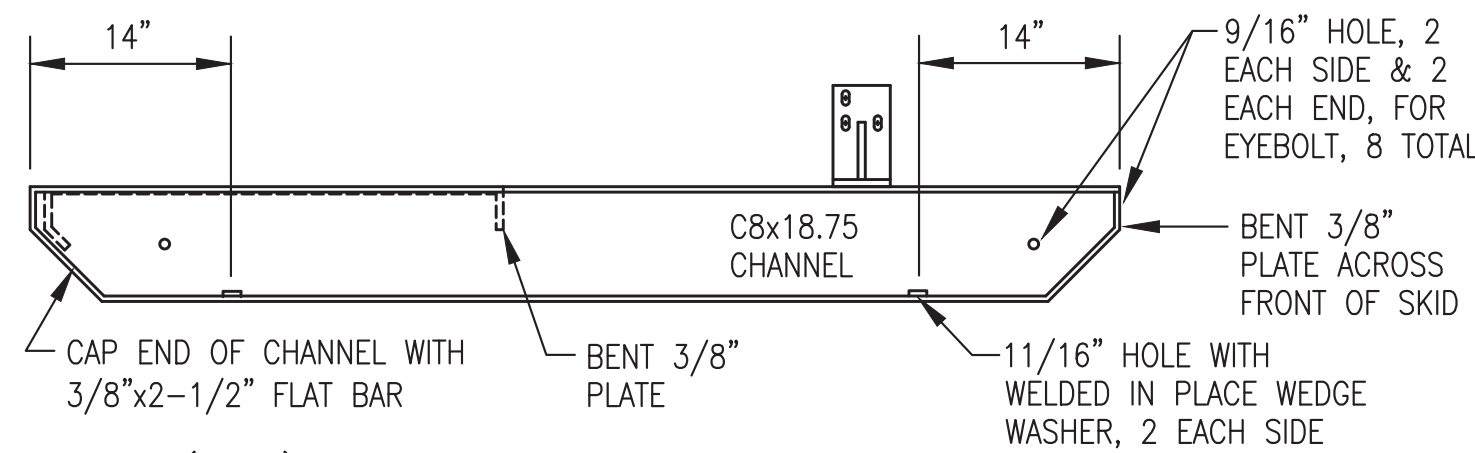

ELEVATION (SIDE) VIEW

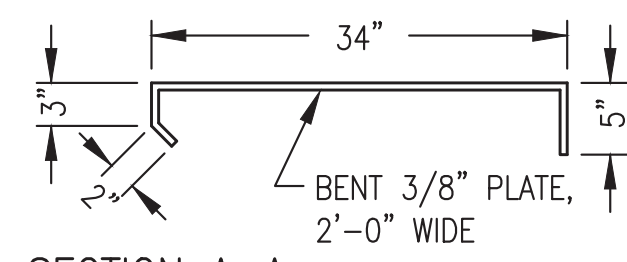

SECTION A-A

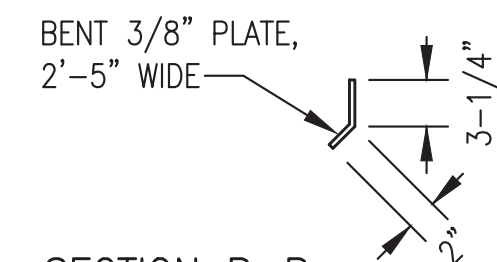


SECTION B-B

NOTES:


- 1) FABRICATE FROM ASTM A-36 STEEL. BEND PLATES & CUT ENDS OF CHANNELS AT 90° & 45° AS SHOWN.
- 2) EXCEPT WHERE INDICATED AS BOLTED MAKE ALL CONNECTIONS WITH CONTINUOUS WELDS (FILLET OR FULL-PENETRATION GROOVE AS REQUIRED) IN ACCORDANCE WITH CURRENT AWS STANDARD CODE.
- 3) ROUND ALL CORNERS & GRIND WELDS SMOOTH AFTER FABRICATION. PAINT TO MATCH ENGINE-GENERATOR.
- 4) PLACE UNIT ON SKID SO THAT THE EXHAUST RISER CENTERLINE IS 39" FROM THE FRONT OF THE SKID.

**2** TYPICAL GENERATOR SKID FABRICATION  
M3.4 NO SCALE

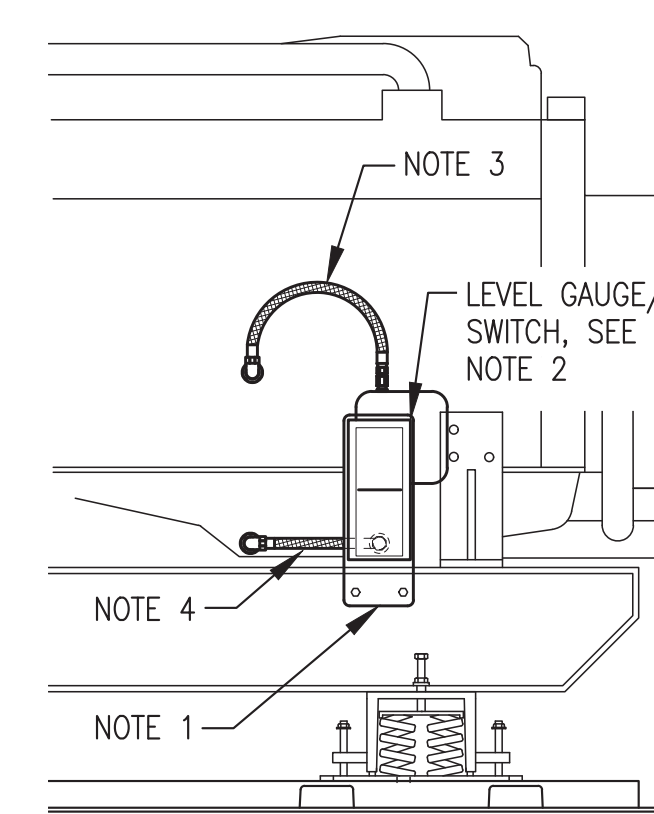


**3** TYPICAL OIL LEVEL GAUGE/SWITCH INSTALLATION  
M3.4 NO SCALE

- NOTES:
- 1) 1/4" STEEL SUPPORT PLATE PRE-DRILLED TO MATCH GAUGE/SWITCH MOUNTS AND BOTTOM HOSE ENTRANCE. BOLT TO INSIDE (BACK) OF CHANNEL SKID AT HEIGHT AS REQUIRED TO CENTER GAUGE AT NORMAL FULL OIL LEVEL.
  - 2) MOUNT OIL LEVEL GAUGE/SWITCH TO STEEL SUPPORT PLATE WITH RUBBER SHOCK MOUNTS. ADJUST SWITCH CONTACTS TO 1/2" ABOVE AND BELOW NORMAL FULL LEVEL. PAINT MARK A RED LINE AT BOTH SWITCH LEVELS.
  - 3) CONNECT TOP (VENT) PORT TO ENGINE CRANK CASE WITH #8 HOSE WITH 1/2" OR 3/8" NPT JIC SWIVEL ENDS. ROUTE UPPER HOSE WITH HIGH POINT 4" MIN ABOVE TOP OF GAUGE.
  - 4) CONNECT BOTTOM PORT TO ENGINE OIL PAN WITH #8 HOSE WITH 1/2" OR 3/8" NPT JIC SWIVEL ENDS. DO NOT TEE INTO OIL DRAIN LINE. ROUTE LOWER HOSE BACK THROUGH PRE-DRILLED HOLE IN STEEL PLATE.


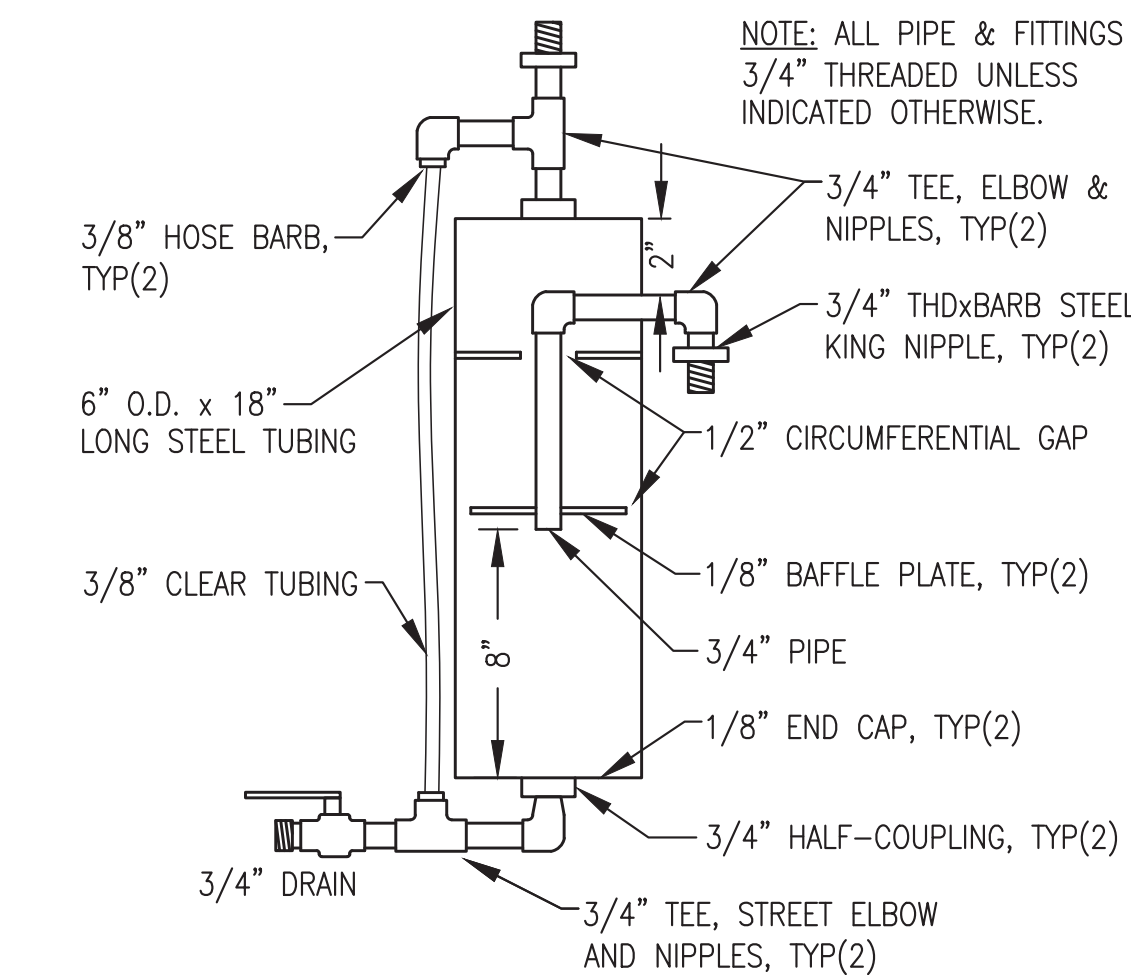


**4** CONDENSATE TRAP FABRICATION  
M3.4 NO SCALE


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		GENERATOR FABRICATION DETAILS	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		M3.4	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

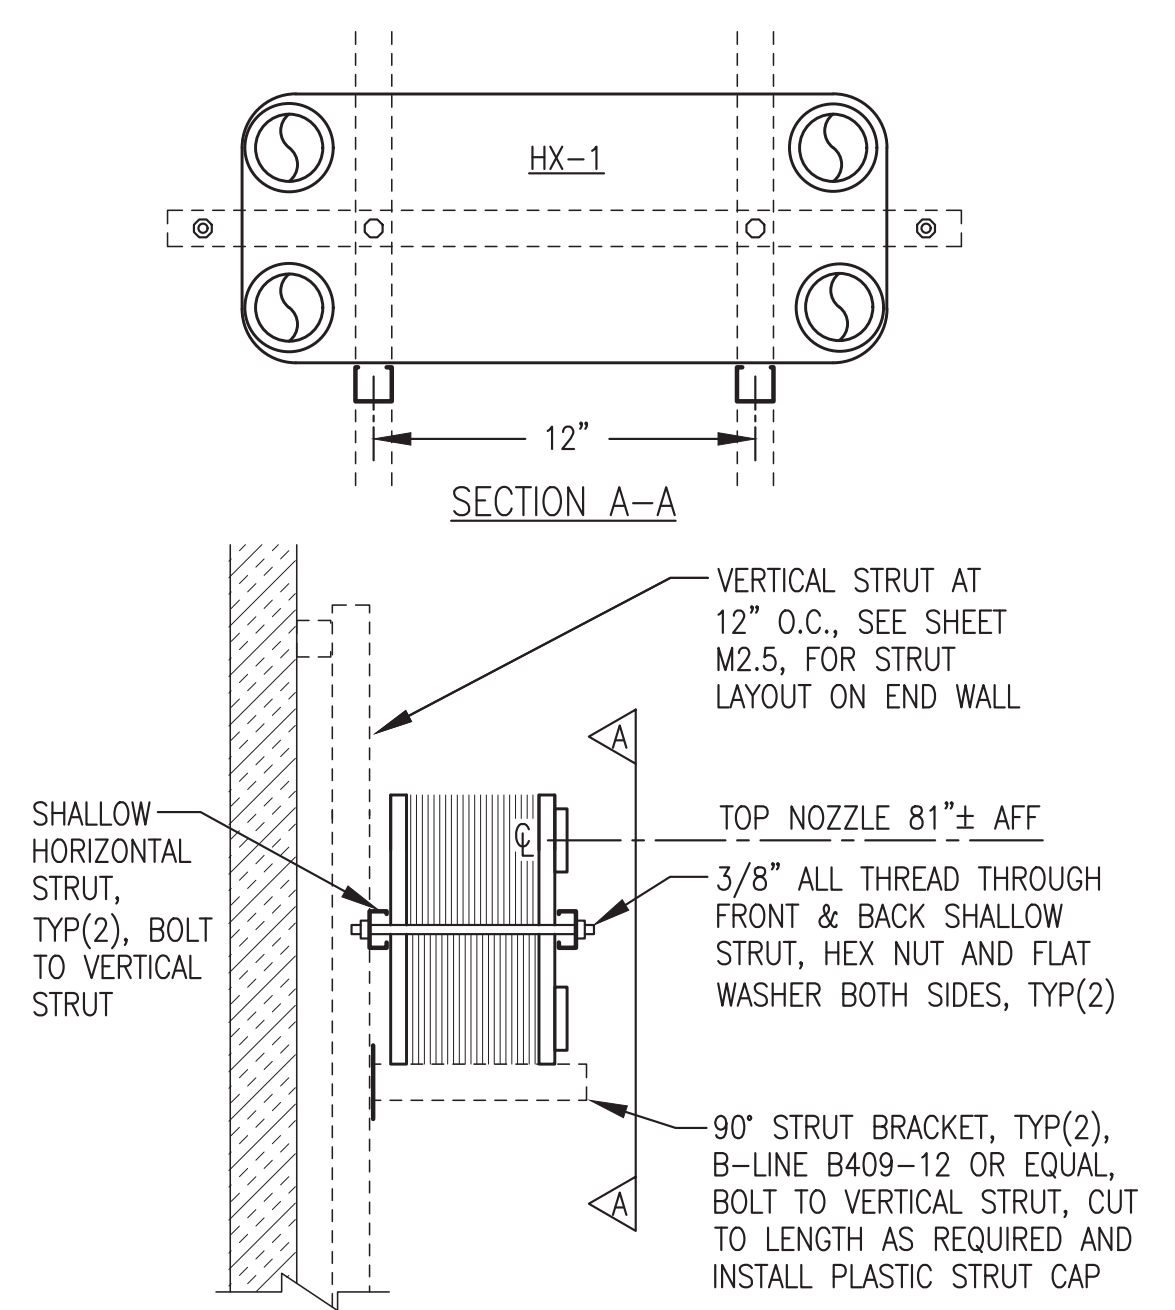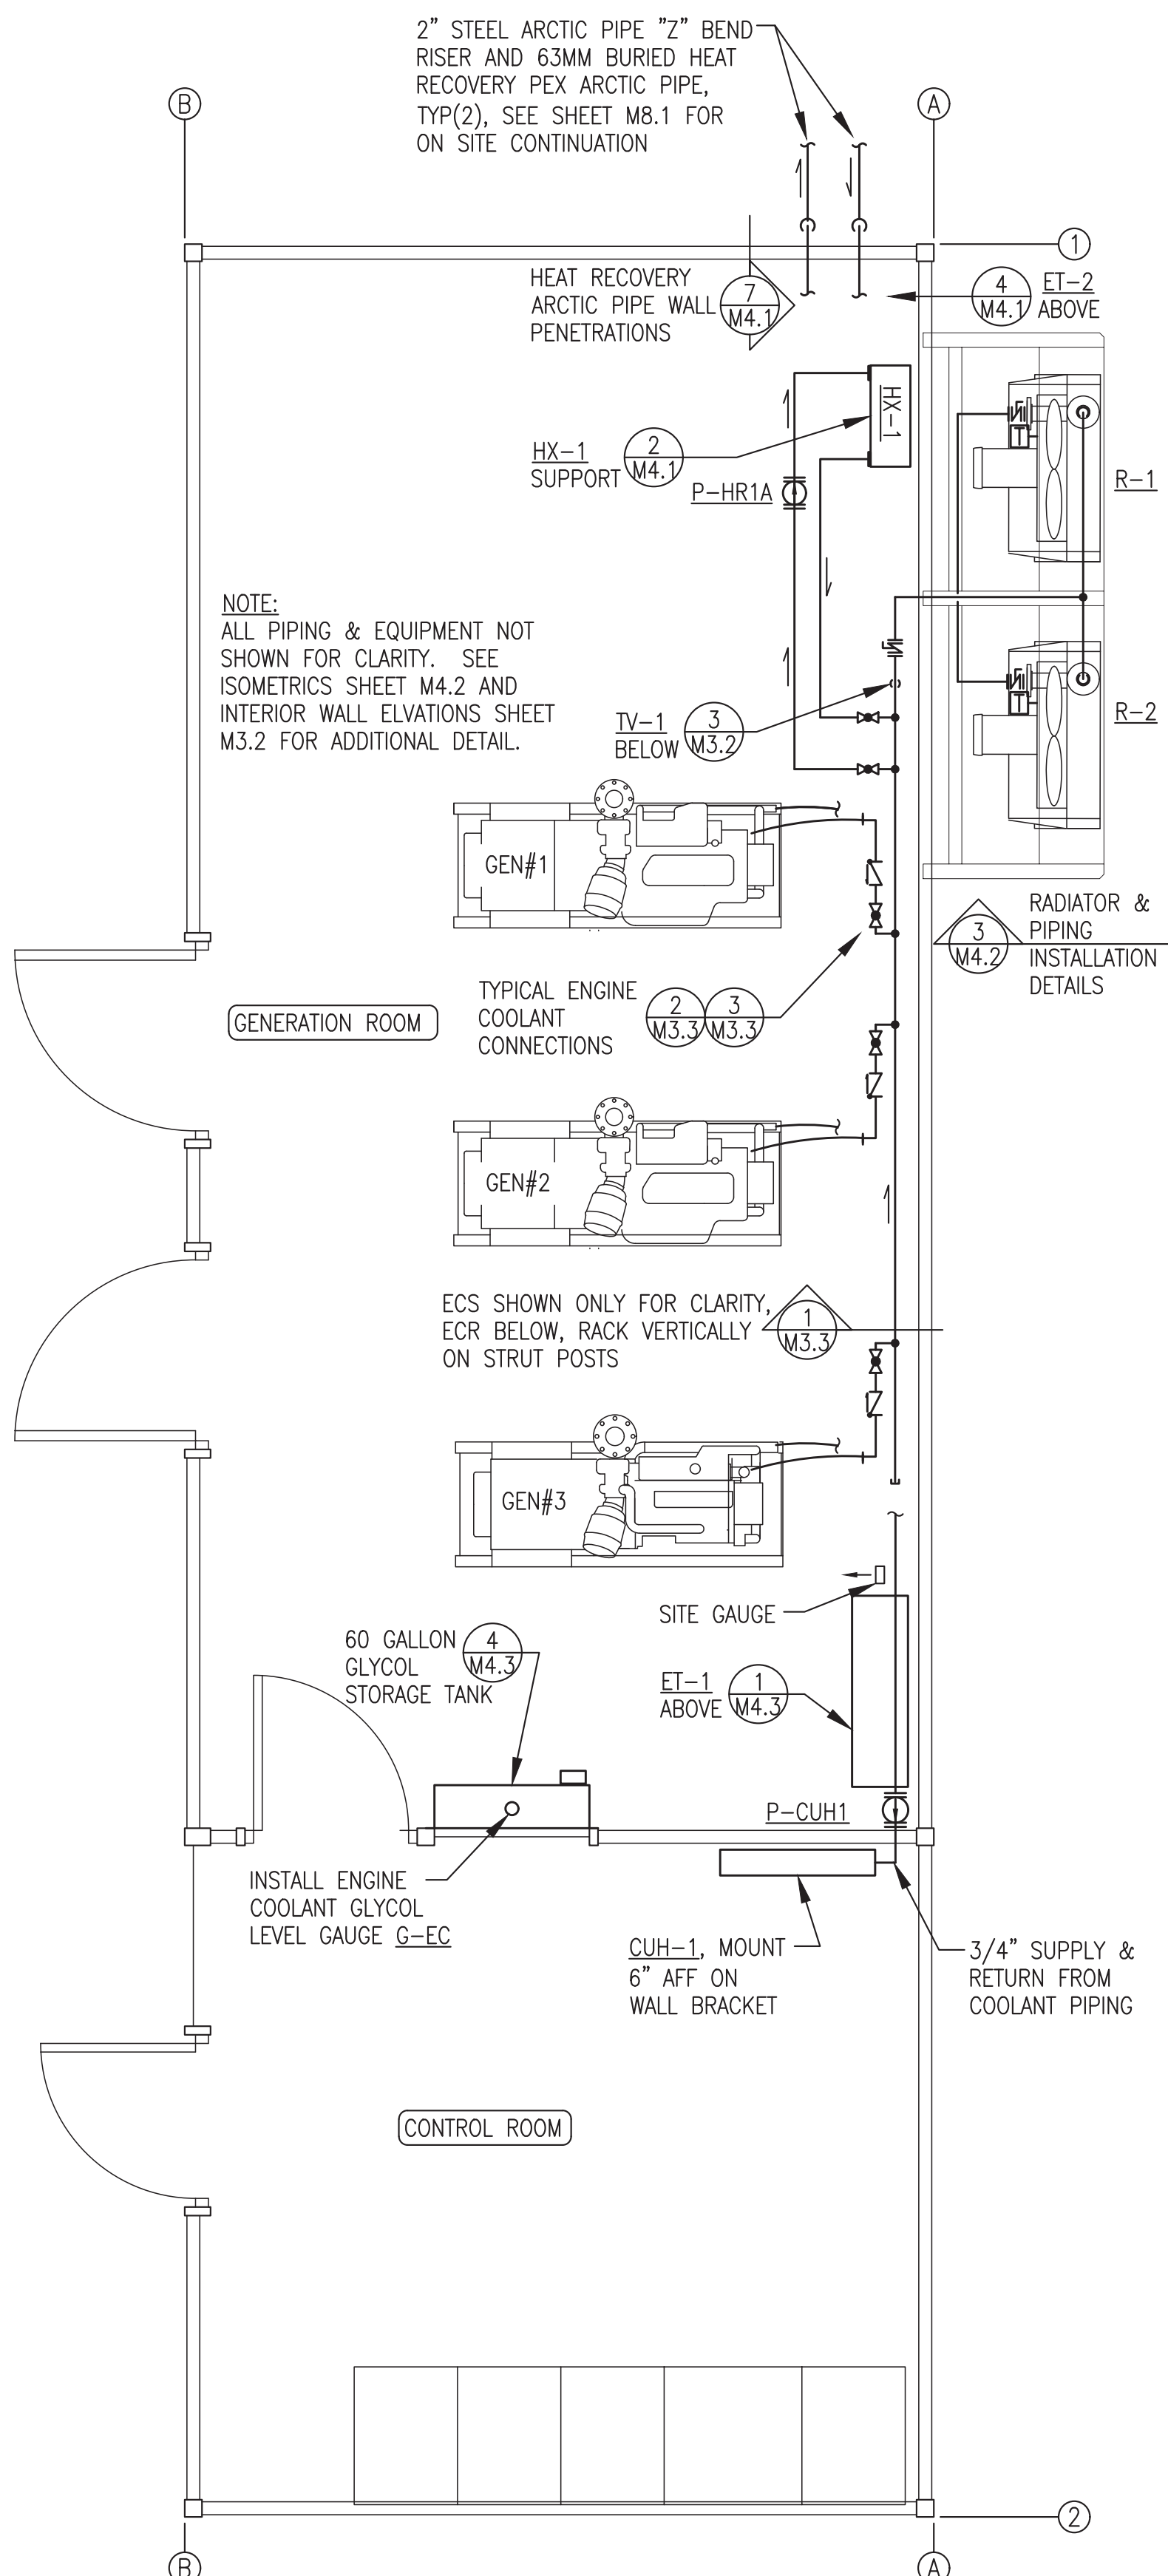


2 HEAT EXCHANGER HX-1 SUPPORT FROM WALL  
M4.1 NO SCALE

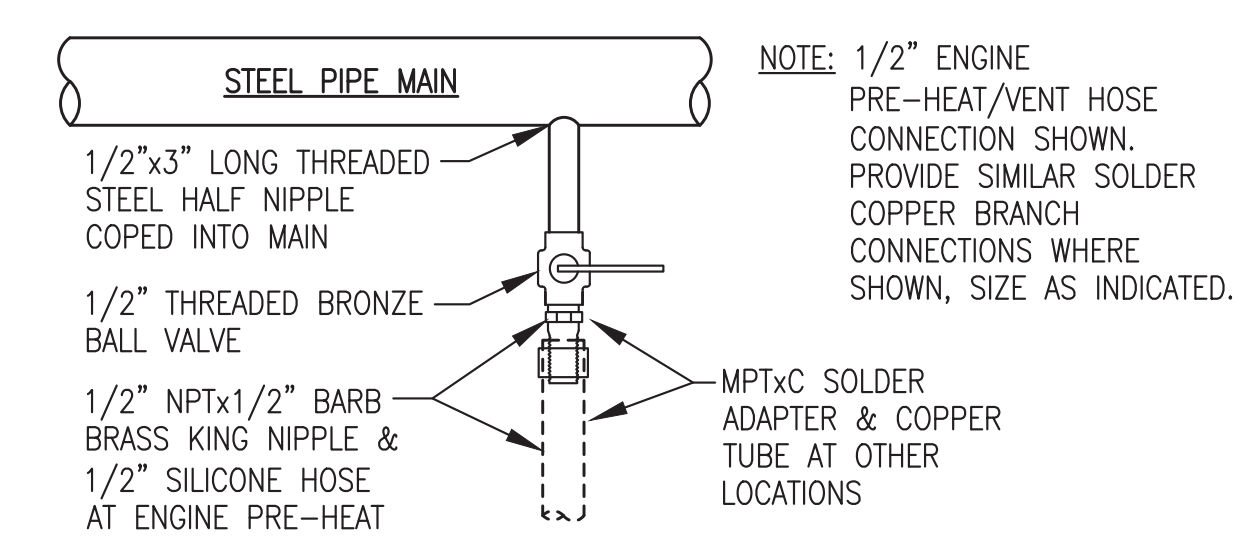


5 TYP VALVED BRANCH CONNECTION TO STEEL MAIN  
M4.1 NO SCALE

**HX CONNECTION NOTES:**

1) PROVIDE MINIMUM 9" LONG STRAIGHT COPPER TUBE SECTION BETWEEN ALL HEAT EXCHANGER NOZZLES AND FIRST SOLDER FITTING TO ALLOW FUTURE INSTALLATION OF NON-DIMPLED REPAIR COUPLING FOR HEAT EXCHANGER TEMPORARY REMOVAL AND/OR REPLACEMENT.

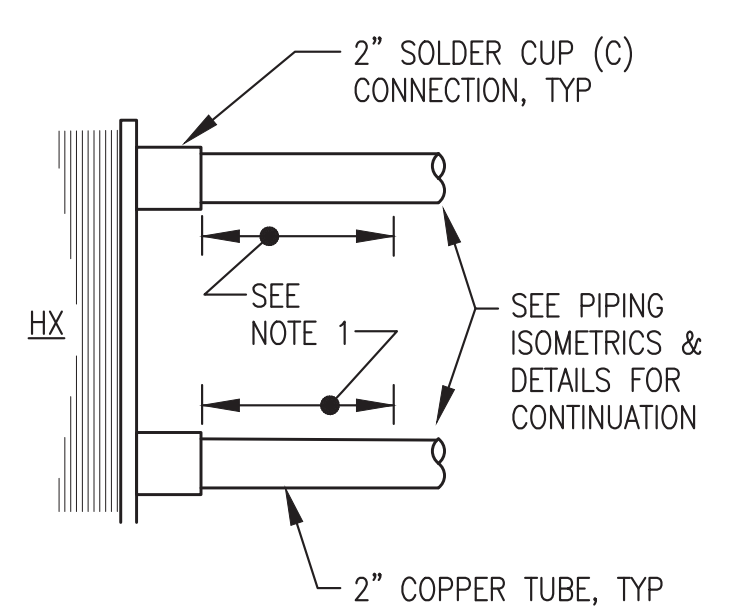

3 TYPICAL HX PIPING CONNECTION  
M4.1 NO SCALE

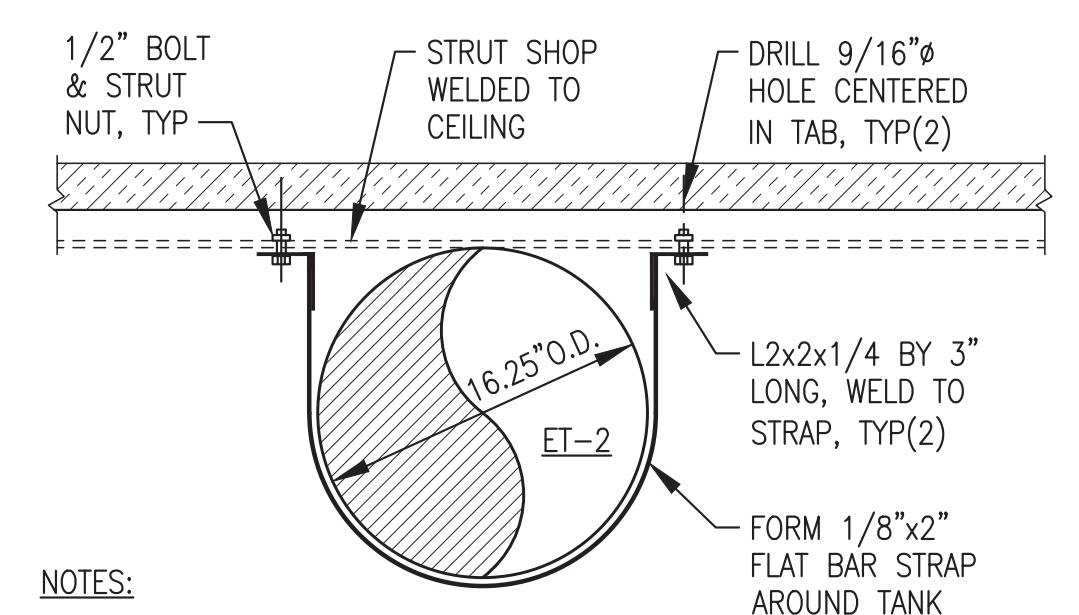


**NOTES:**

1) SMOOTH EDGES AFTER FABRICATION, WIRE BRUSH, SOLVENT CLEAN, AND PAINT WITH TWO COATS OF COLD GALVANIZING COMPOUND.

2) ONE STRAP SHOWN. INSTALL FOUR IDENTICAL STRAPS.

4 HEAT RECOVERY EXP TANK ET-2 SUPPORT  
M4.1 NO SCALE

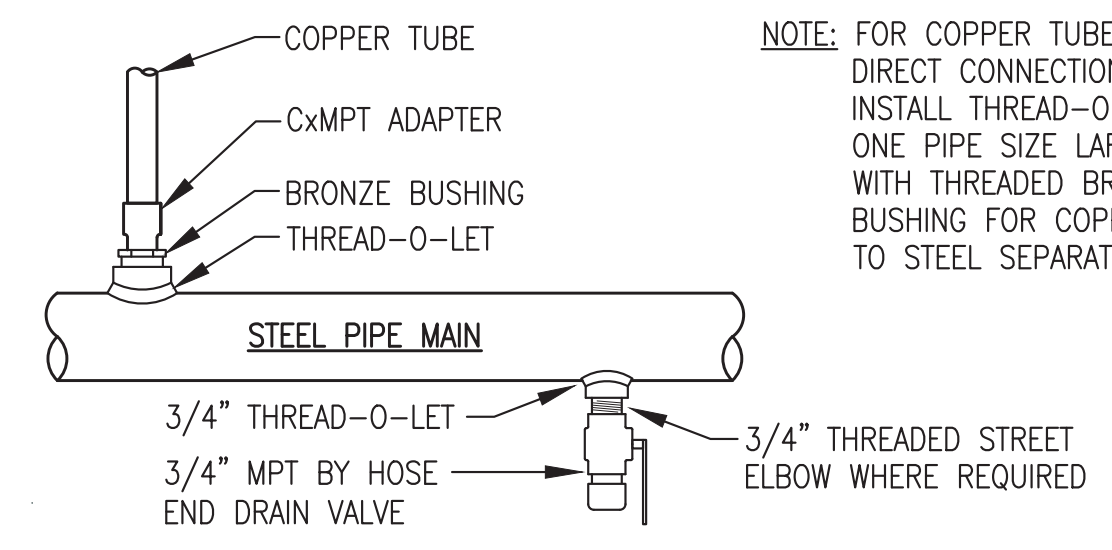

**NOTE:** FOR COPPER TUBE DIRECT CONNECTION INSTALL THREAD-O-LET ONE PIPE SIZE LARGER WITH THREADED BRONZE BUSHING FOR COPPER TO STEEL SEPARATION.

6 TYP DIRECT CONNECTION TO STEEL MAIN  
M4.1 NO SCALE

**ARCTIC PIPE GENERAL NOTES:**

1) SEE END WALL ELEVATION 2/M3.2 FOR PIPE WALL PENETRATION LAYOUT.

2) ONE PIPE SHOWN. PROVIDE TWO SIMILAR.


**ARCTIC PIPE SHOP/ON-SITE NOTES:**

1) SHOP INSTALLATION SHOWN. STUB PIPE 8" MIN BEYOND WALL & TEMPORARILY CONNECT SUPPLY TO RETURN FOR TESTING.

2) AFTER TESTING REMOVE TEMPORARY CONNECTION, BREAK FLANGE JOINT, AND STORE PIPE IN MODULE. INSTALL THREADED PIPE CAP FOR SHIPPING.

3) AS PART OF ON-SITE INSTALLATION REMOVE THREADED PIPE CAP, REINSTALL PIPE THROUGH WALL AND CONNECT TO ARCTIC PIPE, SEE SHEET M8.

4) SHOP INSULATE COPPER TUBE UP TO BUTTERFLY VALVE. SHOP CUT & FIT INSULATION & JACKET FOR STEEL PIPE TO WALL BUT SHIP LOOSE FOR FIELD INSTALLATION.

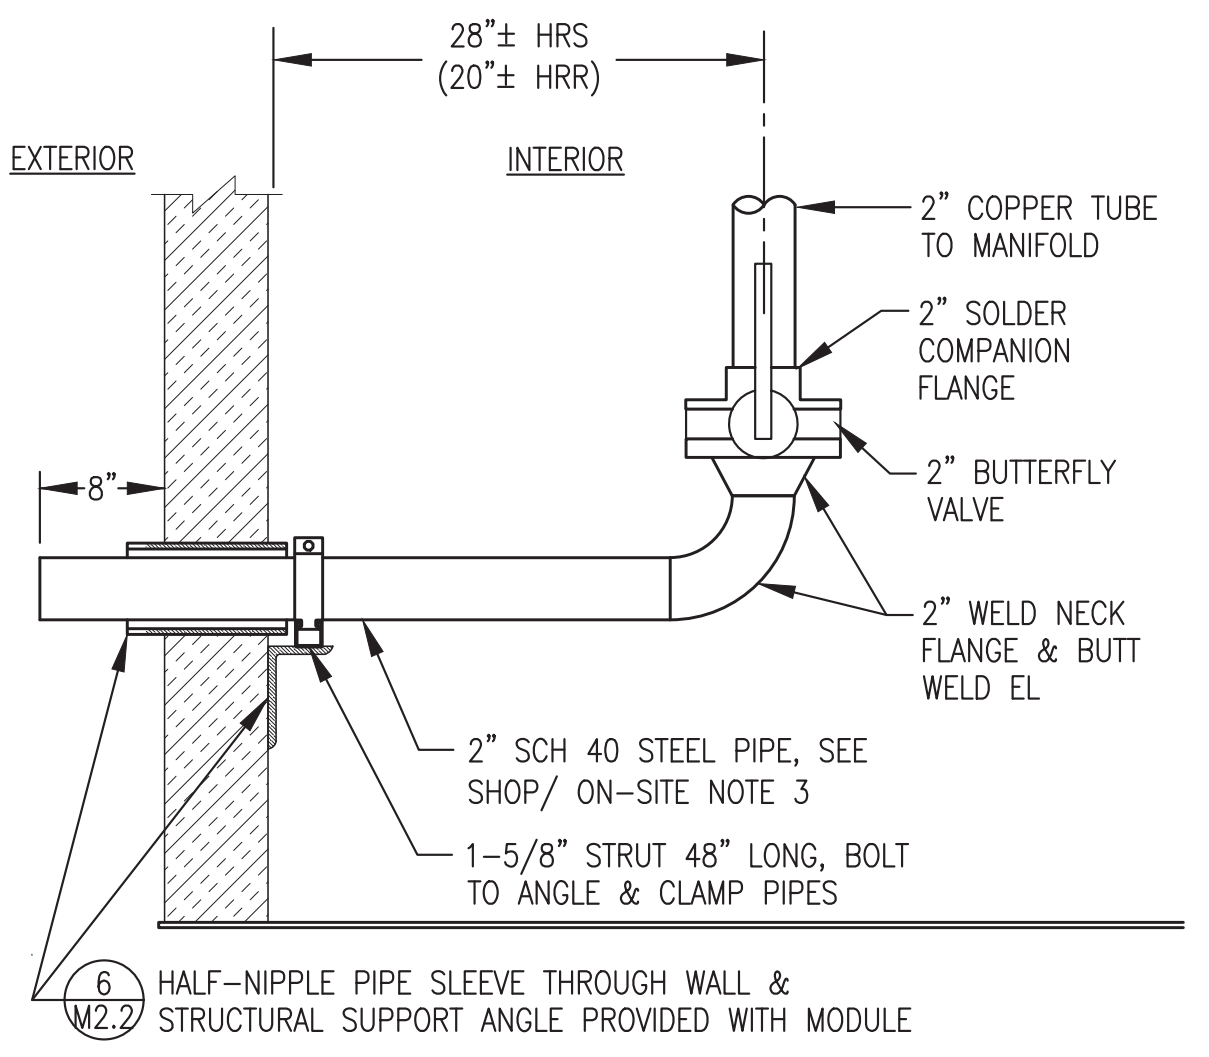

7 HEAT RECOVERY ARCTIC PIPE WALL PENETRATIONS  
M4.1 NO SCALE

1 COOLANT AND HEAT RECOVERY PIPING PLAN  
M4.1 3/8"=1'-0"

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: COOLANT & HEAT RECOVERY PIPING PLAN & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET: M4.1	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

**COOLING SYSTEM ISOMETRIC NOTES:**


- ALL PIPING SHOWN THIS ISOMETRIC 4" SCH 40 STEEL WITH WELDED JOINTS UNLESS SPECIFICALLY INDICATED OTHERWISE. SEE DETAIL 3/M3.2 FOR COOLING MANIFOLD DETAILS. ALL ENGINE BRANCH CONNECTIONS SCH 40 STEEL WITH WELDED AND THREADED JOINTS. ALL OTHER PIPE SHOWN THIS ISOMETRIC TYPE "L" HARD DRAWN COPPER WITH SOLDER JOINTS UNLESS SPECIFICALLY INDICATED OTHERWISE.
- SEE COOLANT MANIFOLD FABRICATION DETAIL 3/M3.2 FOR CONNECTIONS TO STEEL MAINS. SEE DETAILS 2&3/M3.3 FOR BRANCH PIPING CONNECTIONS. SEE DETAILS 2/M4.3 FOR INSTRUMENTATION CONNECTIONS.
- ALL COOLANT PRESSURE GAUGES 0-30 PSIG.
- SEE ELECTRICAL INSTRUMENTATION SCHEDULE FOR TEMPERATURE TRANSMITTERS AND OTHER INSTRUMENTATION.
- UPON COMPLETION OF FABRICATION VALVE OFF CABINET UNIT HEATER AND FLUSH PIPING TO REMOVE ALL DEBRIS, SEE SPECIFICATIONS.
- SHOP INSULATE COOLANT PIPING MAINS FROM GENERATOR VALVES TO BUTTERFLY VALVES AT WALL PENETRATIONS. SHOP CUT & FIT INSULATION & JACKET FROM VALVES TO WALL BUT SHIP LOOSE FOR FIELD INSTALLATION. ALL OTHER PIPING NOT INSULATED.
- 3/4" THREADED BALL VALVE, 3/4"MPTx5/8" BARB BRASS KING NIPPLE, & 1/2" HOSE FOR ENGINE VENT & PRE-HEAT.
- SET P-HR1A TO OPERATE ON SPEED CP2. SET P-CUH1 TO OPERATE ON SPEED 3.

**HYDRONIC PIPING SHOP/ON-SITE NOTES:**

- SEE SPECIFICATION 23 21 13 FOR COOLING AND HEAT RECOVERY PIPING TESTING, FLUSHING, DRAINING, AND FILLING REQUIREMENTS.
- SEE DETAILS 7/M4.1, 3/M4.2, AND 5/M4.3 FOR SHOP/FIELD REQUIREMENTS FOR PIPING THROUGH THE EXTERIOR WALLS.

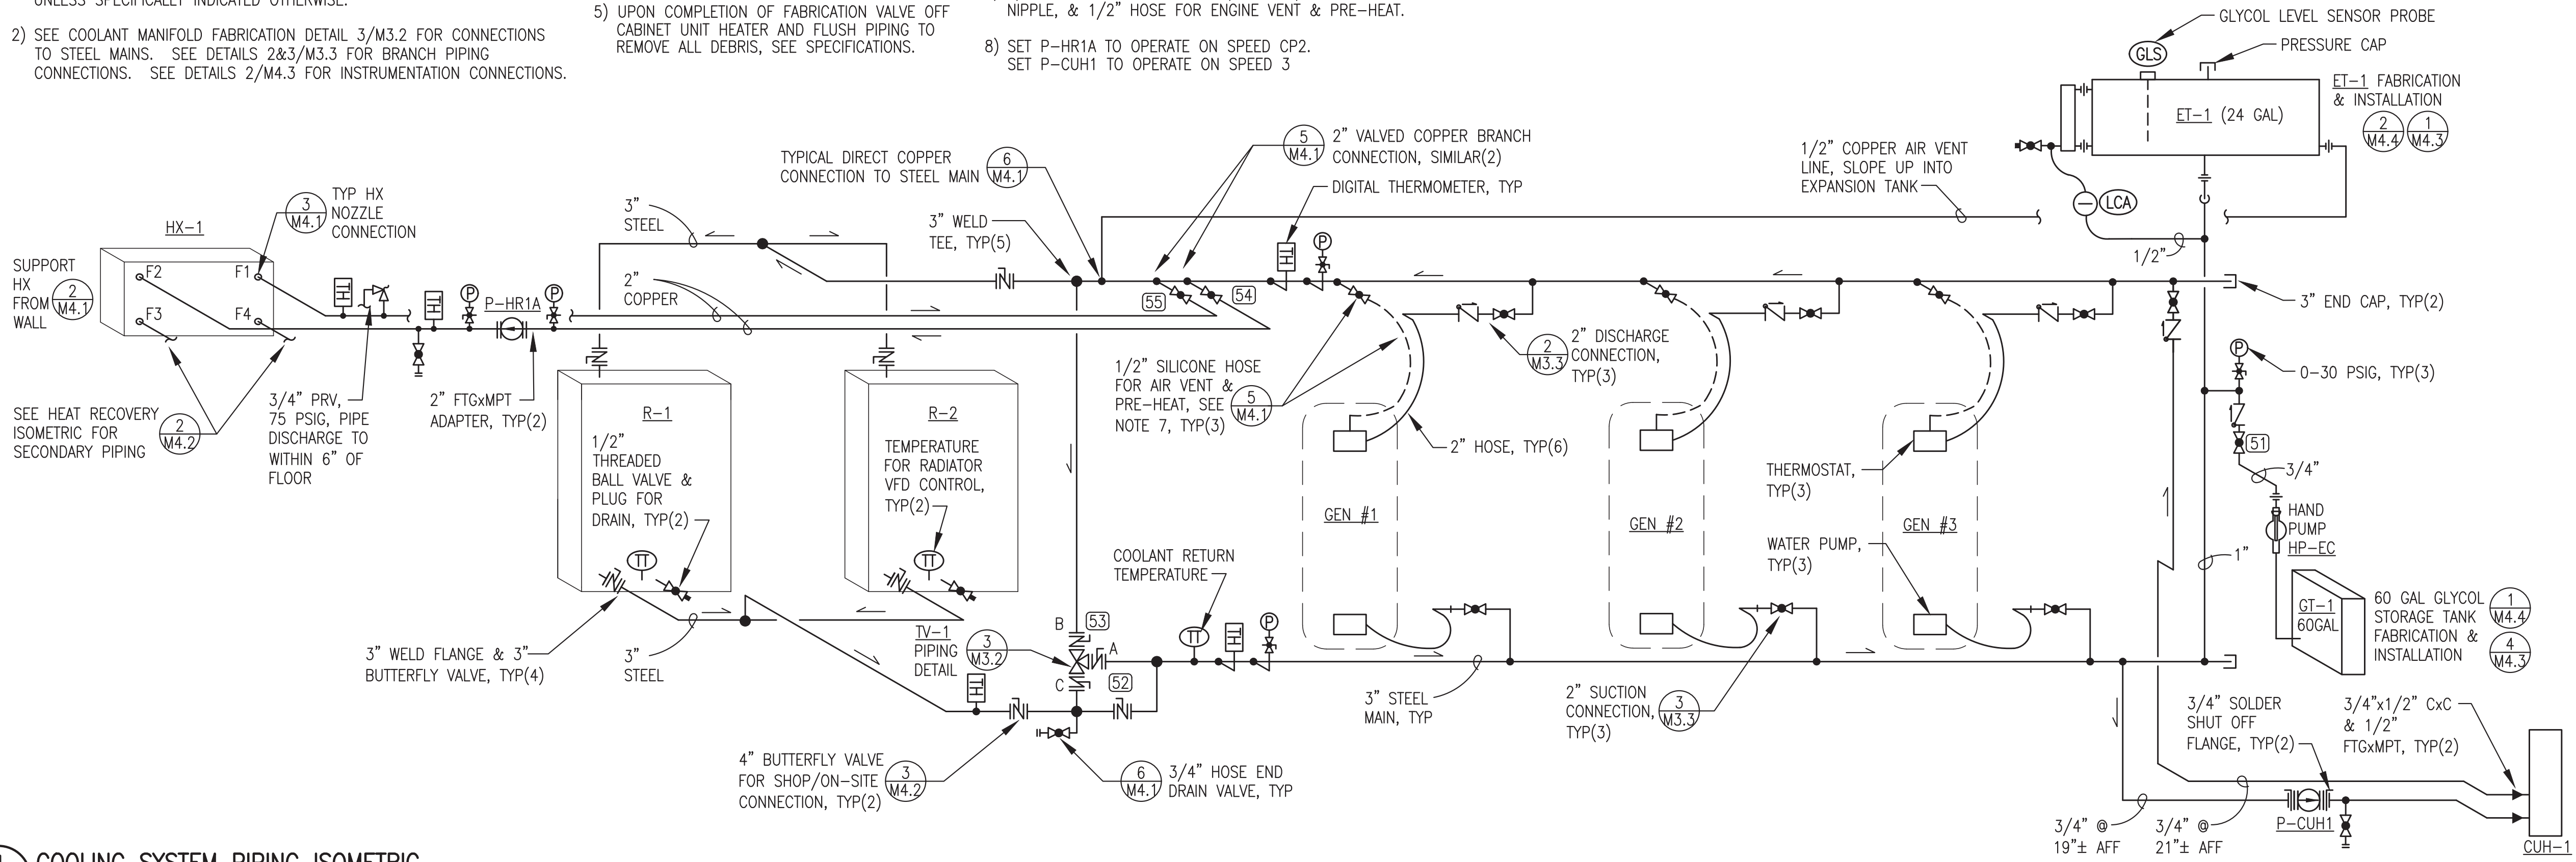


**1 COOLING SYSTEM PIPING ISOMETRIC**  
M4.2 NO SCALE

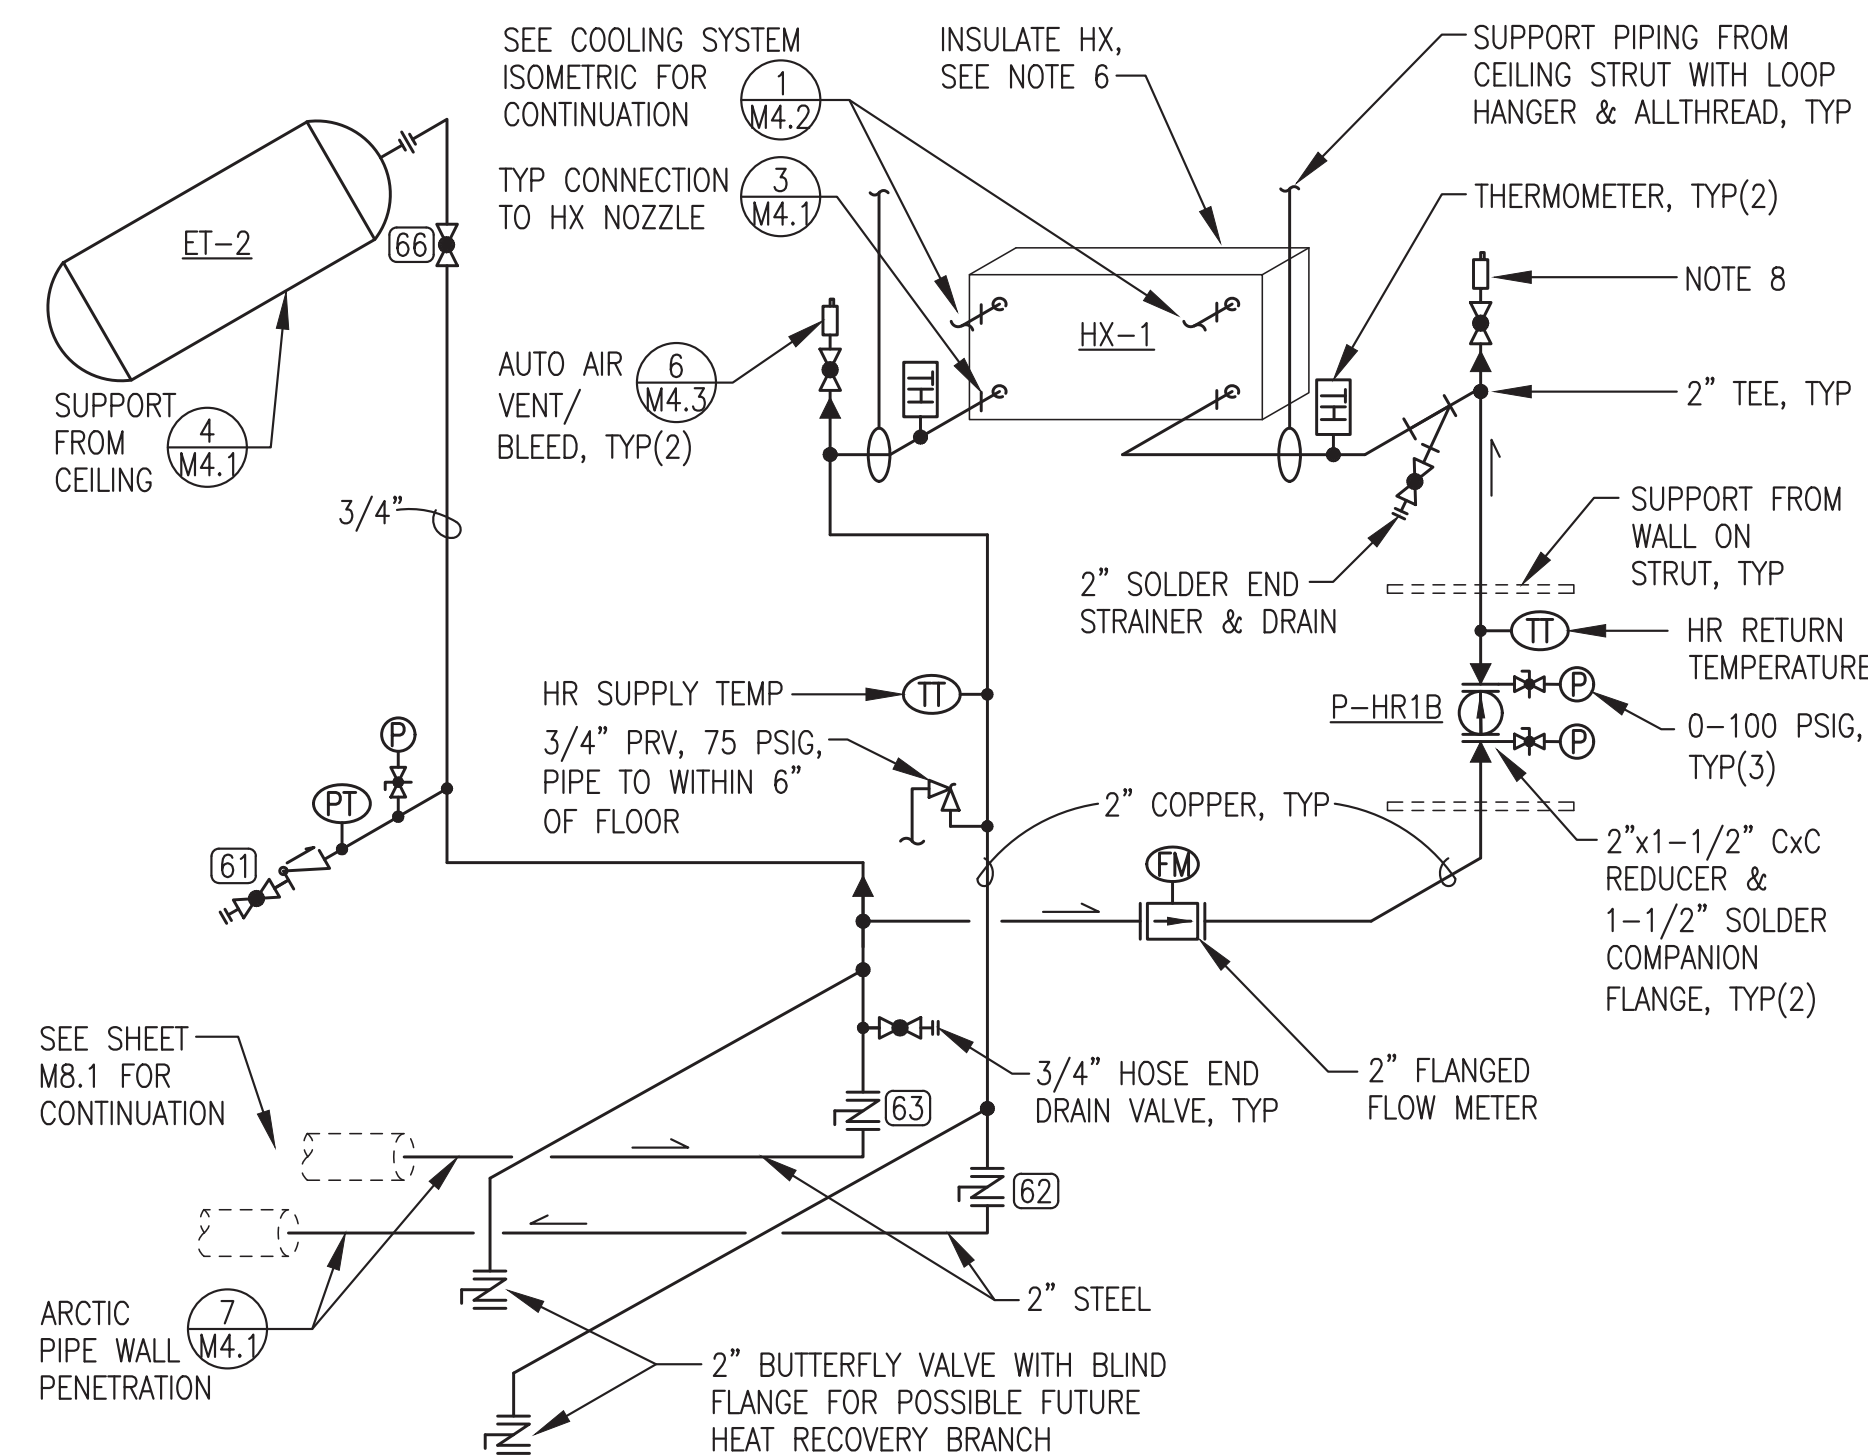

**HEAT RECOVERY ISOMETRIC NOTES:**

- ALL PIPING SHOWN THIS ISOMETRIC TYPE "L" COPPER WITH SOLDER JOINTS, 2" EXCEPT WHERE SPECIFICALLY INDICATED OTHERWISE. ALL FLANGES ANSI 150# PATTERN TWO-PIECE WITH POWDER COATED STEEL FLANGE AND SOLDER COPPER TUBE ADAPTER. FOR ALL JOINTS EXCEPT BUTTERFLY VALVES INSTALL SPIRAL WOUND METALLIC GASKETS AND COAT GASKETS WITH ANTI-SEIZE COMPOUND PRIOR TO ASSEMBLING.
- MAKE ALL CONNECTIONS FOR INSTRUMENTATION WITH T-DRILL TAP OR REDUCING TEE. SEE DETAIL 3/M4.3.
- ALL HEAT RECOVERY PRESSURE GAUGES 0-100 PSIG.
- SEE INSTRUMENTATION SCHEDULE SHEET M1.1 FOR TEMPERATURE AND PRESSURE TRANSMITTERS AND FLOW METER.
- UPON COMPLETION OF FABRICATION FLUSH PIPING TO REMOVE ALL DEBRIS, SEE SPECIFICATIONS.
- INSULATE ALL 2" HEAT RECOVERY PIPING MAINS. WRAP HEAT EXCHANGER WITH 1" RIGID FOIL-BACK FIBERGLASS INSULATION ALL AROUND AND TAPE ALL SEAMS.
- SET P-HR1B TO OPERATE ON CP2 FOR PRESENT OPERATION. INCREASE TO CP3 TO ADD FUTURE CLINIC.
- RISE UP BEHIND WIREWAY FOR THIS AIR VENT CONNECTION.

**2 HEAT RECOVERY SYSTEM PIPING ISOMETRIC**  
M4.2 NO SCALE

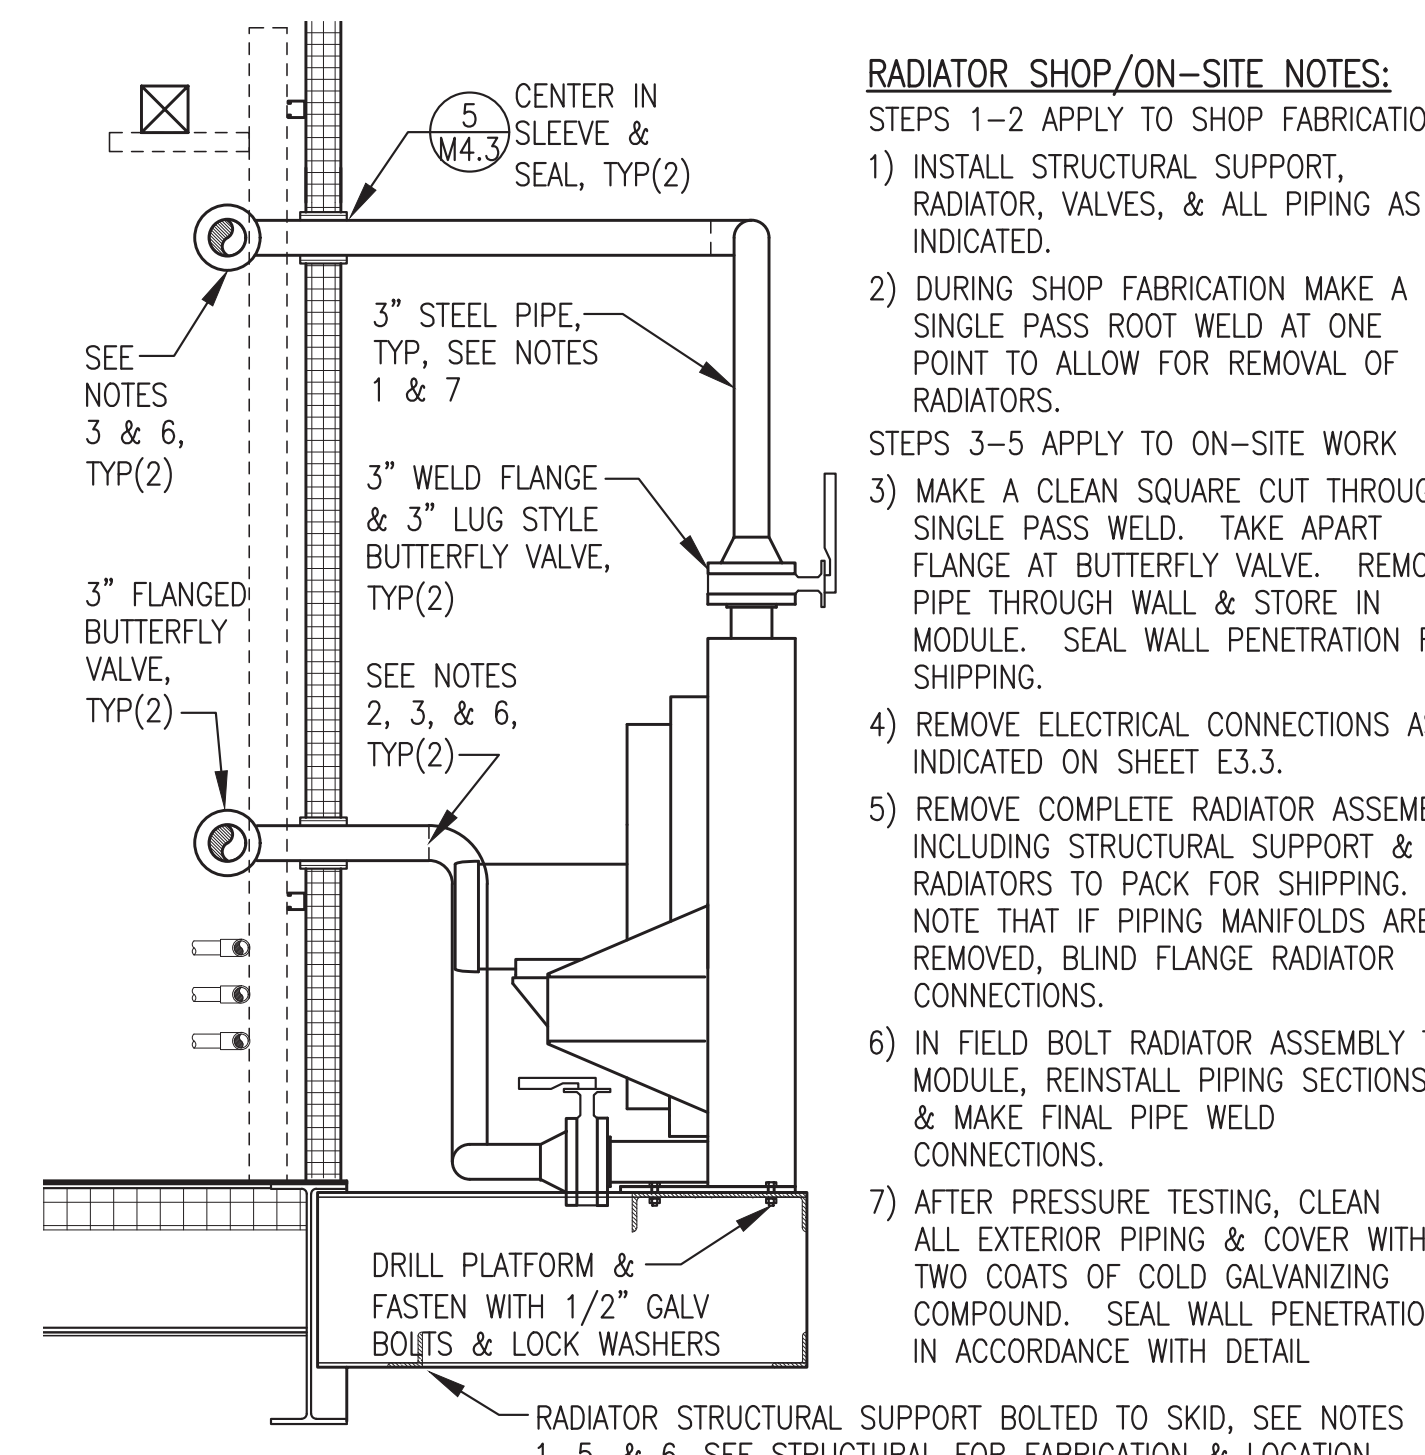


**RADIATOR SHOP/ON-SITE NOTES:**


- STEPS 1-2 APPLY TO SHOP FABRICATION
- INSTALL STRUCTURAL SUPPORT, RADIATOR, VALVES, & ALL PIPING AS INDICATED.
  - DURING SHOP FABRICATION MAKE A SINGLE PASS ROOT WELD AT ONE POINT TO ALLOW FOR REMOVAL OF RADIATORS.
- STEPS 3-5 APPLY TO ON-SITE WORK
- MAKE A CLEAN SQUARE CUT THROUGH SINGLE PASS WELD. TAKE APART FLANGE AT BUTTERFLY VALVE. REMOVE PIPE THROUGH WALL & STORE IN MODULE. SEAL WALL PENETRATION FOR SHIPPING.
  - REMOVE ELECTRICAL CONNECTIONS AS INDICATED ON SHEET E3.3.
  - REMOVE COMPLETE RADIATOR ASSEMBLY INCLUDING STRUCTURAL SUPPORT & RADIATORS TO PACK FOR SHIPPING. NOTE THAT IF PIPING MANIFOLDS ARE REMOVED, BLIND FLANGE RADIATOR CONNECTIONS.
  - IN FIELD BOLT RADIATOR ASSEMBLY TO MODULE, REINSTALL PIPING SECTIONS, & MAKE FINAL PIPE WELD CONNECTIONS.
  - AFTER PRESSURE TESTING, CLEAN ALL EXTERIOR PIPING & COVER WITH TWO COATS OF COLD GALVANIZING COMPOUND. SEAL WALL PENETRATION IN ACCORDANCE WITH DETAIL

**3 RADIATOR & PIPING INSTALLATION**  
M4.2 3/4"=1'-0"


**REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022**




1	UPDATED TO COORDINATE WITH NAPAKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
<b>PROJECT:</b> RAMPART POWER SYSTEM UPGRADE			
<b>TITLE:</b> COOLANT & HEAT RECOVERY ISOMETRICS & DETAILS			
DRAWN BY: JTD DESIGNED BY: BCG		SCALE: AS NOTED DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7 PROJECT NUMBER:		<b>M4.2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

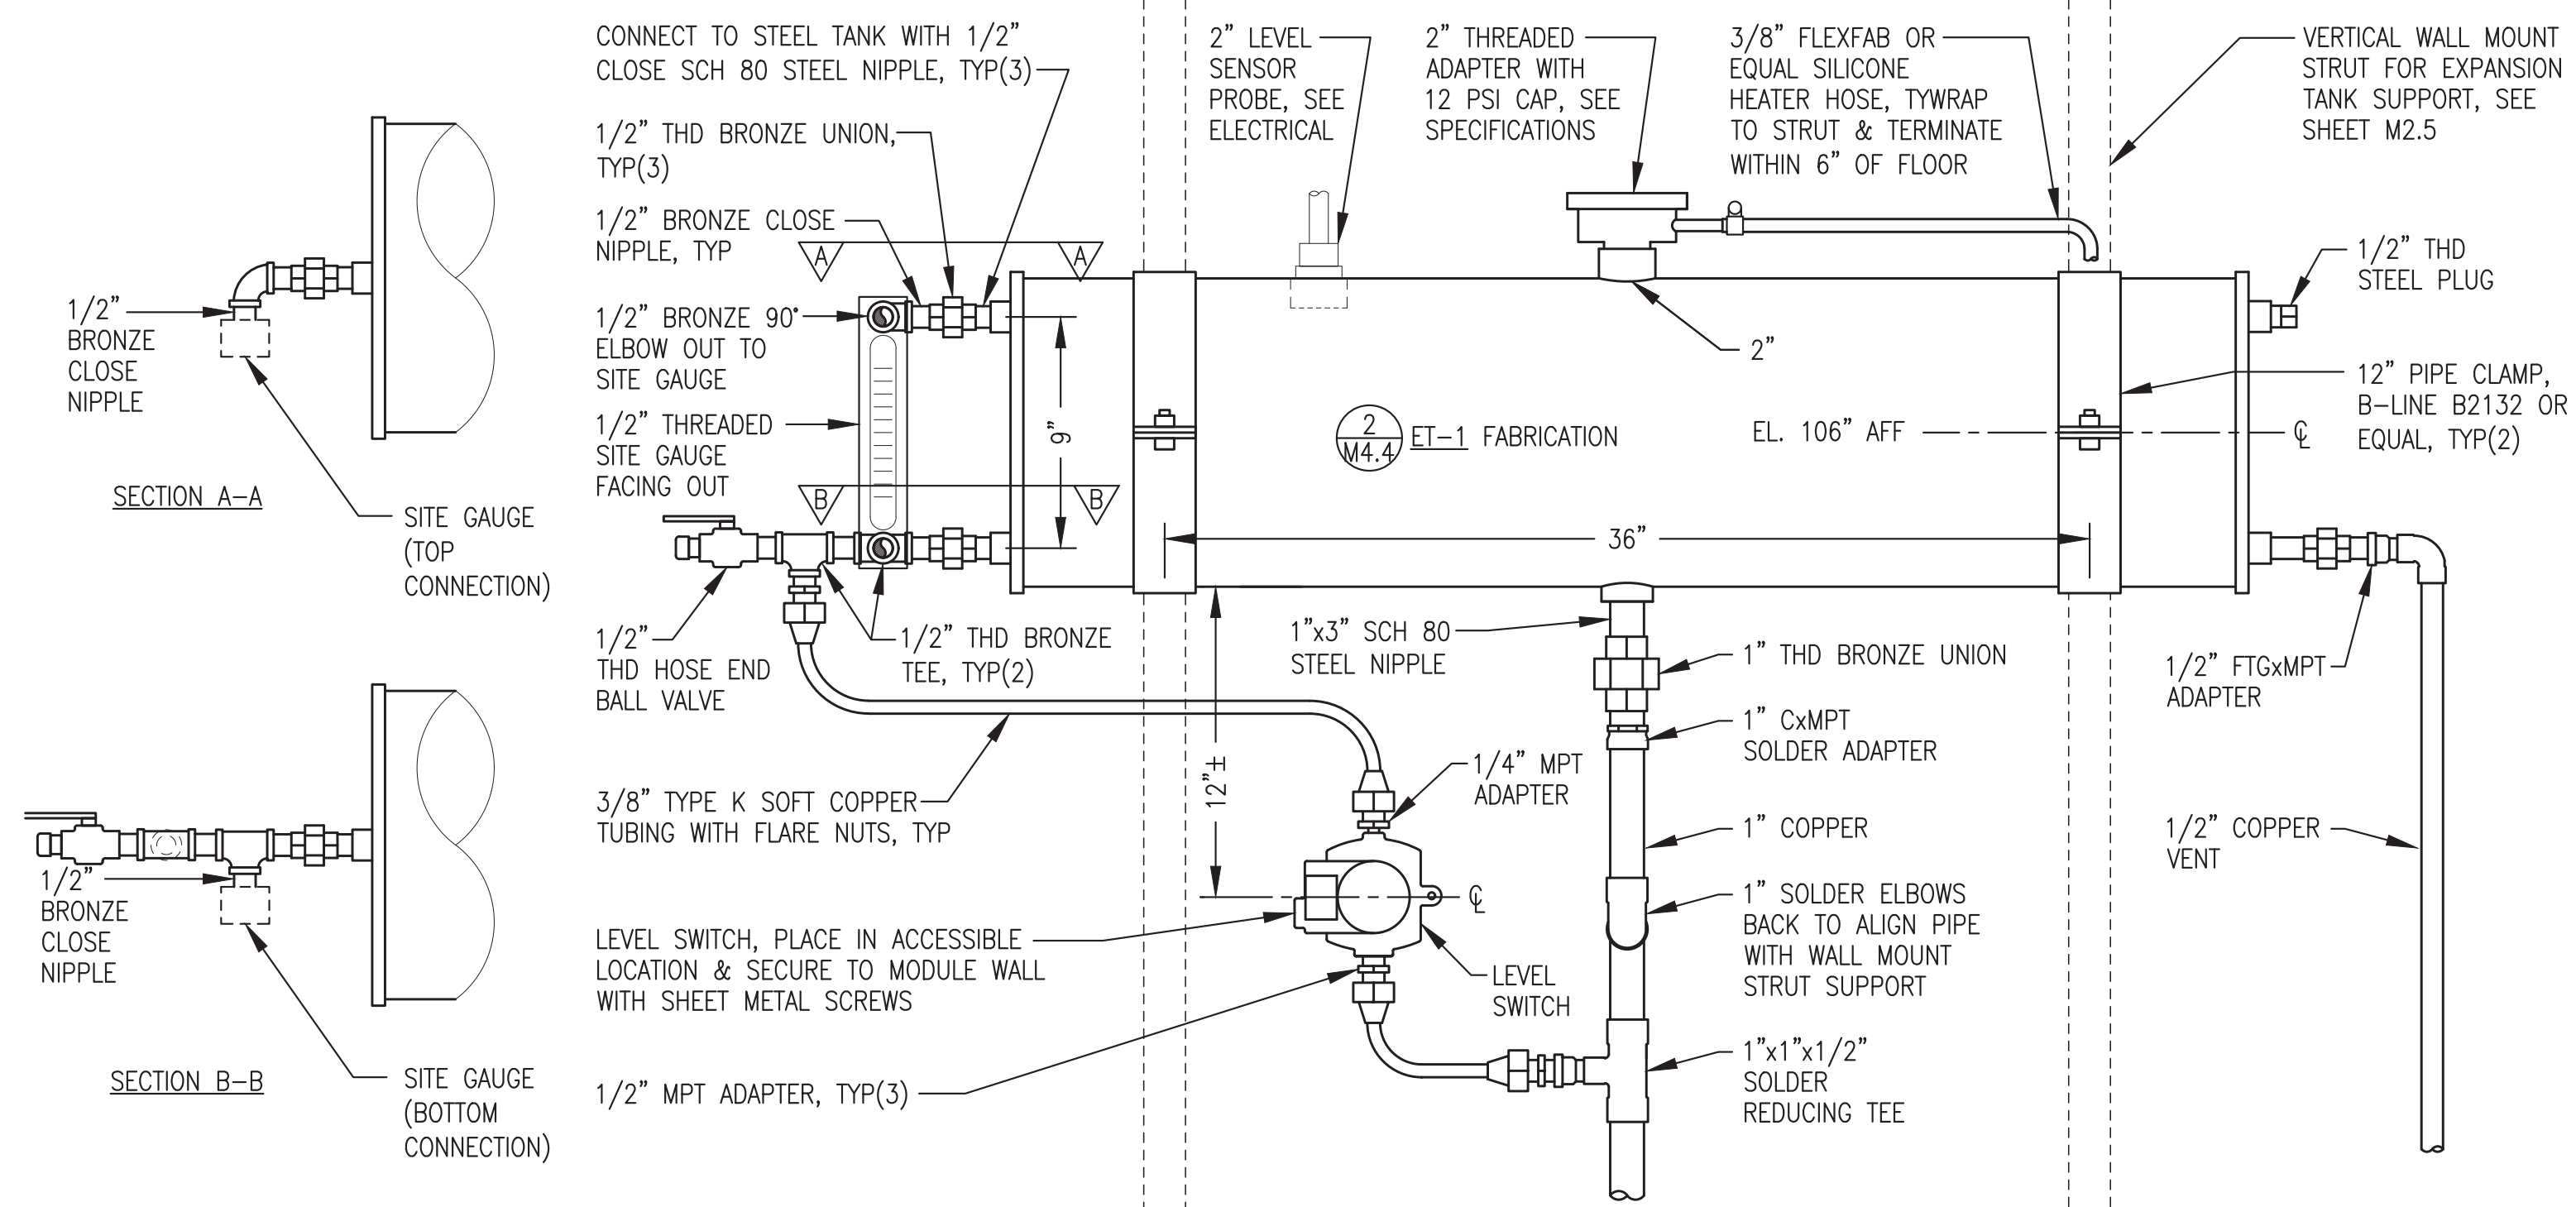


**1** 24 GAL EXPANSION TANK ET-1 INSTALLATION  
M4.3 NO SCALE

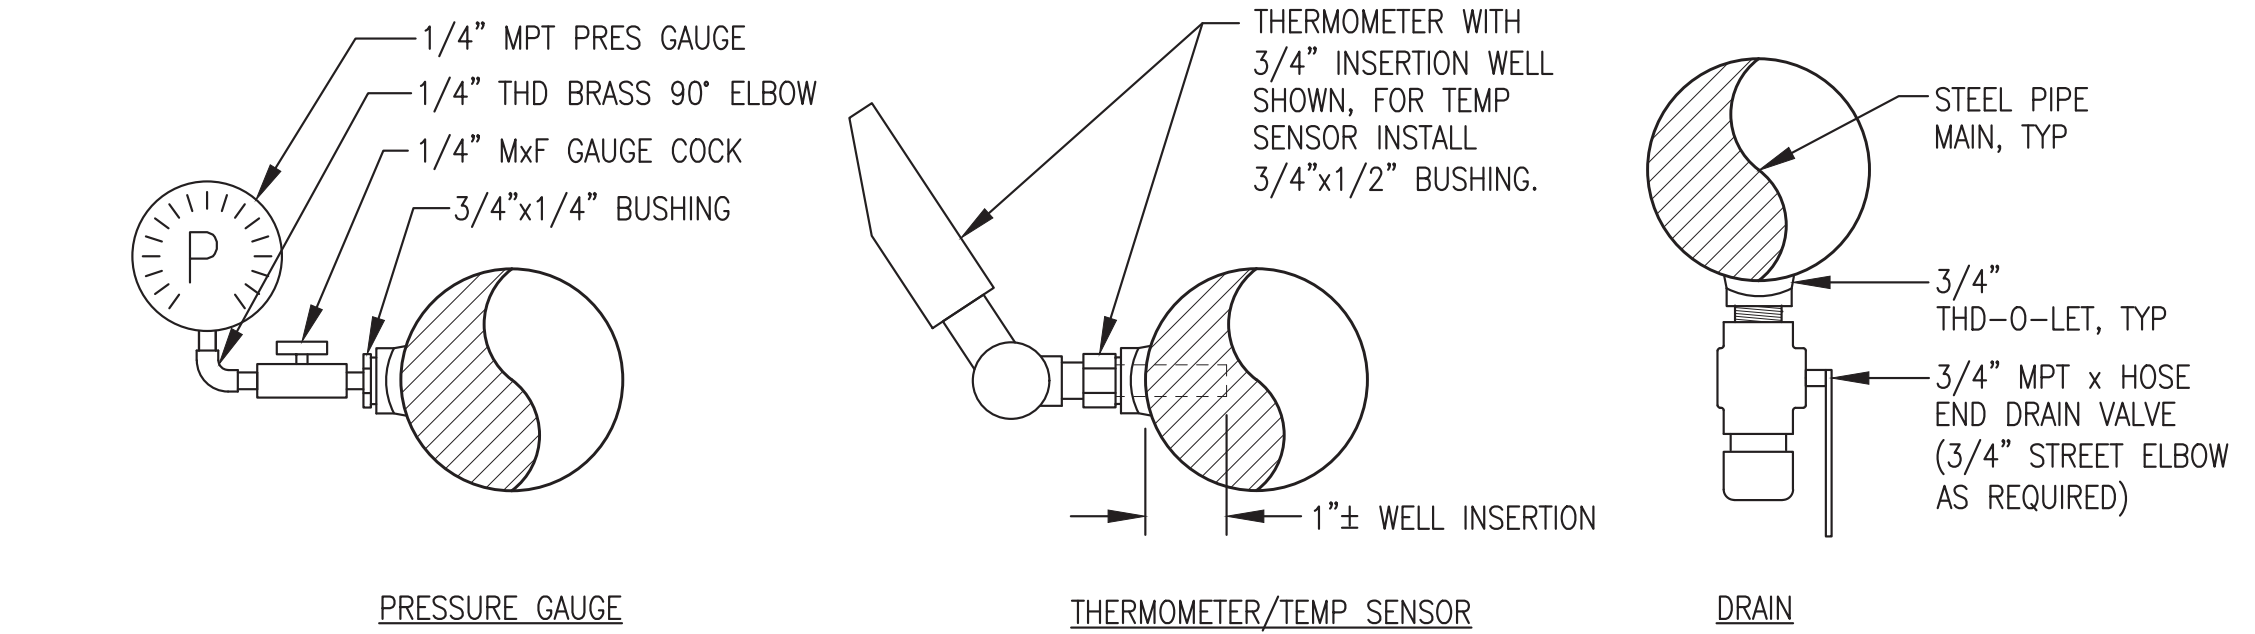

**2** TYP INSTRUMENT/DRAIN INSTALLATION IN STEEL PIPE  
M4.3 NO SCALE

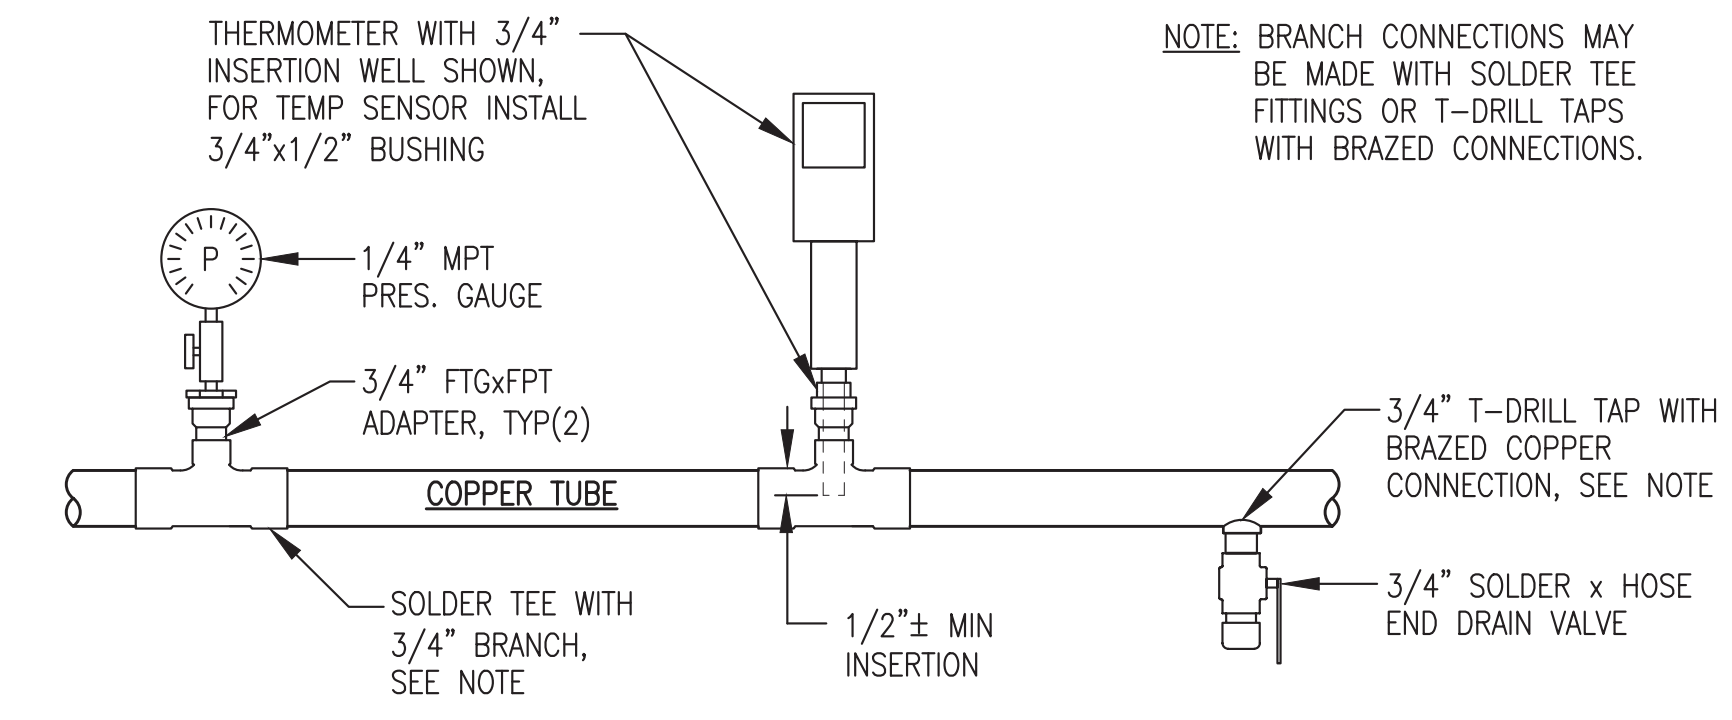

**3** TYP INSTRUMENT/DRAIN INSTALLATION IN COPPER TUBE  
M4.3 NO SCALE

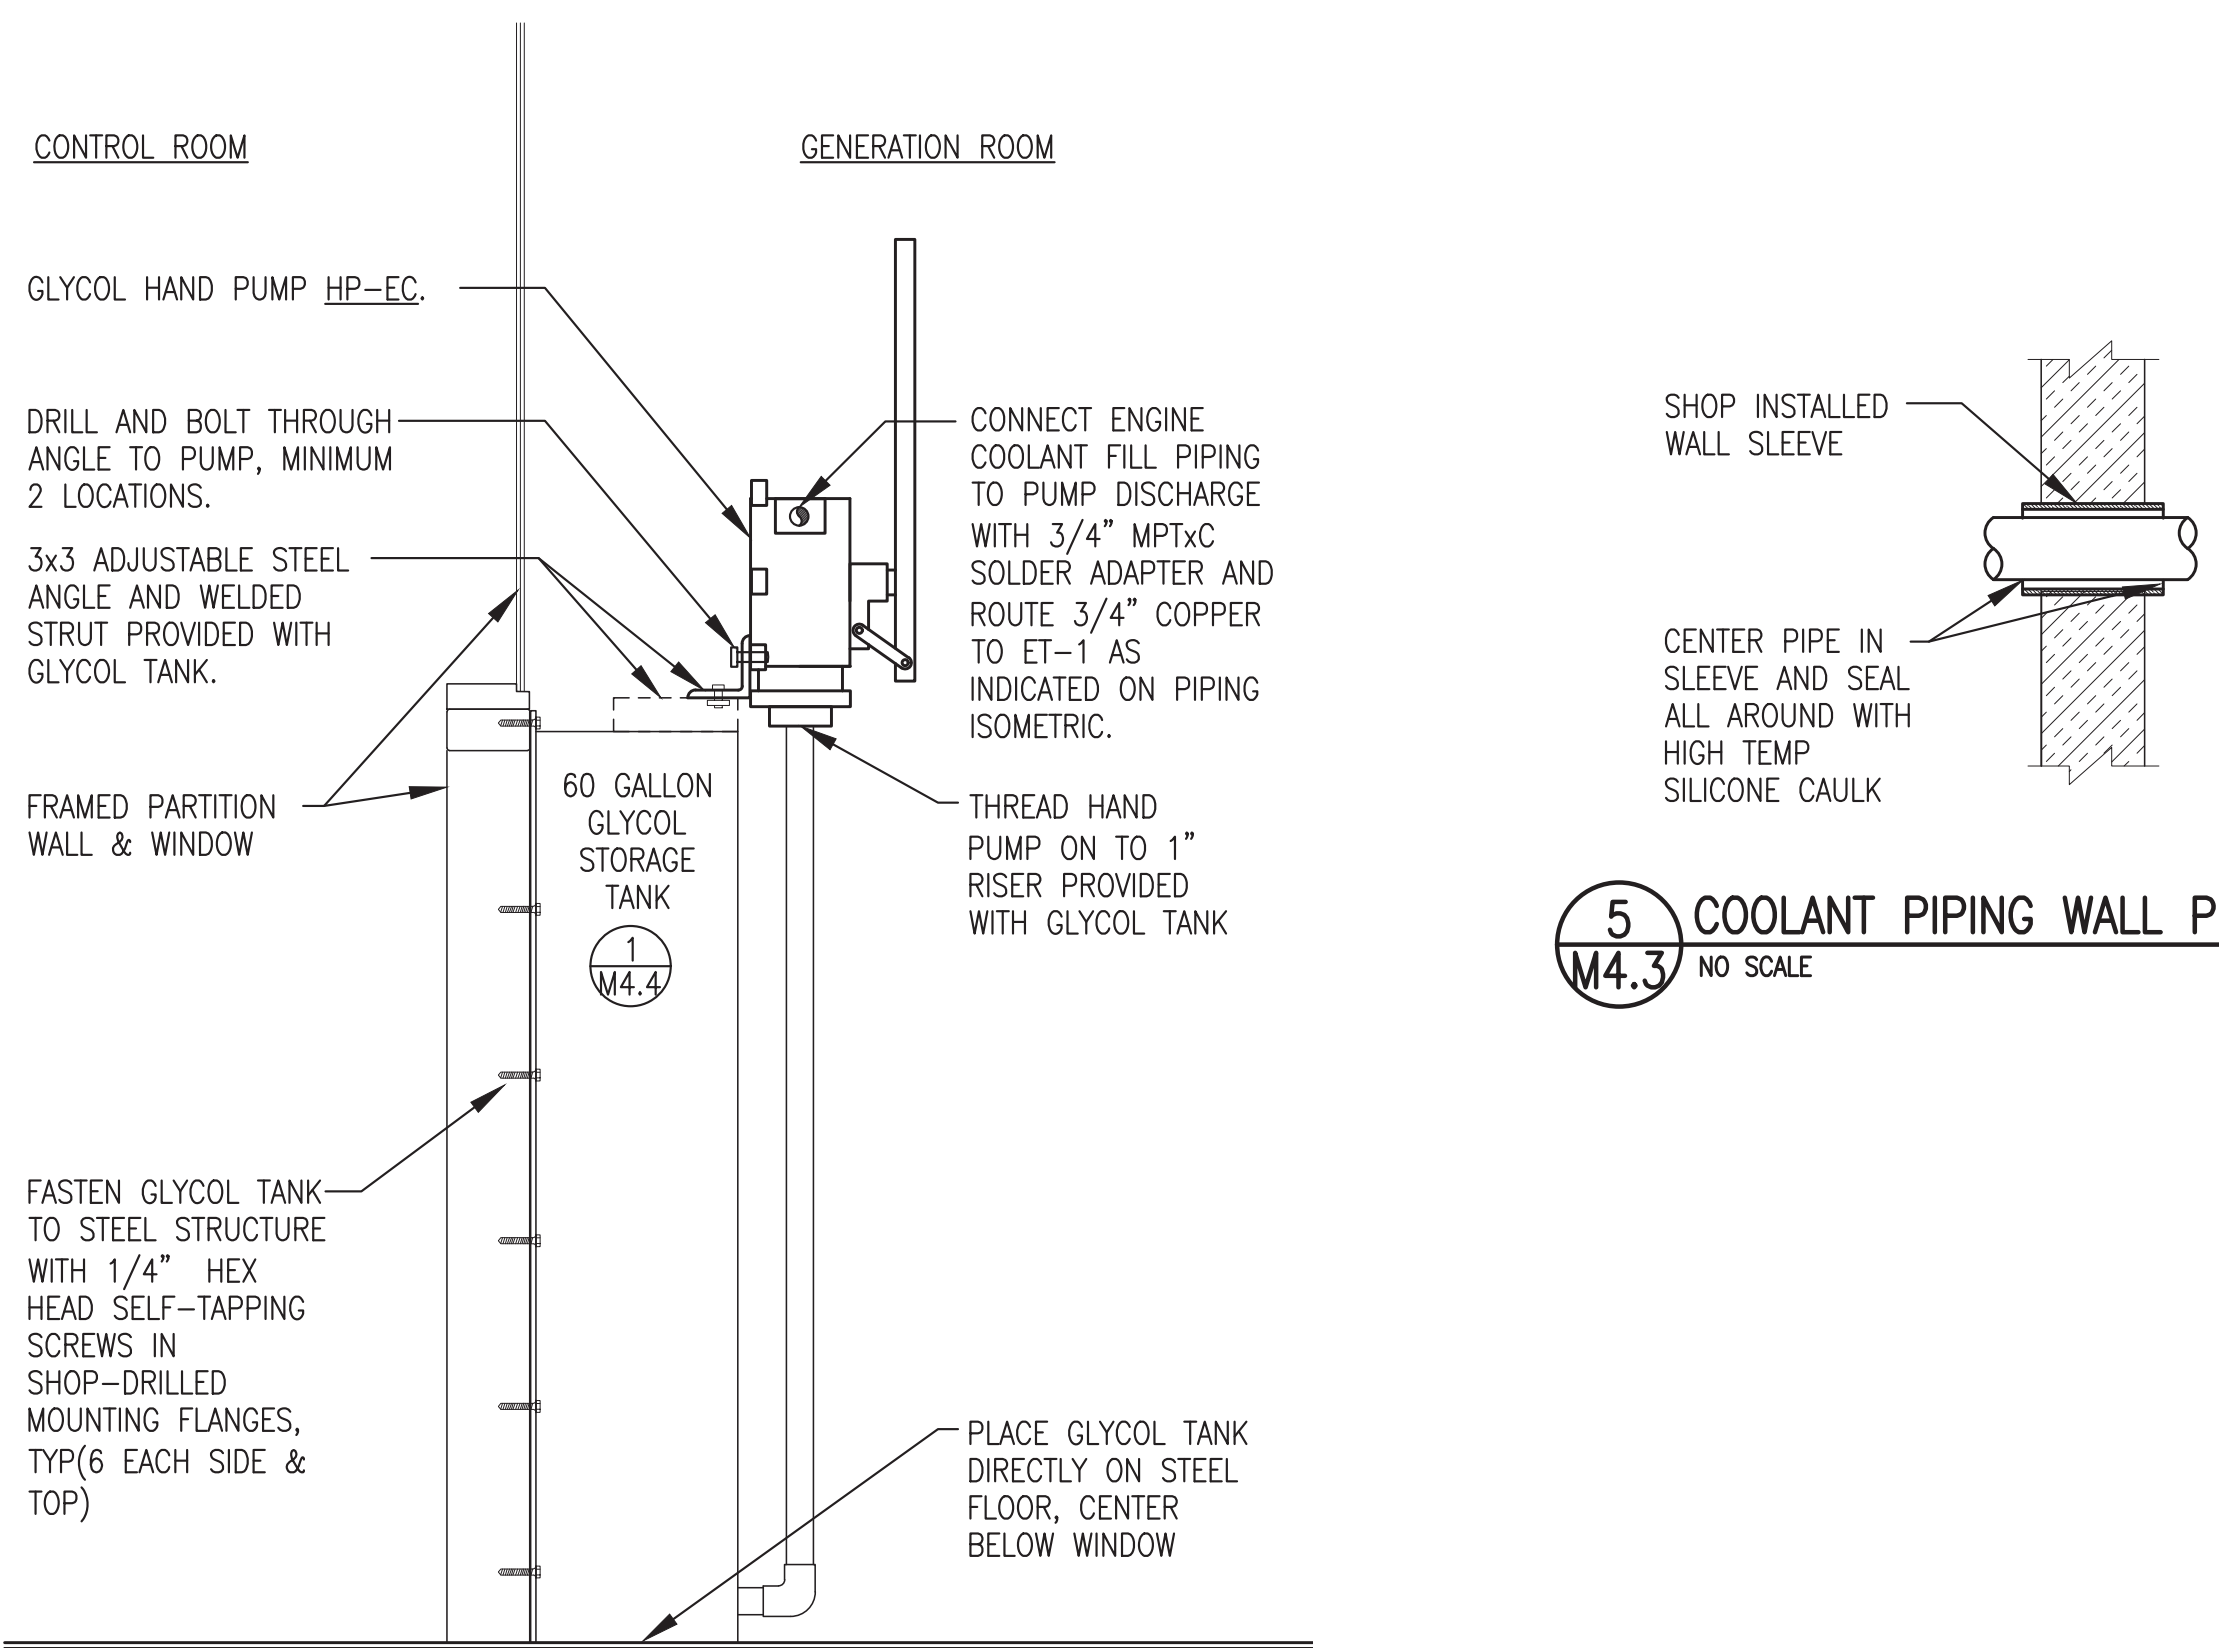


**4** GLYCOL STORAGE TANK & HAND PUMP HP-EC INSTALLATION DETAIL  
M4.3 NO SCALE

**SHOP/ON-SITE NOTES:**


- 1) SEAL OPENINGS AS PART OF ON-SITE WORK.

**GENERAL NOTES:**

- 1) THIS DETAIL FOR COOLANT PIPING WITH SHOP INSTALLED WALL SLEEVES.
- 2) FOR ALL PIPE/CONDUIT LESS THAN 2" O.D. AND WITHOUT A SHOP INSTALLED WALL SLEEVE, HOLE SAW OPENING APPROXIMATELY 1/4" LARGER THAN PIPE O.D. THROUGH WALL & SEAL ALL AROUND WITH POLYURETHANE CAULKING.

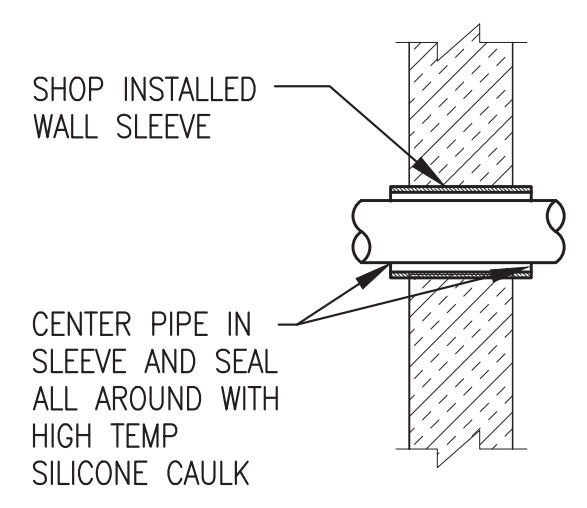

**5** COOLANT PIPING WALL PENETRATION  
M4.3 NO SCALE

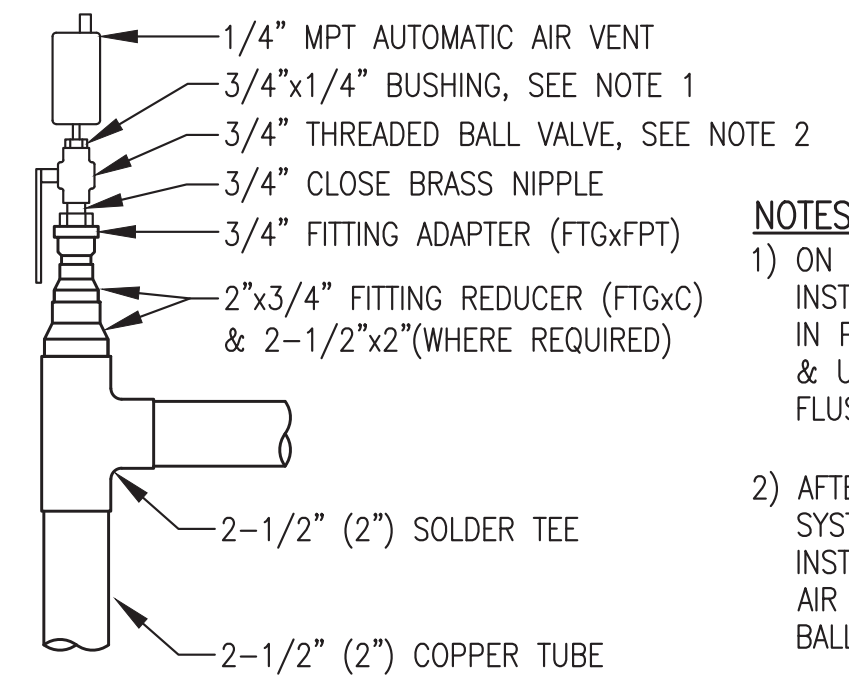


**NOTES:**

- 1) ON INITIAL STARTUP INSTALL HOSE ADAPTER IN PLACE OF BUSHING & USE HOSE TO FLUSH & BLEED.
- 2) AFTER BLEEDING SYSTEM OF AIR INSTALL BUSHING & AIR VENT & CLOSE BALL VALVE.

**6** TYPICAL AIR VENT INSTALLATION IN COPPER  
M4.3 NO SCALE

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: ENGINE COOLANT & HEAT RECOVERY PIPING DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET: M4.3	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			



**GLYCOL TANK GENERAL NOTES:**



- FABRICATE SINGLE WALL 60 GALLON NOMINAL CAPACITY GLYCOL TANK.
- FABRICATE FROM ASTM A-36 STEEL PLATE, 10 GAUGE MINIMUM EXCEPT FOR TOP 3/16" MINIMUM. ALL TANK SEAM JOINTS TO BE FULL CONTINUOUS WELDS.
- PROVIDE WITH ALL OPENINGS AND ATTACHMENTS INDICATED. SEAL WELD ALL TANK ATTACHMENTS.
- ALL FPT OPENINGS TO BE FORGED STEEL HALF COUPLINGS.
- PRESSURE TEST COMPLETED ASSEMBLY TO 5 PSIG MAXIMUM USING SOAPY WATER SOLUTION ON ALL WELD JOINTS.
- UPON COMPLETION OF FABRICATION, ROUND ALL CORNERS AND SHARP EDGES. SANDBLAST TANK EXTERIOR AND ALL ATTACHMENTS IN ACCORDANCE WITH SSPC-SP-6. PRIME AND COVER WITH TWO COATS OF EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, COLOR ANSI 61 GRAY.
- UPON COMPLETION FLUSH INTERIOR OF TANK TO REMOVE ALL DIRT AND DEBRIS AND AIR DRY INTERIOR. INSTALL 2" SCREENED VENT ON 2" FPT FILL CONNECTION WITH 2" CLOSE NIPPLE FOR SHIPPING. SEAL ALL OTHER OPENINGS WITH PLASTIC OR STEEL PLUGS..

**GLYCOL TANK SPECIFIC NOTES:**

- 1-1/2" FPT (TANK GAUGE)
- 2" FPT (VENT) - INSTALL 2" THREADED VENT CAP
- 1" SCHEDULE 80 PIPE WITH THREADED TOP CONNECTION (WITHDRAWAL)
- 1" SOCKETWELD 90° ELBOW
- 6" LONG STRUT, END FLUSH WITH FRONT OF TANK
- 2x1/4" FLAT BAR CONTINUOUS THREE SIDES
- 3/8" HOLE AT 8" O.C. ALL AROUND
- L3x3x1/4"x6" LONG FOR FUTURE CONNECTION TO HAND PUMP BY OTHERS. PAINT TO MATCH TANK AND FASTEN TO STRUTS WITH 1/2" BOLTS & STRUT NUTS.

**EXPANSION TANK GENERAL NOTES:**


- FABRICATE SINGLE WALL 24 GALLON NOMINAL CAPACITY GLYCOL EXPANSION TANK.
- FABRICATE SHELL FROM MINIMUM 10 GAUGE ASTM A-36 PLATE STEEL ROLLED AND WELDED OR SCHEDULE 5 LIGHTWALL ASTM A53 STEEL PIPE. FABRICATE HEADS FROM 3/16" THICK ASTM A-36 PLATE STEEL. MAKE ALL JOINTS WITH CONTINUOUS FULL-PENETRATION WELDS.
- PROVIDE WITH ALL OPENINGS INDICATED USING MINIMUM 3000# FORGED STEEL PIPE HALF COUPLINGS IN ACCORDANCE WITH U.L 142 FIGURE 7.1 #2.
- PRESSURE TEST COMPLETED ASSEMBLY TO 15 PSIG MINIMUM.
- UPON COMPLETION OF FABRICATION, ROUND ALL CORNERS AND SHARP EDGES. SANDBLAST TANK EXTERIOR AND ALL ATTACHMENTS IN ACCORDANCE WITH SSPC-SP-6. PAINT WITH TWO COATS EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, COLOR ANSI 61 GRAY.
- UPON COMPLETION FLUSH INTERIOR OF TANK TO REMOVE ALL DIRT AND DEBRIS, AIR DRY INTERIOR, AND SEAL ALL TANK OPENINGS WITH PLASTIC PLUGS.

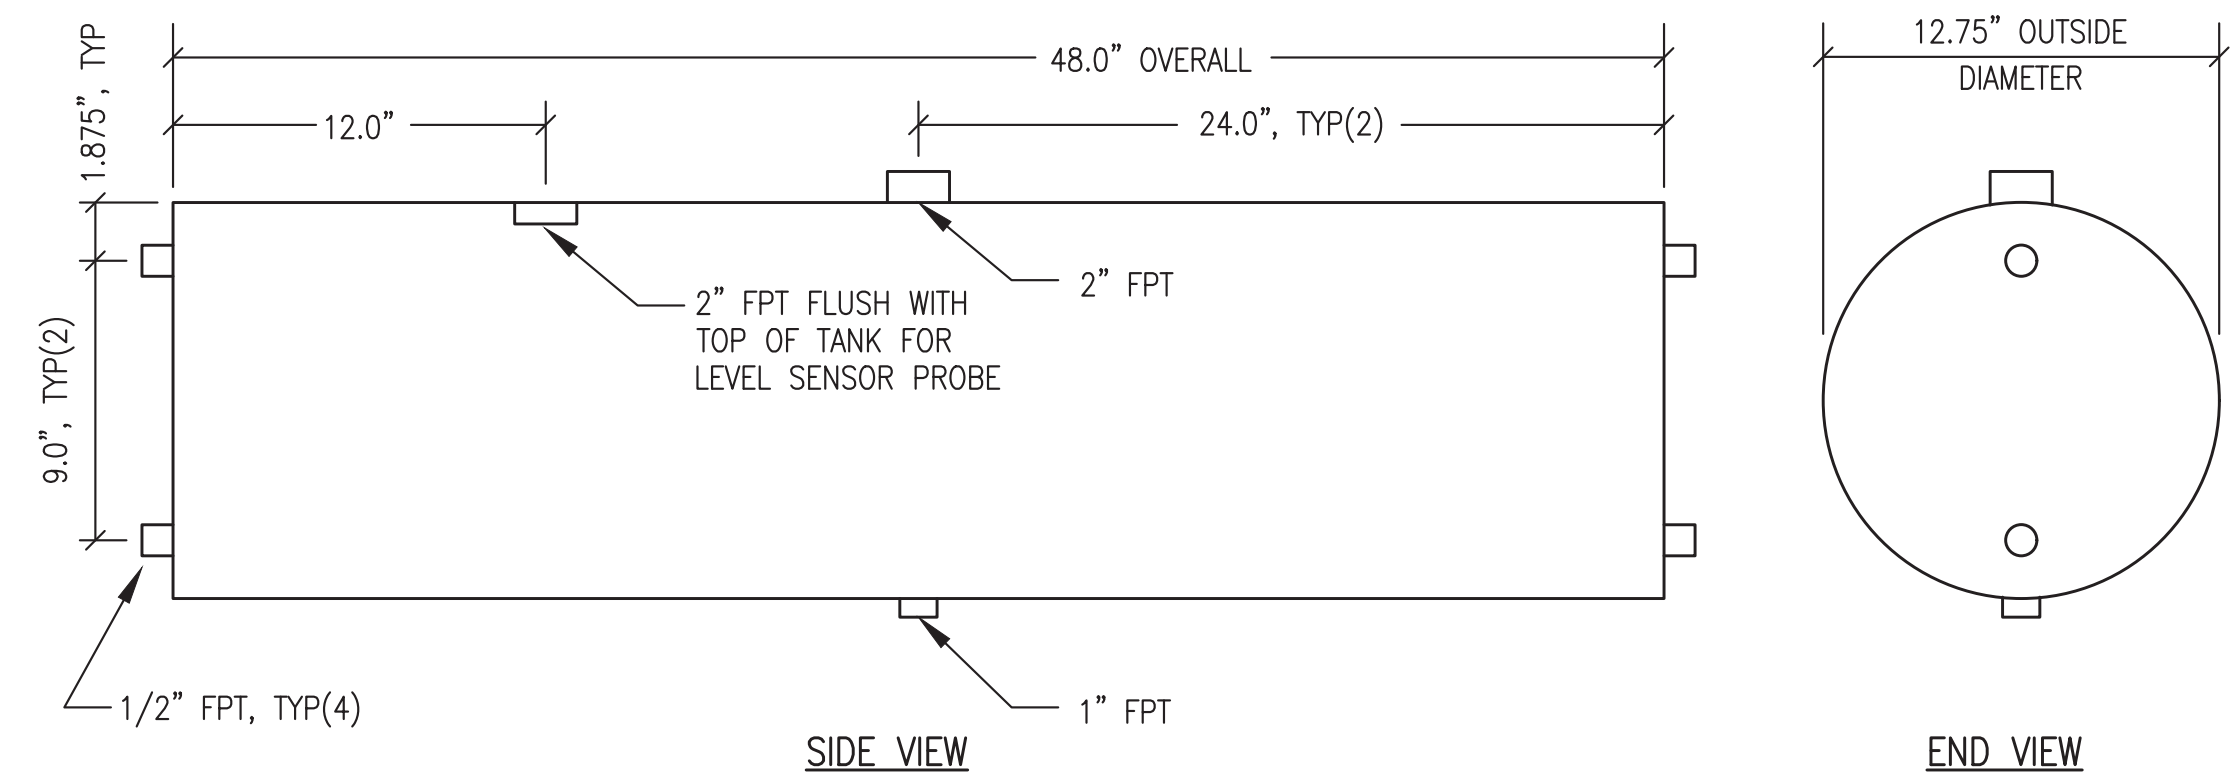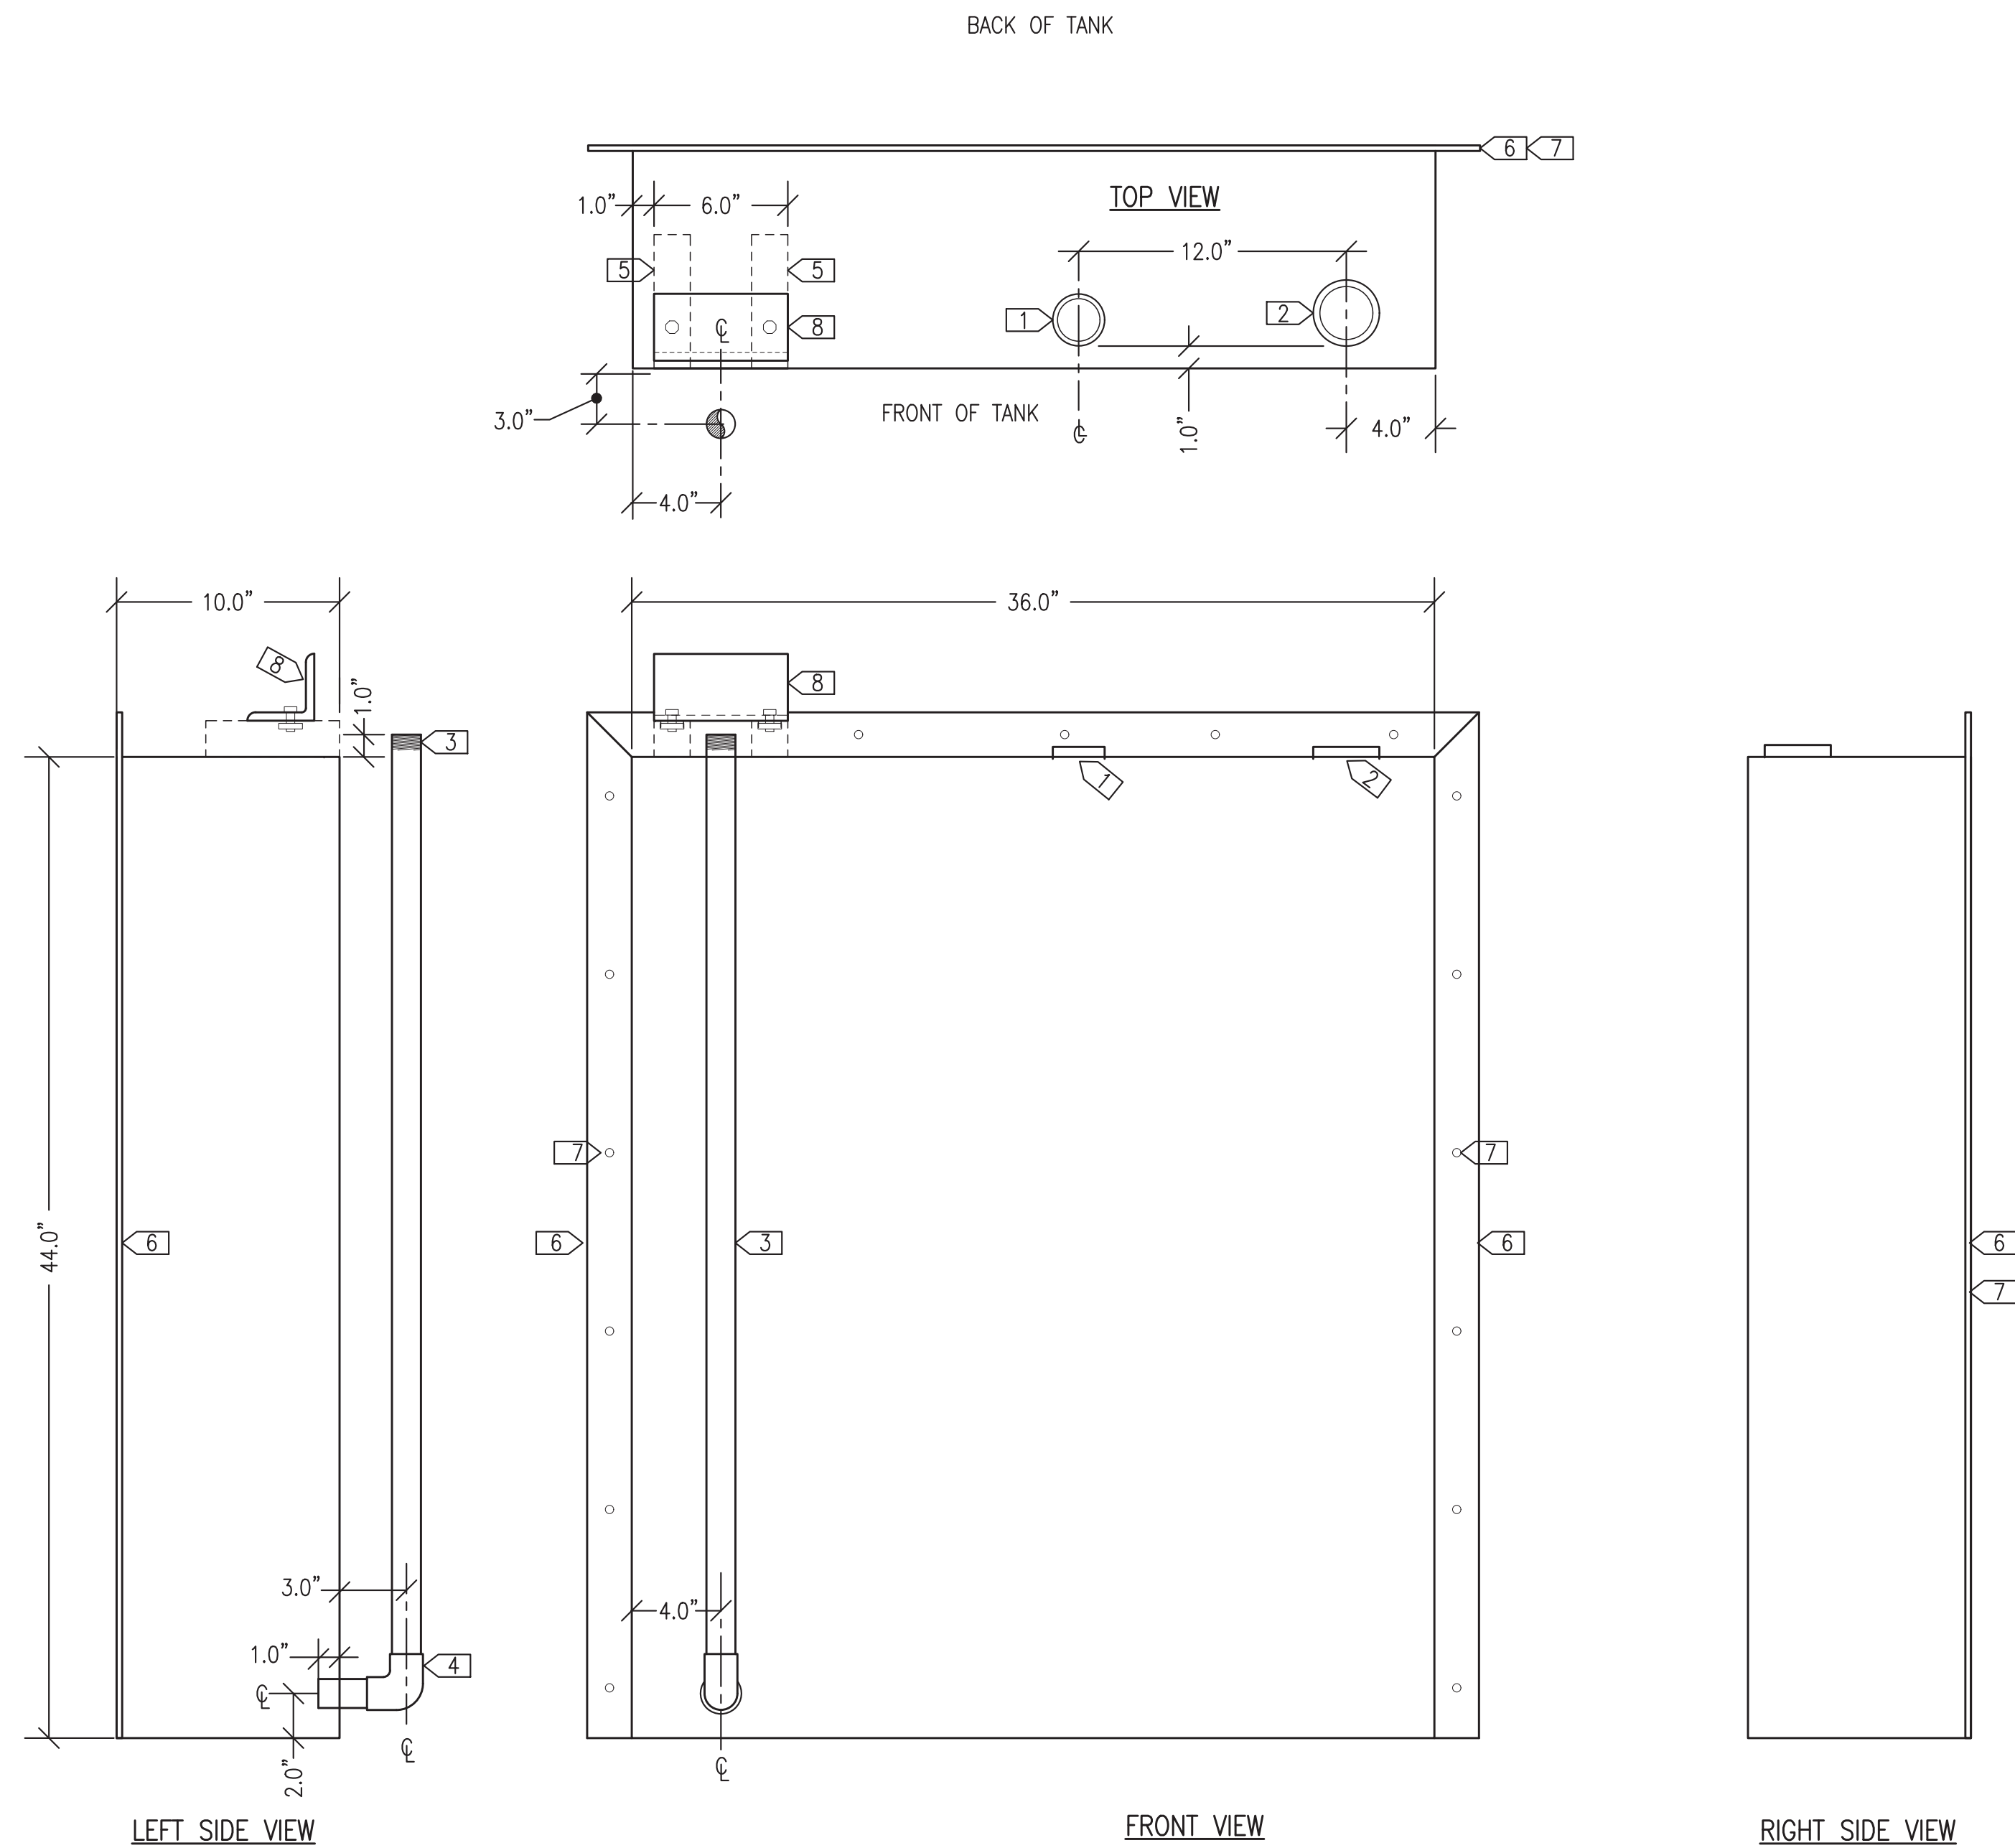


**2 24 GALLON GLYCOL EXPANSION TANK**  
M4.4 1"=6"

**1 60 GALLON GLYCOL STORAGE TANK**  
M4.4 1"=6"


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		GLYCOL STORAGE & EXPANSION TANKS FABRICATION	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		M4.4	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

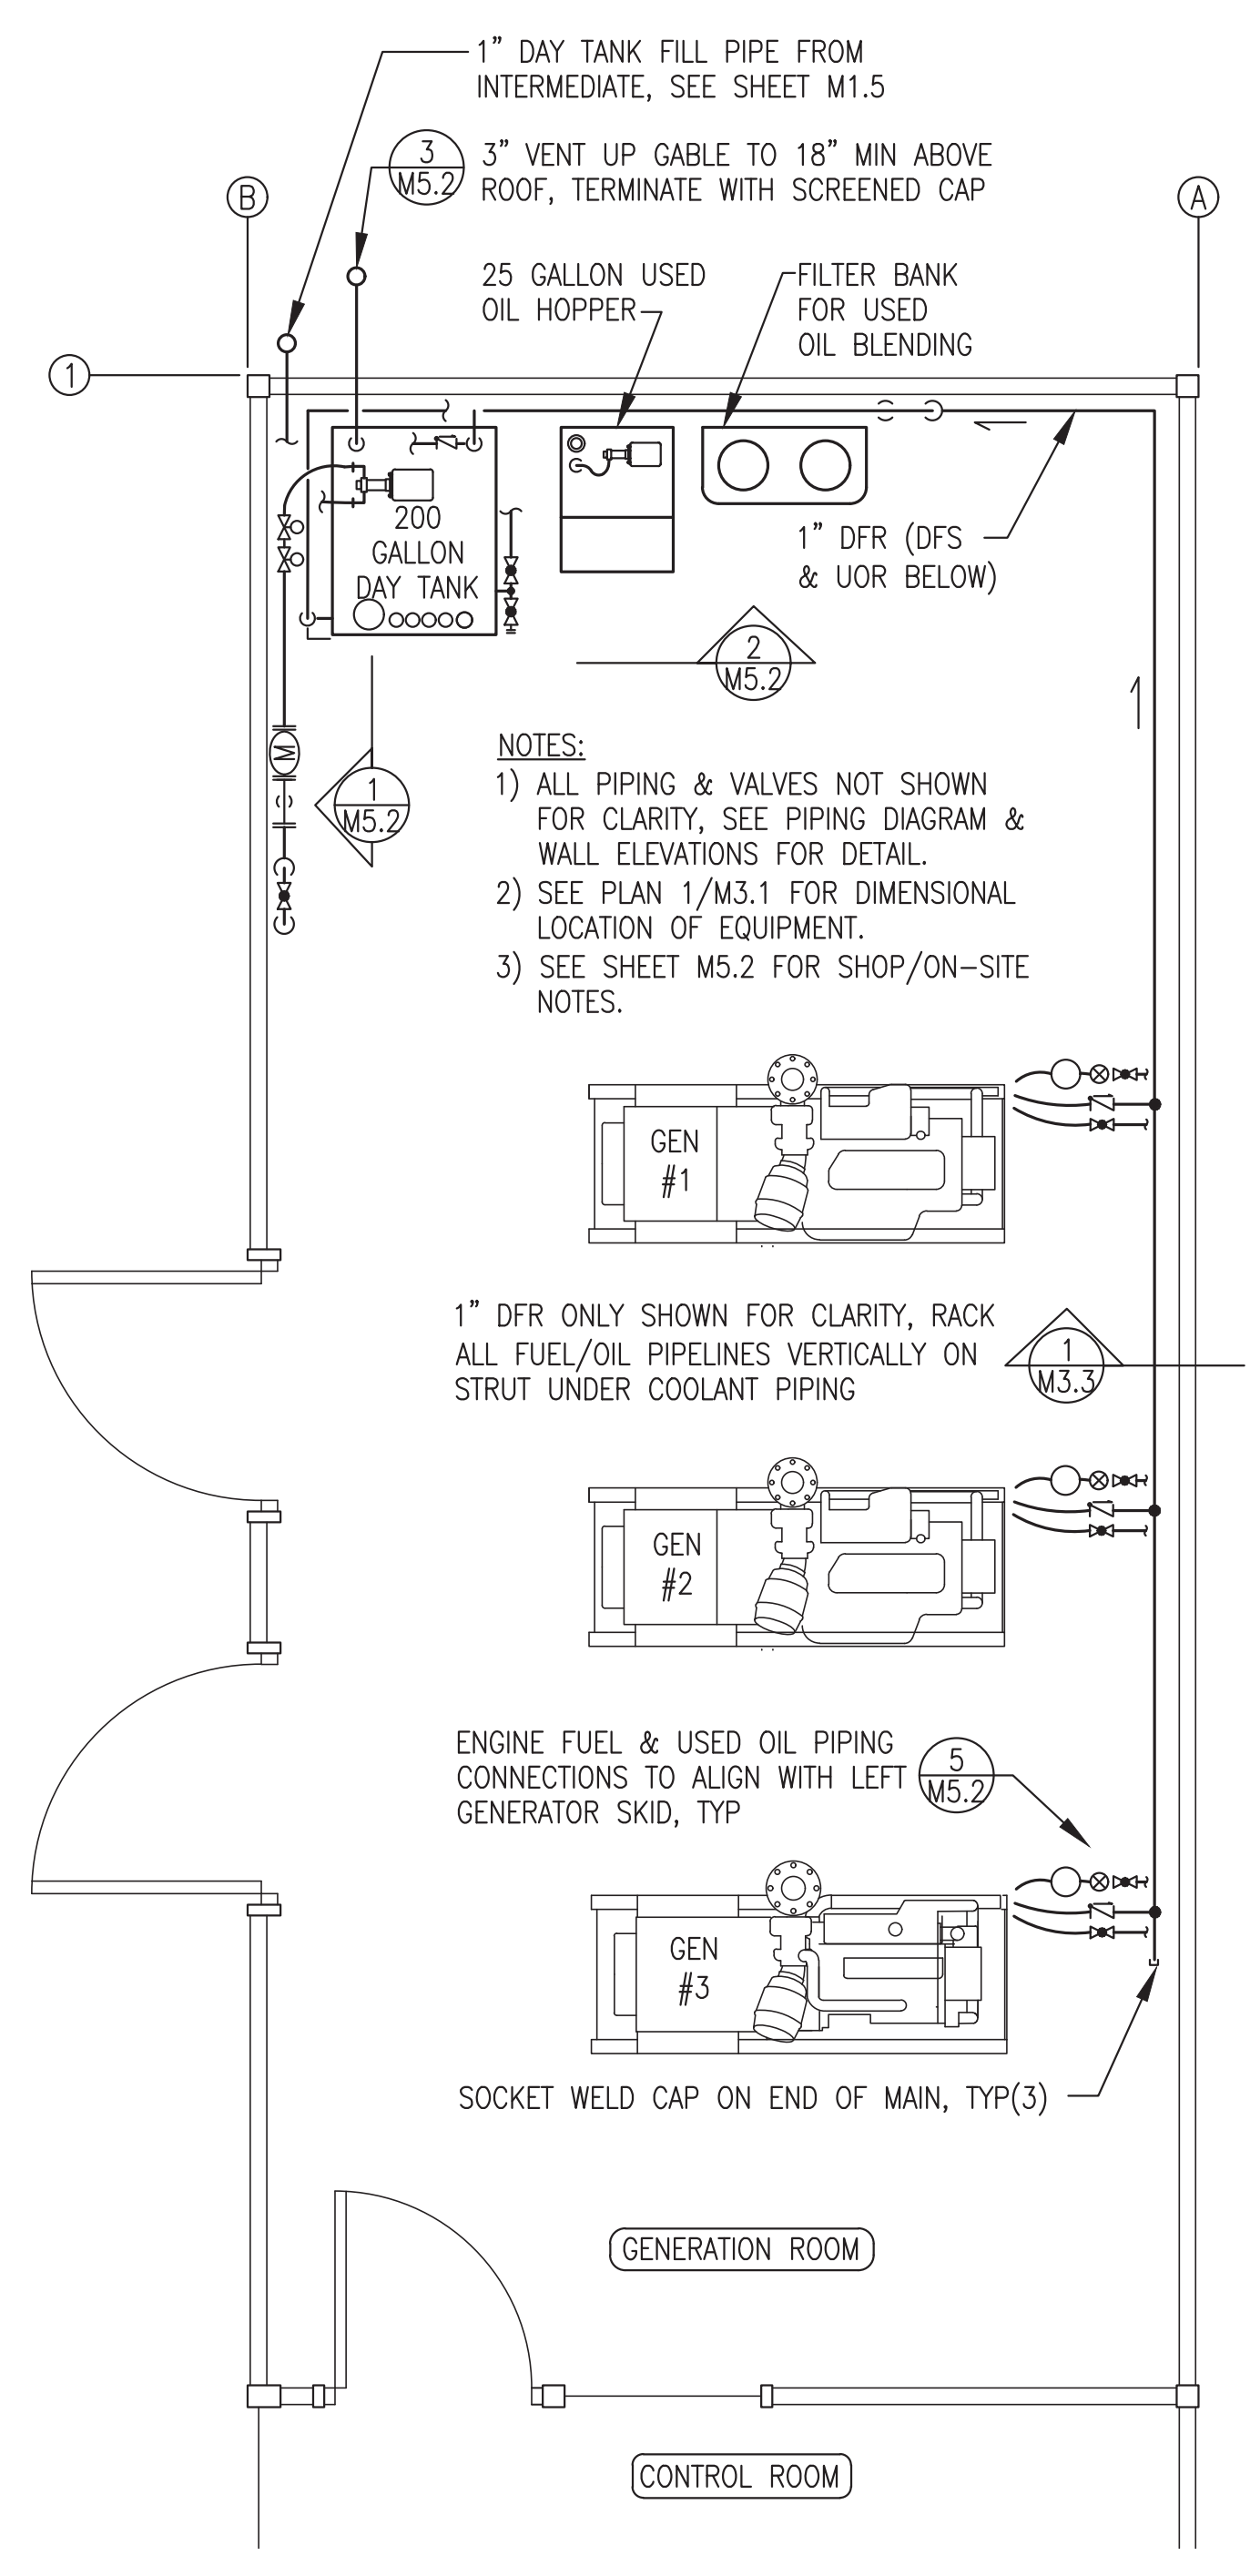


**1**  
**M5.1** DIESEL FUEL SYSTEM & USED OIL PIPING PLAN  
3/8"=1'

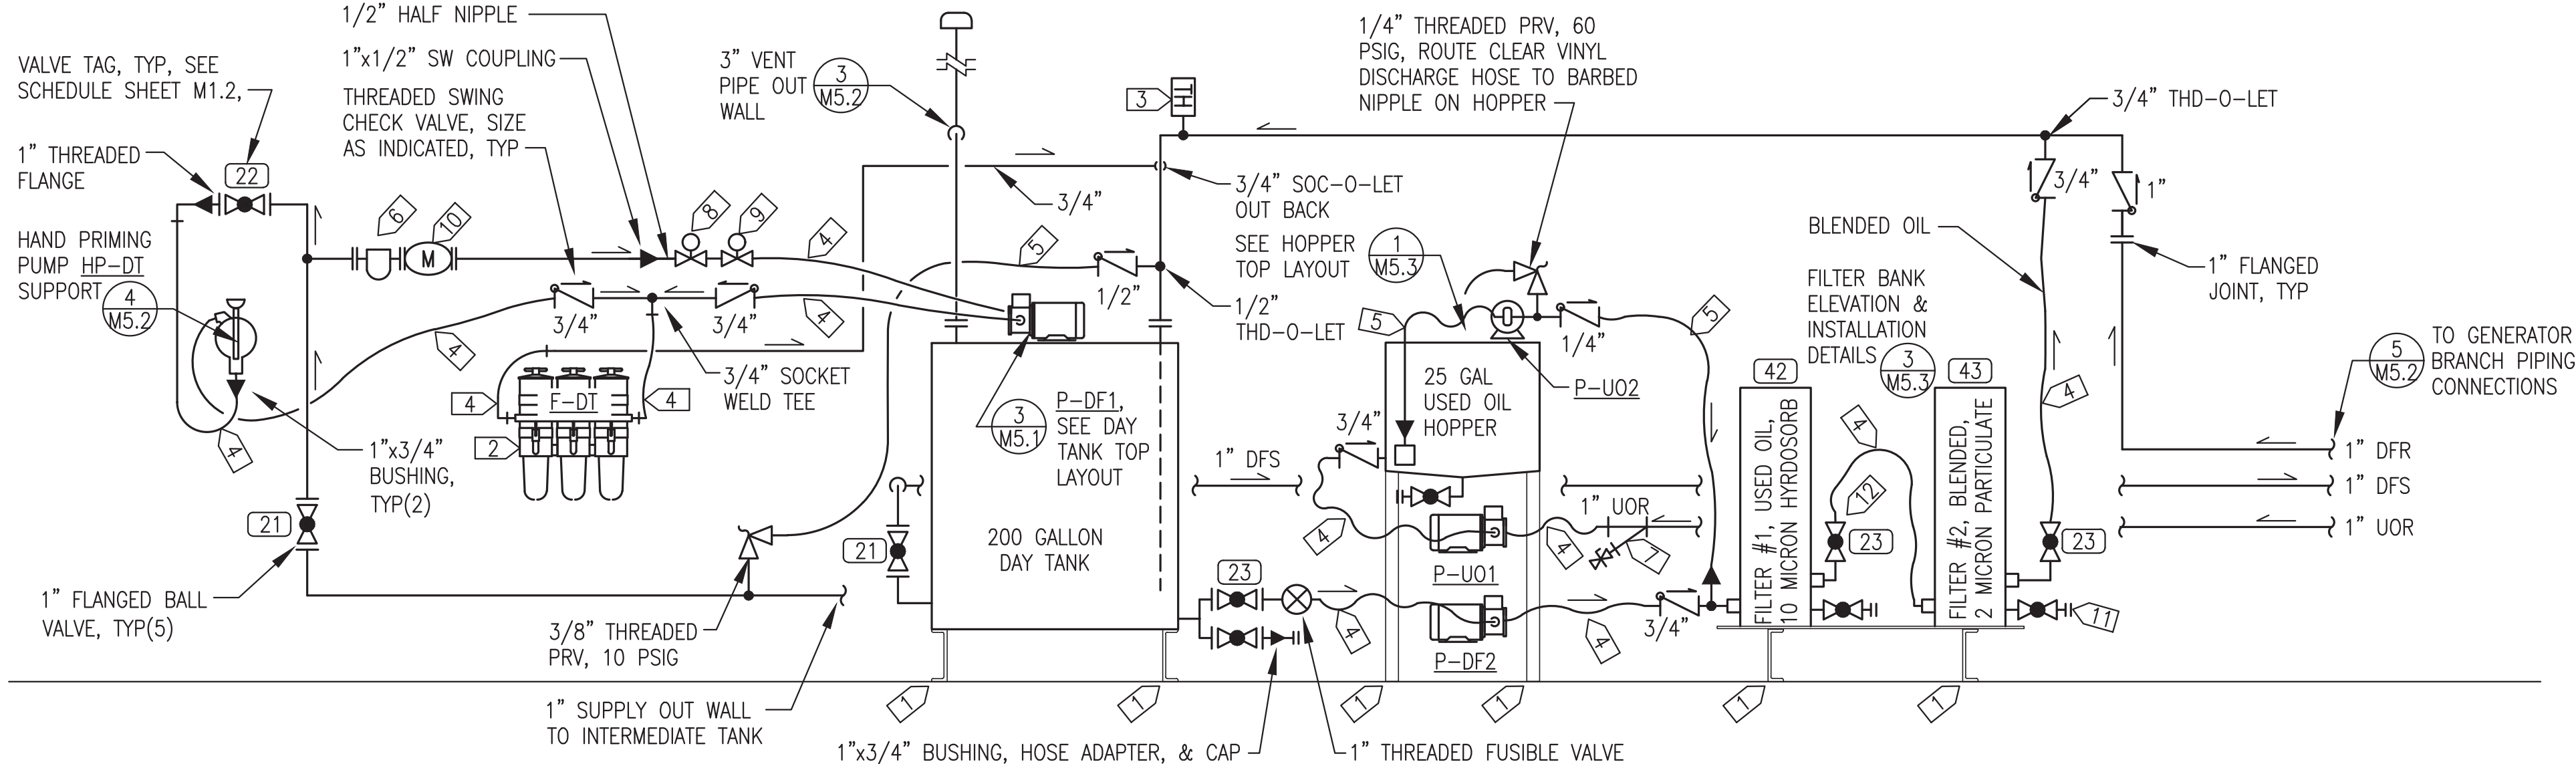


**2**  
**M5.1** DIESEL FUEL & USED OIL PIPING DIAGRAM  
NO SCALE

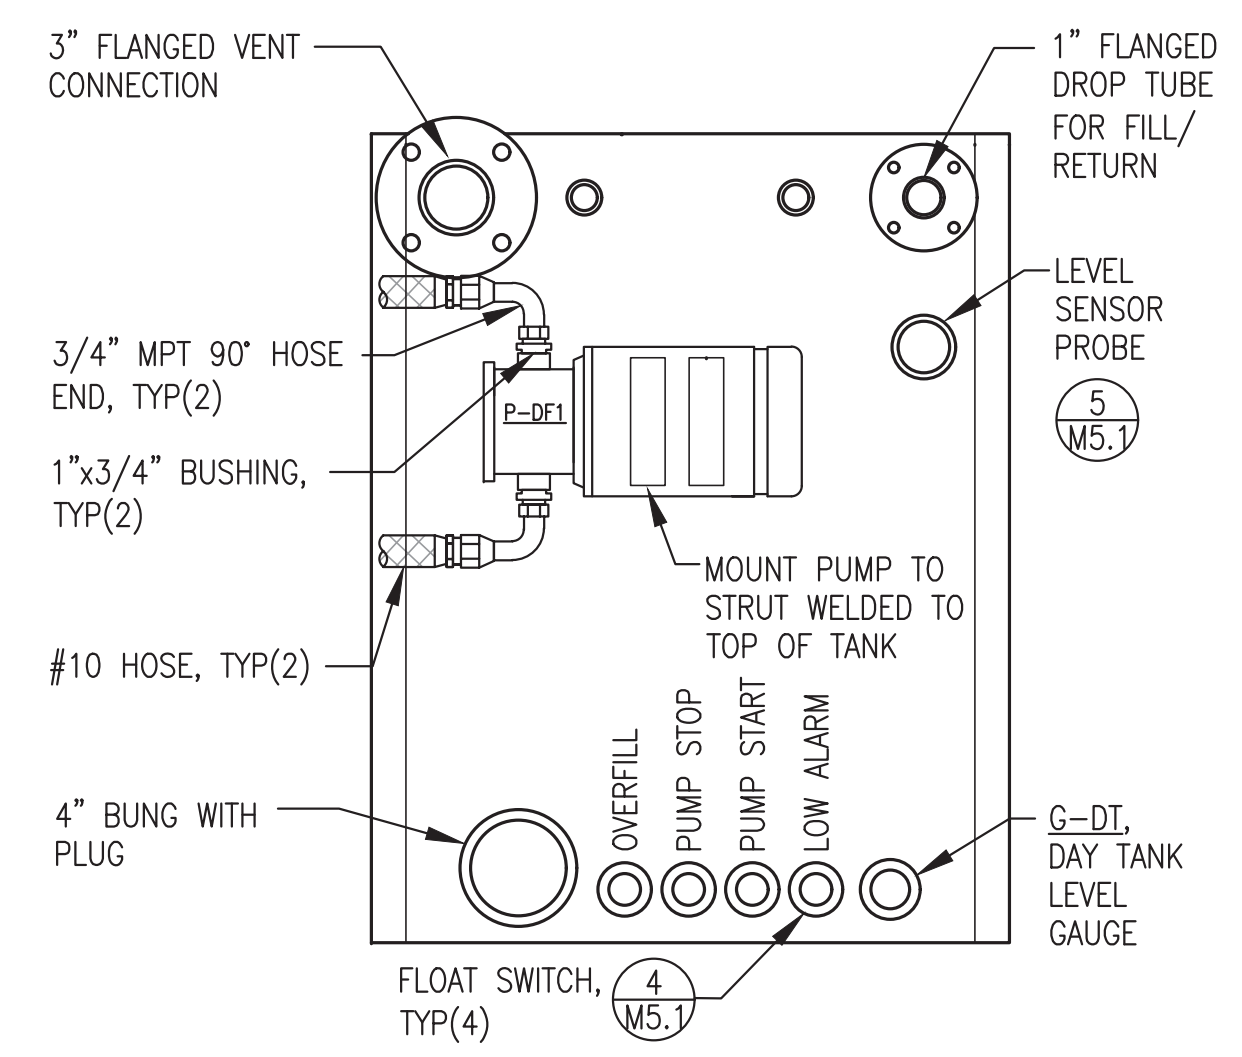

**3**  
**M5.1** TOP OF DAY TANK - PLAN VIEW  
NO SCALE

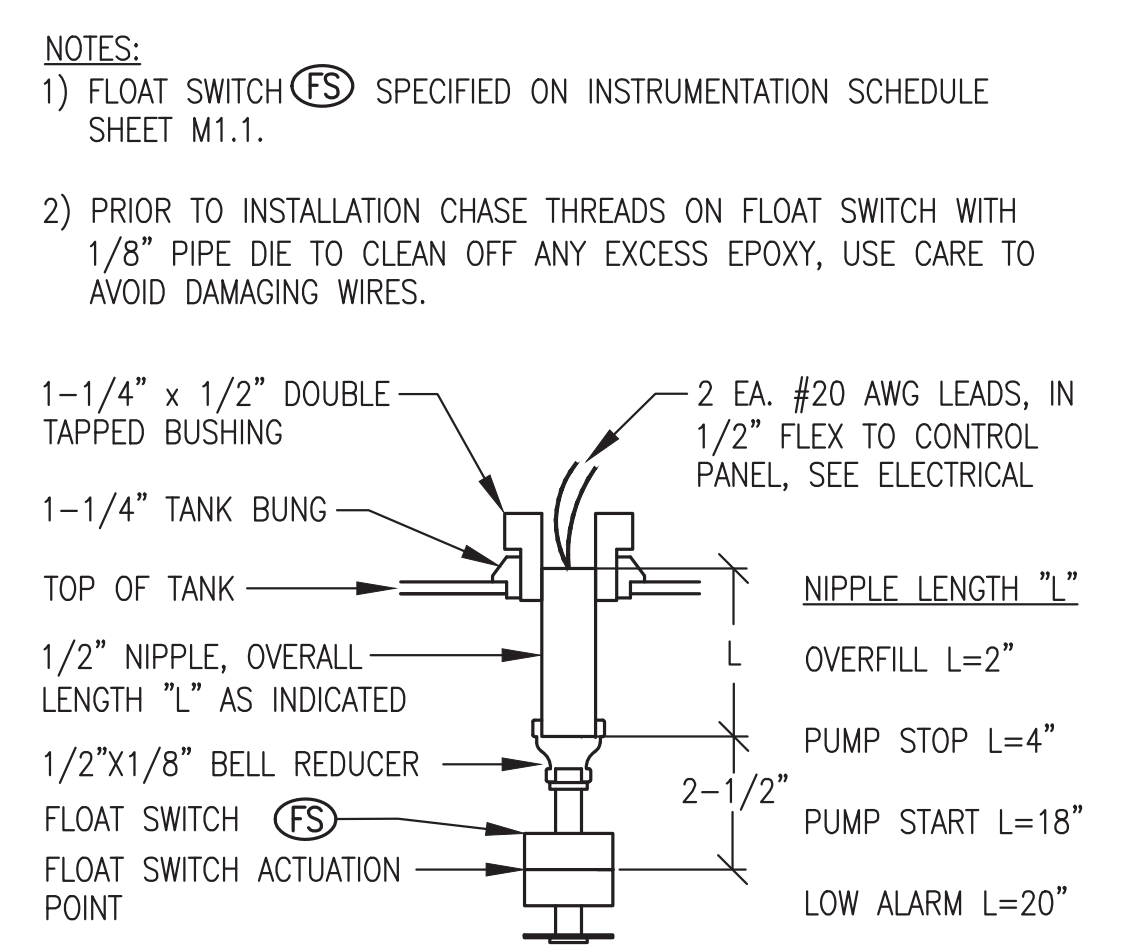


**4**  
**M5.1** DAY TANK FLOAT SWITCH INSTALLATION  
NO SCALE

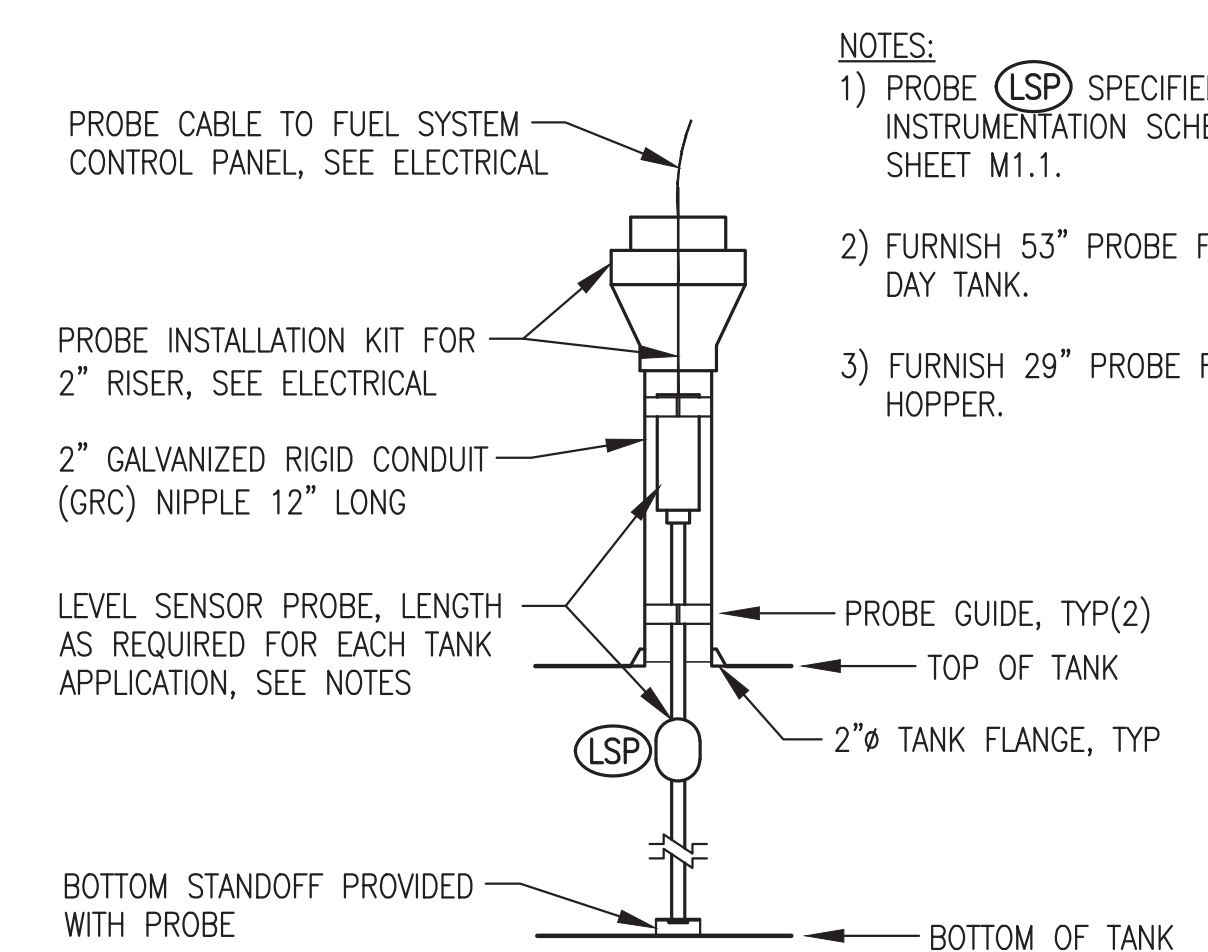

**5**  
**M5.1** TYPICAL LEVEL SENSOR PROBE INSTALLATION  
NO SCALE

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




REV.	DESCRIPTION	DATE	BY
1	UPDATED TO COORDINATE WITH NAPAKIAK MODULE	7/15/22	BCG

**ALASKA ENERGY AUTHORITY**

PROJECT: **RAMPART POWER SYSTEM UPGRADE**

TITLE: **DIESEL FUEL & USED OIL PIPING PLAN, DIAGRAM, & DETAILS**


DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP_M2-M7	SHEET: <b>M5.1</b>
PROJECT NUMBER:	

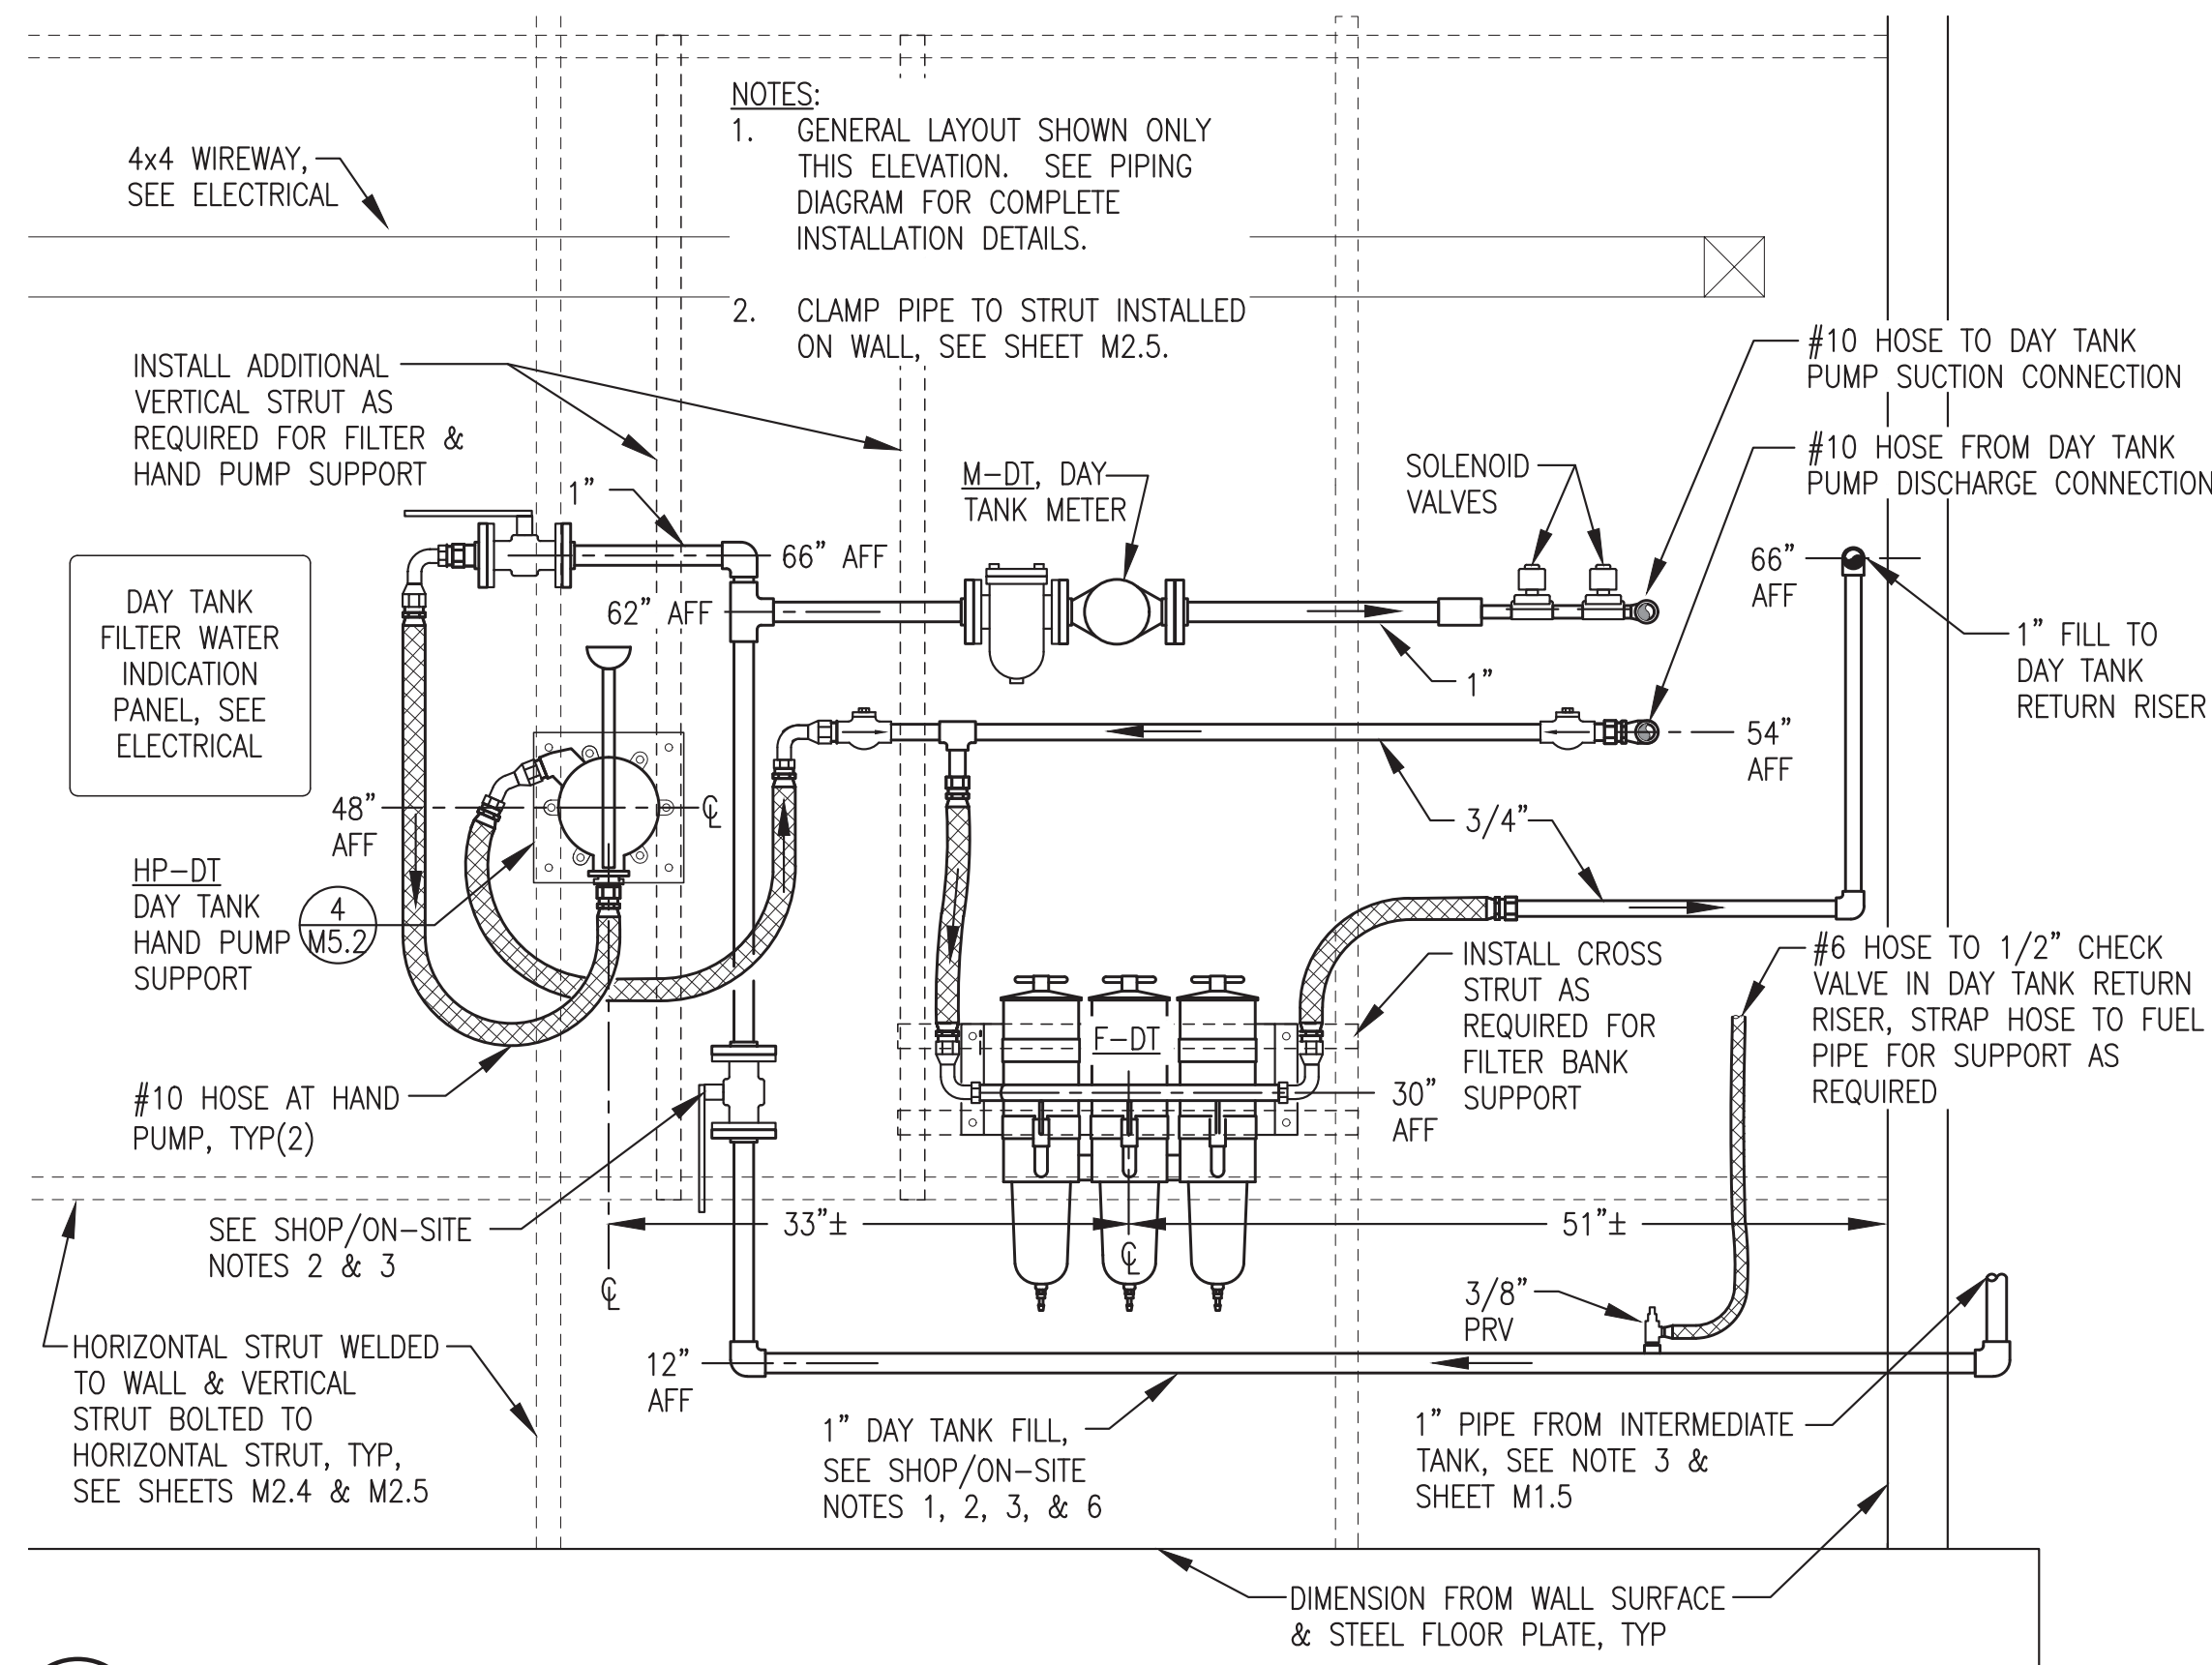


**1** DIESEL FUEL FRONT WALL ELEVATION  
 M5.2 1"=1'

**FUEL SHOP/ON-SITE NOTES:**

- DURING SHOP FABRICATION HOLE SAW 1-1/2"Ø OPENING FOR DAY TANK FILL PIPE, STUB PIPE 12" MIN BEYOND WALL, & TERMINATE WITH 1" MALE THREAD FOR TESTING.
- UPON COMPLETION OF TESTING CLOSE VALVE, DRAIN PIPE, DISCONNECT FLANGE FROM VALVE THEN SLIDE PIPE OVER & SECURE FOR SHIPPING. SEAL WALL OPENING.
- AS PART OF ON-SITE INSTALLATION REINSTALL FILL PIPE THEN CUT THREADS OFF EXTERIOR END & INSTALL SOCKET WELD ELBOW.
- DURING SHOP FABRICATION INSTALL TEMPORARY VENT PIPE OUT WALL. UPON COMPLETION OF TESTING REMOVE TEMPORARY PIPE & SEAL WALL OPENING FOR SHIPPING.
- AS PART OF ON-SITE INSTALLATION INSTALL 3" GALVANIZED THREADED VENT PIPE OUT WALL & UP TO VENT CAP. SEE DETAIL 3/M5.2.
- UPON FINAL ON-SITE ASSEMBLY SEAL 1" FILL PIPE TO EXTERIOR WALL & 3" VENT PIPE TO WALL SLEEVE WITH POLYURETHANE CAULKING ALL AROUND.

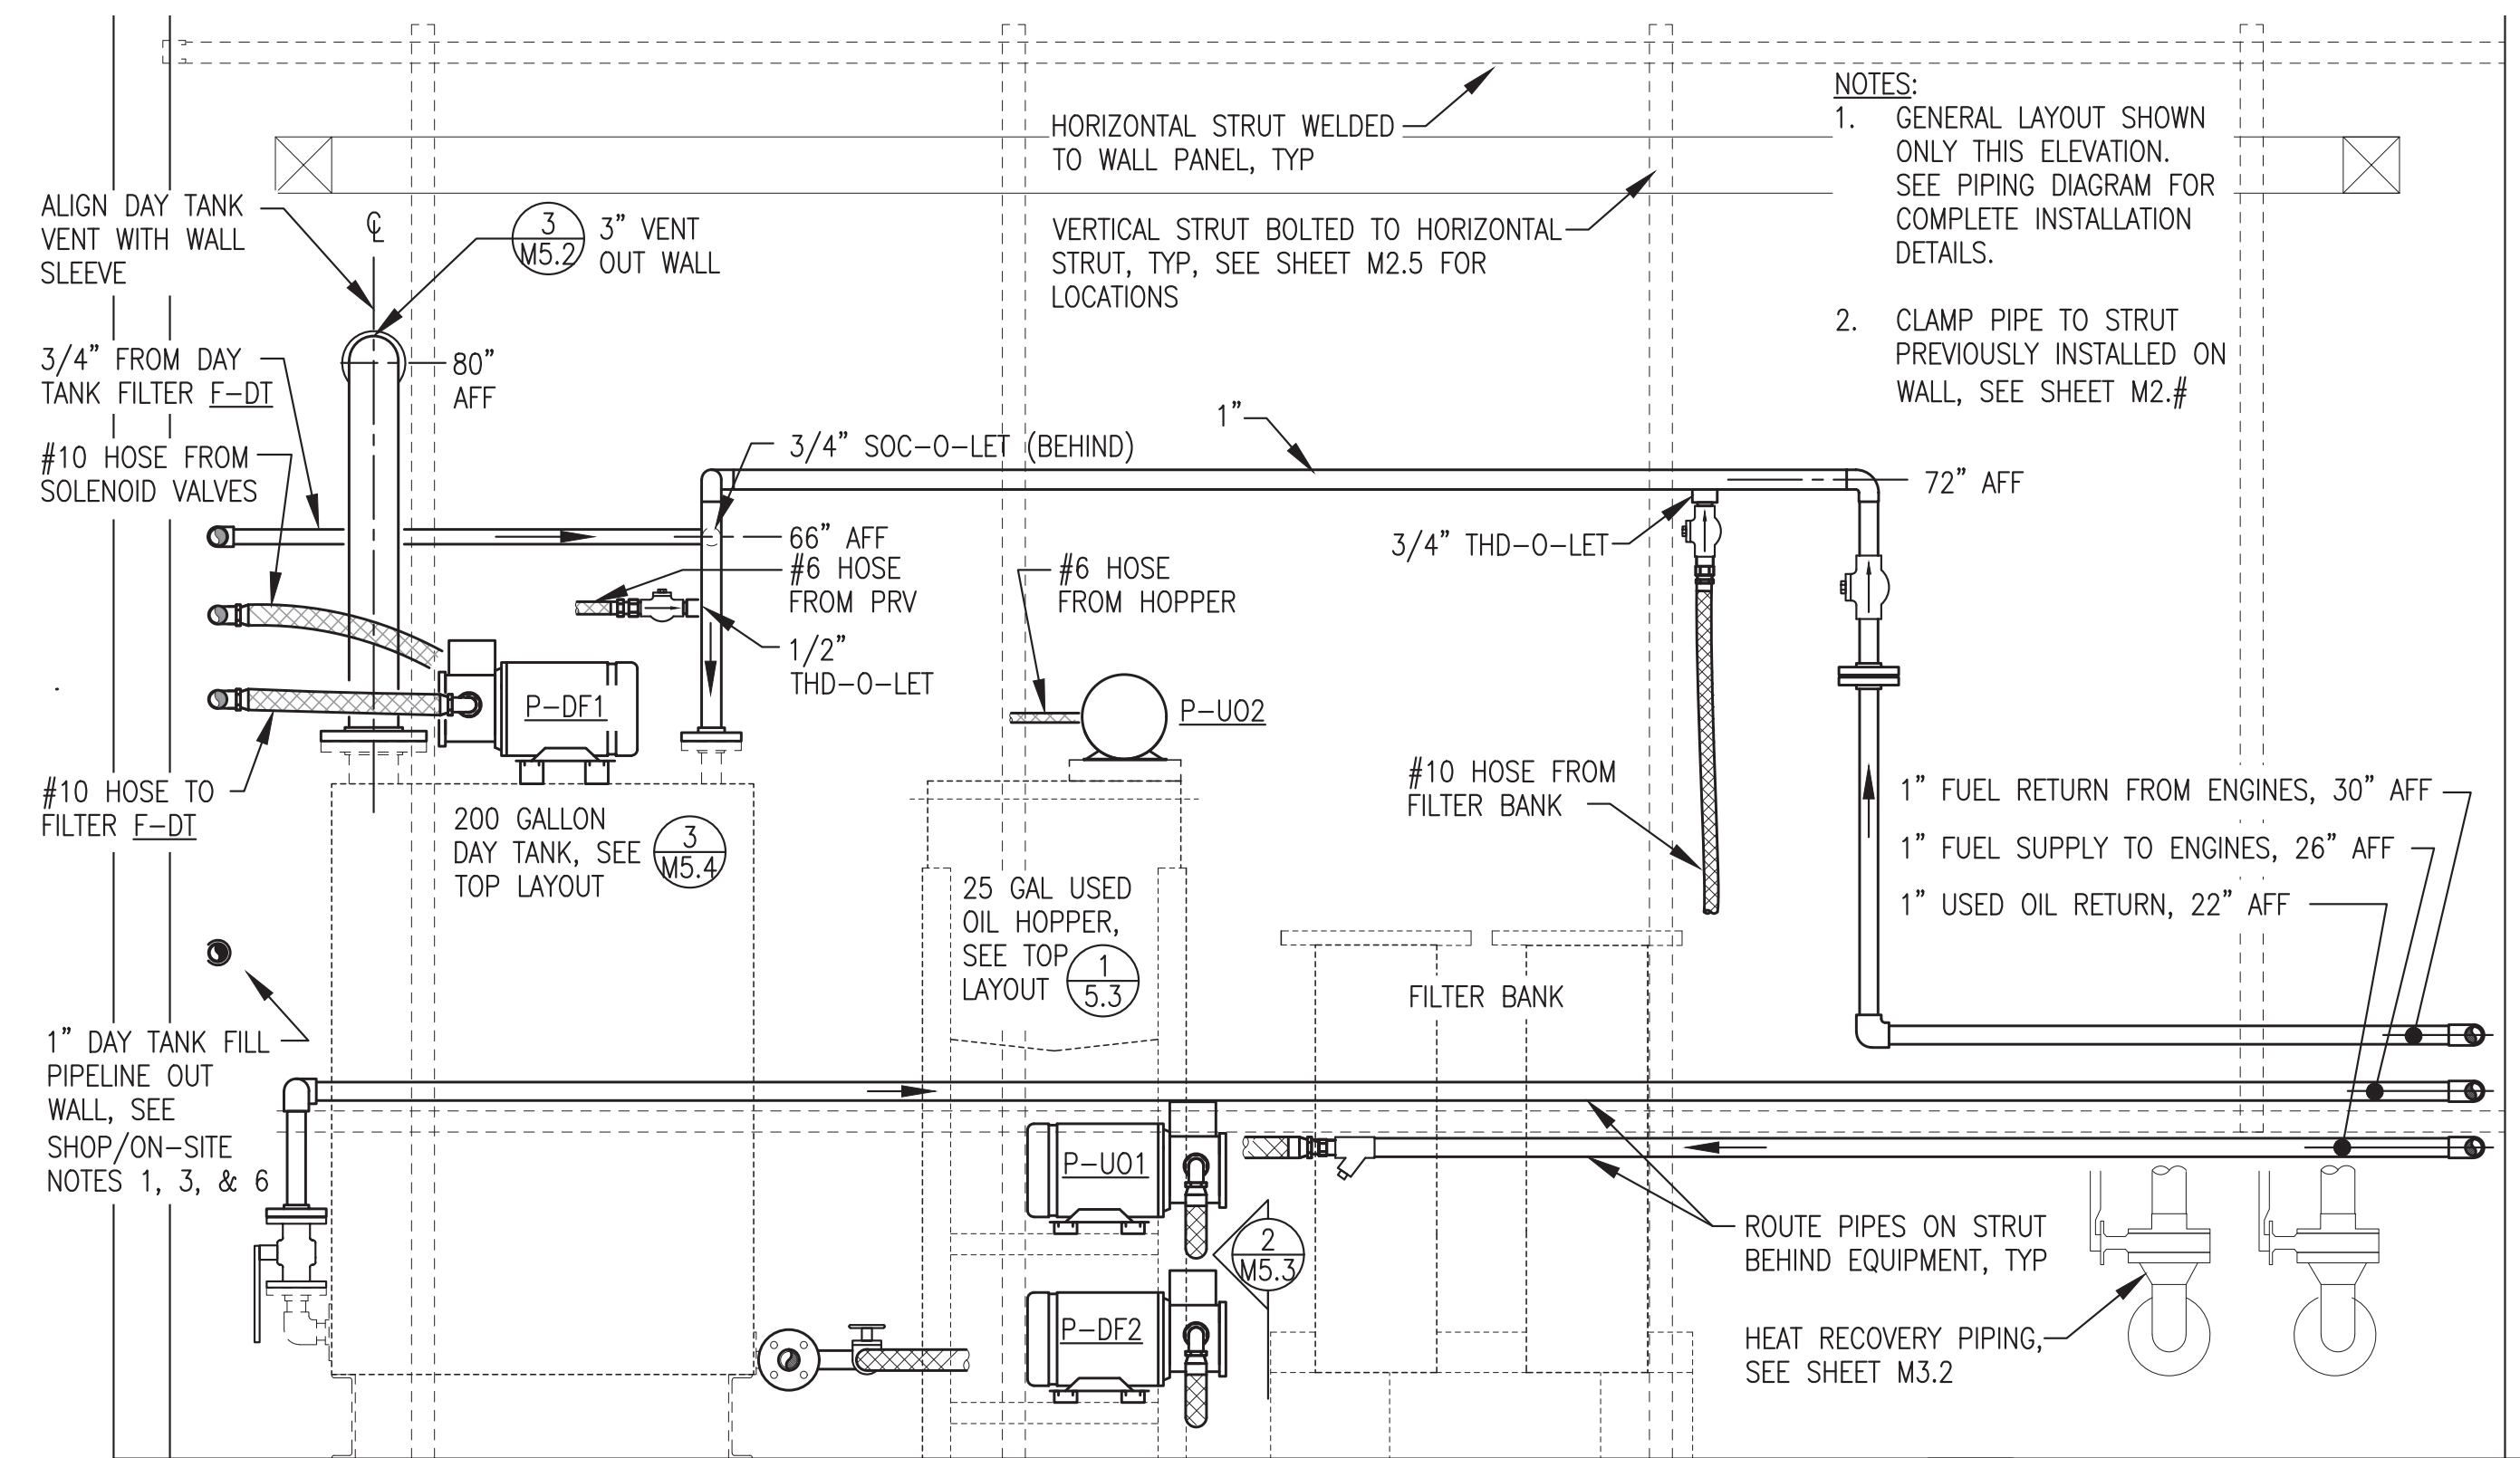


**2** DIESEL FUEL & USED OIL END WALL ELEVATION  
 M5.2 1"=1'

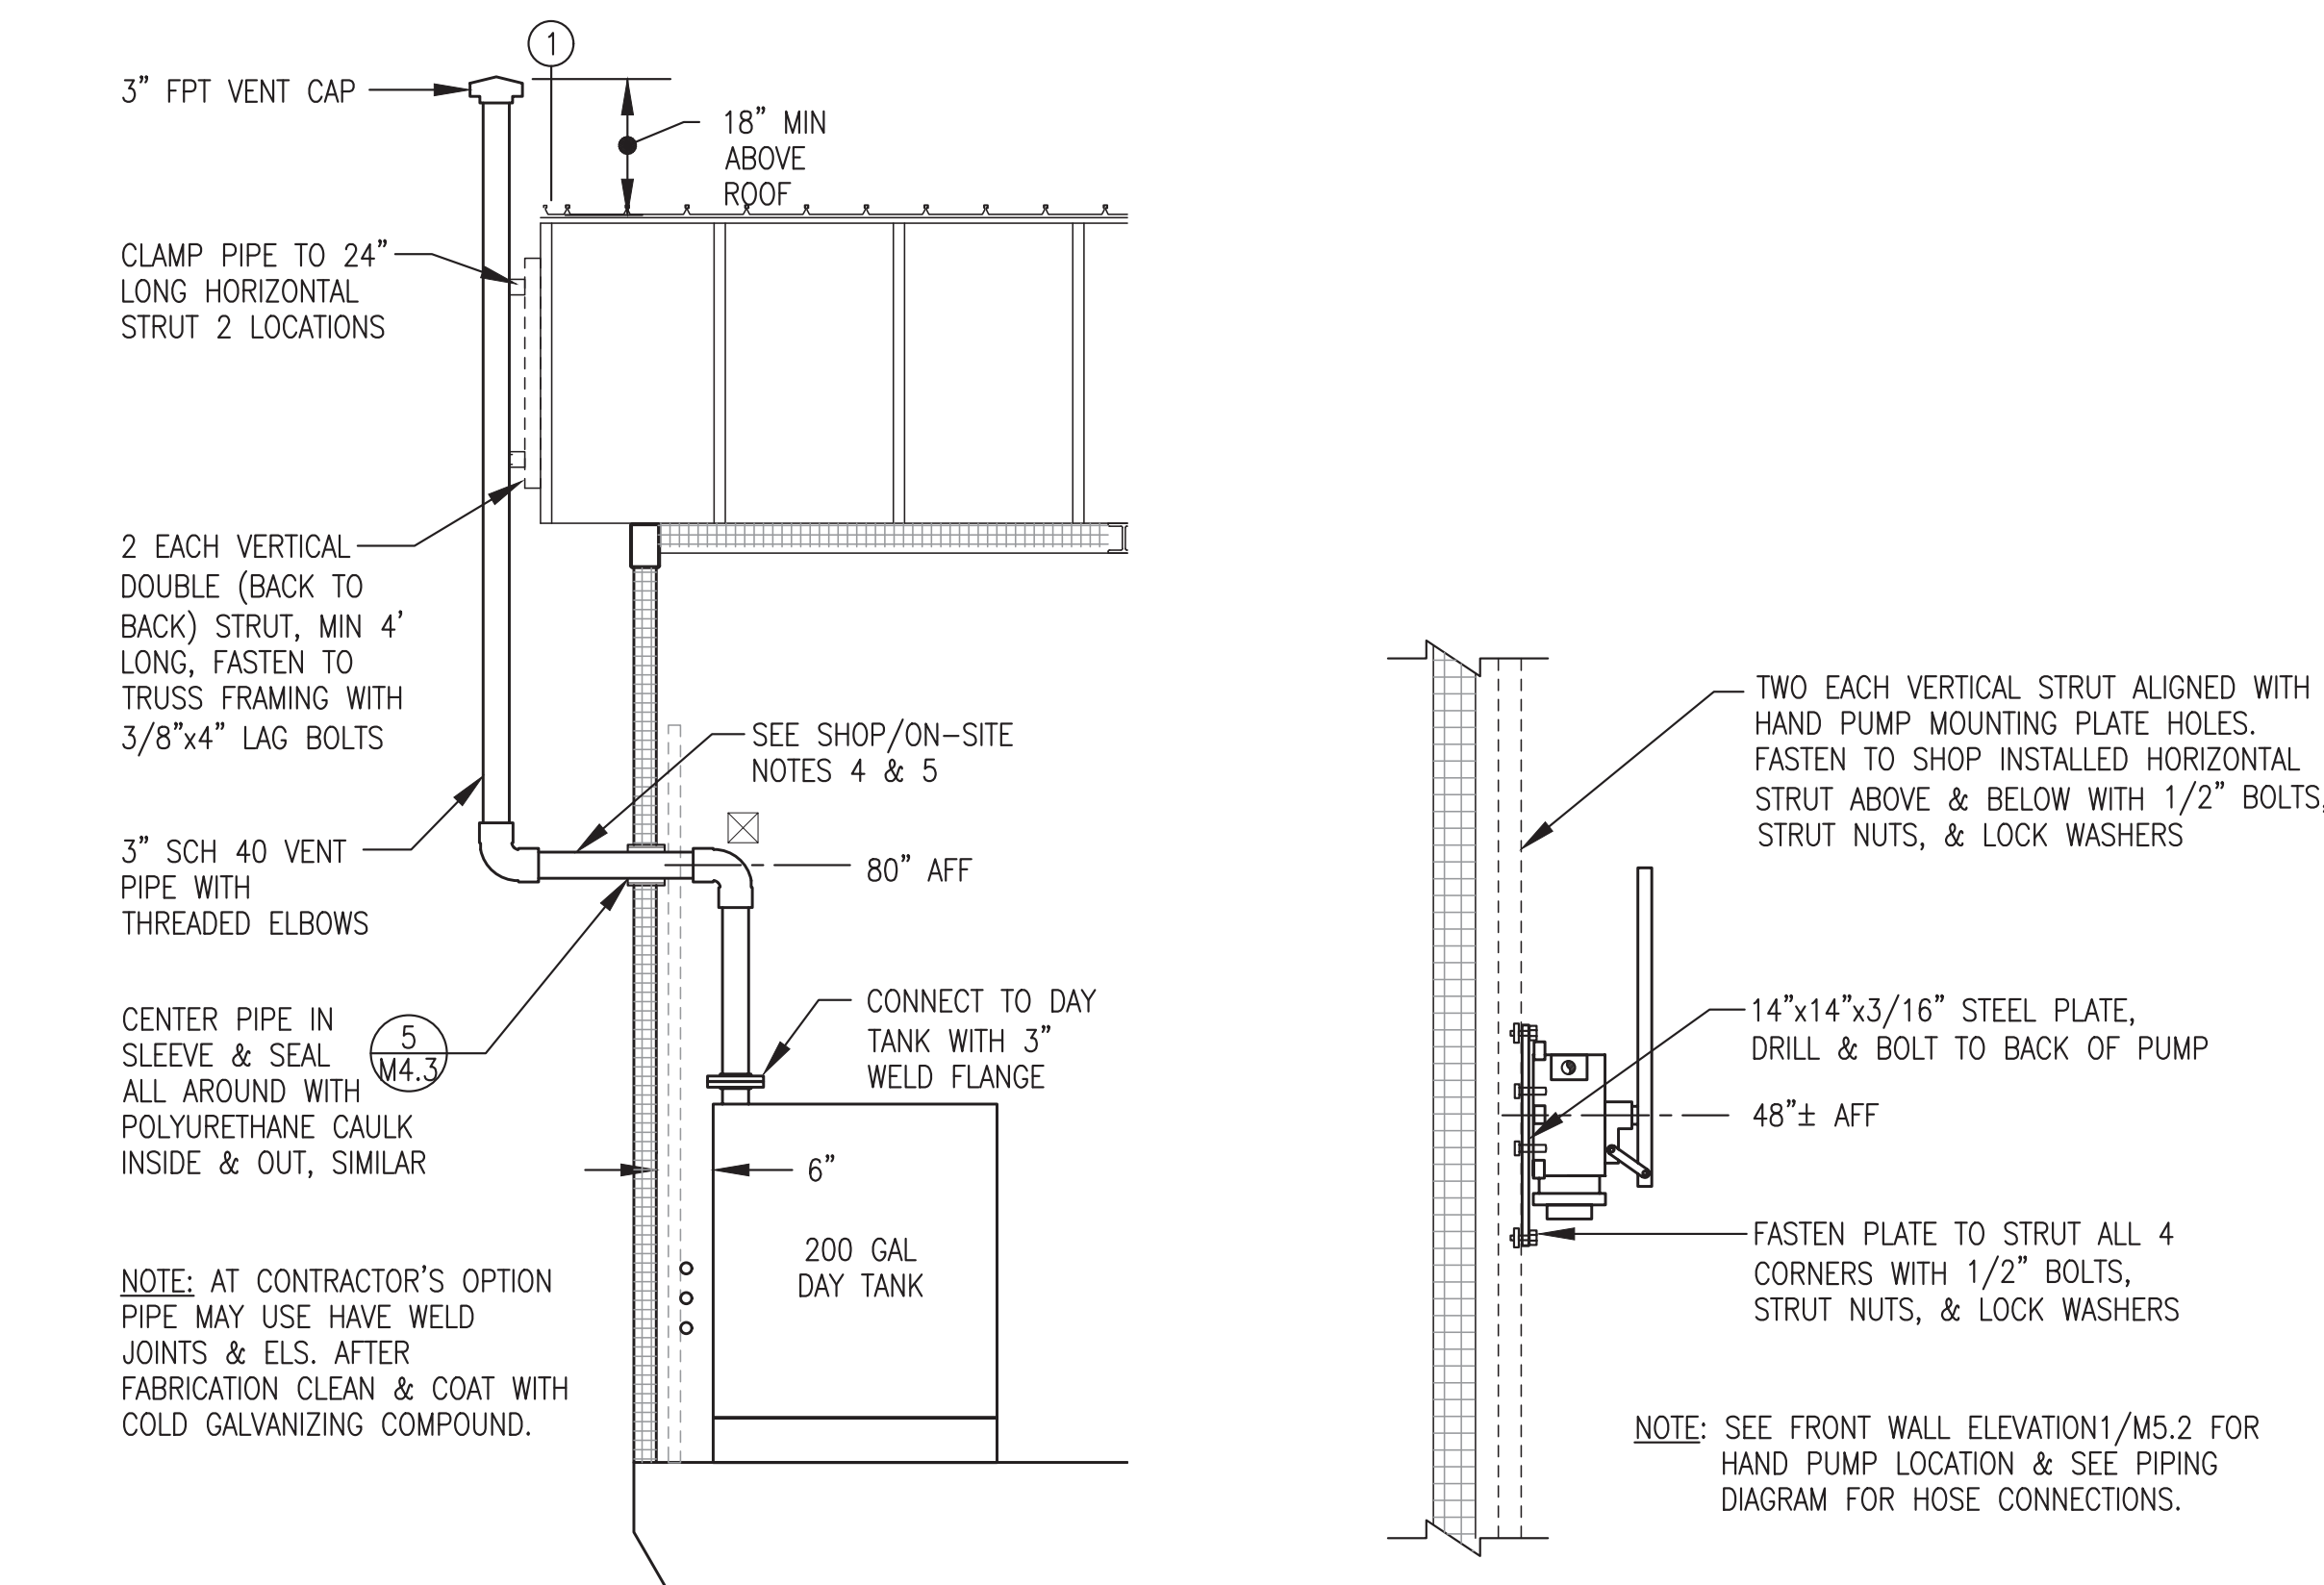

**3** DAY TANK VENT INSTALLATION  
 M5.2 1/2"=1'-0"


**4** DAY TANK HAND PUMP HP-DT WALL SUPPORT  
 M5.2 NO SCALE

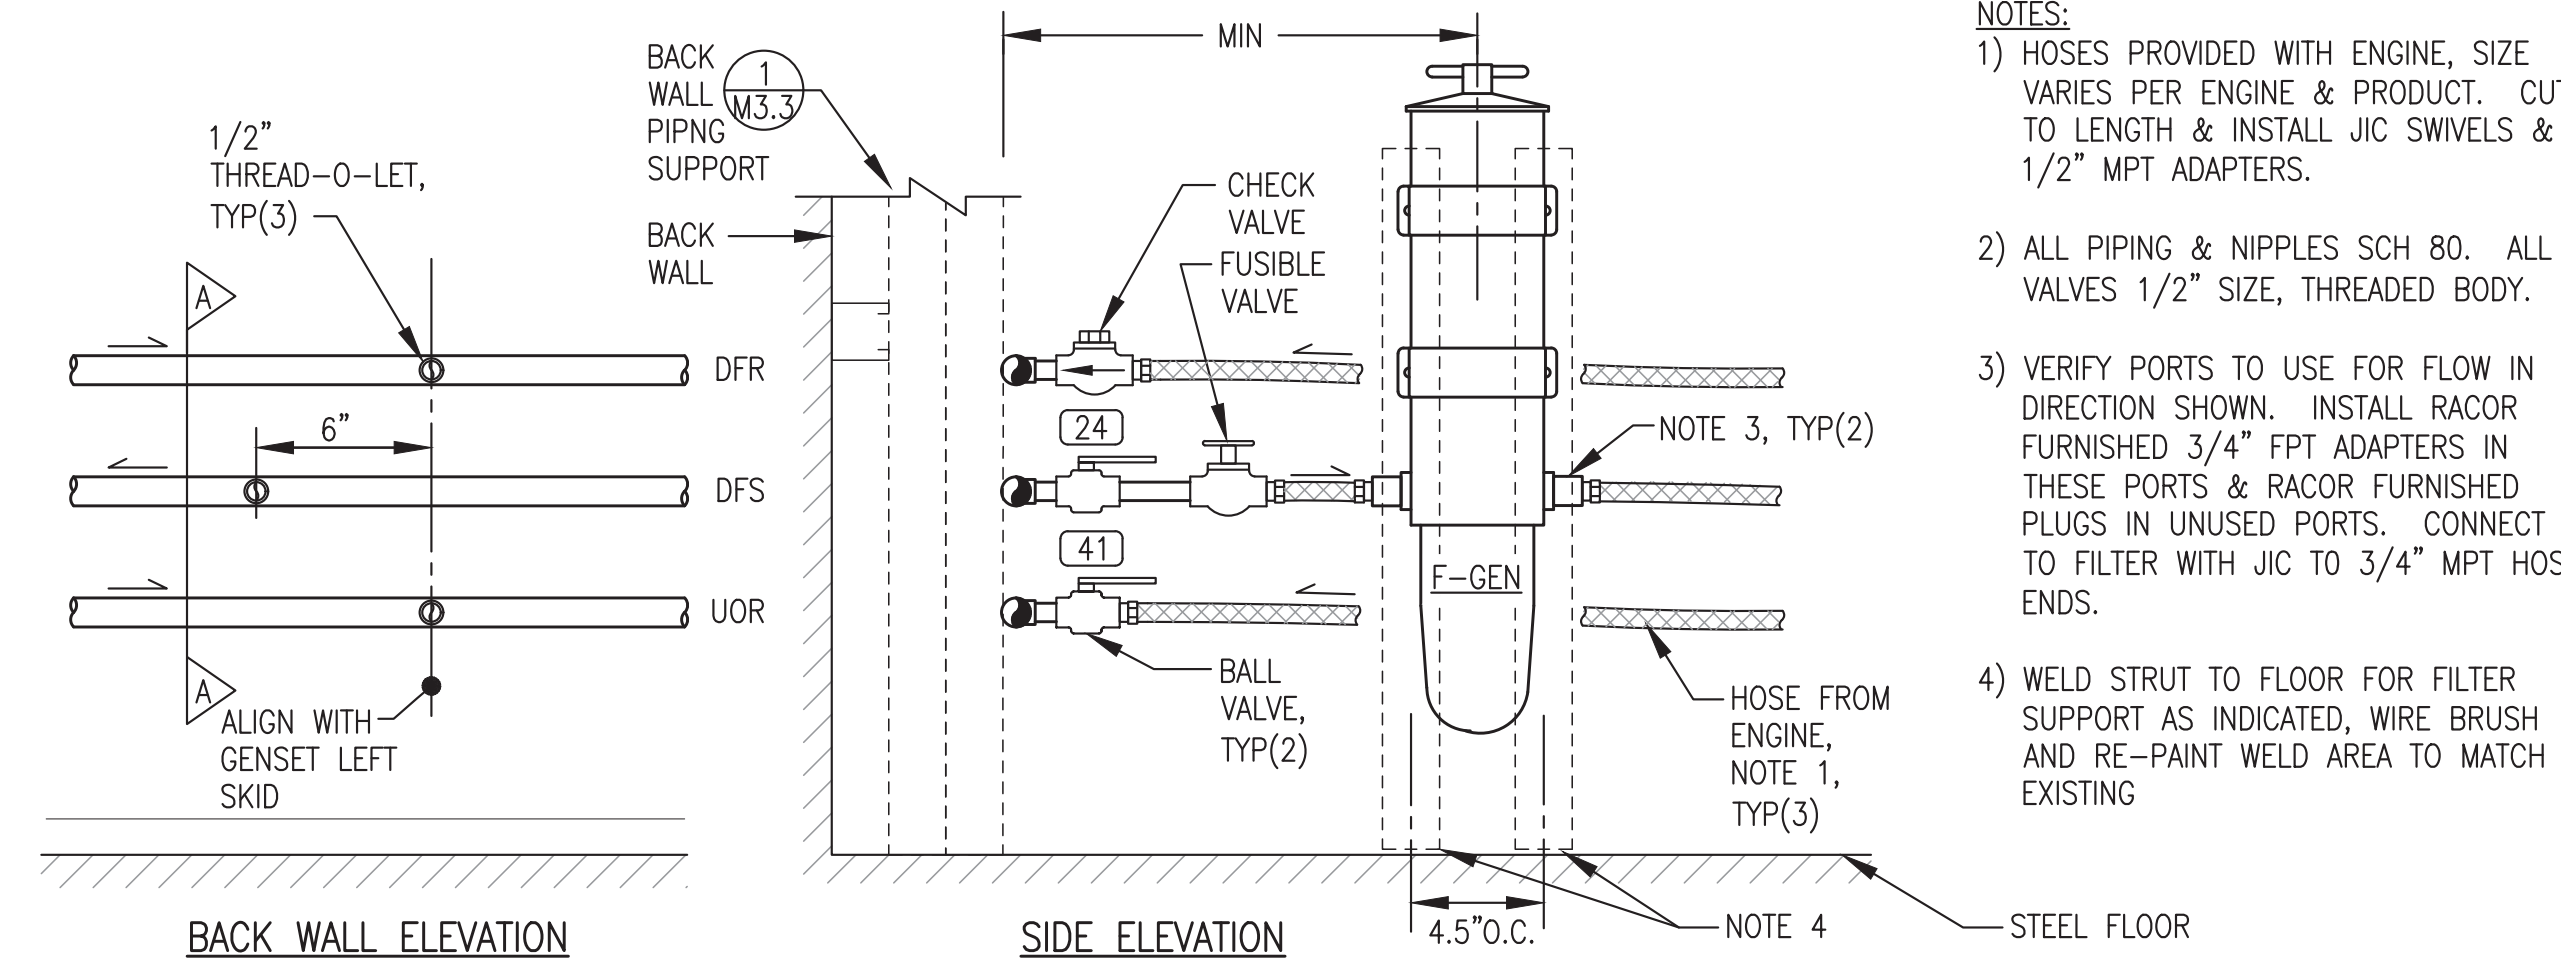


**5** ENGINE FUEL PIPING CONNECTION  
 M5.2 NO SCALE

- NOTES:**
- HOSES PROVIDED WITH ENGINE, SIZE VARIES PER ENGINE & PRODUCT. CUT TO LENGTH & INSTALL JIC SWIVELS & 1/2" MPT ADAPTERS.
  - ALL PIPING & NIPPLES SCH 80. ALL VALVES 1/2" SIZE, THREADED BODY.
  - VERIFY PORTS TO USE FOR FLOW IN DIRECTION SHOWN. INSTALL RACOR FURNISHED 3/4" FPT ADAPTERS IN THESE PORTS & RACOR FURNISHED PLUGS IN UNUSED PORTS. CONNECT TO FILTER WITH JIC TO 3/4" MPT HOSE ENDS.
  - WELD STRUT TO FLOOR FOR FILTER SUPPORT AS INDICATED, WIRE BRUSH AND RE-PAINT WELD AREA TO MATCH EXISTING


REVISION #1  
 ISSUED FOR  
 CONSTRUCTION  
 JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAKI MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
<b>RAMPART POWER SYSTEM UPGRADE</b>			
<b>DIESEL FUEL &amp; USED OIL        PIPING ELEVATIONS &amp; DETAILS</b>			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		<b>M5.2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

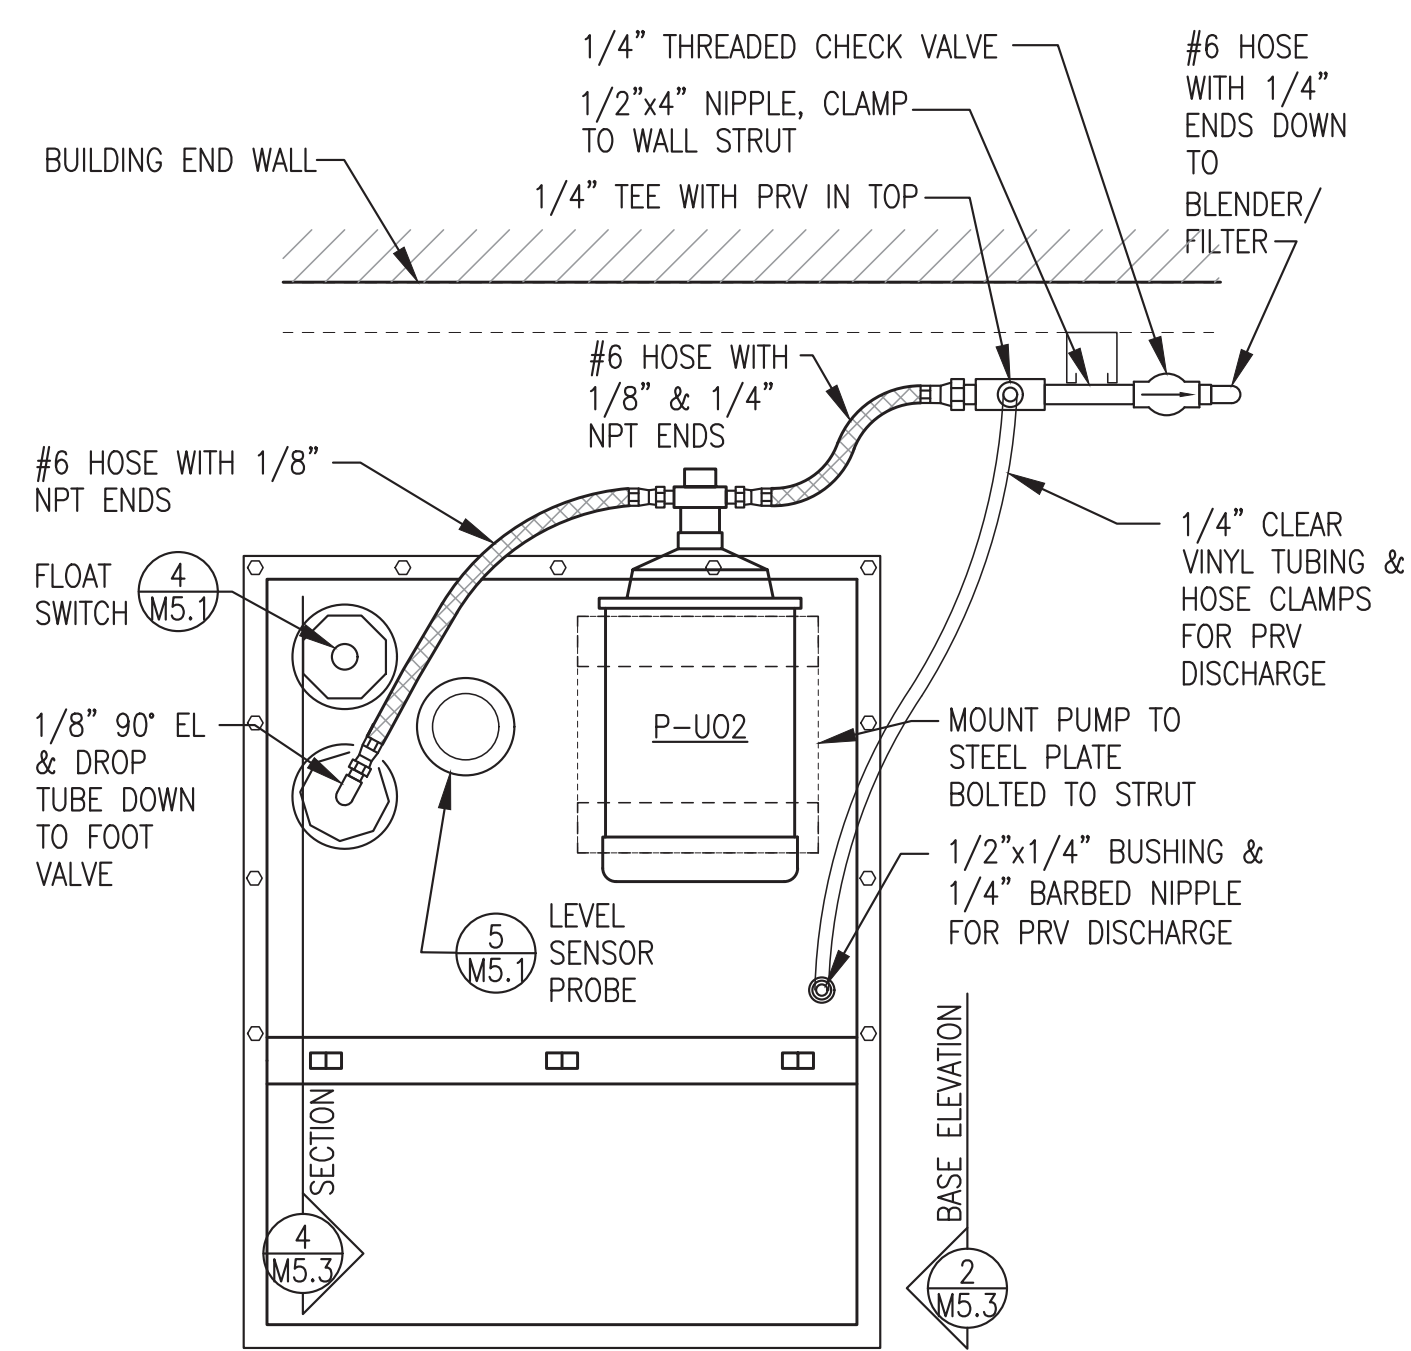

1 TOP OF HOPPER - PLAN VIEW  
M5.3 NO SCALE

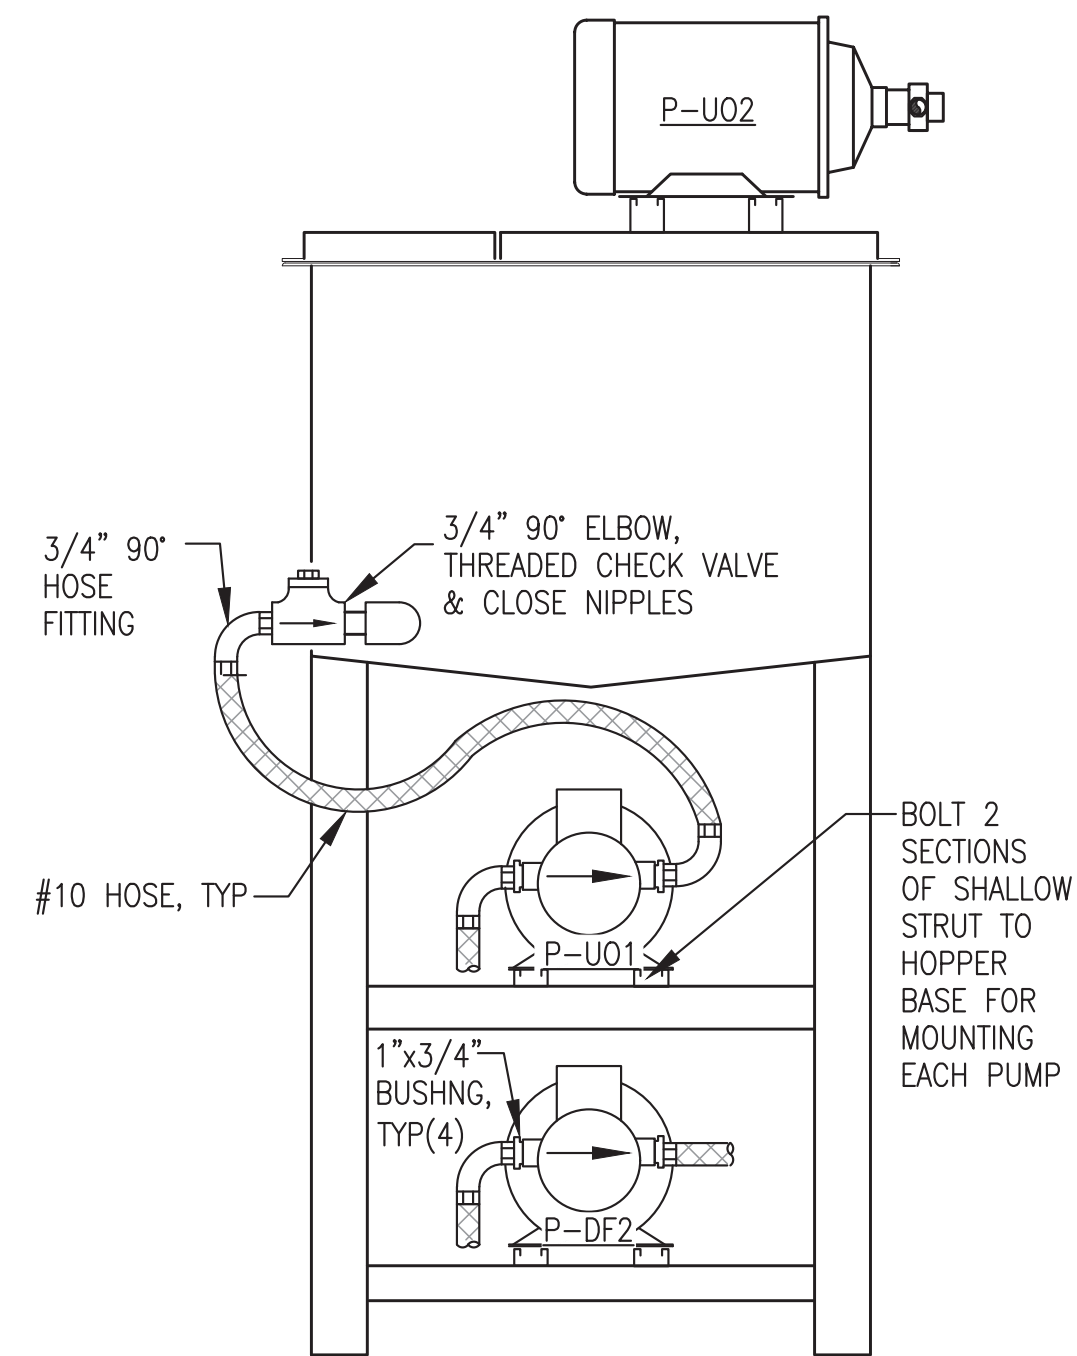


2 HOPPER BASE ELEVATION  
M5.3 NO SCALE

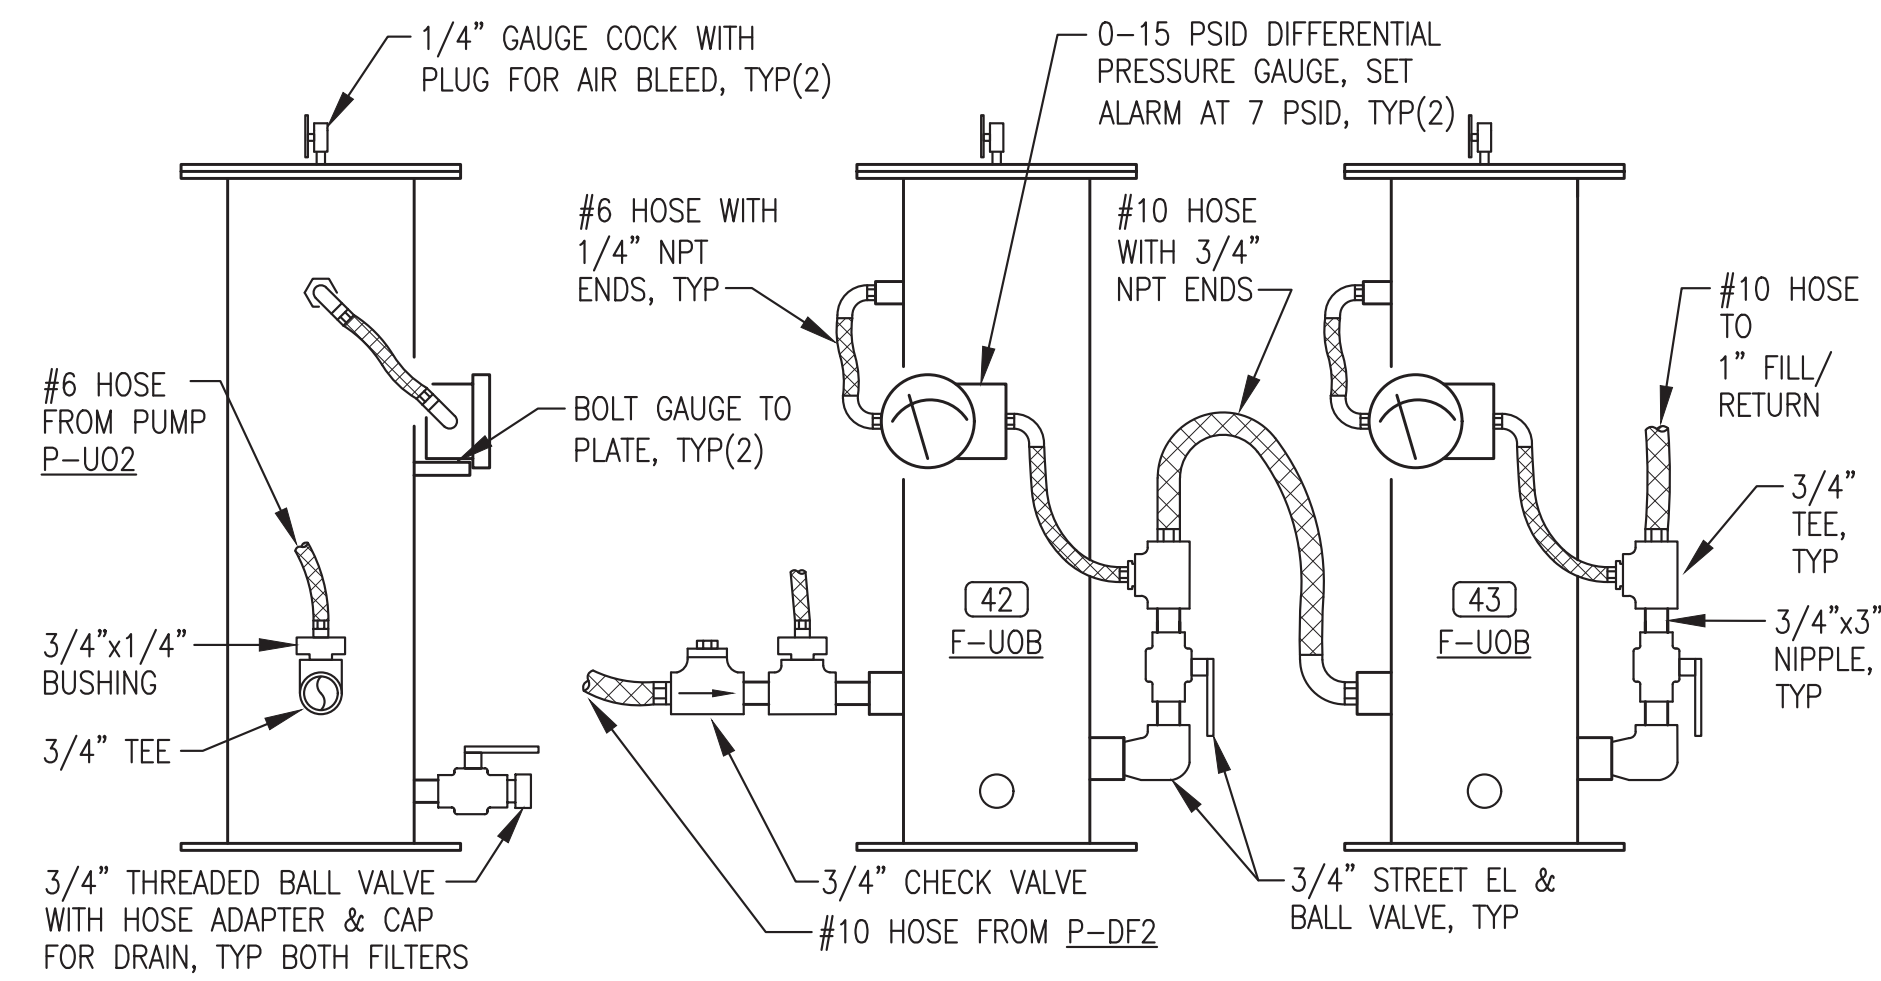

3 FILTER #1 INLET SIDE ELEVATION


FRONT ELEVATION


3 FILTER BANK ELEVATIONS  
M5.3 NO SCALE

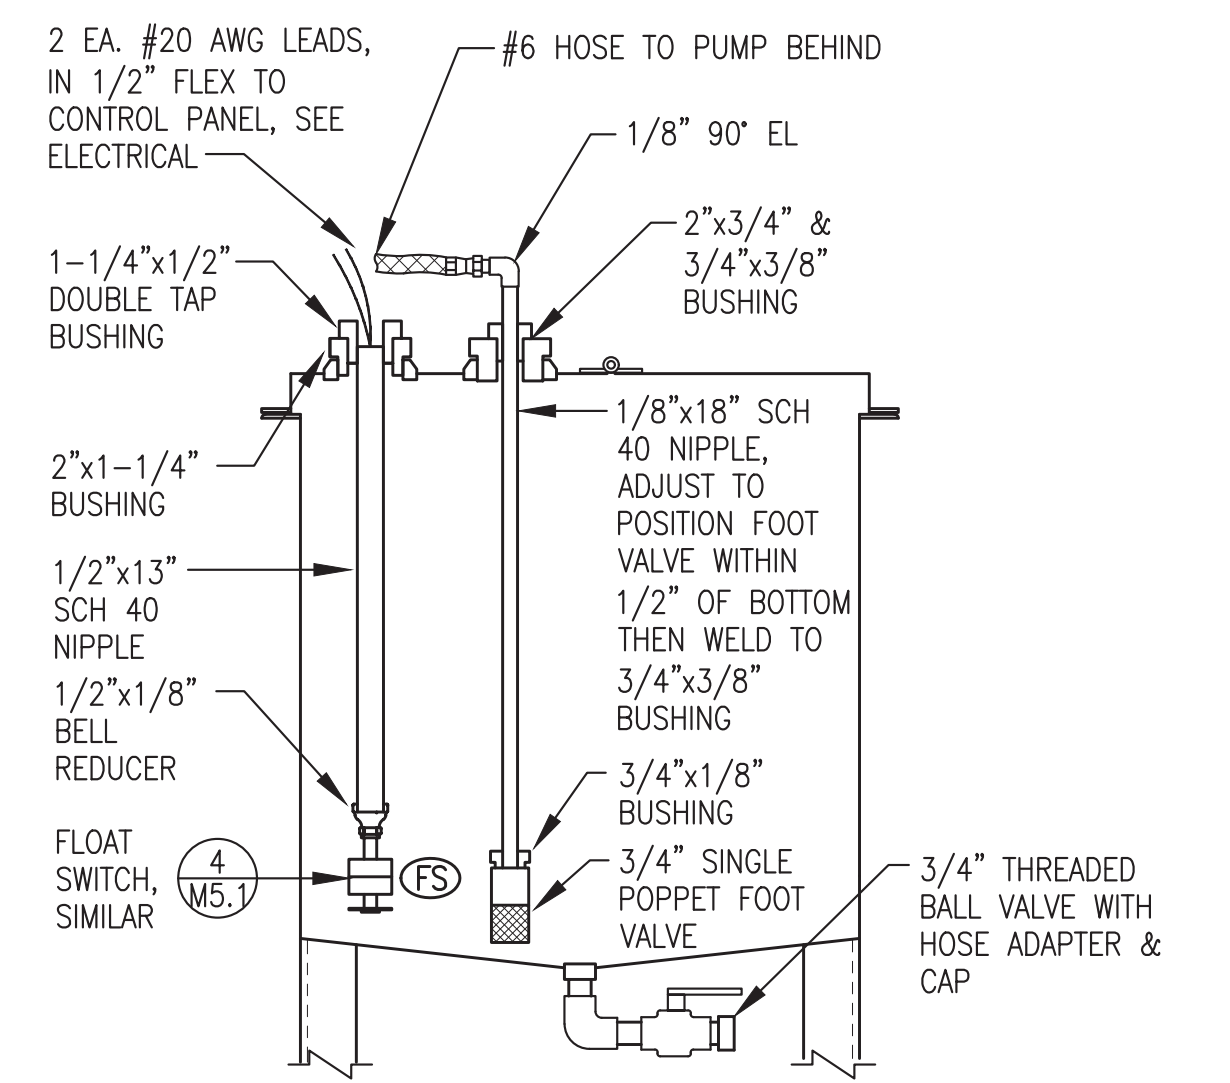


4 SECTION THROUGH HOPPER  
M5.3 NO SCALE

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: USED OIL HOPPER & BLENDER INSTALLATION DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM PP M2-M7		SHEET: M5.3	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

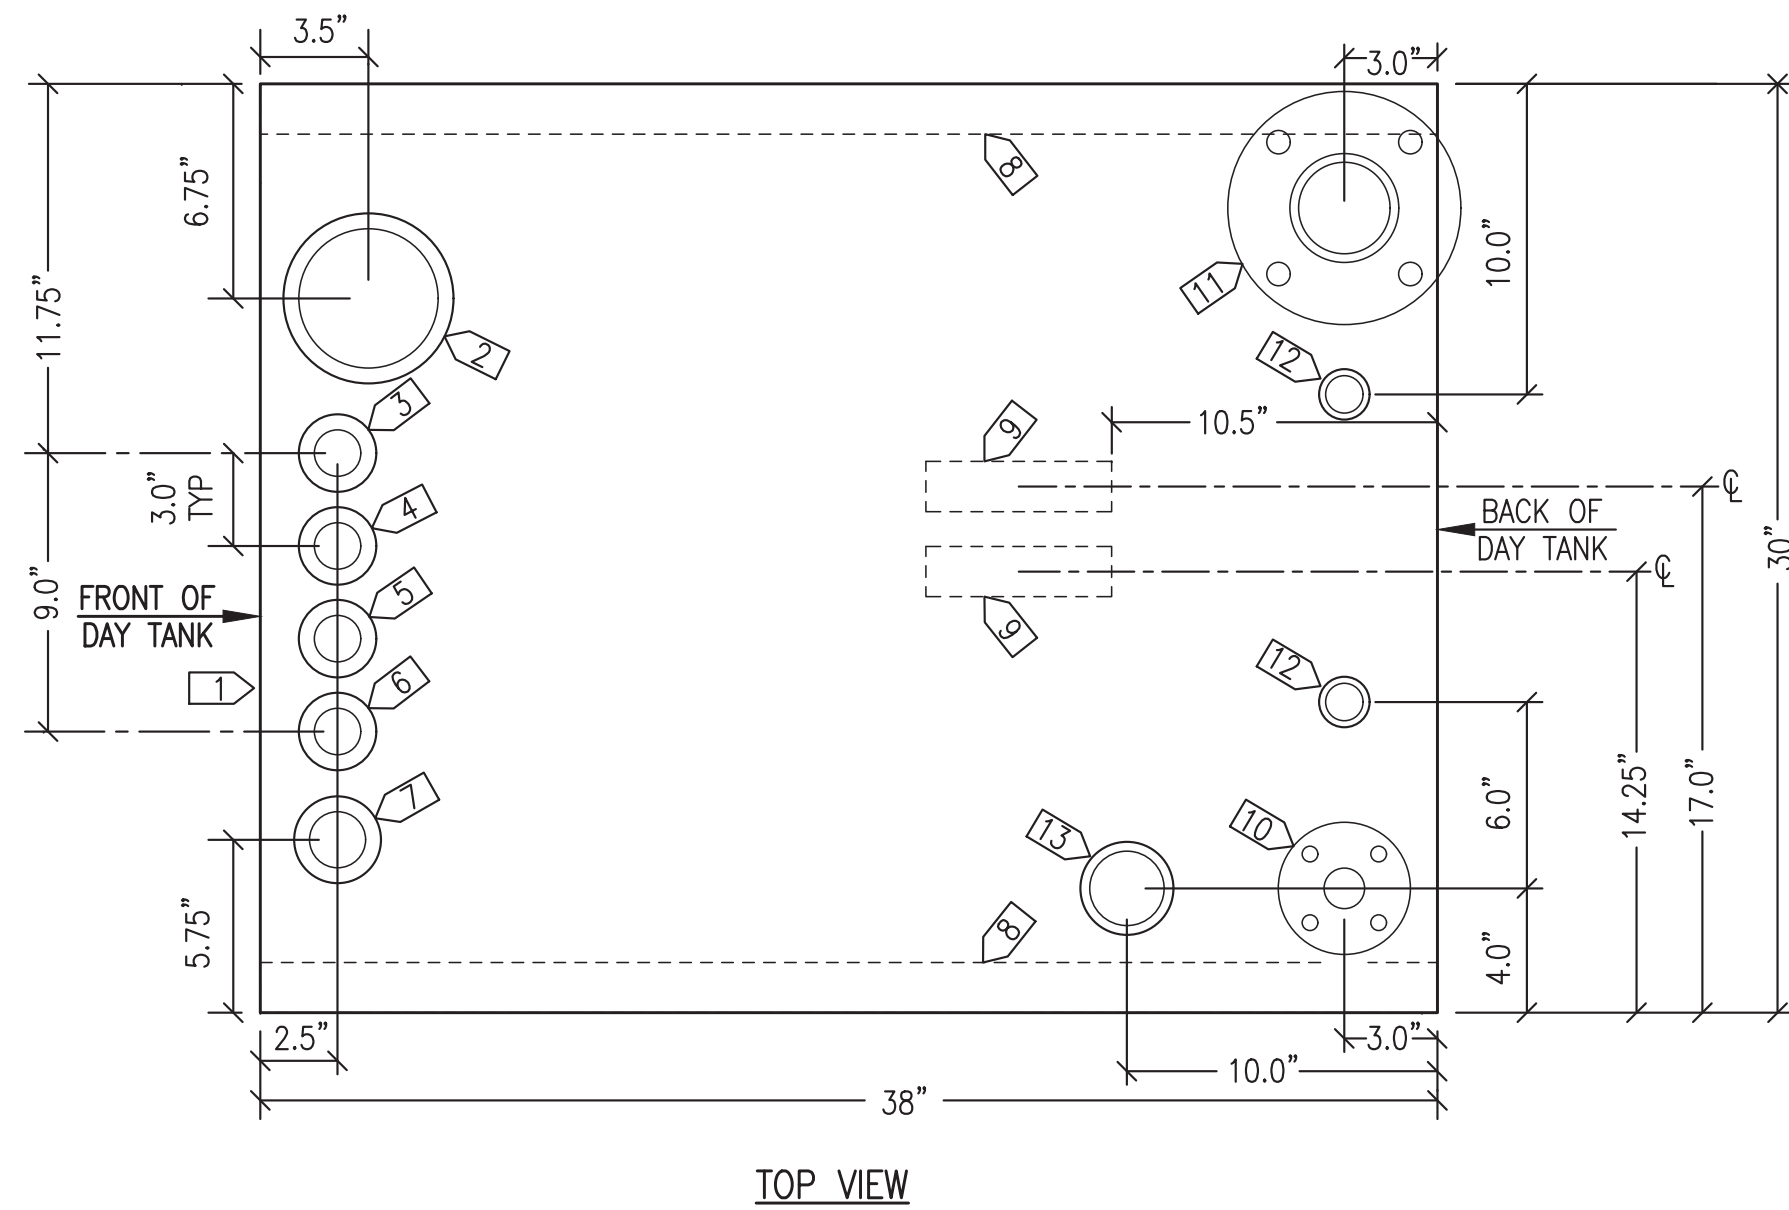


**DAY TANK SPECIFICATIONS:**


- 1) FABRICATE SINGLE WALL 200 GALLON NOMINAL CAPACITY DAY TANK. FABRICATE IN ACCORDANCE WITH UL 142.
- 2) FABRICATE FROM ASTM A-36 STEEL PLATE, 10 GAUGE MINIMUM EXCEPT FOR TOP 3/16" MINIMUM. ALL TANK SEAM JOINTS TO BE FULL CONTINUOUS WELDS IN ACCORDANCE WITH UL 142 FIGURE 6.5 - #1, #6, #7, OR #8.
- 3) PROVIDE WITH ALL OPENINGS AND ATTACHMENTS INDICATED. ALL STRUT TO BE 1-5/8"x1-5/8"x12 GA SOLID BACK PLAIN (BLACK), B-LINE B22 PLN OR EQUAL. SEAL WELD ALL TANK ATTACHMENTS.
- 4) INSTALL ALL FPT OPENINGS IN ACCORDANCE WITH UL 142 FIGURE 7.1 - #4 UNLESS INDICATED OTHERWISE. ALL DROP TUBES SCH 40 ASTM A53 STEEL PIPE WITH MPT OR FLANGED END AS INDICATED.
- 5) PRESSURE TEST COMPLETED ASSEMBLY TO 5 PSIG MAXIMUM USING SOAPY WATER SOLUTION ON ALL WELD JOINTS.
- 6) UPON COMPLETION OF FABRICATION, ROUND ALL CORNERS AND SHARP EDGES. SANDBLAST TANK EXTERIOR AND ALL ATTACHMENTS IN ACCORDANCE WITH SSPC-SP-6. PAINT WITH TWO COATS EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, COLOR ANSI 61 GRAY.
- 7) LABEL ALL OPENINGS WITH 1/4" BLACK LETTERS INDICATING FUNCTION AS LISTED IN PARENTHESES IN SPECIFIC NOTES.
- 8) UPON COMPLETION FLUSH INTERIOR OF TANK TO REMOVE ALL DIRT AND DEBRIS AND AIR DRY INTERIOR. SEAL ALL MPT OPENINGS WITH THREADED STEEL CAPS. SEAL FPT TANK OPENINGS WITH THREADED STEEL PIPE PLUGS WHERE INDICATED. INSTALL 1-1/4" VENT CAP WHERE INDICATED. SEAL ALL OTHER FPT OPENINGS WITH PLASTIC OR STEEL PLUGS.

**DAY TANK SPECIFIC NOTES:**


- 1) PROVIDE 2" HIGH LETTERING: "DIESEL FUEL 200 GALLONS"
- 2) 4" FPT (MANUAL FILL) - INSTALL THREADED STEEL PLUG
- 3) 1-1/4" FPT (OVERFILL) - INSTALL VENT CAP FOR SHIPPING
- 4) 1-1/4" FPT (PUMP STOP)
- 5) 1-1/4" FPT (PUMP START)
- 6) 1-1/4" FPT (LOW ALARM)
- 7) 1-1/2" FPT (TANK GAUGE)
- 8) 38"L STRUT, ENDS FLUSH WITH TANK
- 9) 6"L STRUT
- 10) 1" SCH 40 DROP TUBE (FILL) WITH 1" 150# FLANGE
- 11) 3" 150# FLANGED VENT CONNECTION
- 12) 1" FPT (SPARE) - INSTALL THREADED STEEL PLUG
- 13) 2" FPT (TANK LEVEL PROBE)
- 14) C6x8.2, 38" LONG

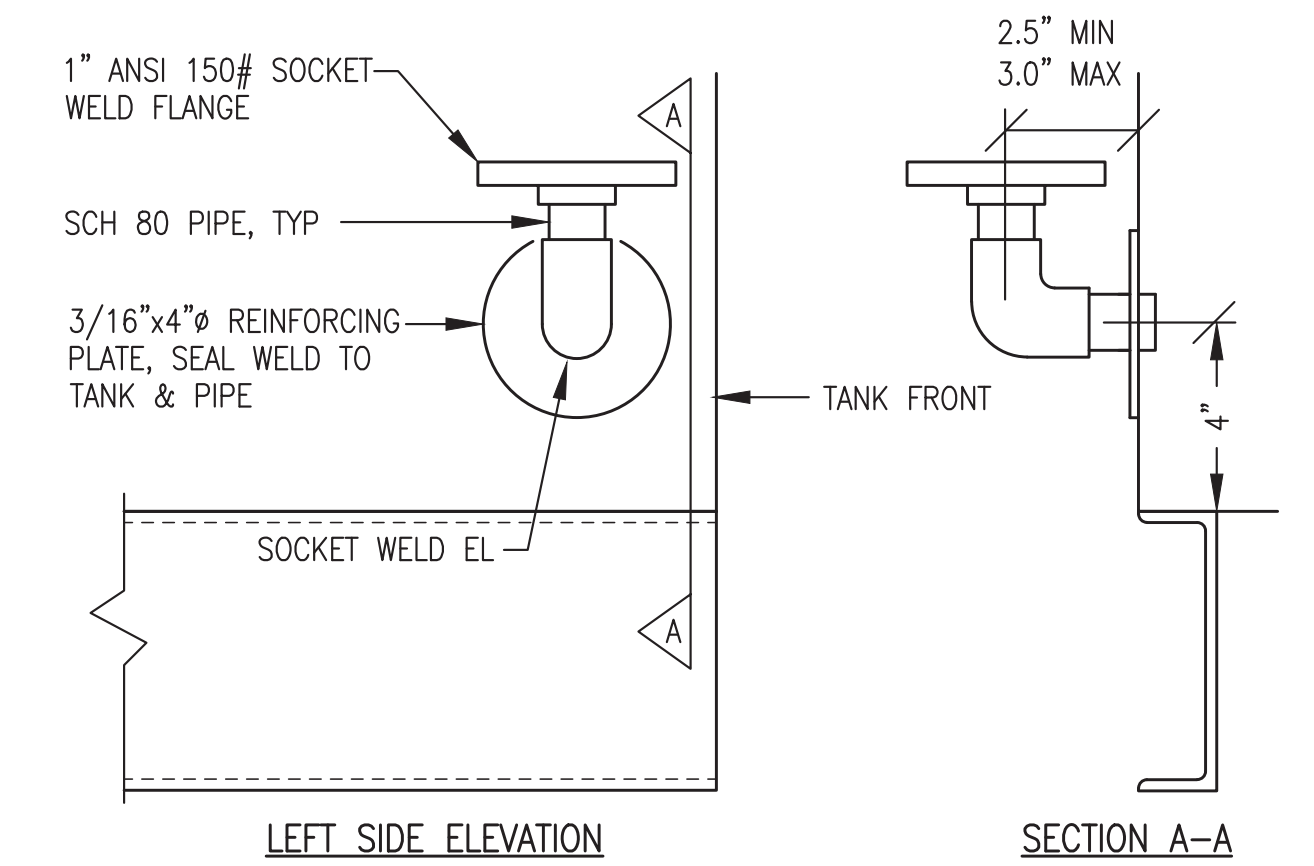


**2 1" FLANGED SUPPLY CONNECTION**  
M5.4 NO SCALE

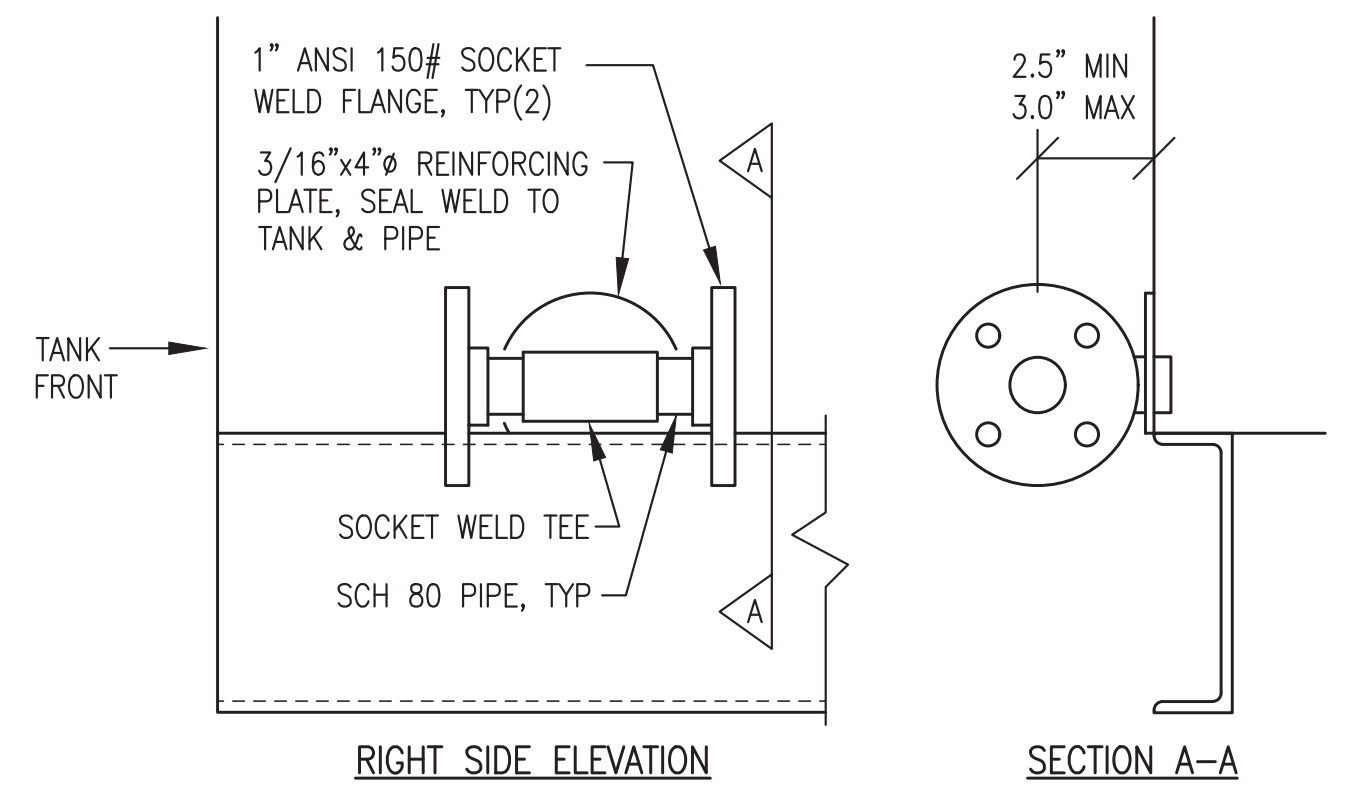

**3 1" FLANGED DRAIN CONNECTION**  
M5.4 NO SCALE

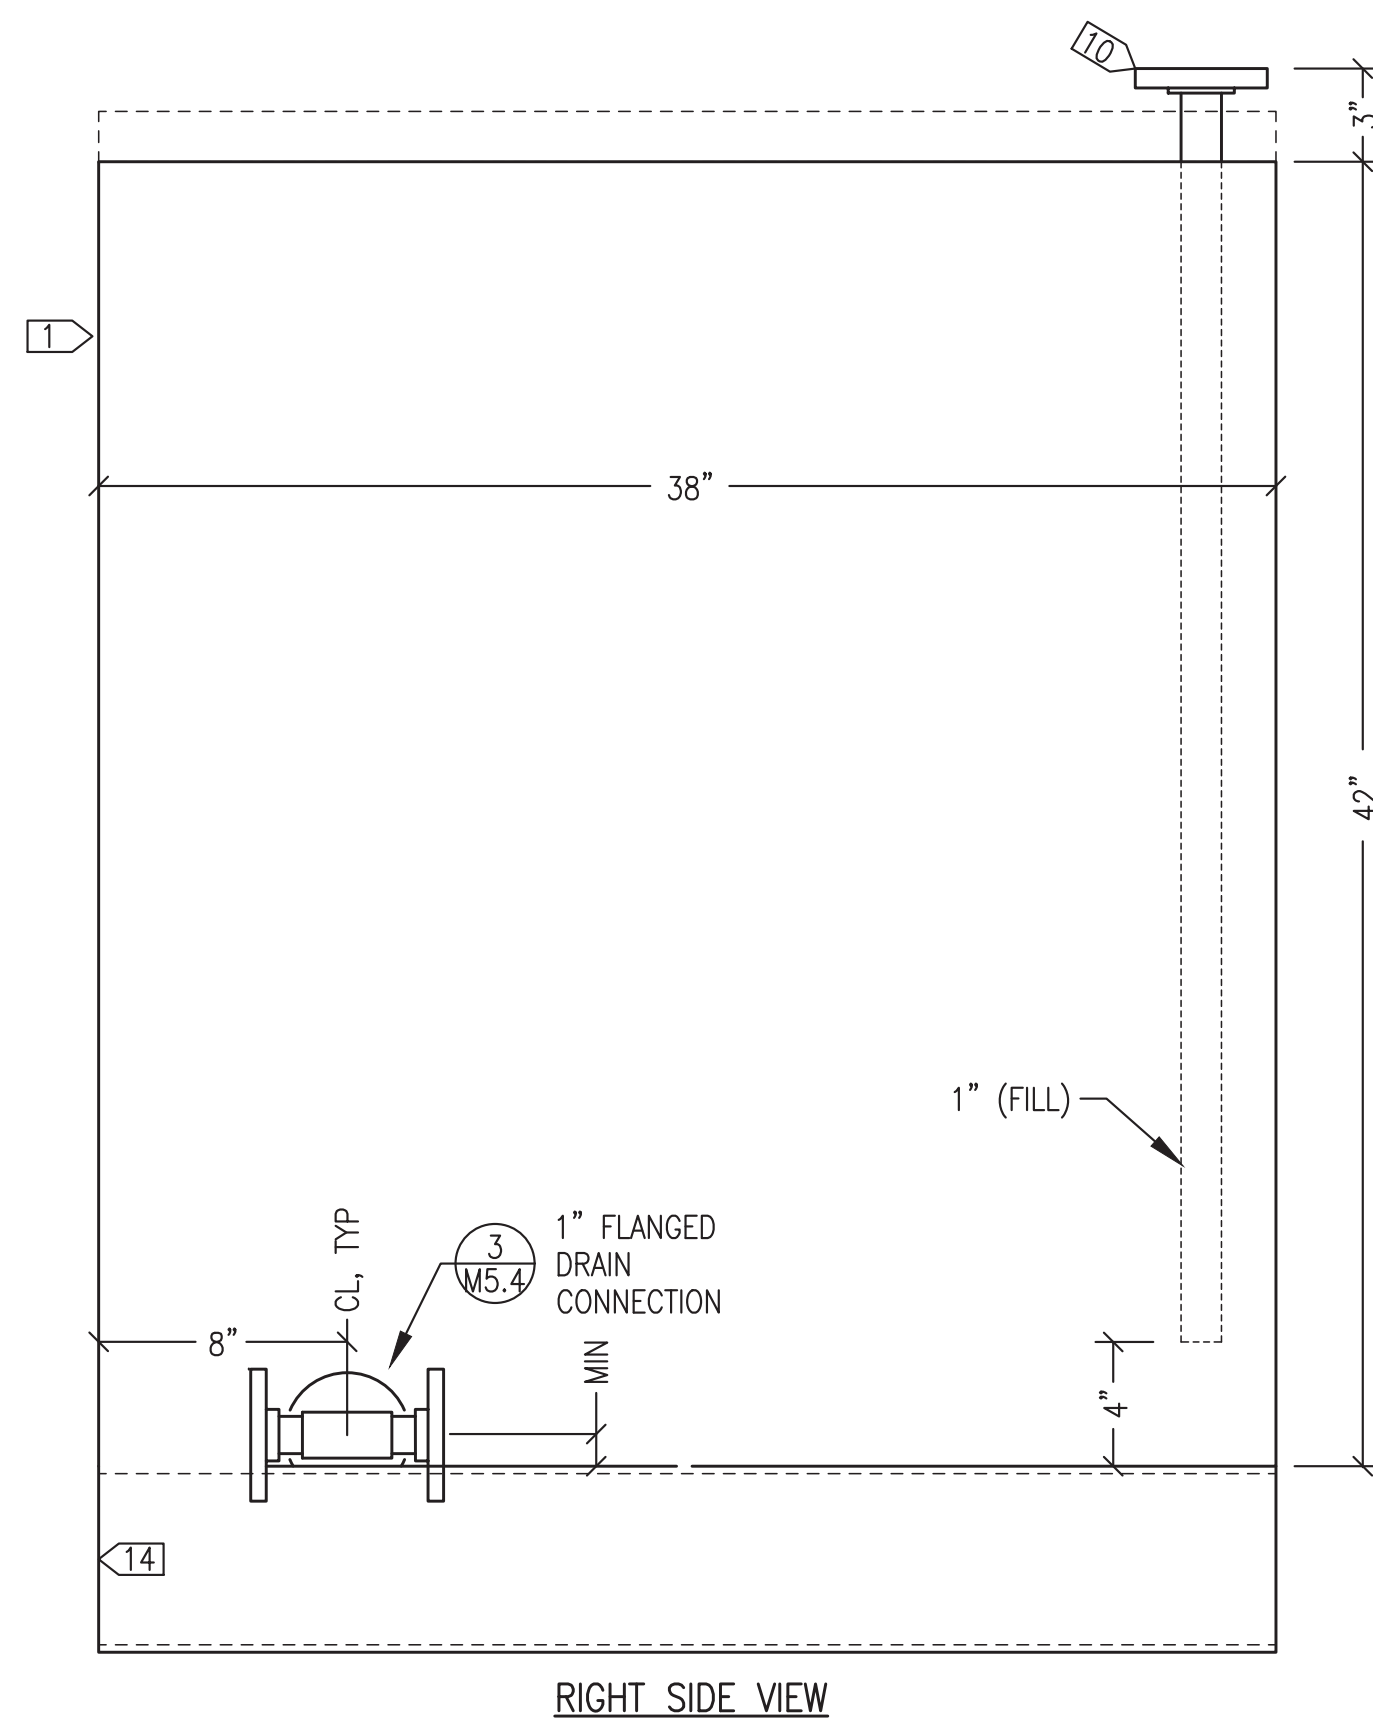


RIGHT SIDE VIEW

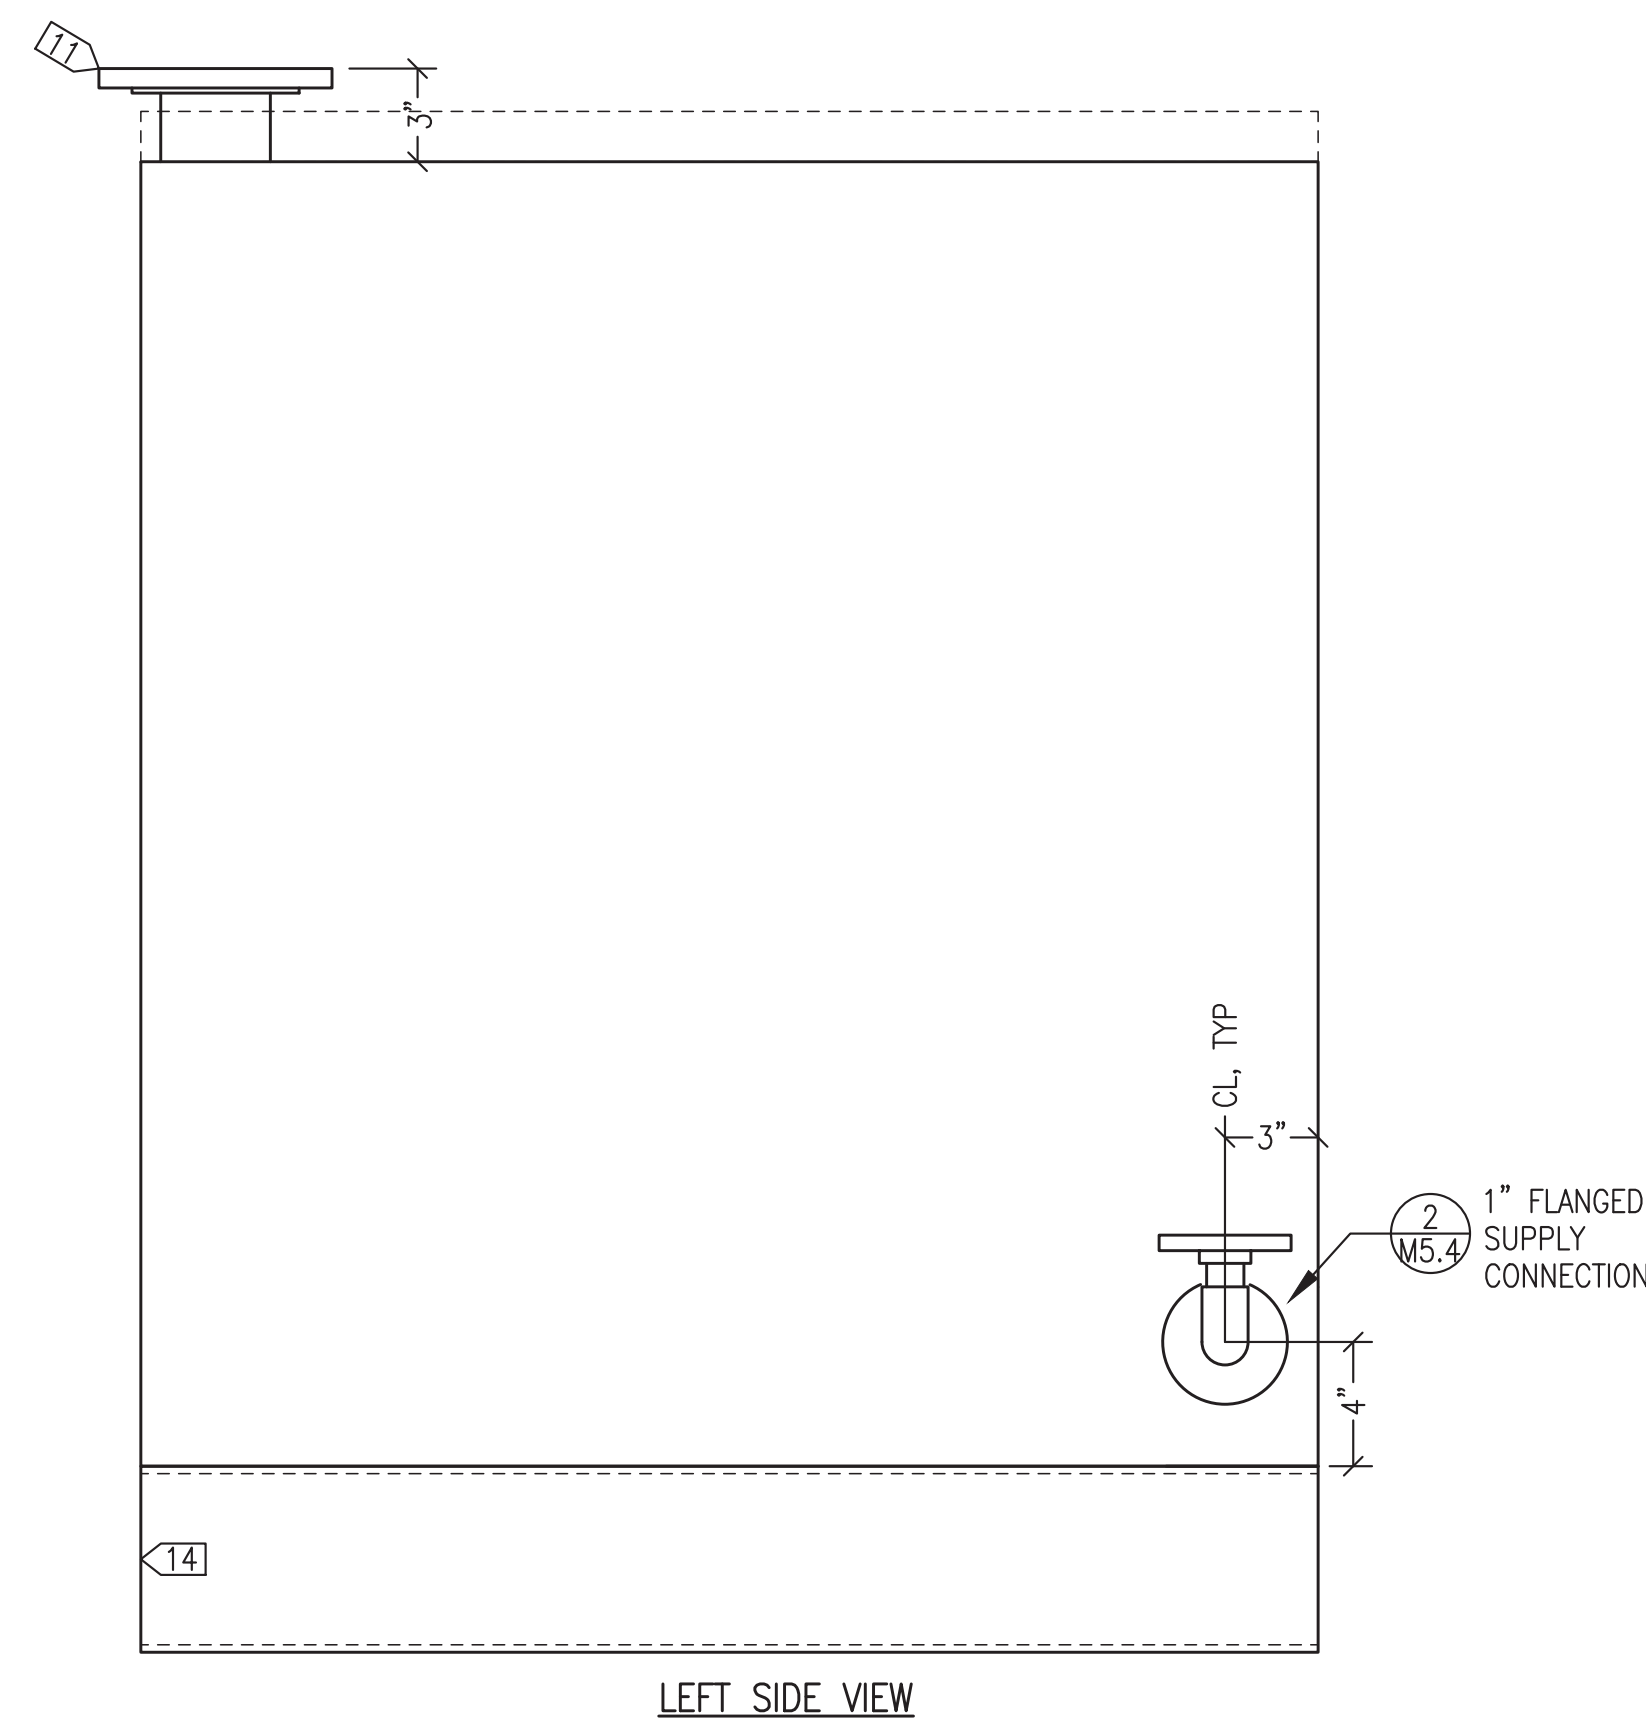


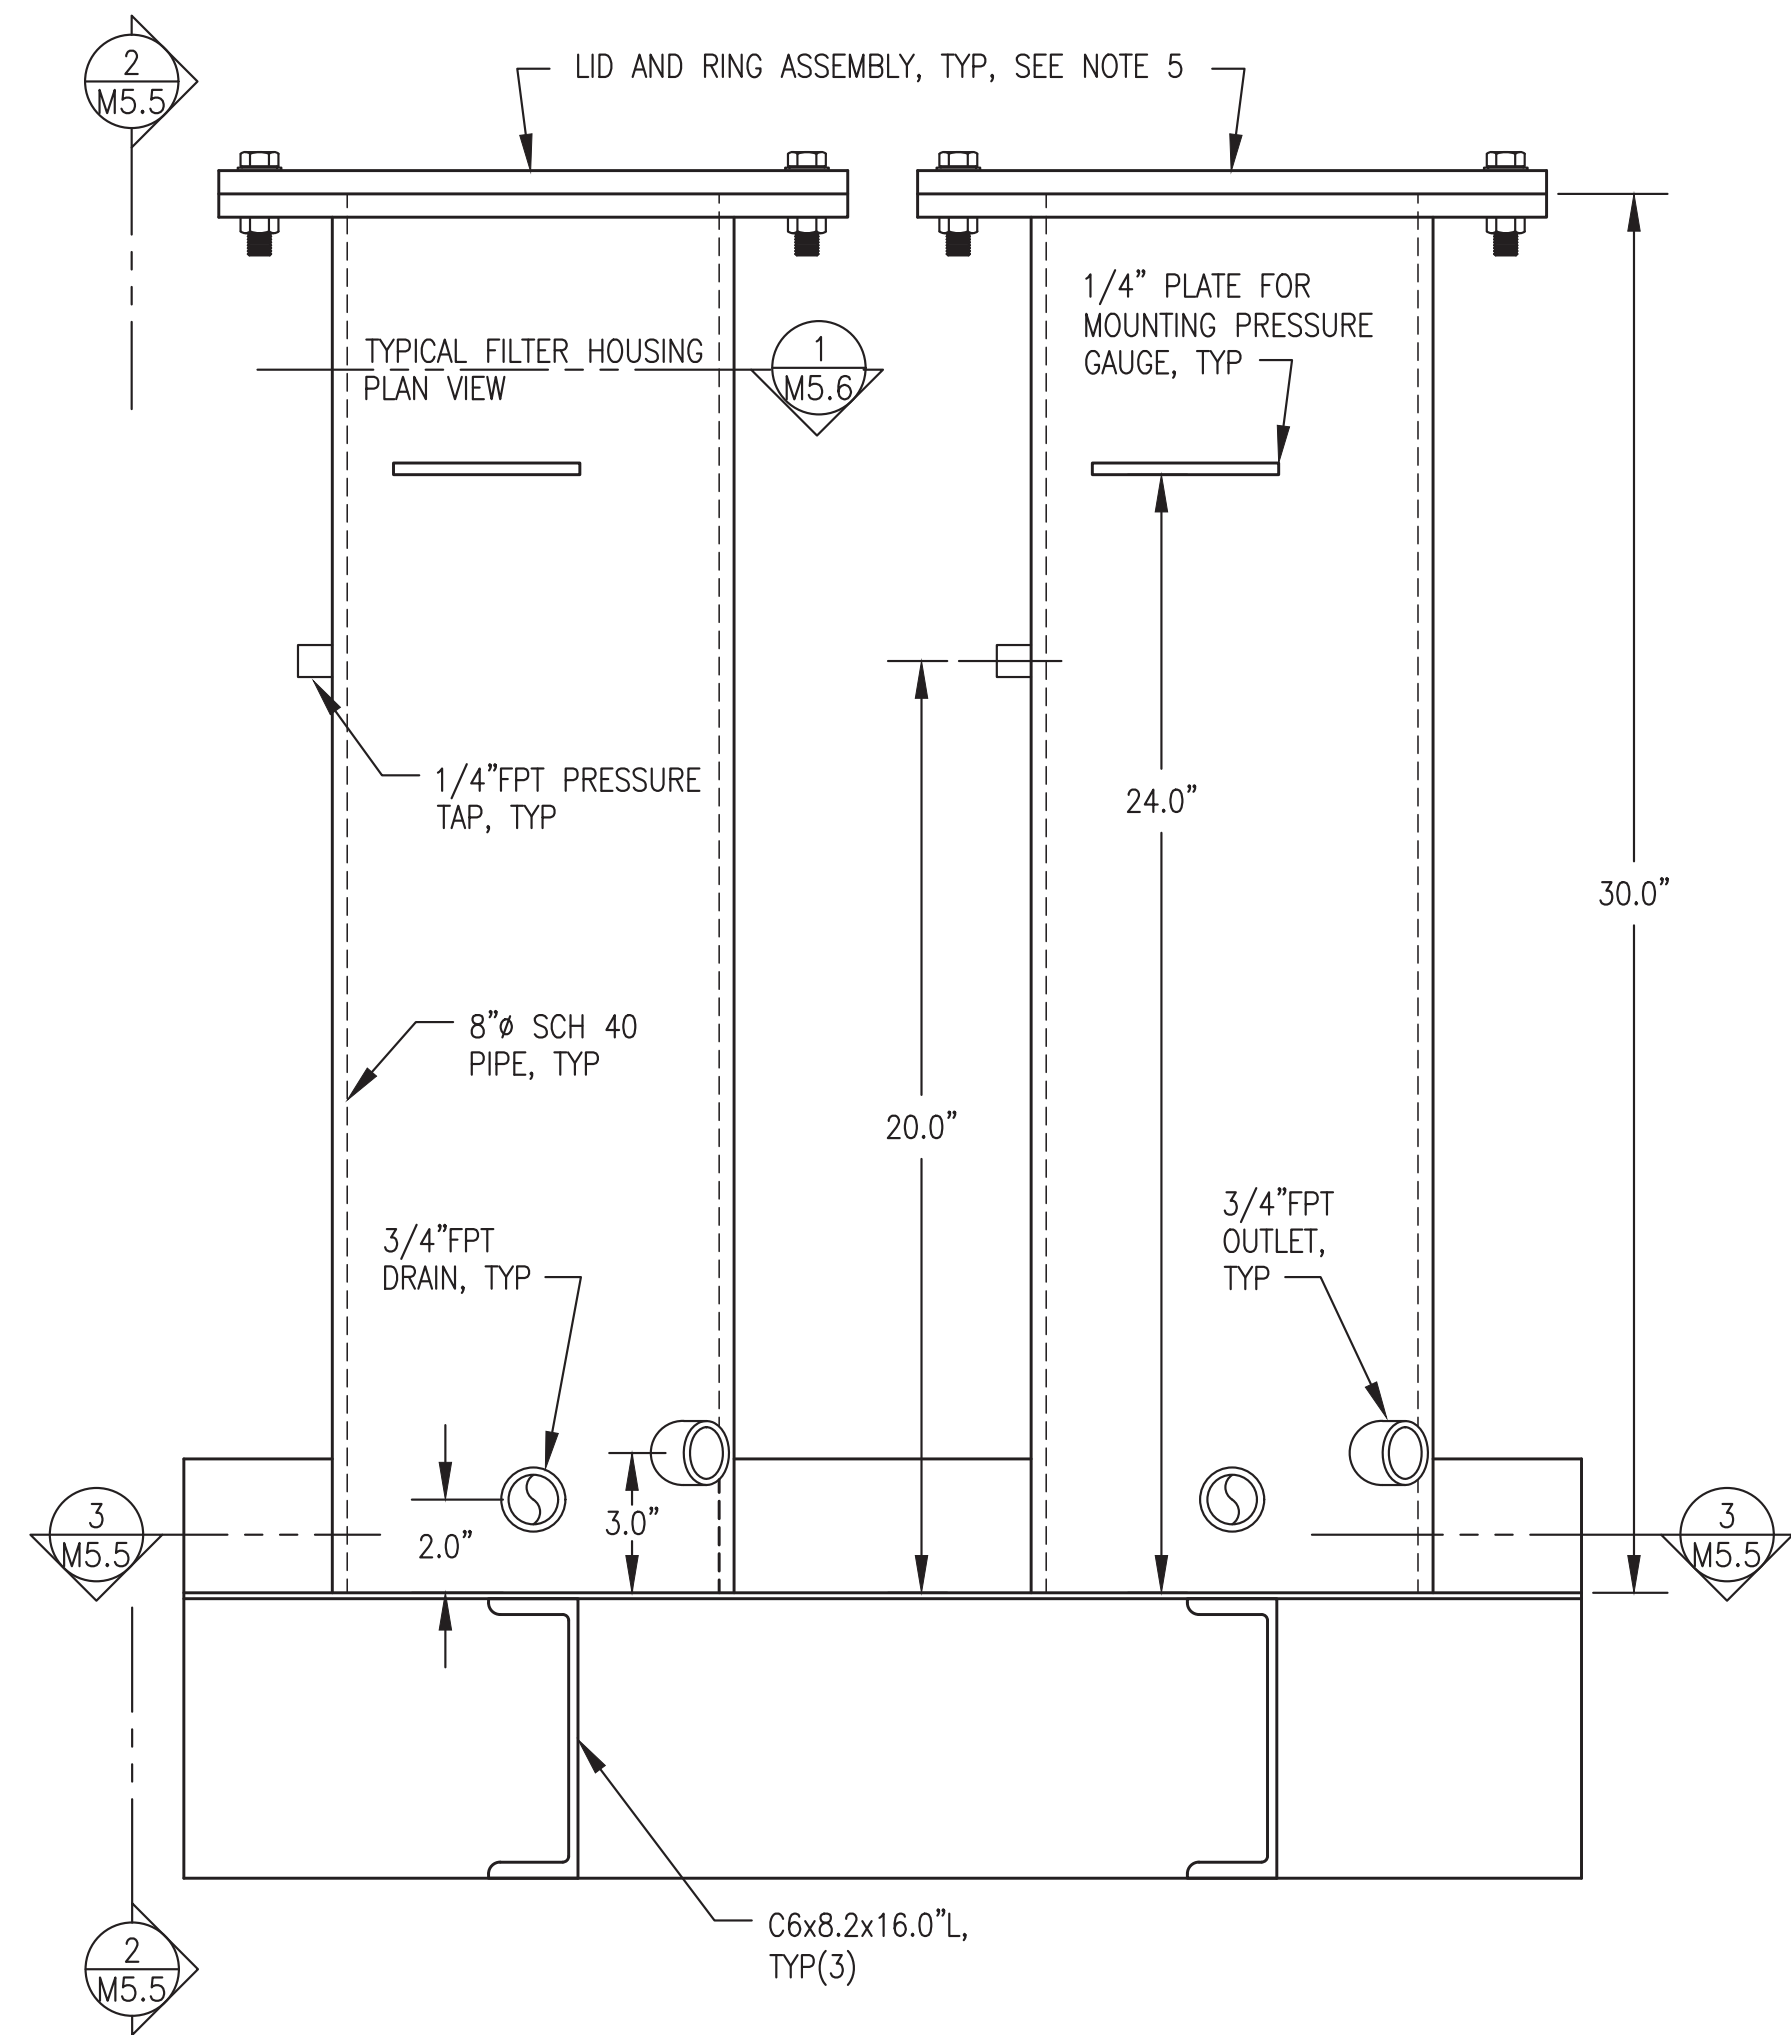
LEFT SIDE VIEW

**1 200 GALLON SINGLE WALL DAY TANK**  
M5.5 1"=6"


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		200 GALLON DAY TANK FABRICATION	
DRAWN BY: JTD	SCALE: AS NOTED	DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP_M2-M7	PROJECT NUMBER:	SHEET: <b>M5.4</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			



1 OIL FILTER BANK FRONT ELEVATION  
M5.5 1/4" = 1"

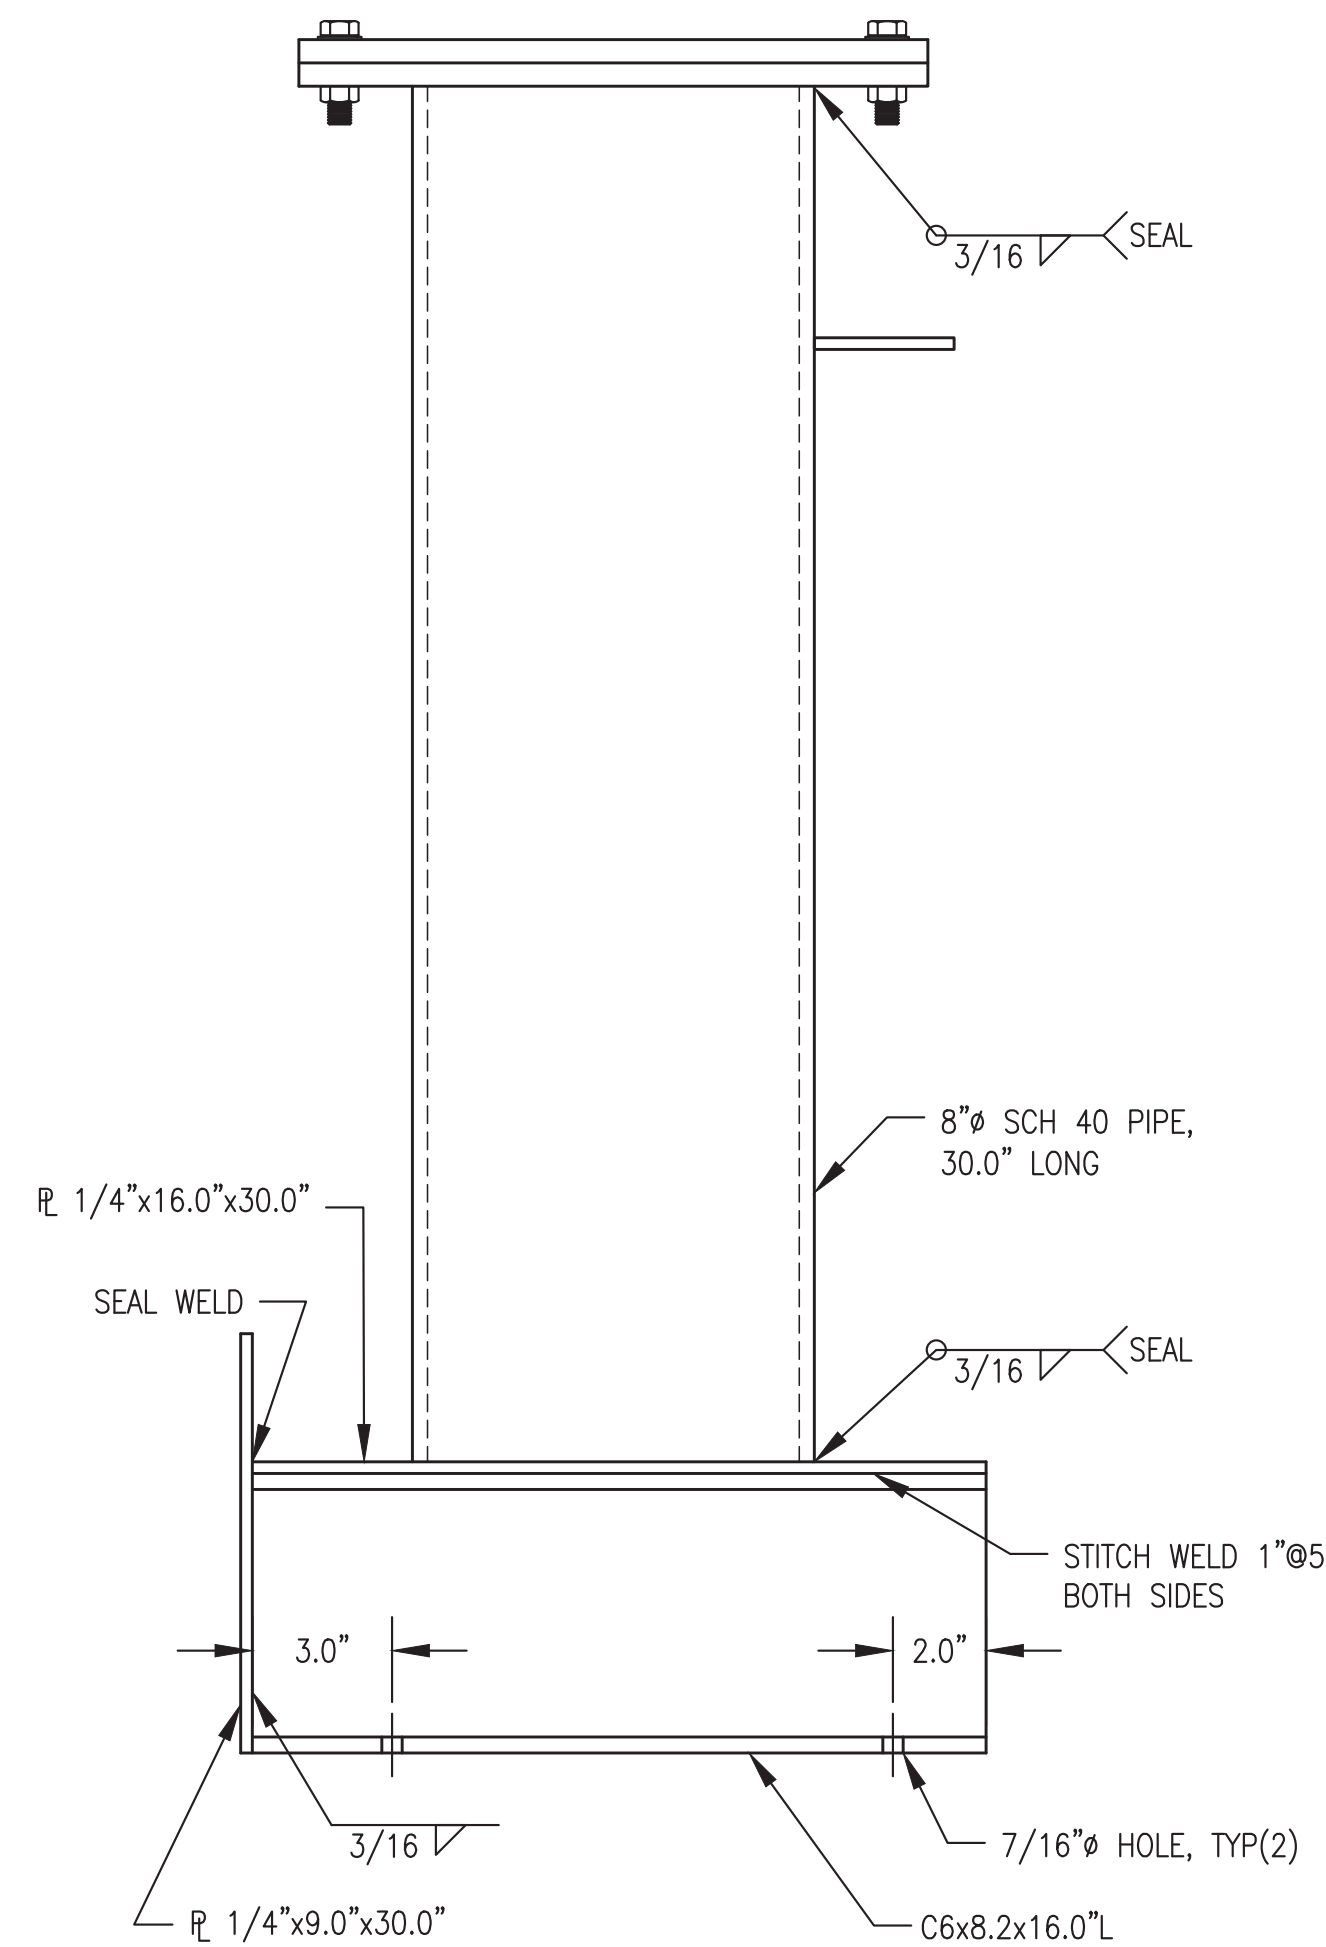

2 SECTION THROUGH FILTER & BASE  
M5.5 1/4" = 1"

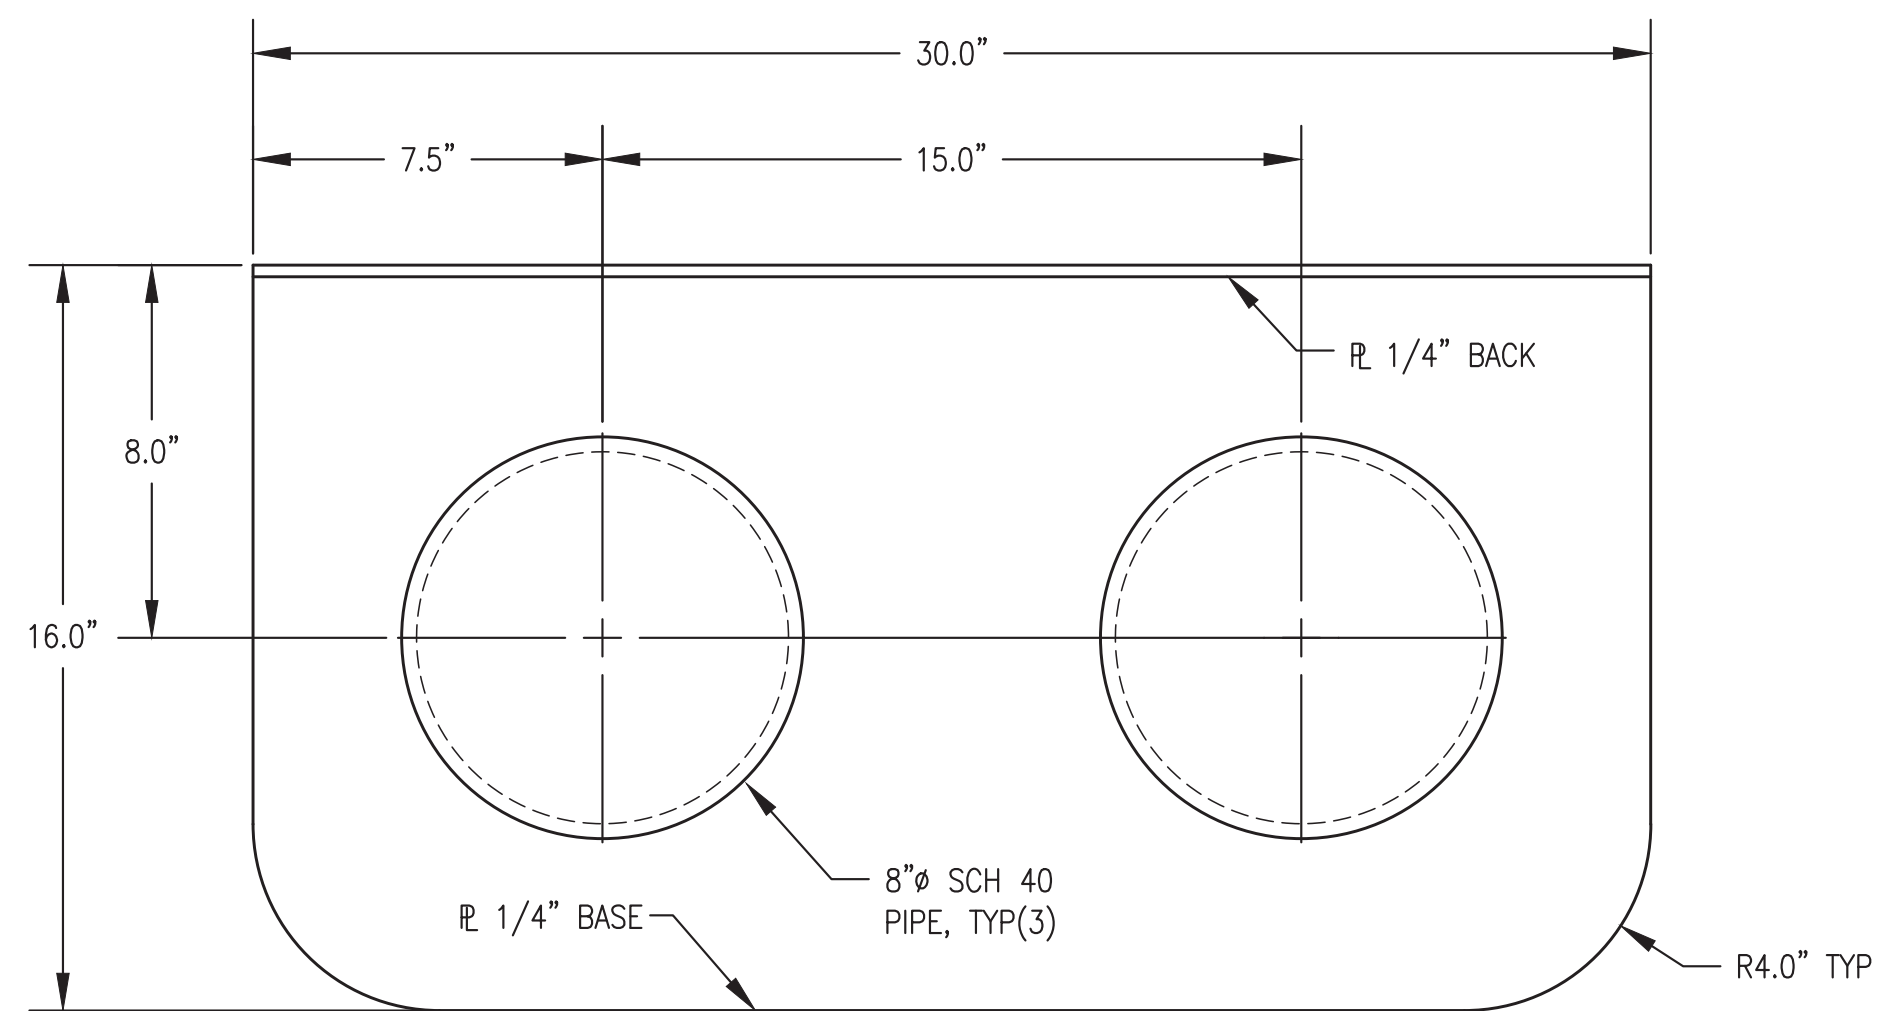


3 OIL FILTER BANK BASE PLAN  
M5.5 1/4" = 1"


FILTER BANK GENERAL NOTES:

1. FABRICATE TWO CHAMBER FILTER BANK AS INDICATED. SEE SHEET M5.5 FOR INTERNAL DETAILS.
2. FABRICATE FROM ASTM A-36 STEEL PLATE AND SHAPES AND ASTM A-53 PIPE. ALL JOINTS TO BE FULL CONTINUOUS SEAL WELDS EXCEPT WHERE SPECIFICALLY INDICATED OTHERWISE.
3. PROVIDE WITH ALL OPENINGS AND ATTACHMENTS INDICATED. INSTALL MINIMUM 3,000# FORGED STEEL HALF COUPLINGS FOR ALL FPT OPENINGS IN ACCORDANCE WITH UL 142 FIGURE 7.1 - #2.
4. PRESSURE TEST COMPLETED ASSEMBLY TO MINIMUM 50 PSIG USING SOAPY WATER SOLUTION ON ALL WELD JOINTS.
5. UPON COMPLETION OF FABRICATION, ROUND ALL CORNERS AND SHARP EDGES. SANDBLAST TANK EXTERIOR AND ALL ATTACHMENTS IN ACCORDANCE WITH SSPC-SP-6. PAINT WITH TWO COATS EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, COLOR ANSI 61 GRAY.
6. AFTER PAINTING REMOVE LID, WIRE BRUSH MATING SURFACES OF LID AND RING TO REMOVE ALL PAINT AND POLISH SURFACES SMOOTH. APPLY A LIGHT COAT OF GREASE OR ANTI-SIEZE PASTE TO BOTH FACES PRIOR TO INSTALLING GASKET. INSTALL 13.5" O.D. FULL-FACED 1/4" BUNA-N RUBBER GASKET (ALASKA RUBBER OR EQUAL) ON FILTER LIDS.
7. FURNISH FASTENERS AS INDICATED AND COAT WITH ANTI-SIEZE.
8. PRESSURE TEST EACH FILTER HOUSING ASSEMBLY TO 50 PSIG MINIMUM.
9. UPON COMPLETION FLUSH INTERIOR OF TANK TO REMOVE ALL DIRT AND DEBRIS, AIR DRY INTERIOR, AND SEAL ALL TANK OPENINGS WITH PLASTIC PLUGS.


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022





1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		USED OIL BLENDER FILTER BANK LAYOUT & CONFIGURATION	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM PP M2-M7		SHEET:	
PROJECT NUMBER:		<b>M5.5</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

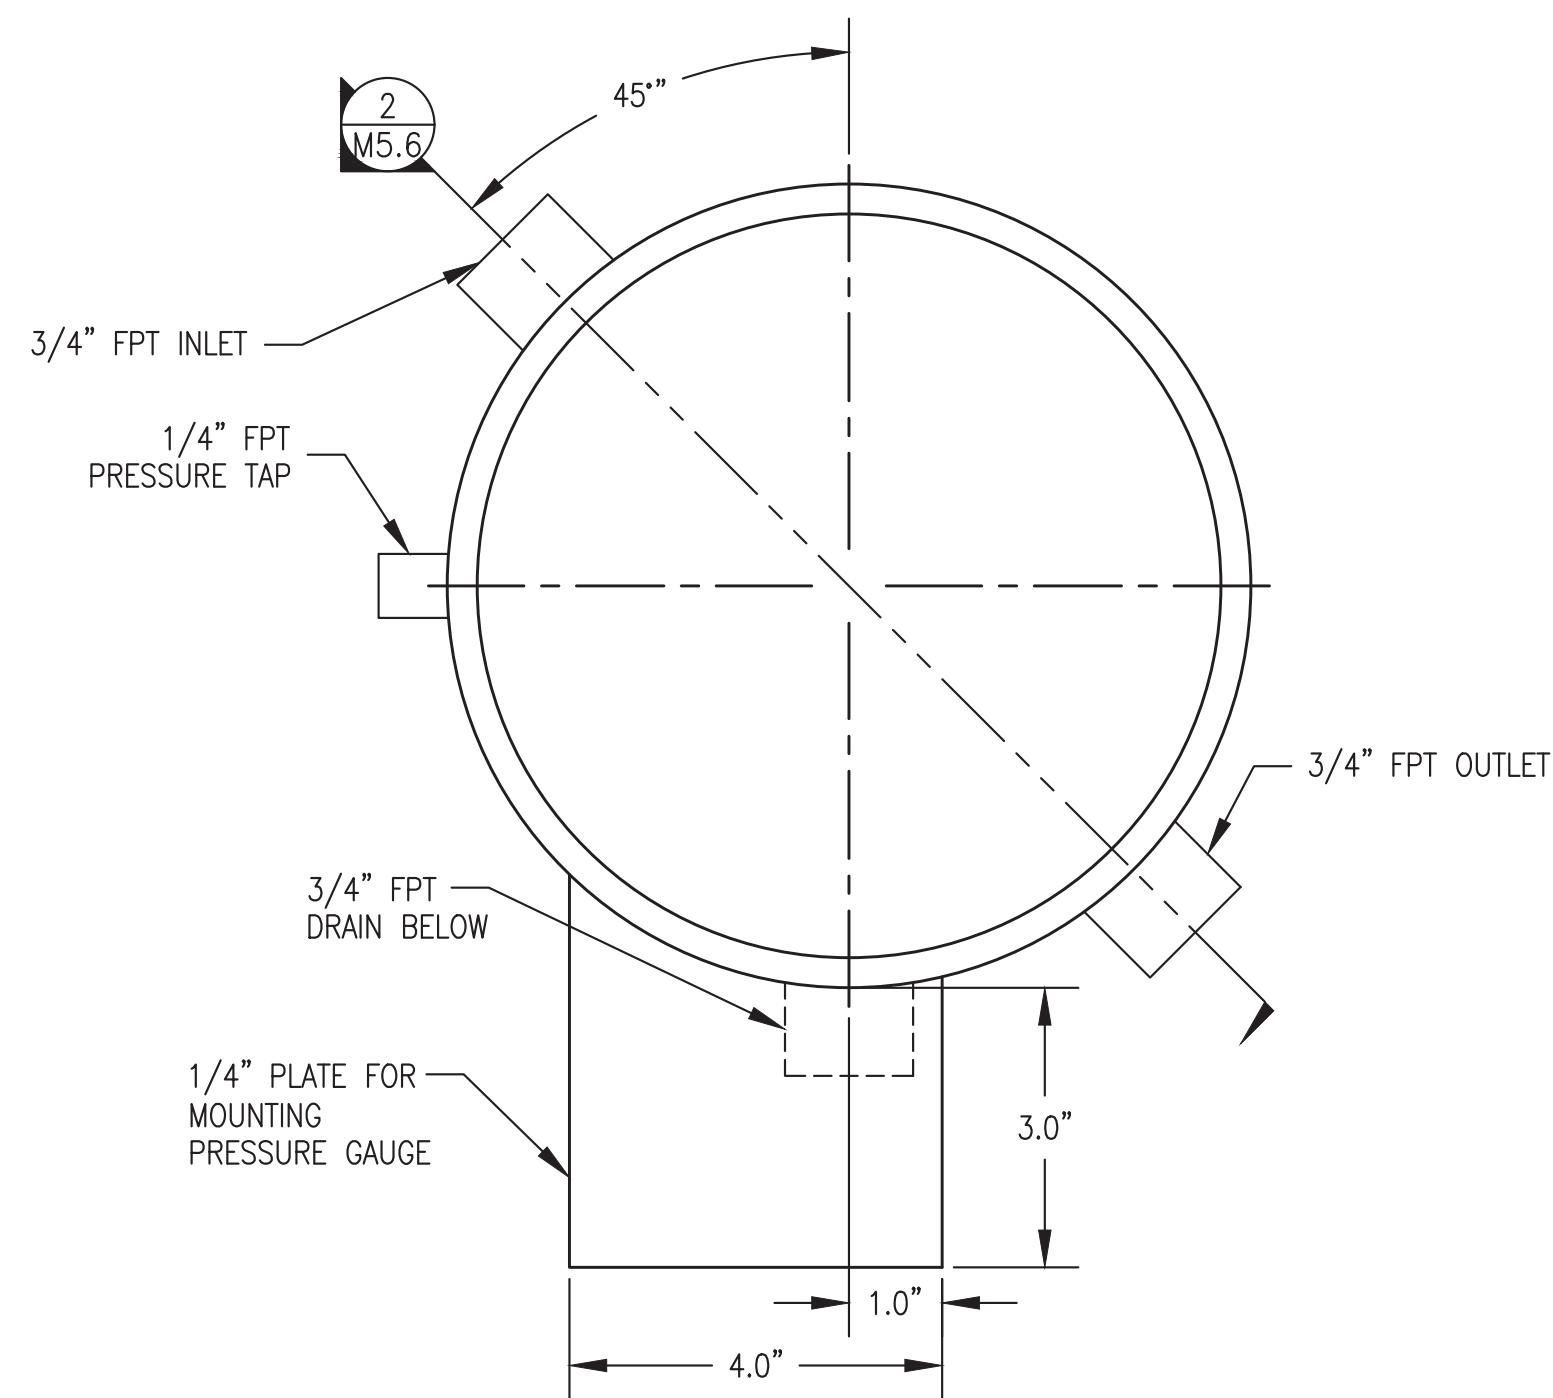


**1** TYPICAL FILTER HOUSING – PLAN VIEW  
M5.6 1/2" = 1"

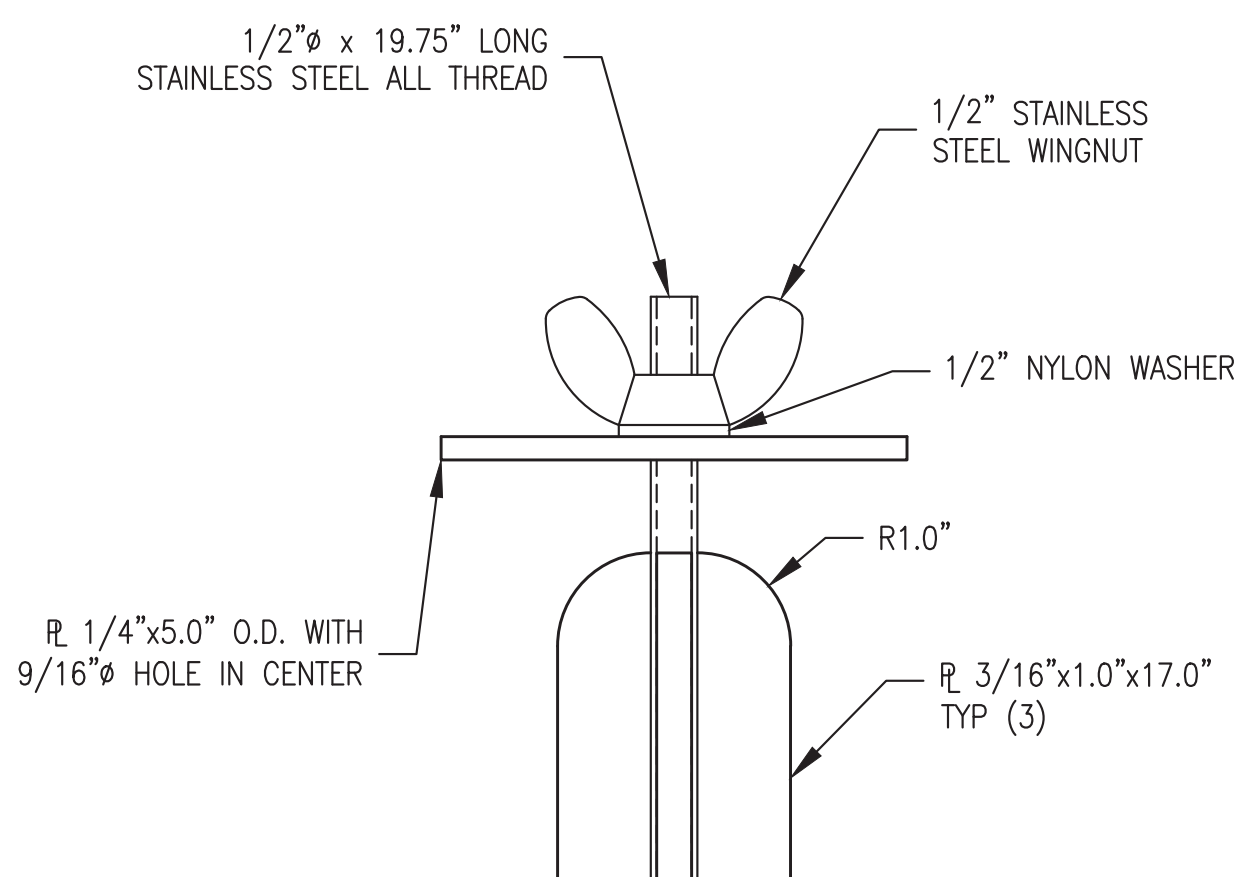


**3** ELEMENT RETAINER CAP  
M5.6 1/2" = 1"

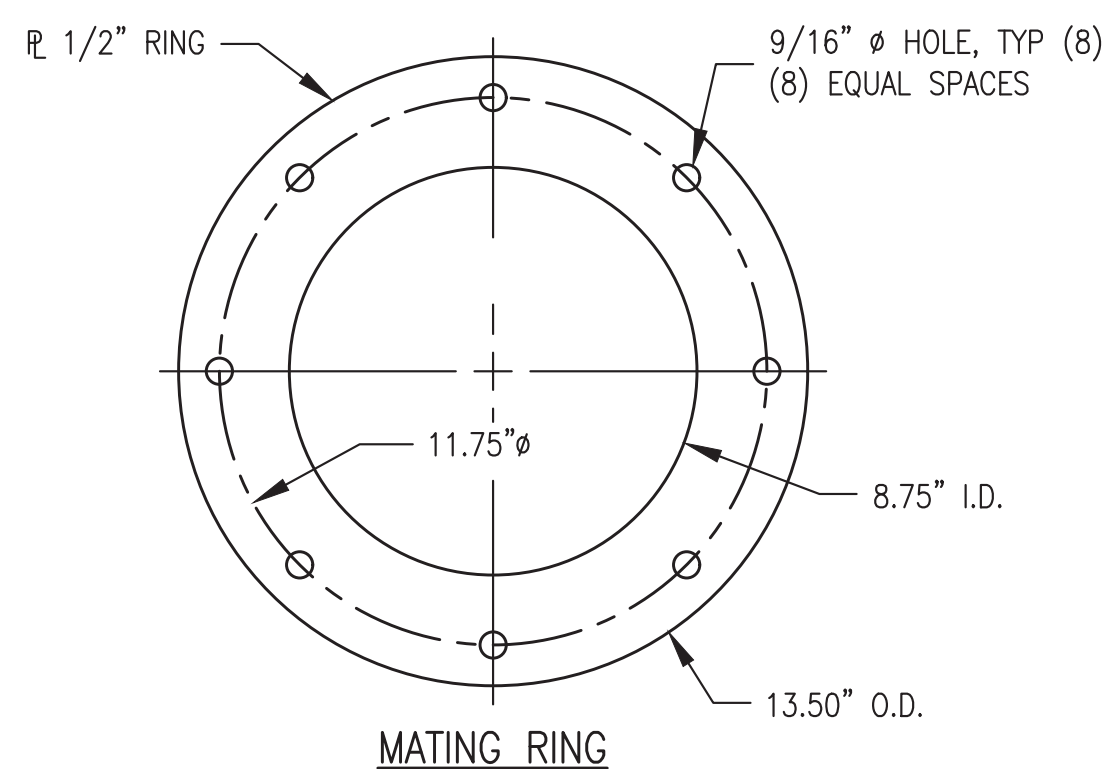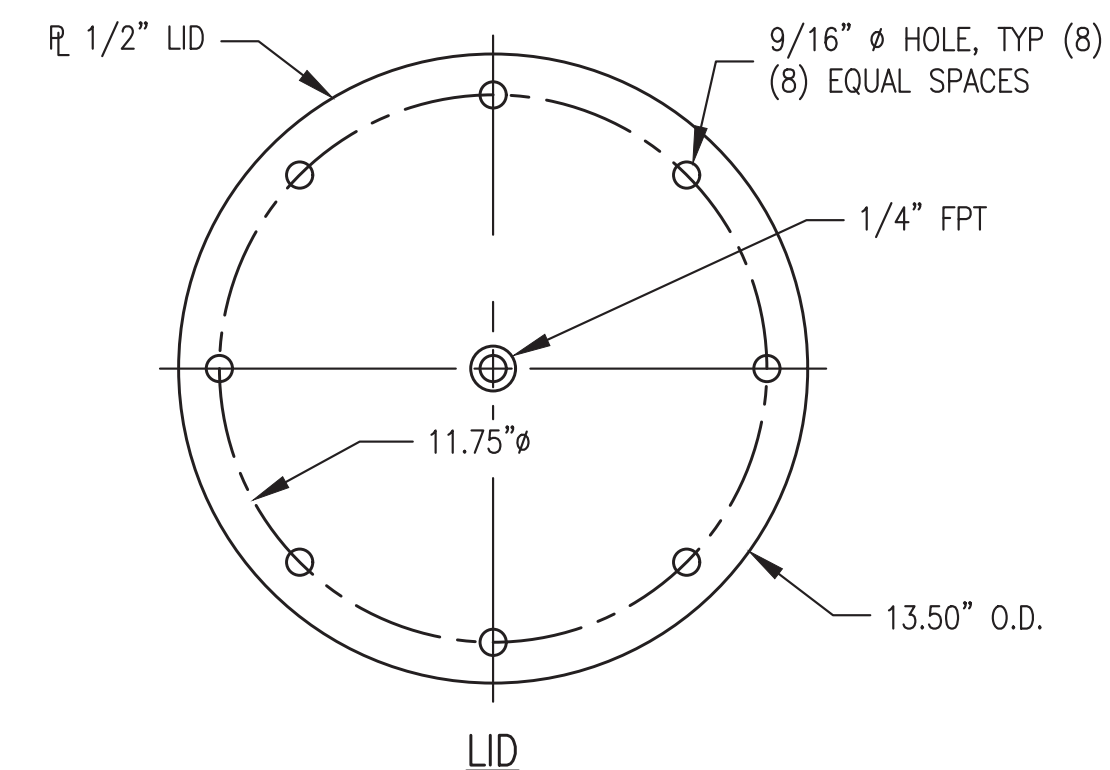


**6** LID & MATING RING – PLAN VIEW  
M5.6 1/4" = 1"

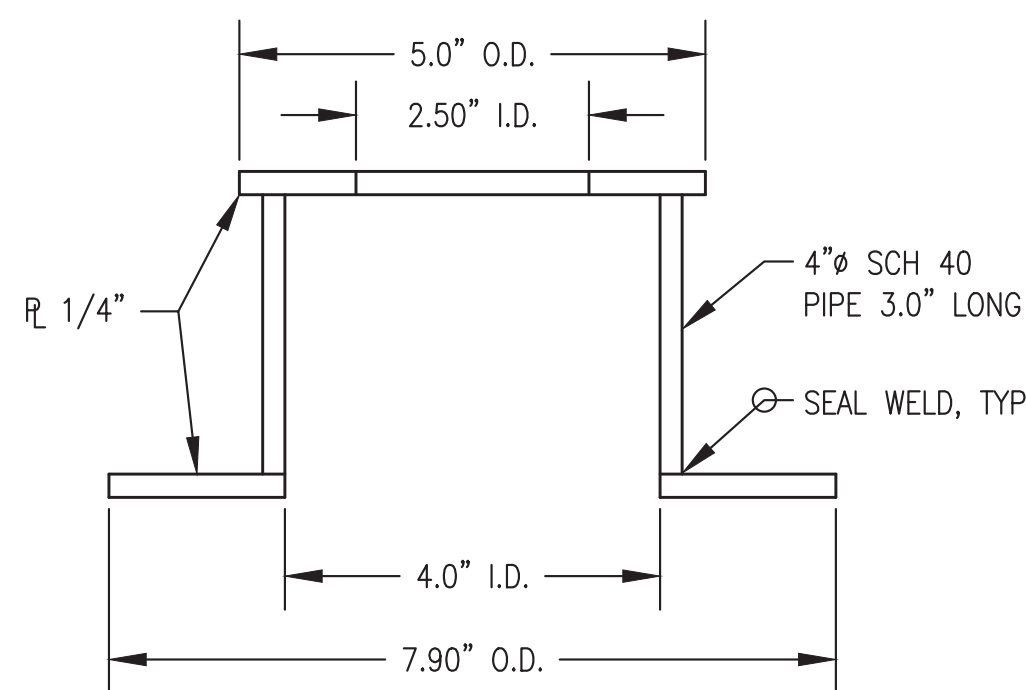

**4** ELEMENT BASE STAND  
M5.6 1/2" = 1"

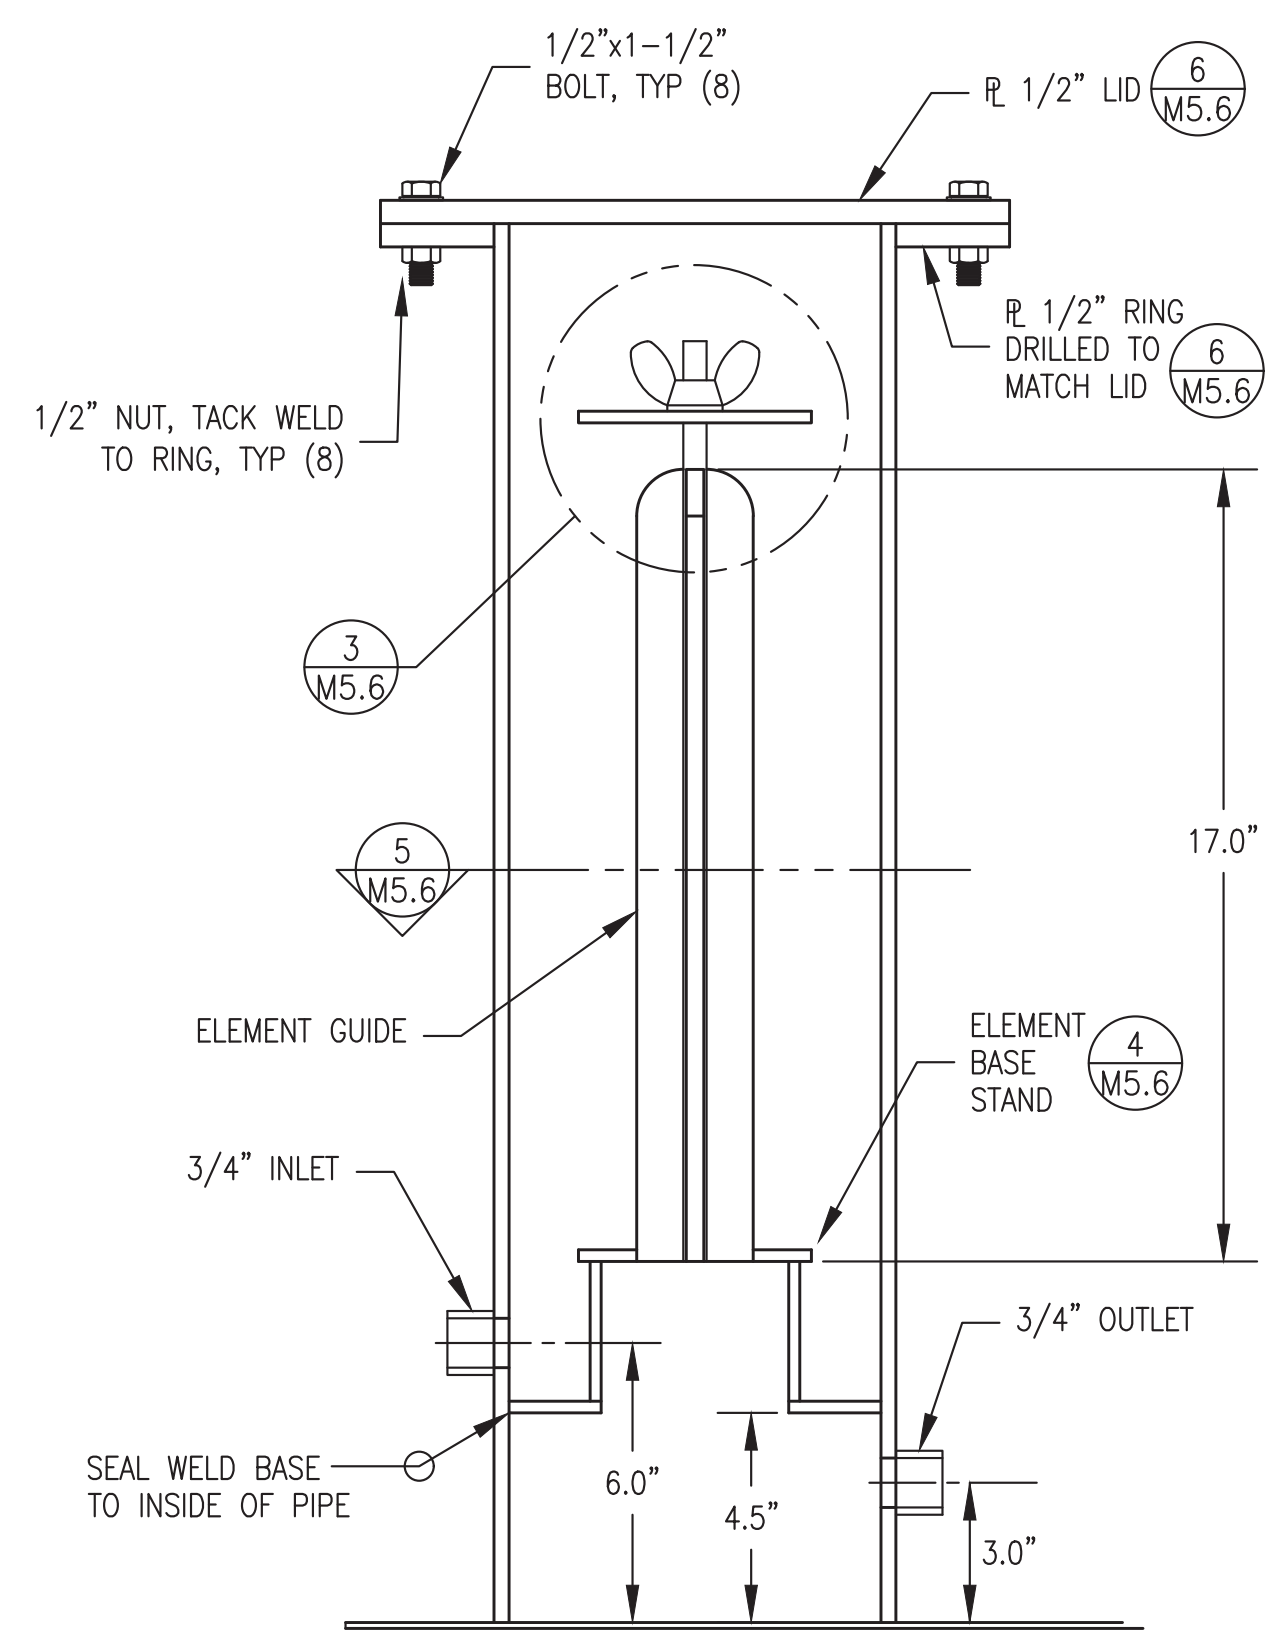


**2** TYPICAL SECTION THROUGH FILTER HOUSING  
M5.6 1/4" = 1"

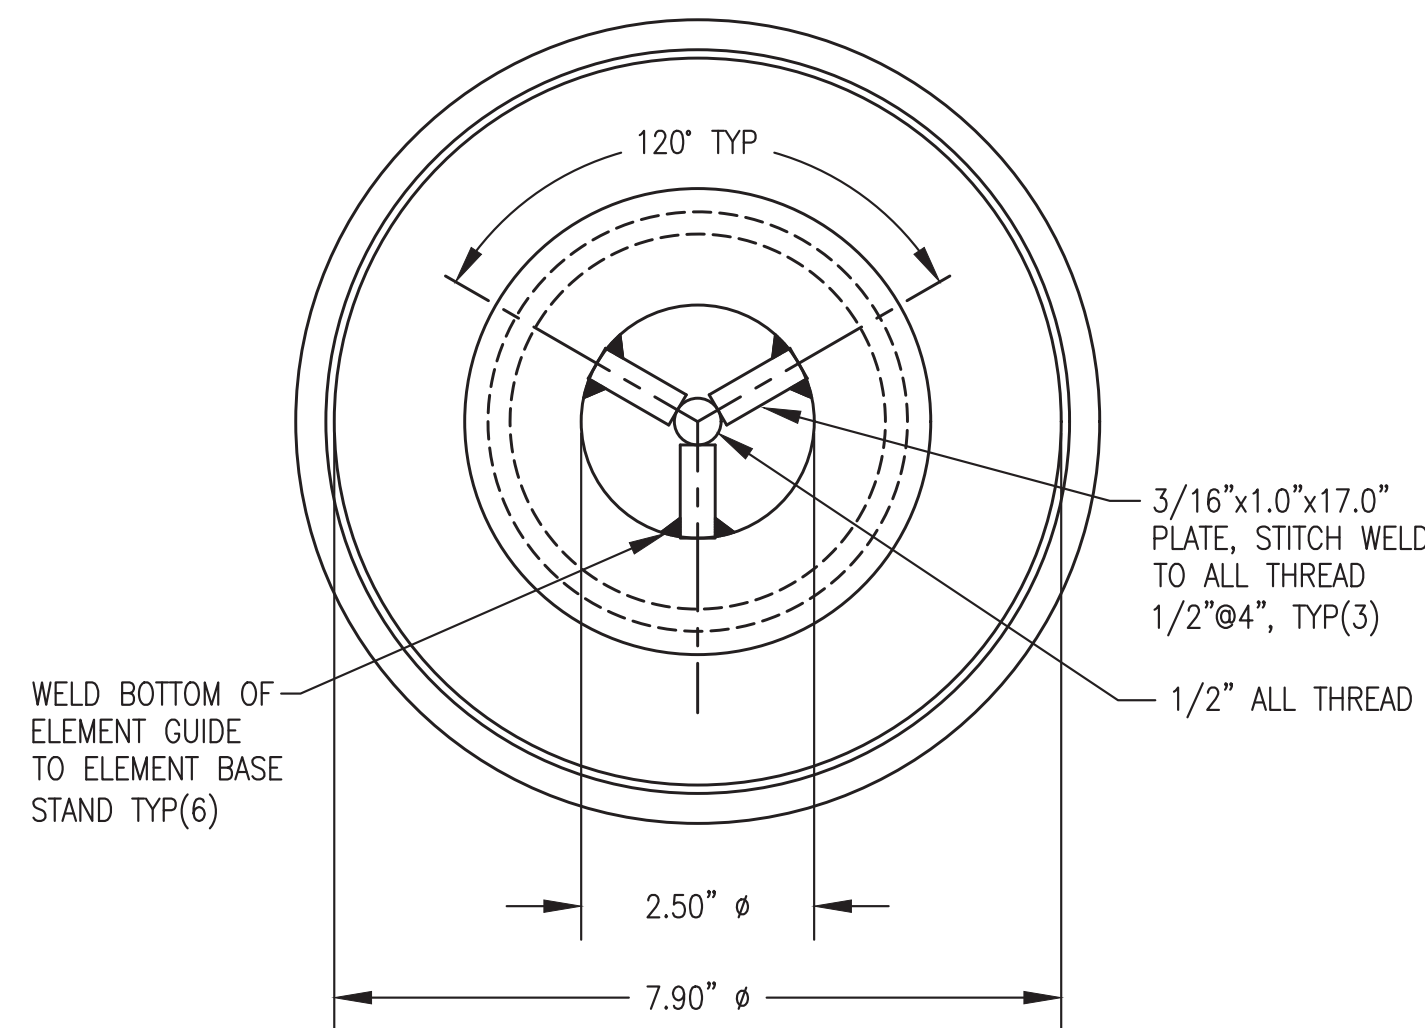

**5** SECTION THROUGH ELEMENT GUIDE  
M5.6 1/2" = 1"

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022










REV.	DESCRIPTION	DATE	BY
1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG

ALASKA ENERGY AUTHORITY

PROJECT: RAMPART POWER SYSTEM UPGRADE

TITLE: USED OIL BLENDER  
TYPICAL FILTER HOUSING DETAILS

DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: BCG	DATE: 3/15/22
FILE NAME: RAM_PP_M2-M7	SHEET: M5.6
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100	

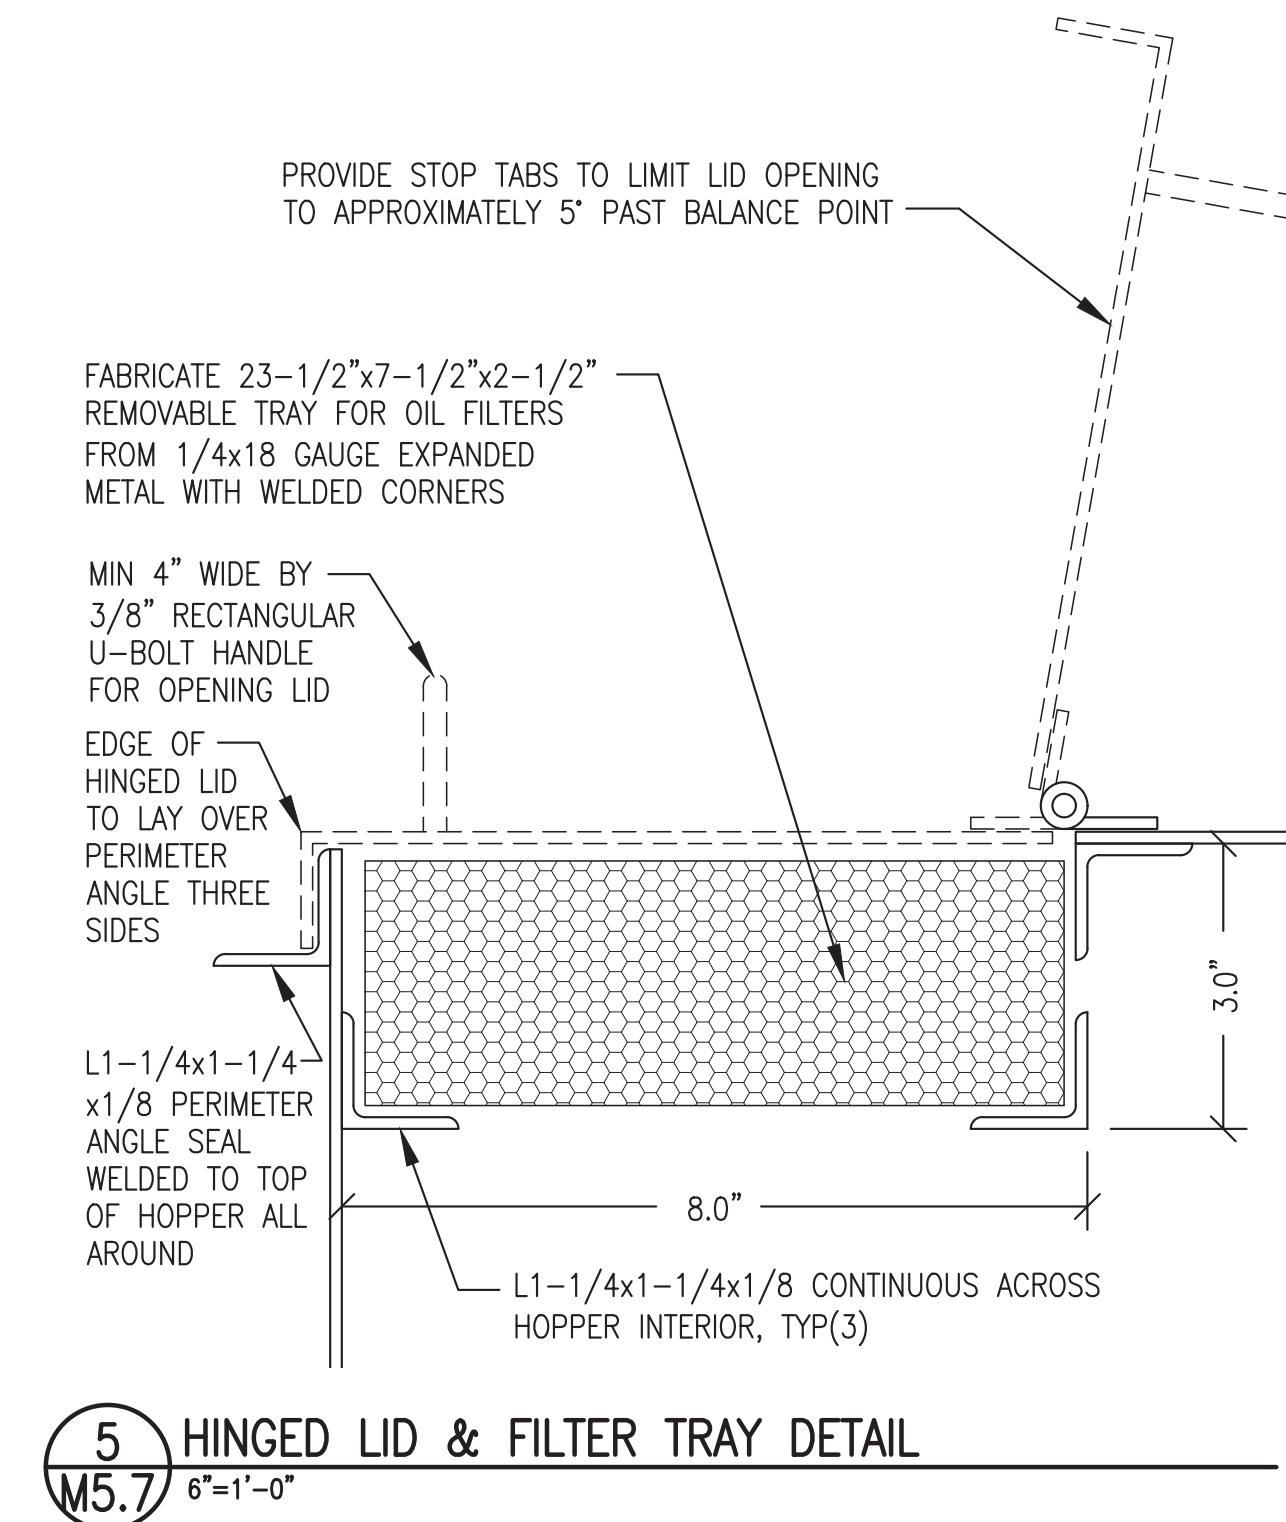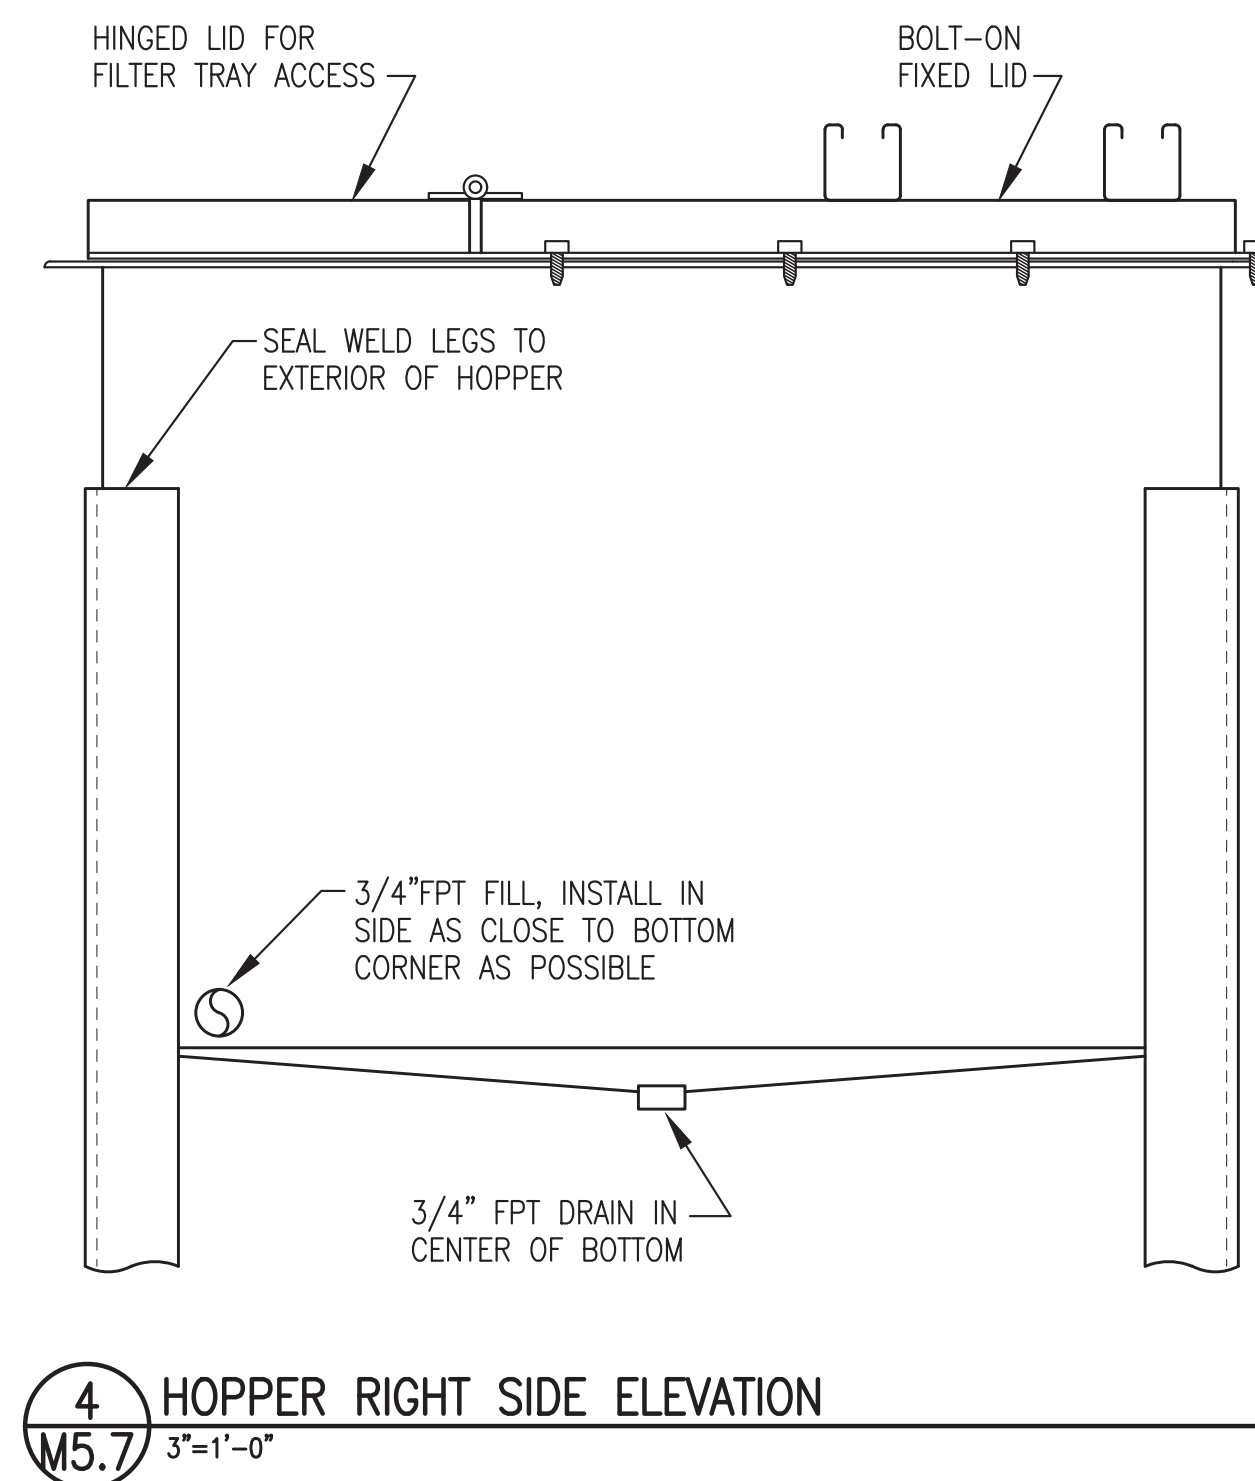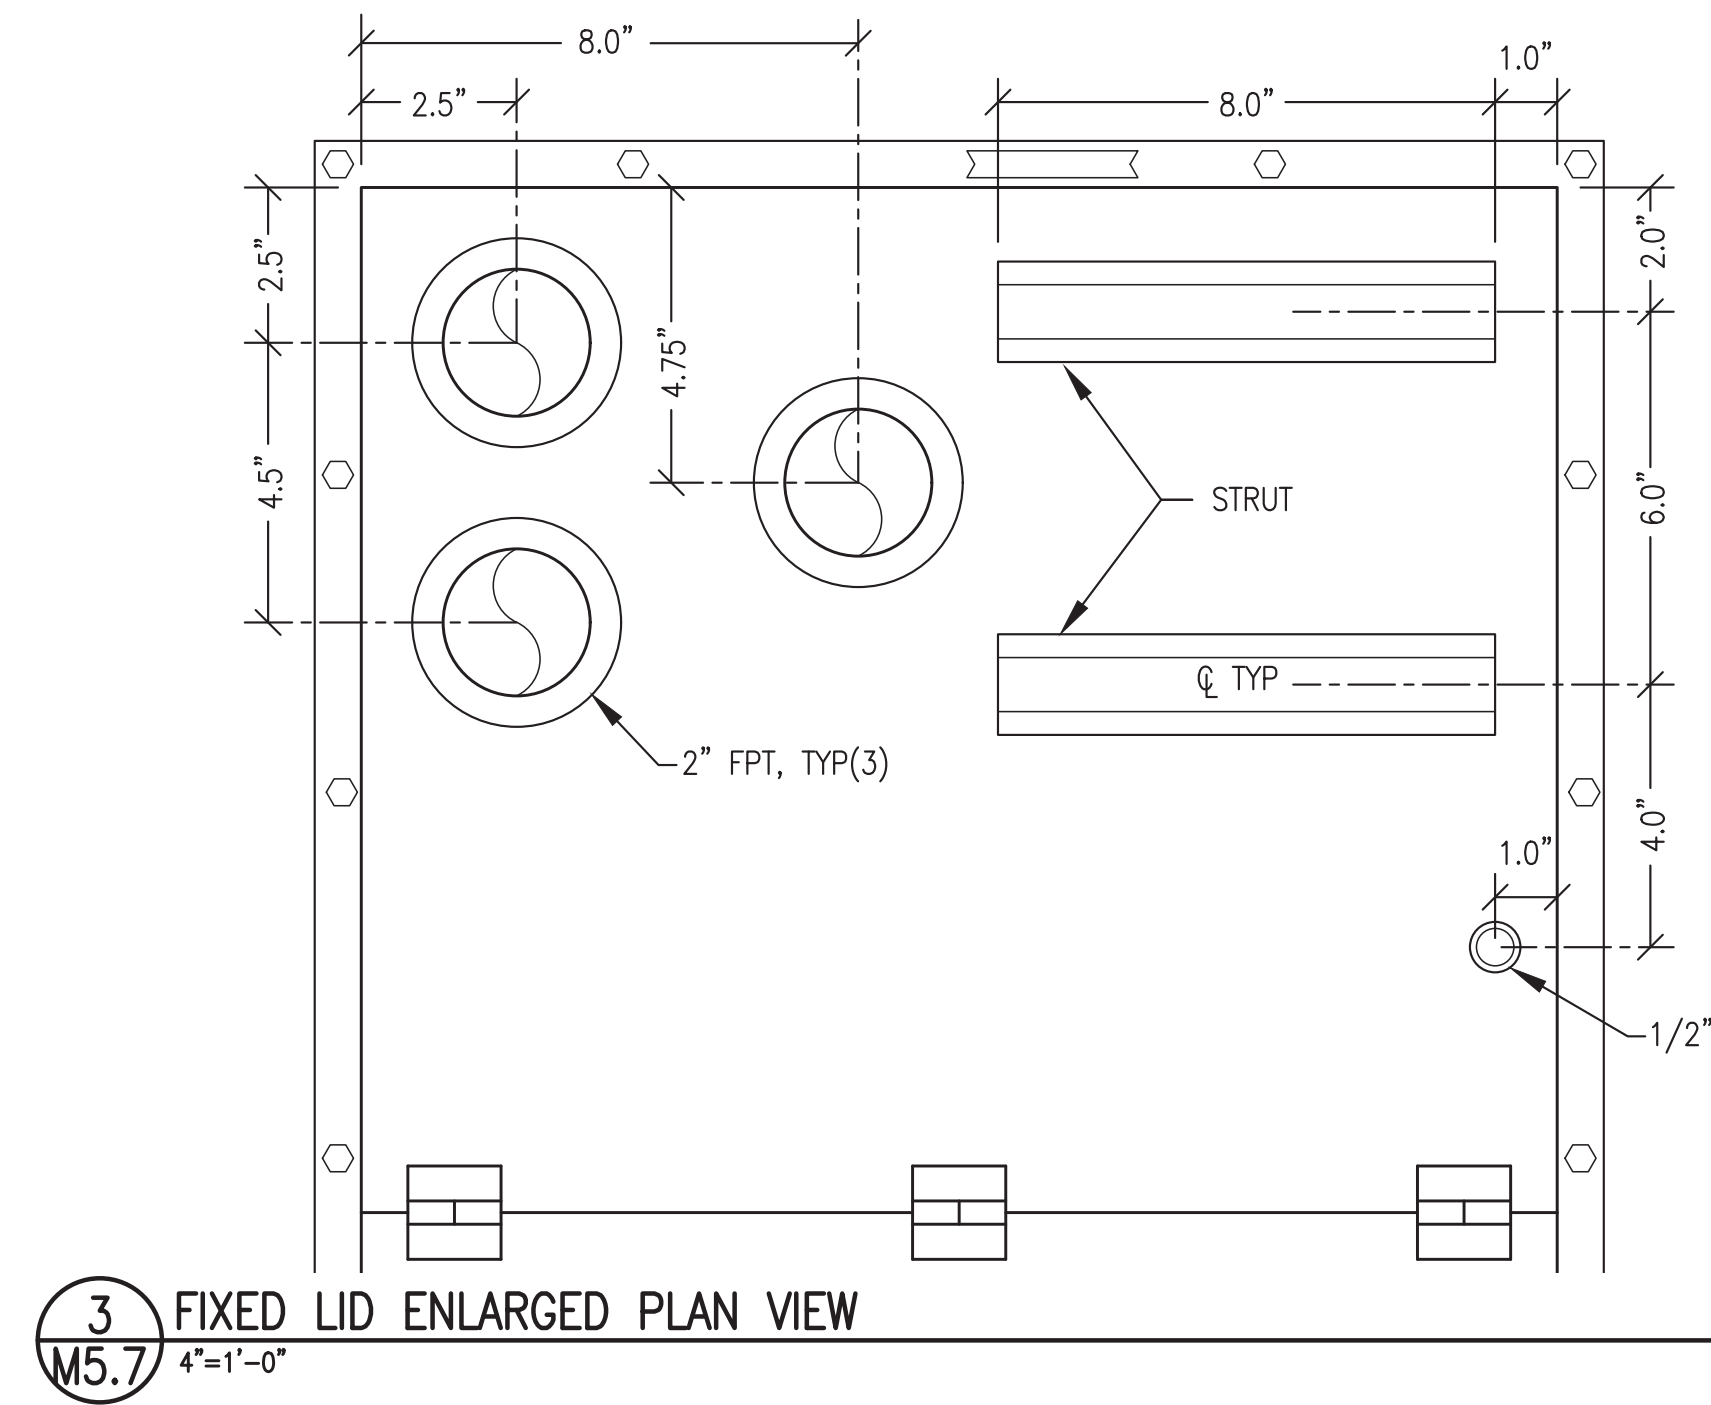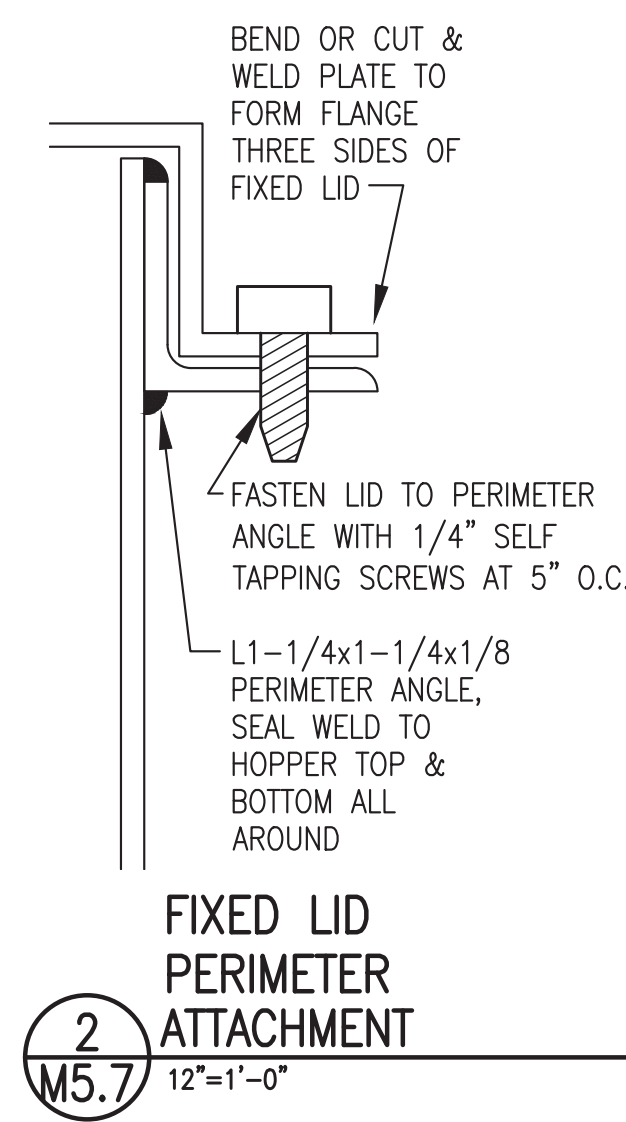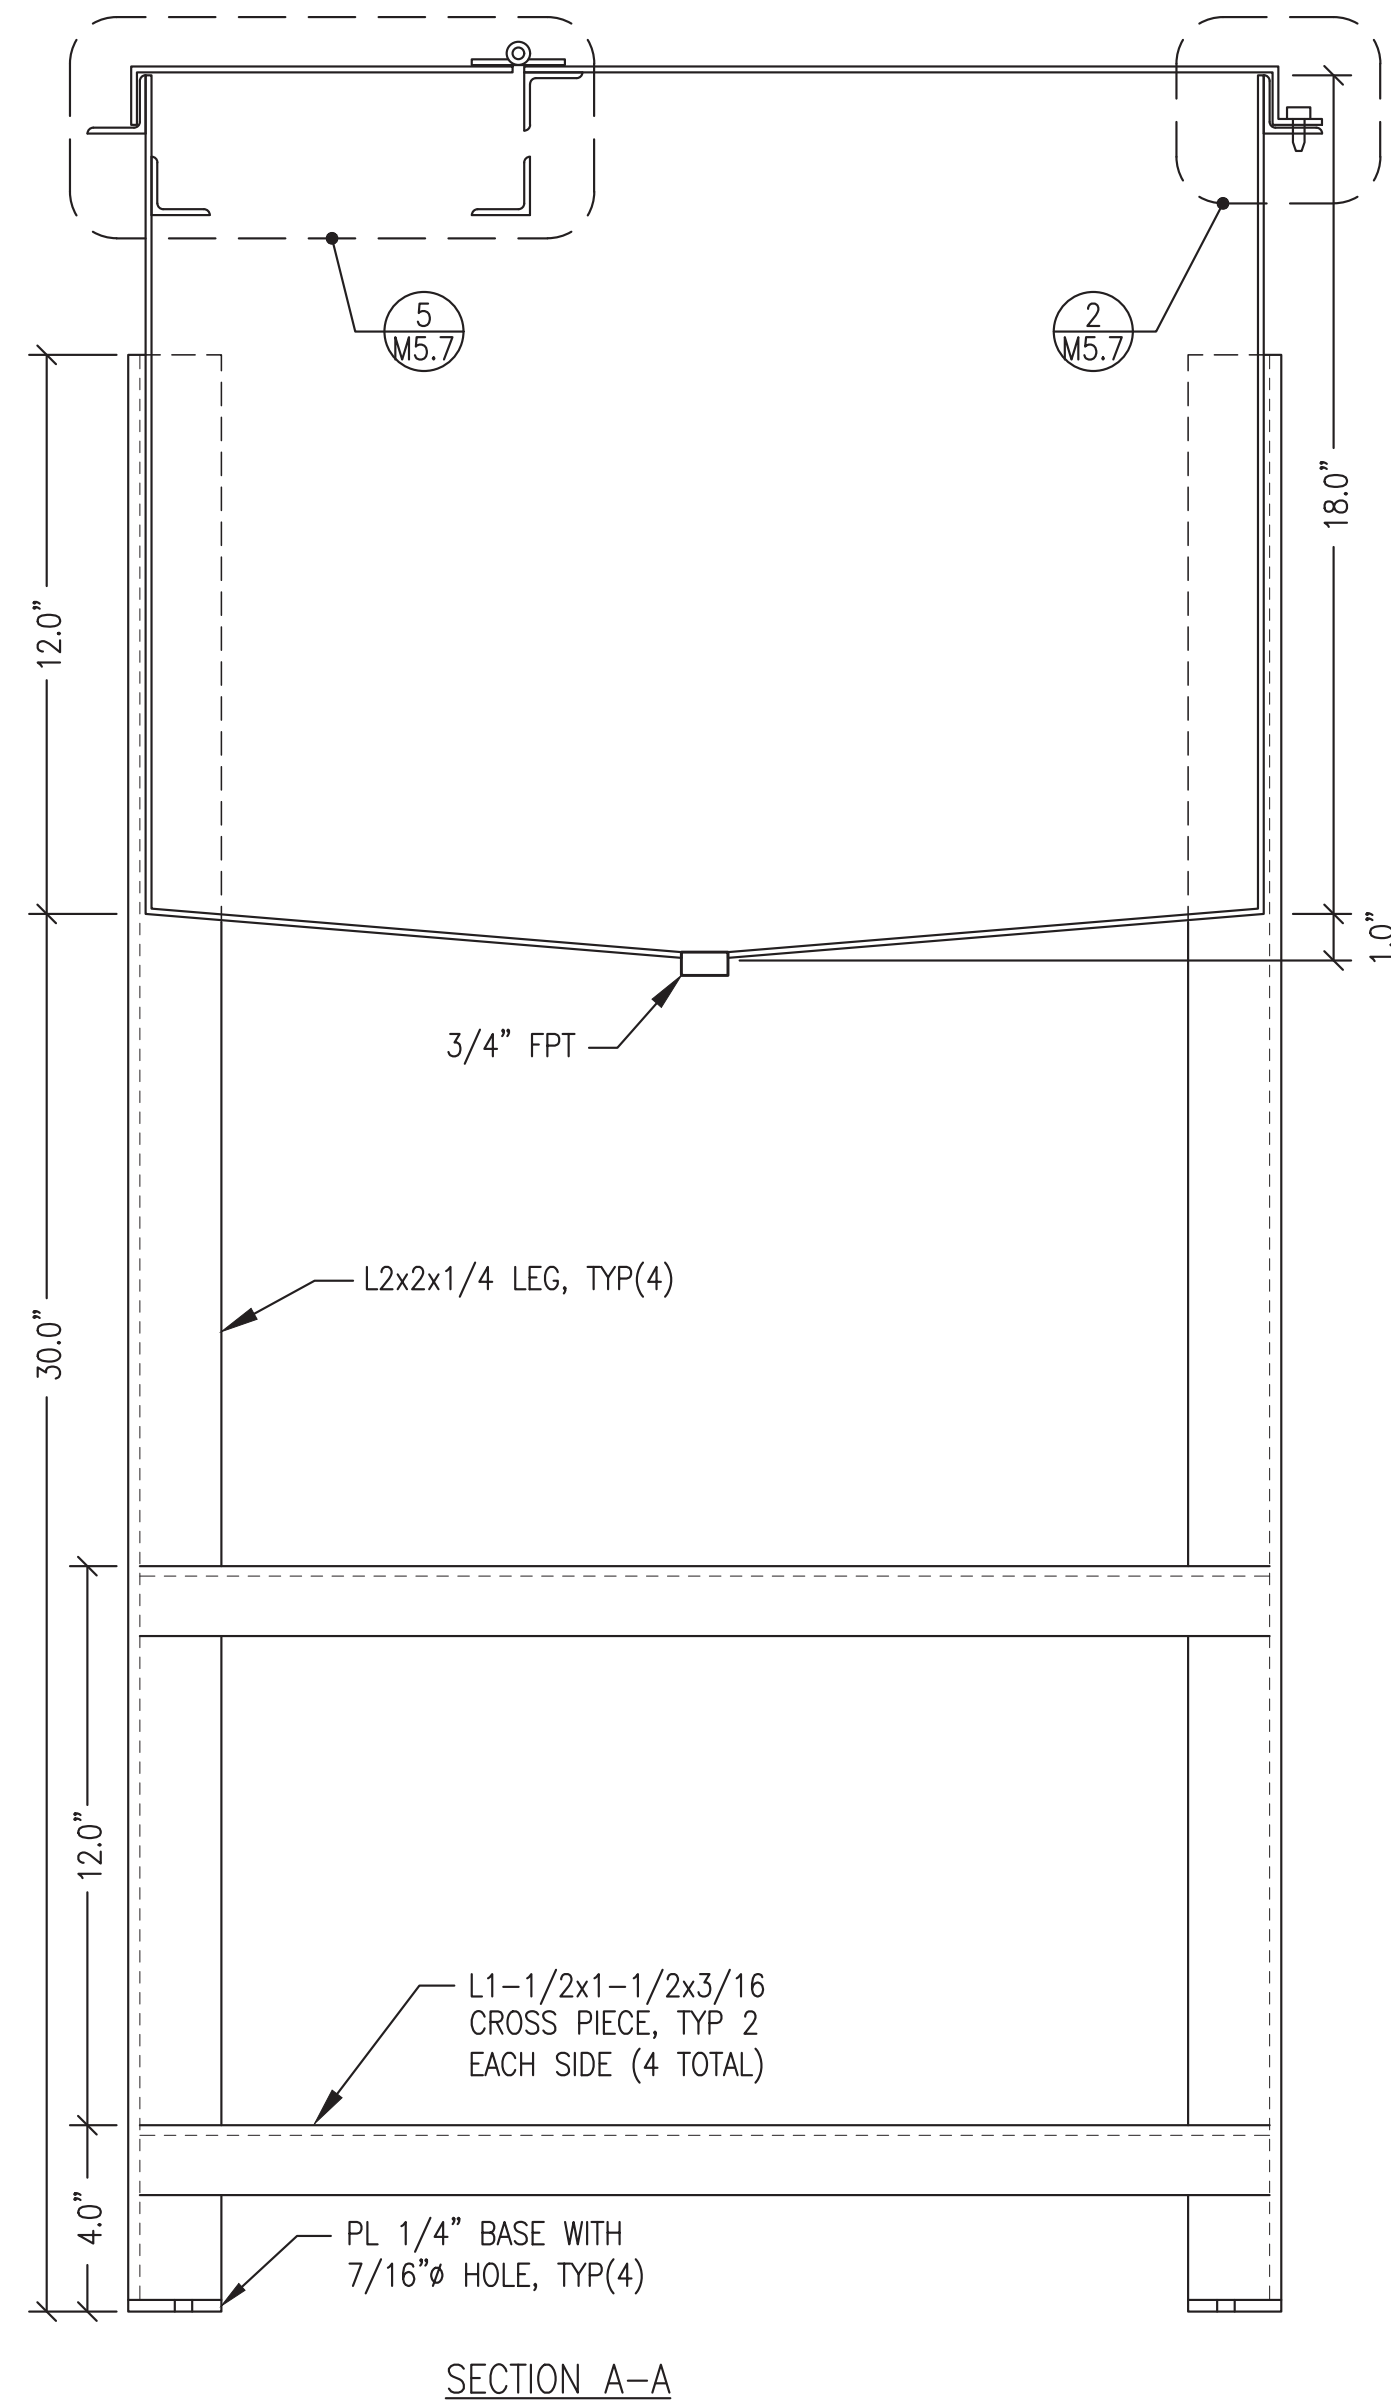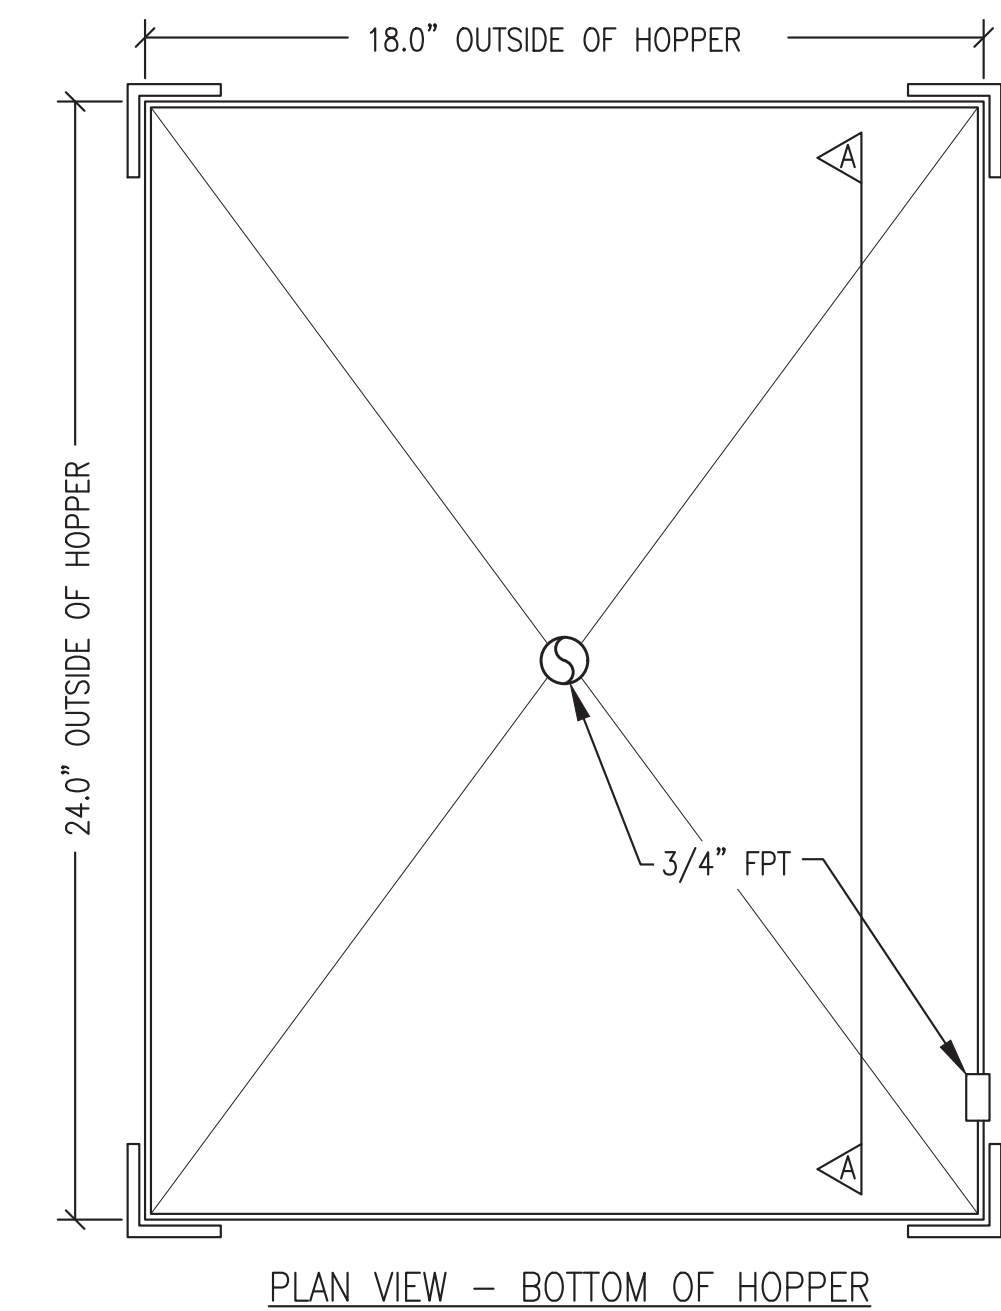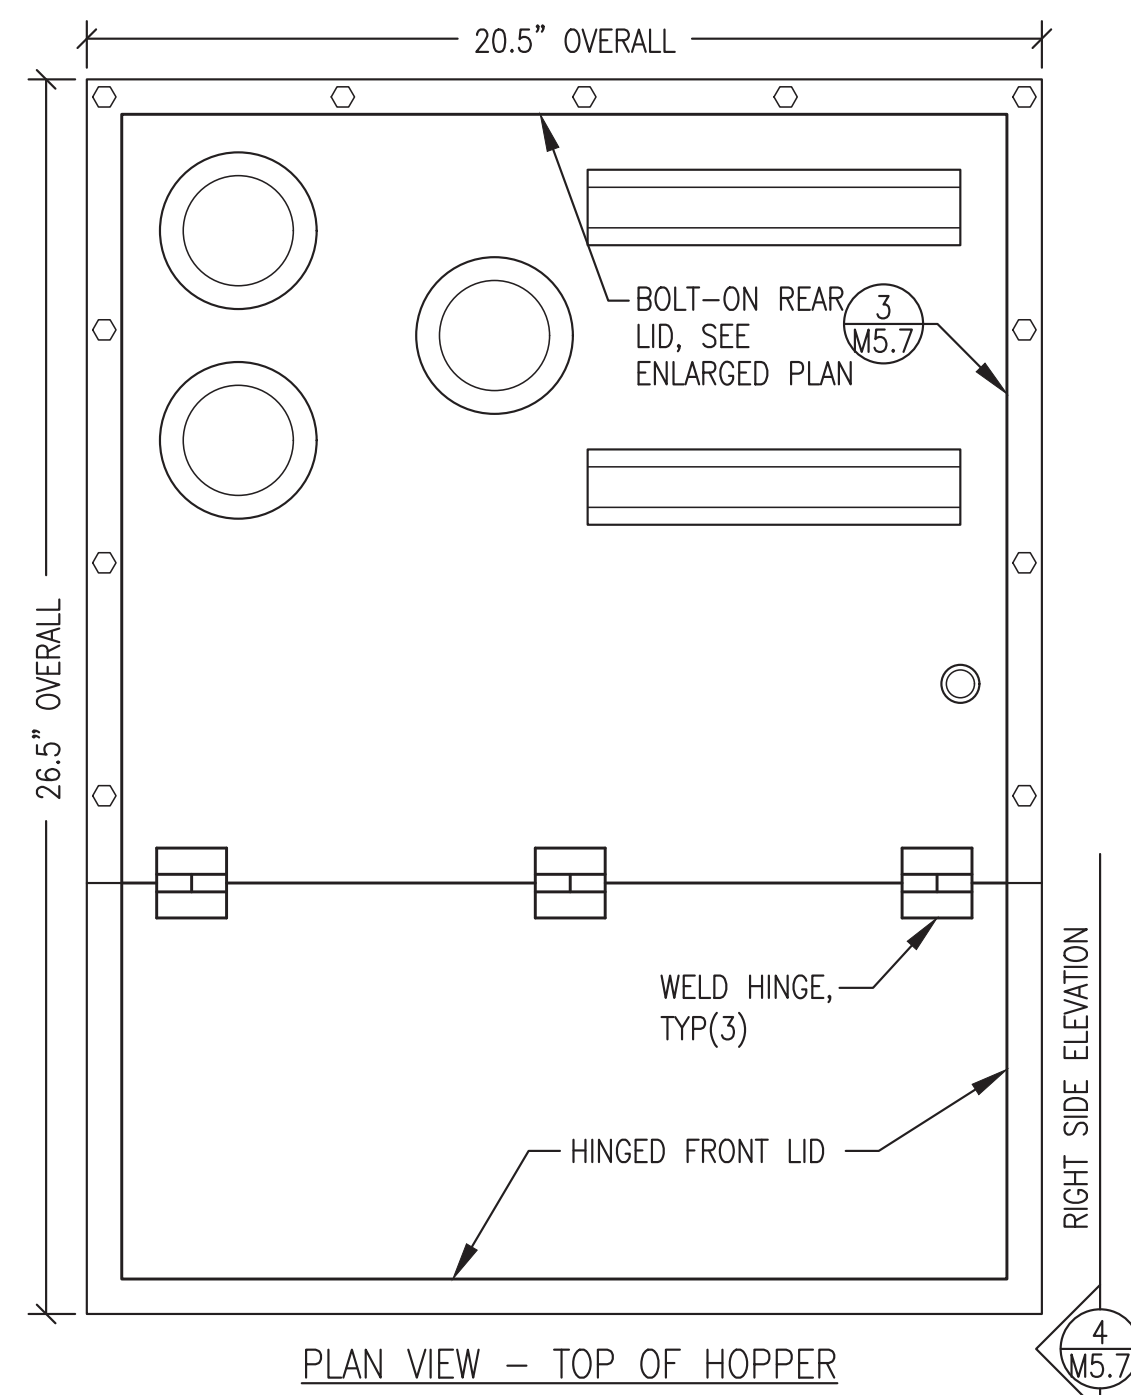


1 HOPPER PLAN & SECTION

M5.7 3'-1'-0"

FABRICATION NOTES:


- FABRICATE SINGLE WALL 25 GALLON USABLE CAPACITY HOPPER.
- FABRICATE FROM MINIMUM 10 GAUGE ASTM A-36 STEEL PLATE. ALL TANK SEAM JOINTS TO BE FULL CONTINUOUS WELDS. SEAL WELD ALL TANK ATTACHMENTS.
- PROVIDE WITH ALL OPENINGS AND ATTACHMENTS INDICATED. INSTALL ALL FPT OPENINGS IN ACCORDANCE WITH UL 142 FIGURE 7.1 - #1, #2, #4, OR #6. ALL STRUT TO BE 1-5/8"x1-5/8"x12 GA SOLID BACK PLAIN (BLACK), B-LINE B22 PLN OR EQUAL. FURNISH ALL FASTENERS AS INDICATED.
- UPON COMPLETION OF FABRICATION, ROUND ALL CORNERS AND SHARP EDGES. SANDBLAST TANK EXTERIOR AND ALL ATTACHMENTS IN ACCORDANCE WITH SSPC-SP-6. PAINT WITH TWO COATS EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, COLOR ANSI 61 GRAY.
- PRIOR TO SHIPPING, SEAL ALL FPT OPENINGS WITH PLASTIC OR STEEL PLUGS.

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
<p>ALASKA ENERGY AUTHORITY</p>			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: USED OIL BLENDER 25 GALLON HOPPER FABRICATION			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET: M5.7	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			



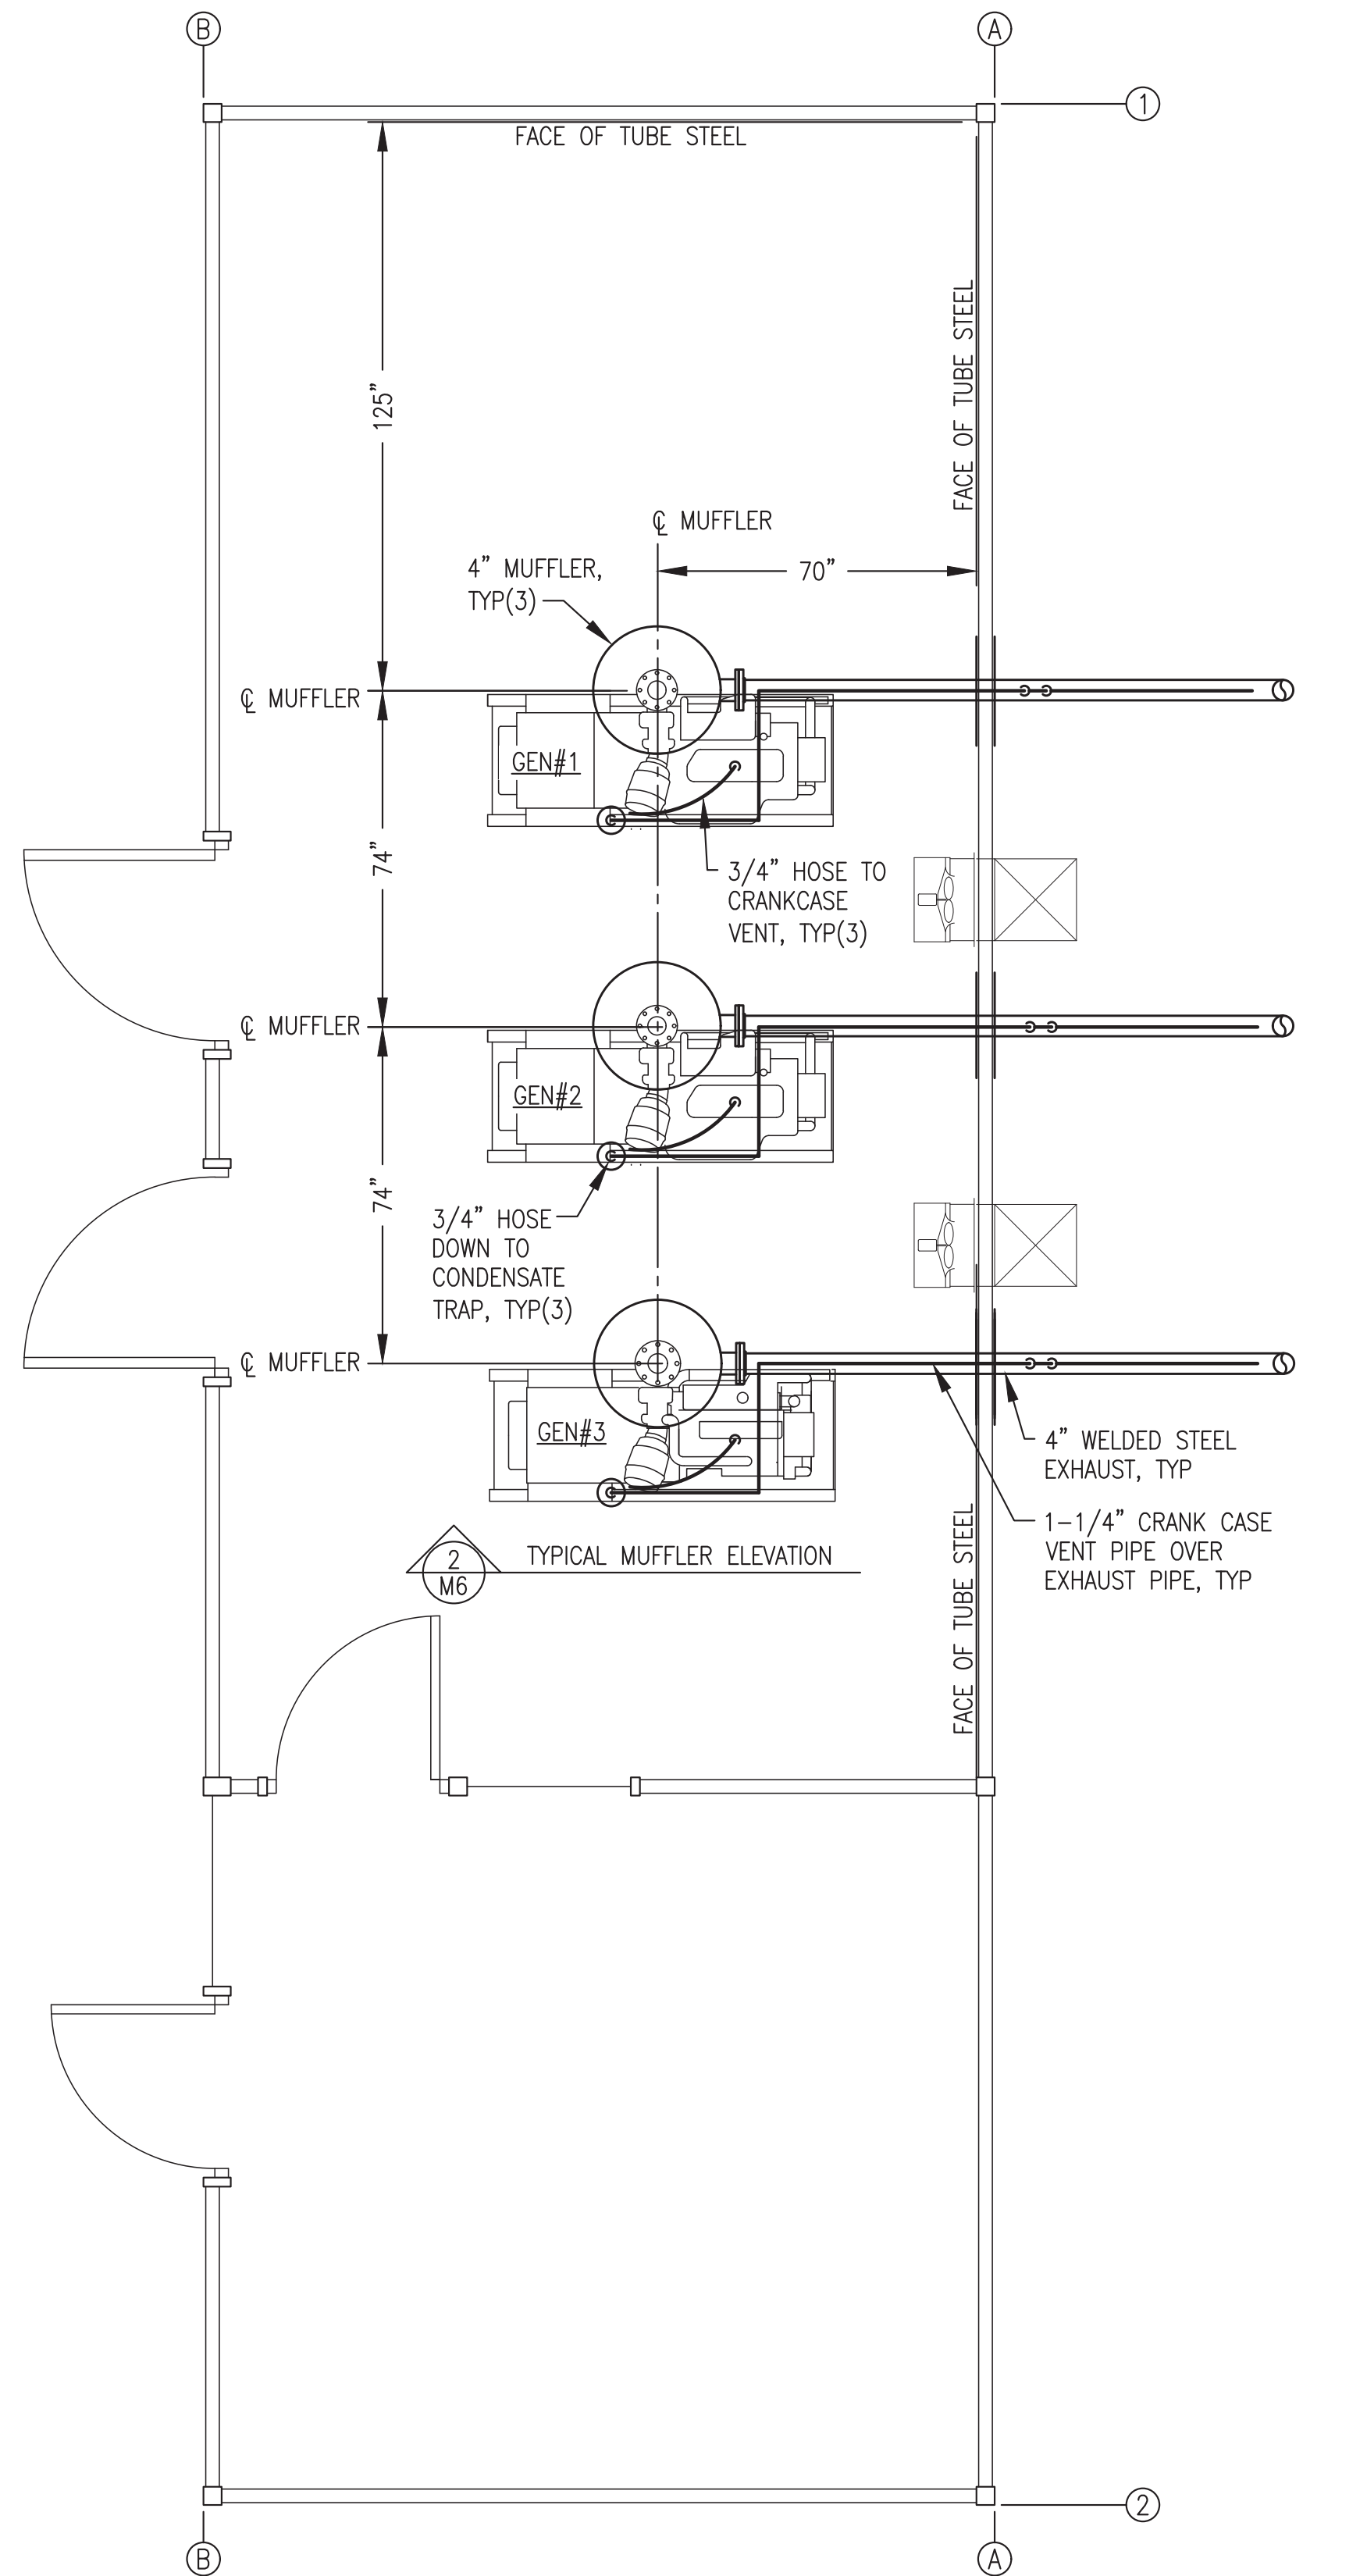

**1**  
**M6** MUFFLER, EXHAUST & CRANK VENT PIPE PLAN  
3/8"=1'-0"


**EXHAUST & CRANK VENT GENERAL NOTES:**

- 1) THE MAXIMUM EXHAUST TEMPERATURE FOR THE ENGINES IS LESS THAN 1400°F. THE WALLS AND CEILING ARE NON-COMBUSTIBLE CONSTRUCTION CONSISTING OF STEEL WITH HIGH TEMPERATURE ROCKWOOL INSULATION.
- 2) ALL EXTERIOR EXHAUST PIPE AND FITTINGS (FROM MUFFLER TO RAIN CAP) TYPE 304L STAINLESS STEEL WITH BUTT WELD FITTINGS. INTERIOR EXHAUST PIPE RISER (FROM FLEX TO MUFFLER) CARBON STEEL OR MAY BE STAINLESS AT CONTRACTORS OPTION. ALL FLANGES ANSI 150# FLAT FACED SLIP ON.
- 3) ALL EXTERIOR CRANK VENT PIPE AND FITTINGS TYPE 304L STAINLESS STEEL WITH BUTT WELD FITTINGS. ALL INTERIOR CRANK VENT PIPE AND FITTINGS CARBON STEEL WITH SOCKET WELD FITTINGS OR MAY BE STAINLESS AT CONTRACTORS OPTION. ALL FLANGES ANSI 150# RAISED FACE SOCKET WELD.


- 4) ALL EXHAUST FLANGE BOLTS BLACK OR STAINLESS STEEL. COAT WITH HIGH TEMPERATURE ANTI-SIEZE COMPOUND. ALL EXHAUST FLANGE GASKETS HIGH TEMPERATURE FULL FACE.

**EXHAUST & CRANK VENT SHOP/ON-SITE NOTES:**

- 1) SHOP FABRICATE COMPLETE EXHAUST AND CRANK VENT PIPING SYSTEM AS INDICATED.
- 2) SHOP INSTALL BLANKET INSULATION ON FLEX AND RIGID INSULATION FROM FLEX TO MUFFLER. SHOP FIT INSULATION FROM MUFFLER TO WALL, LABEL FOR THE ASSOCIATED GENERATOR AND STORE INSIDE MODULE. SHOP FURNISH ROCK WOOL INSULATION AND PACKAGE LOOSE SHIP WITH COVER PLATES.
- 3) SHOP FABRICATE STAINLESS STEEL COVER PLATES BUT DO NOT INSTALL. LABEL COVER PLATES FOR THE ASSOCIATED GENERATOR AND STORE INSIDE MODULE. SHOP FURNISH ROCK WOOL INSULATION AND PACKAGE LOOSE SHIP WITH COVER PLATES.
- 4) UPON COMPLETION OF TESTING BREAK EXHAUST FLANGE JOINT ON MUFFLER OUTLET AND CRANK VENT FLANGE JOINT AND REMOVE U-BOLTS. REMOVE PIPING FOR SHIPPING AND TEMPORARILY SEAL WALL PENETRATION.
- 5) IN FIELD REINSTALL PIPING WITH NEW FLANGE GASKETS. RE-INSTALL PIPING INSULATION. INSULATE WALL PENETRATION, INSTALL COVER PLATES, AND SEAL TO WALL.

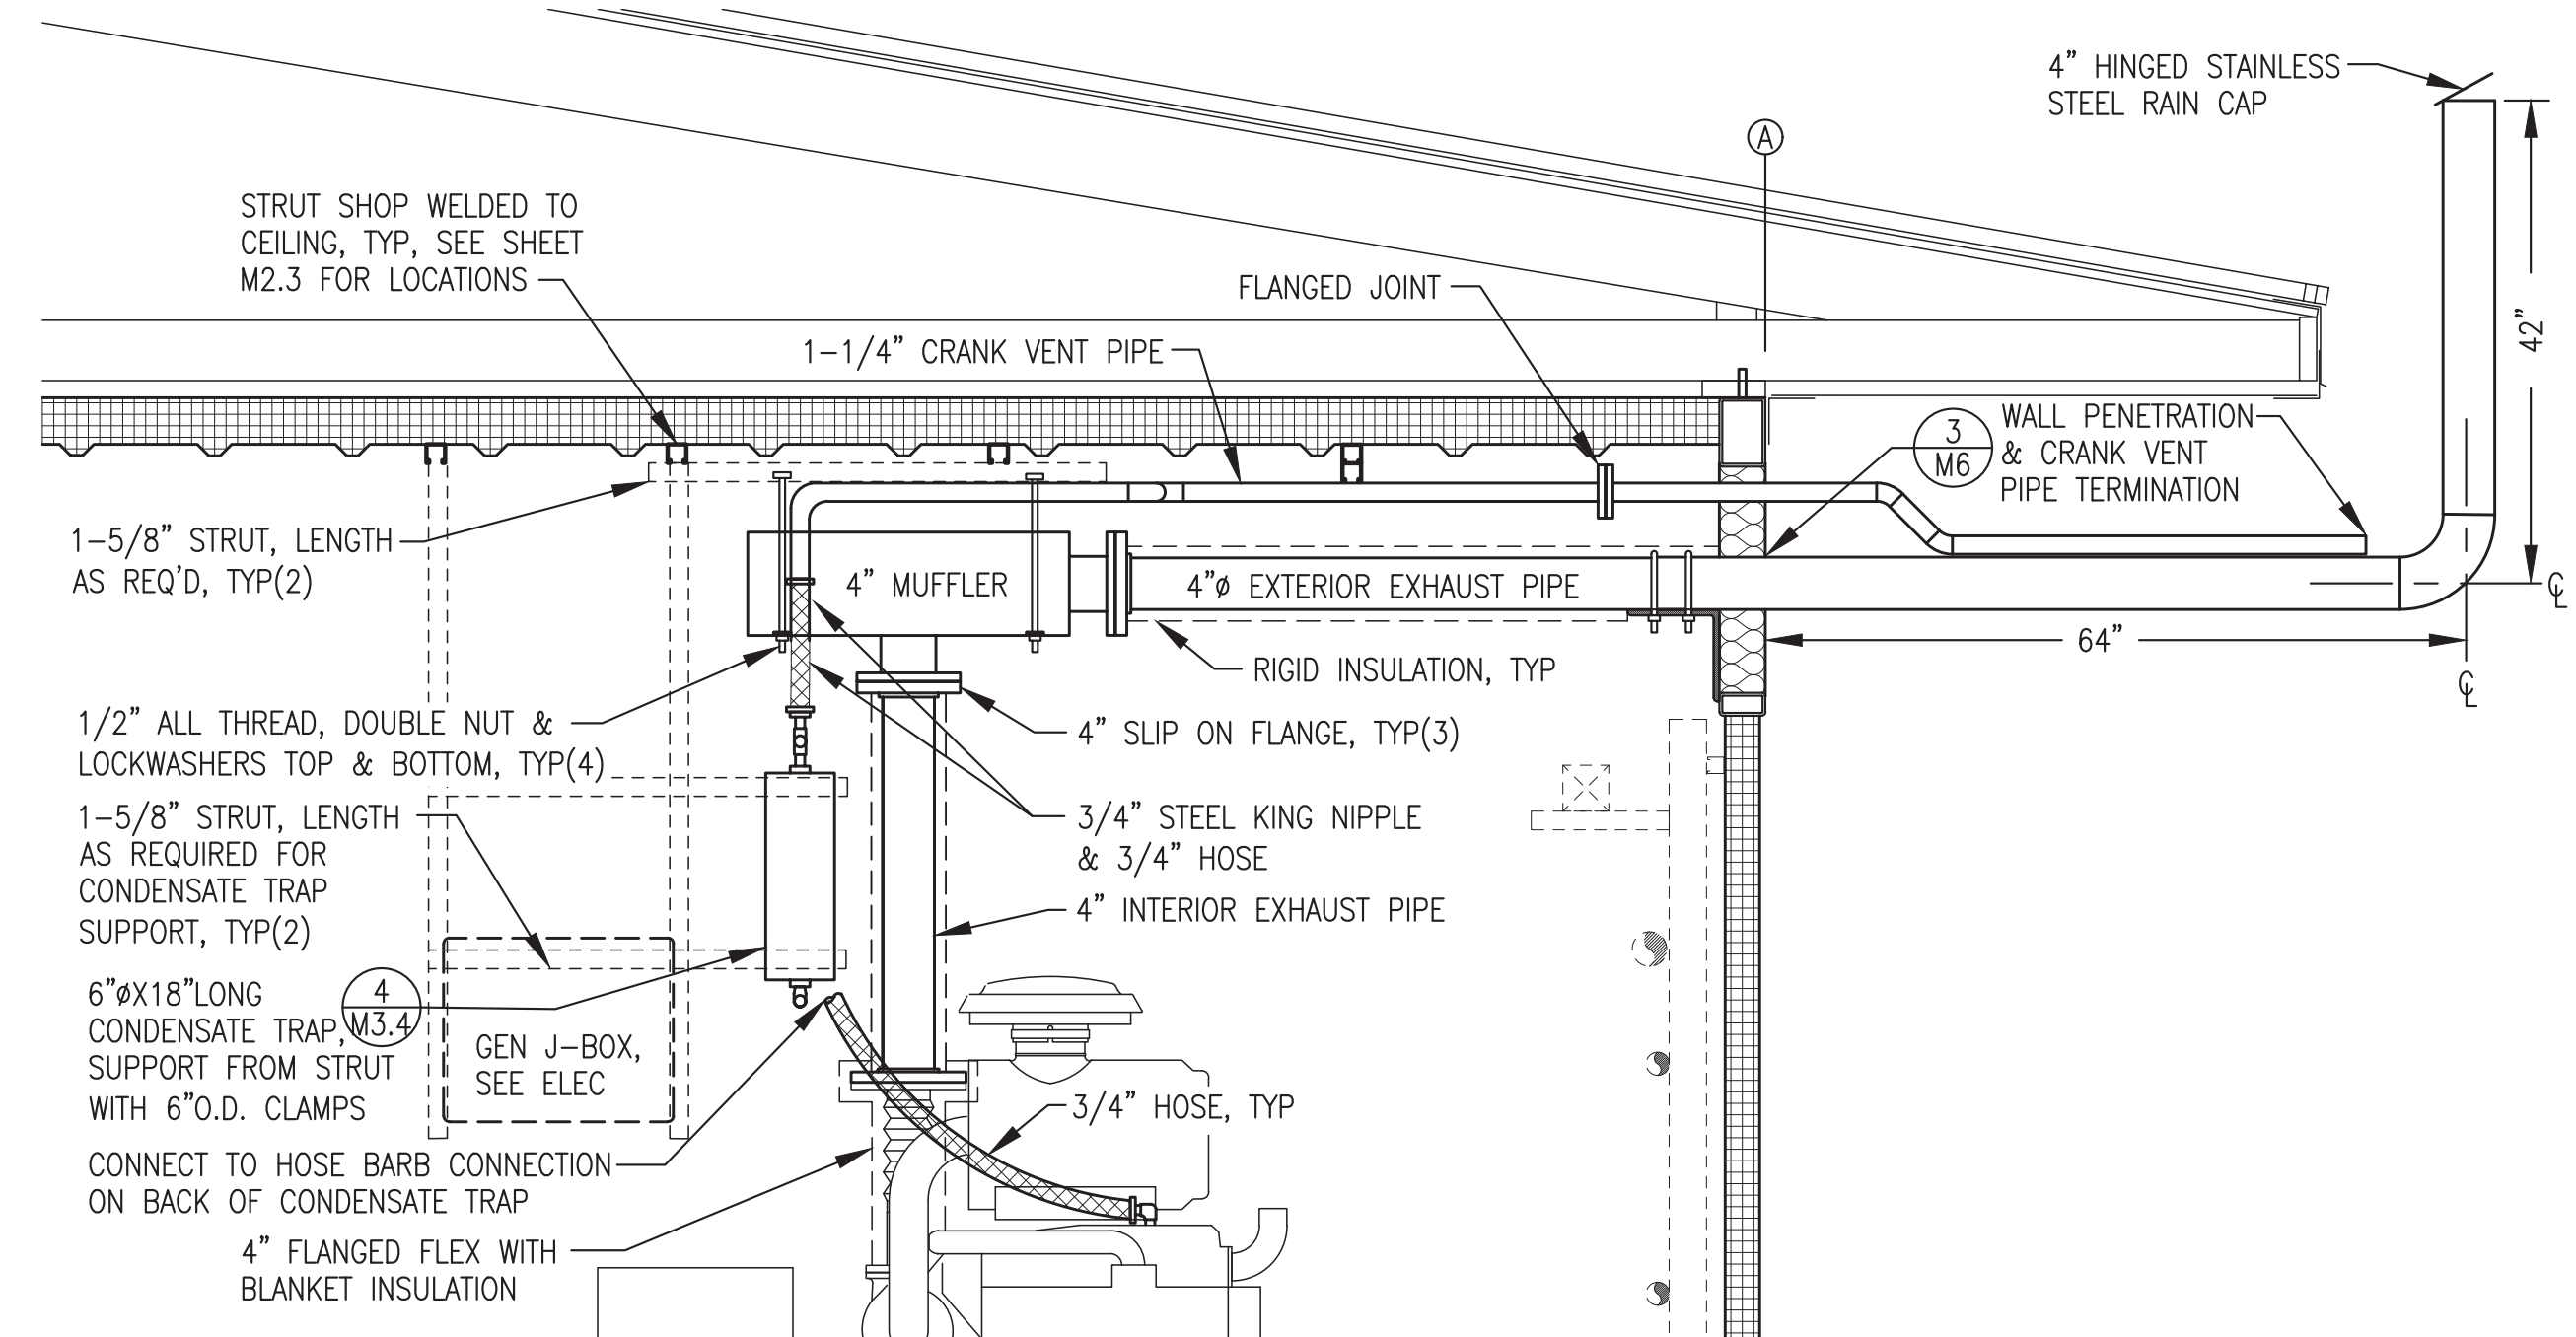

**2**  
**M6** TYPICAL MUFFLER, EXHAUST, CONDENSATE TRAP & CRANK VENT PIPE INSTALLATION  
3/4"=1'-0"

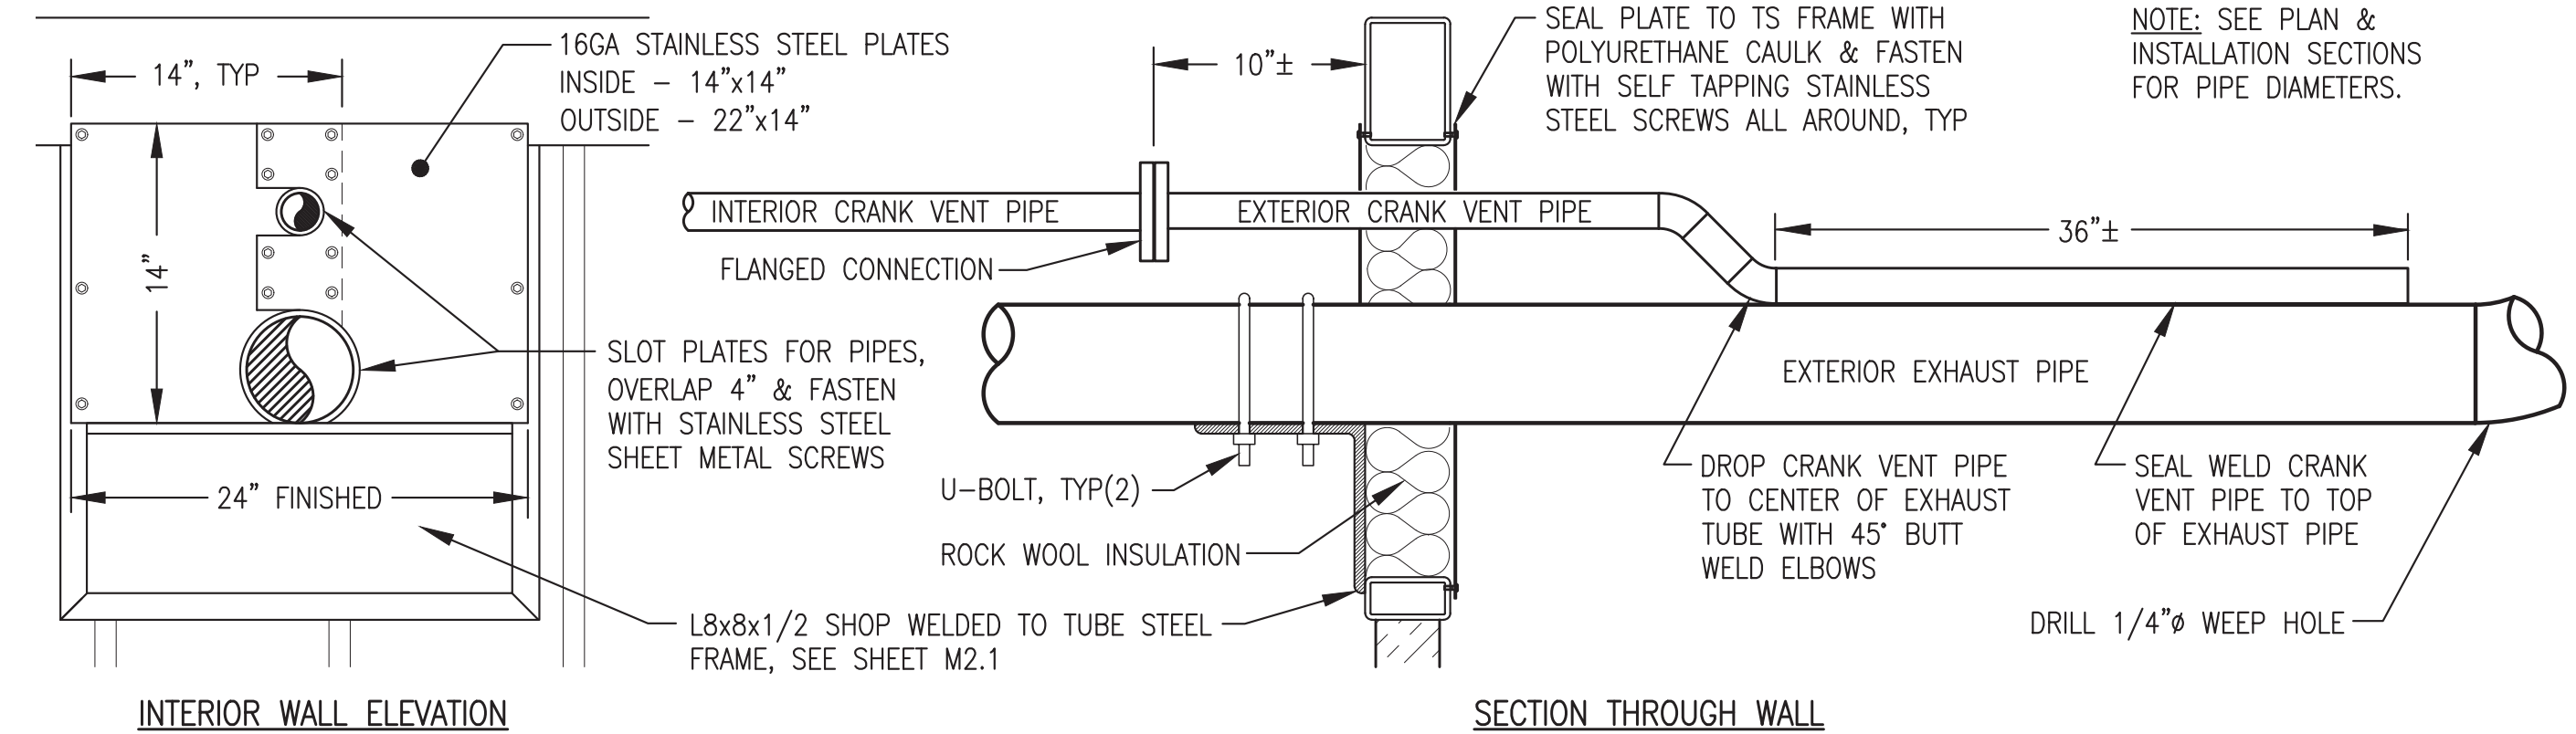


**3**  
**M6** WALL PENETRATION & CRANK VENT PIPE TERMINATION  
NO SCALE


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: EXHAUST & CRANK VENT PLAN & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		PROJECT NUMBER:	
P.O. 111405, Anchorage, AK 99511 (907)349-0100		<b>M6</b>	

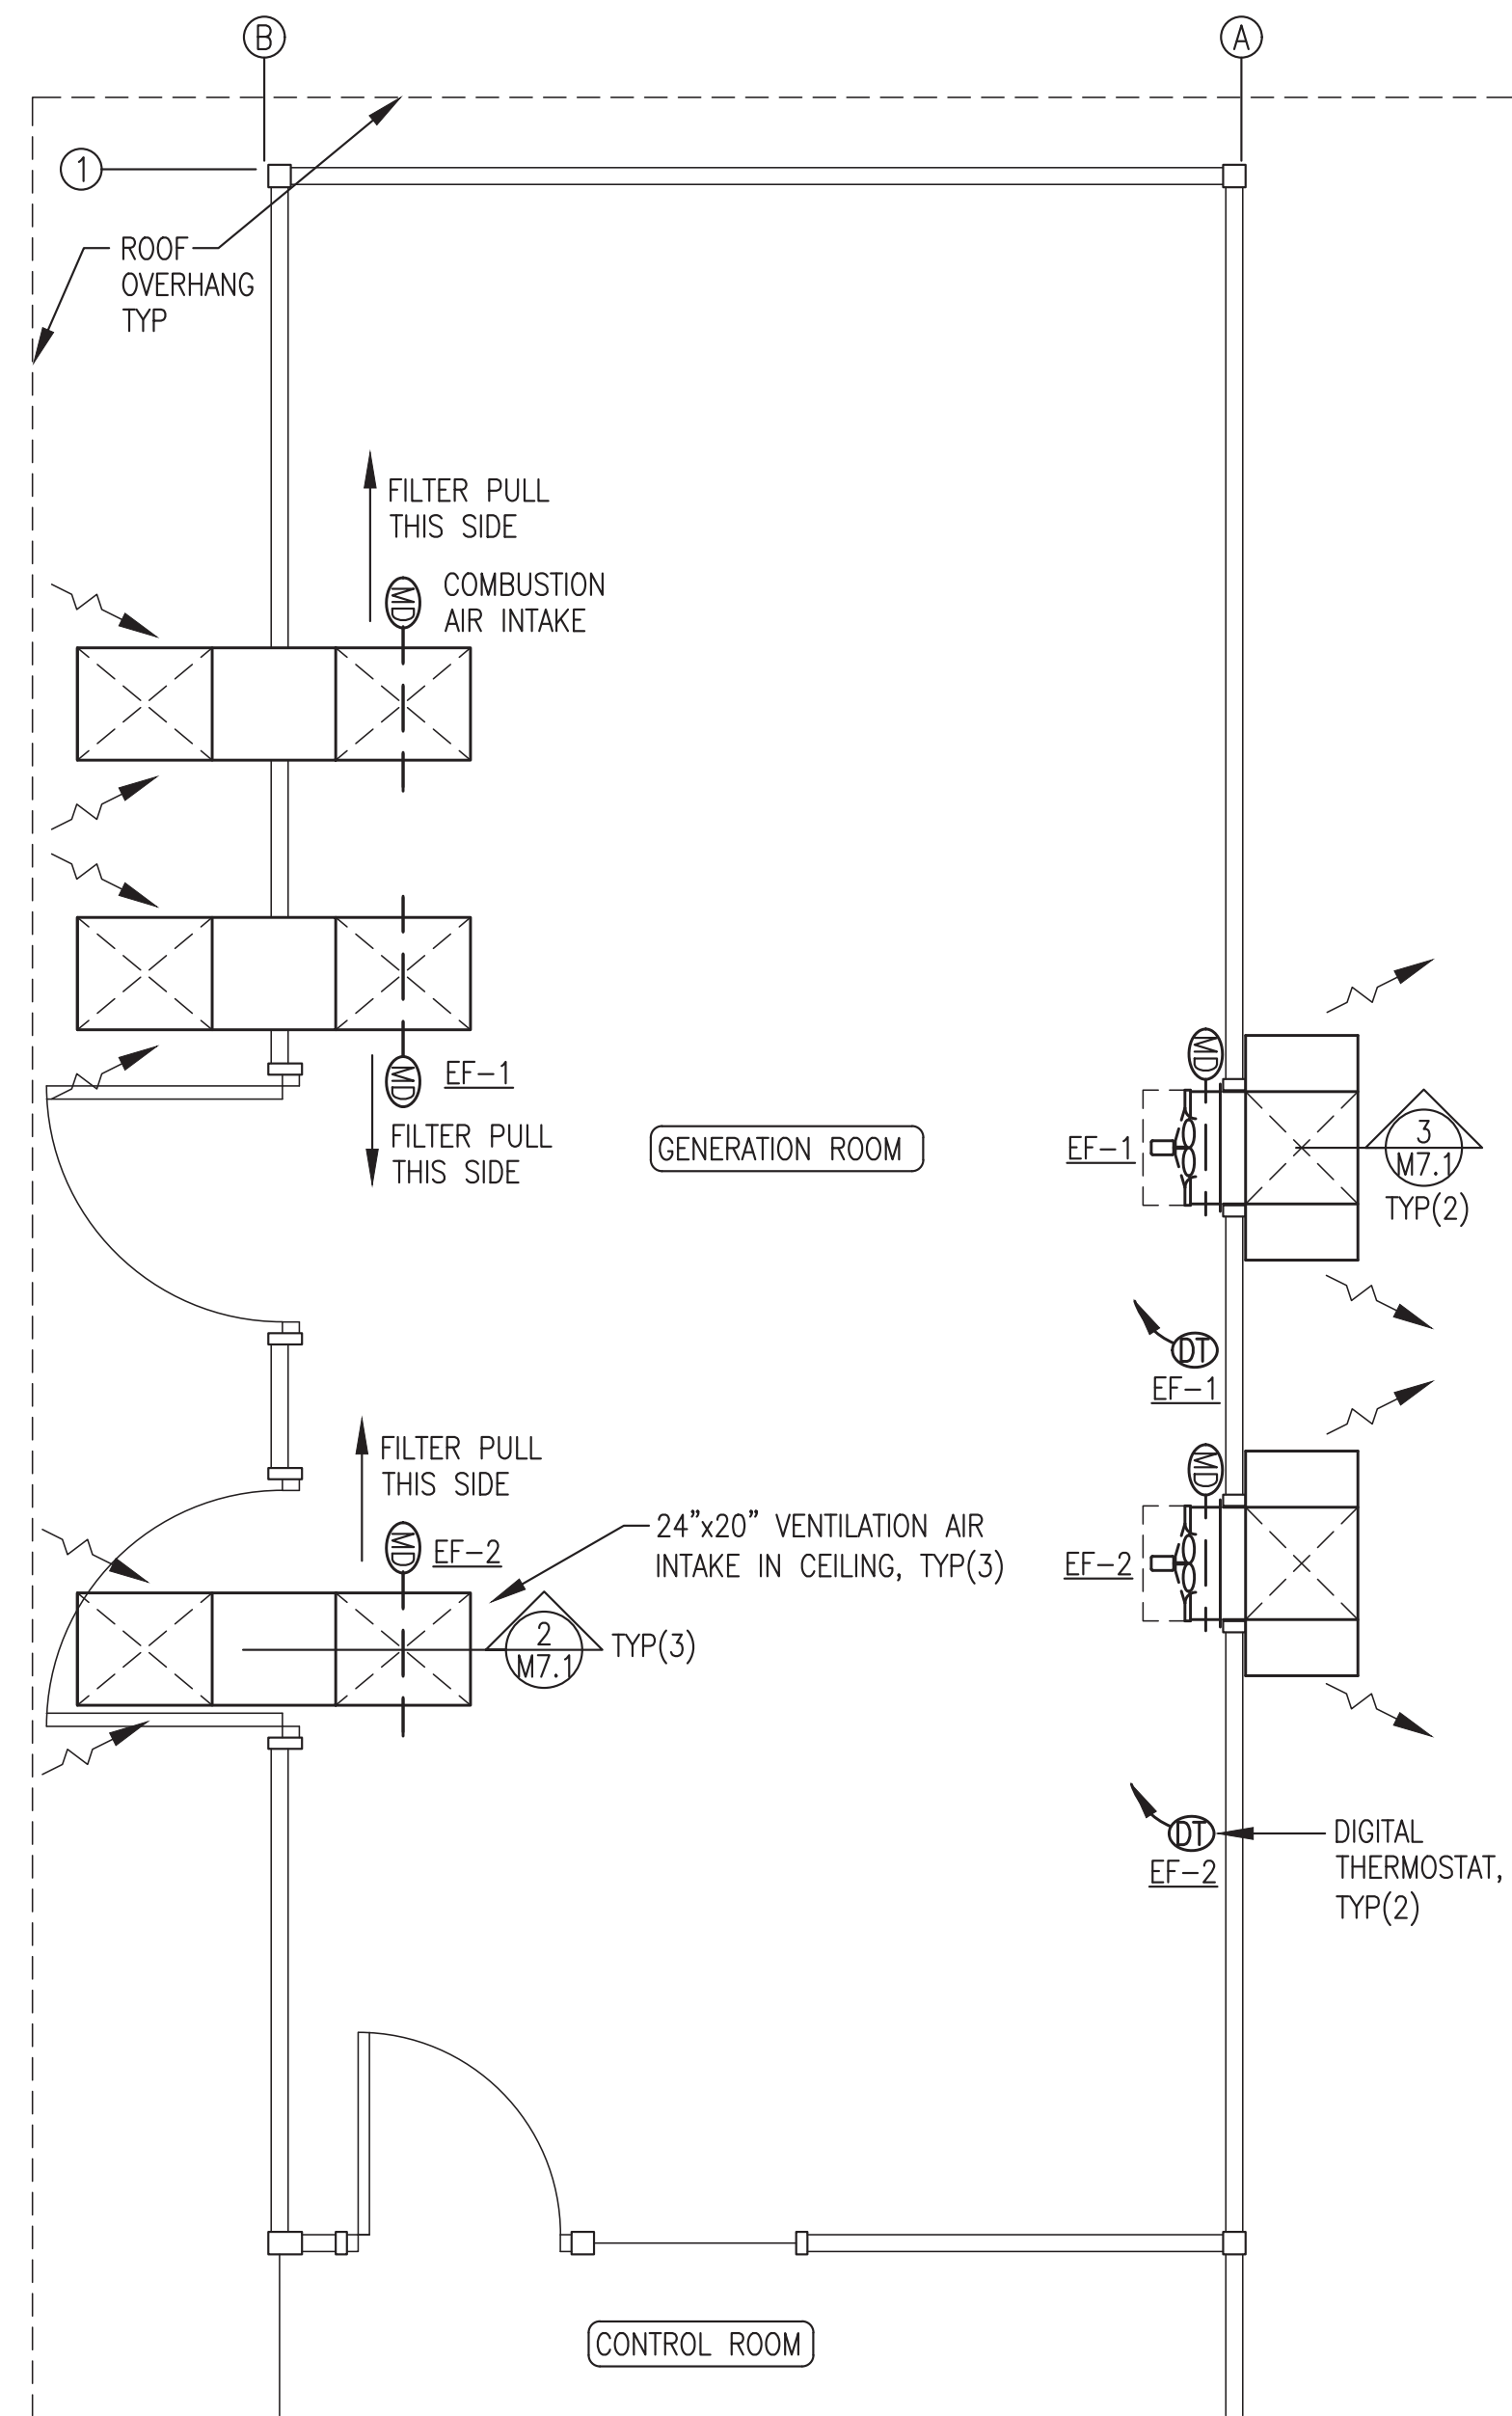


**1** VENTILATION PLAN  
M7.1 3/8"=1'-0"

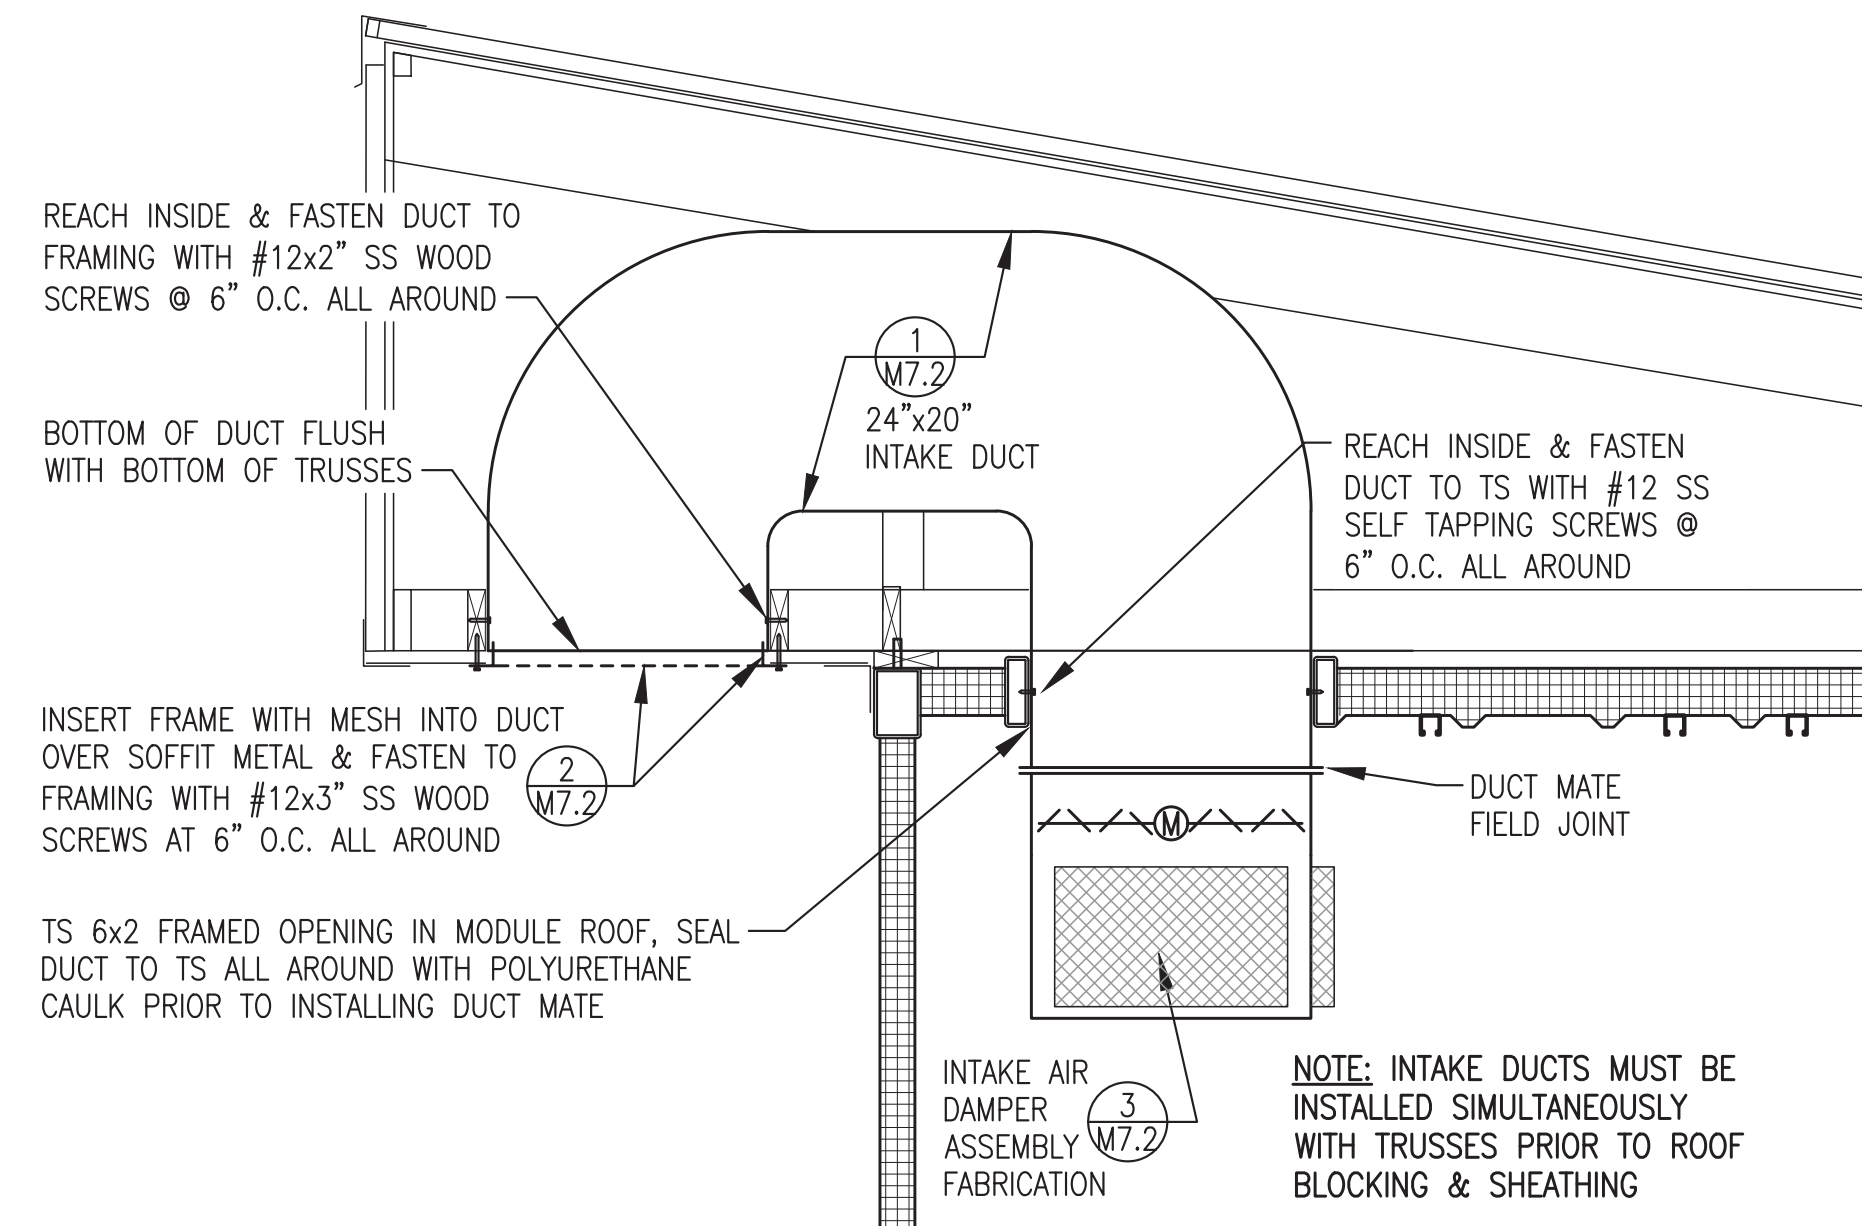

**2** INTAKE DUCT INSTALLATION  
M7.1 3/4"=1'-0"

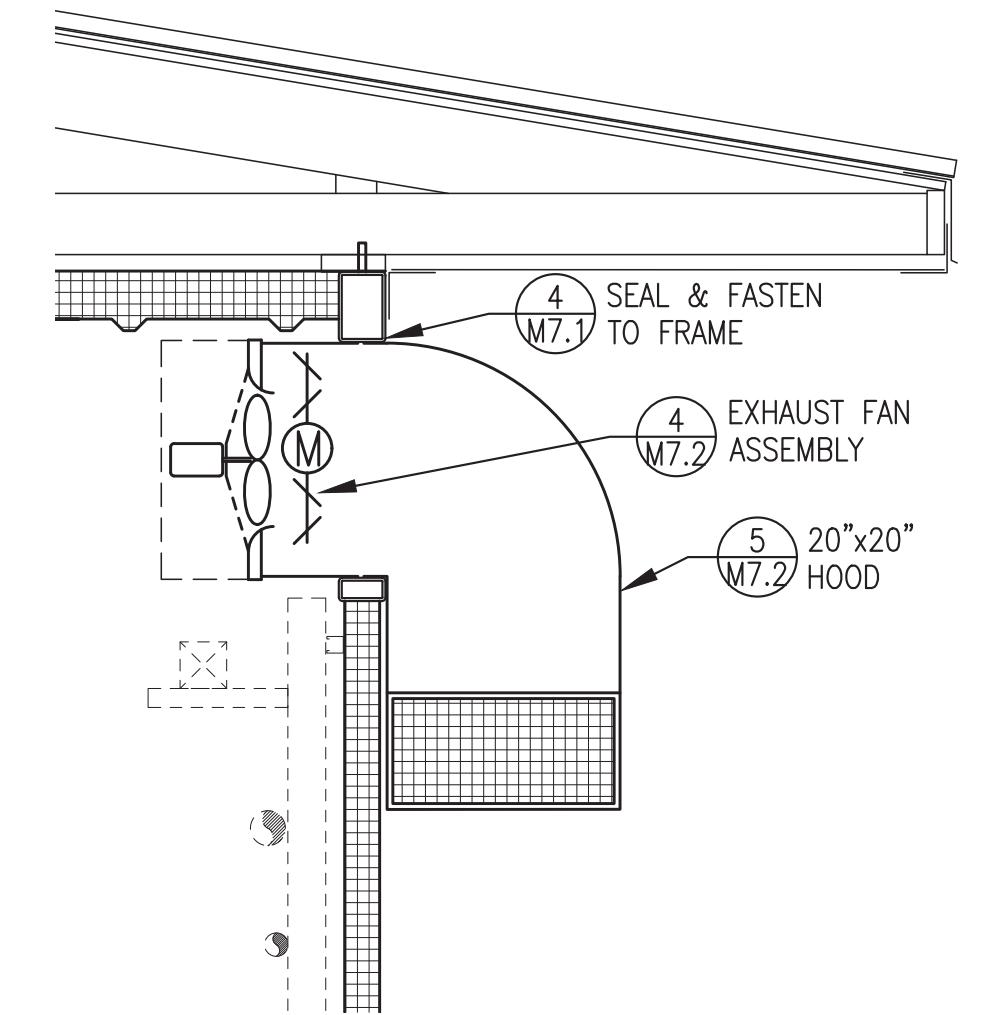

**3** EXHAUST FAN INSTALLATION  
M7.1 3/4"=1'-0"

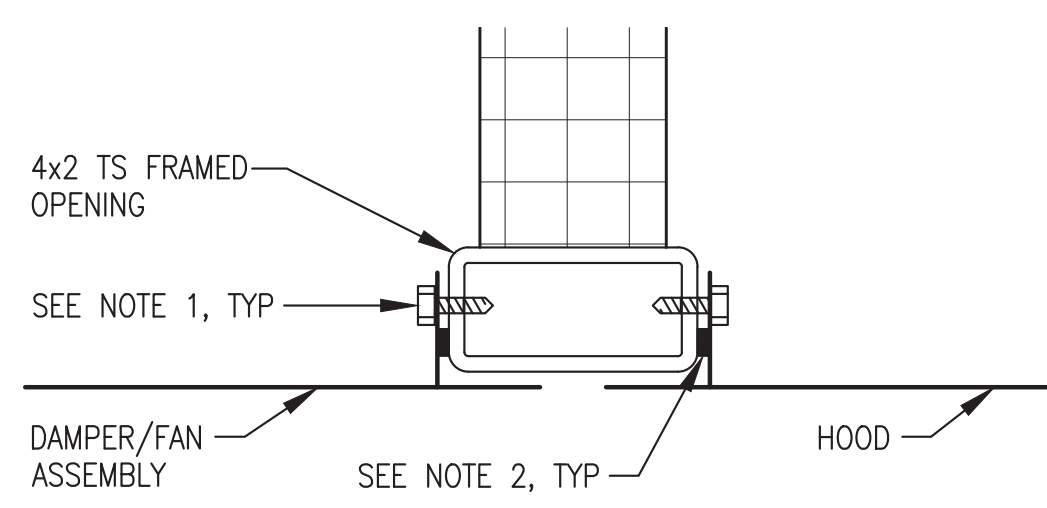


**4** TYPICAL WALL PENETRATION  
M7.1 4"=1'-0"

**VENTILATION SYSTEM SHOP/ON-SITE NOTES:**


- 1) FURNISH ENTIRE VENTILATION SYSTEM AS PART OF MODULE SHOP FABRICATION.
- 2) DURING SHOP FABRICATION INSTALL EXHAUST FAN ASSEMBLIES. TEST FIT EXTERIOR HOODS AND INTAKE DUCTS BUT DO NOT INSTALL.
- 3) DURING SHOP FABRICATION TEMPORARILY CONNECT INTAKE DAMPERS TO ELECTRICAL ROUGH IN AND TEST TO VERIFY FUNCTION. SEE SHEET E4-2.
- 4) AS PART OF ON-SITE WORK INSTALL EXHAUST HOODS AND INTAKE DUCTING AS INDICATED.

- NOTES:**
- 1) FASTEN MOUNTING FLANGE TO TS WITH #12 STAINLESS STEEL SELF TAPPING SCREWS. ON HOODS FASTEN ON TOP AND SIDES ONLY. ON EXHAUST FANS FASTEN ON SIDES ONLY.
  - 2) SEAL MOUNTING FLANGE TO TS WITH CONTINUOUS BEAD OF POLYURETHANE CAULKING ALL AROUND.

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT:		RAMPART POWER SYSTEM UPGRADE	
TITLE:		VENTILATION PLAN & DETAILS	
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		M7.1	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

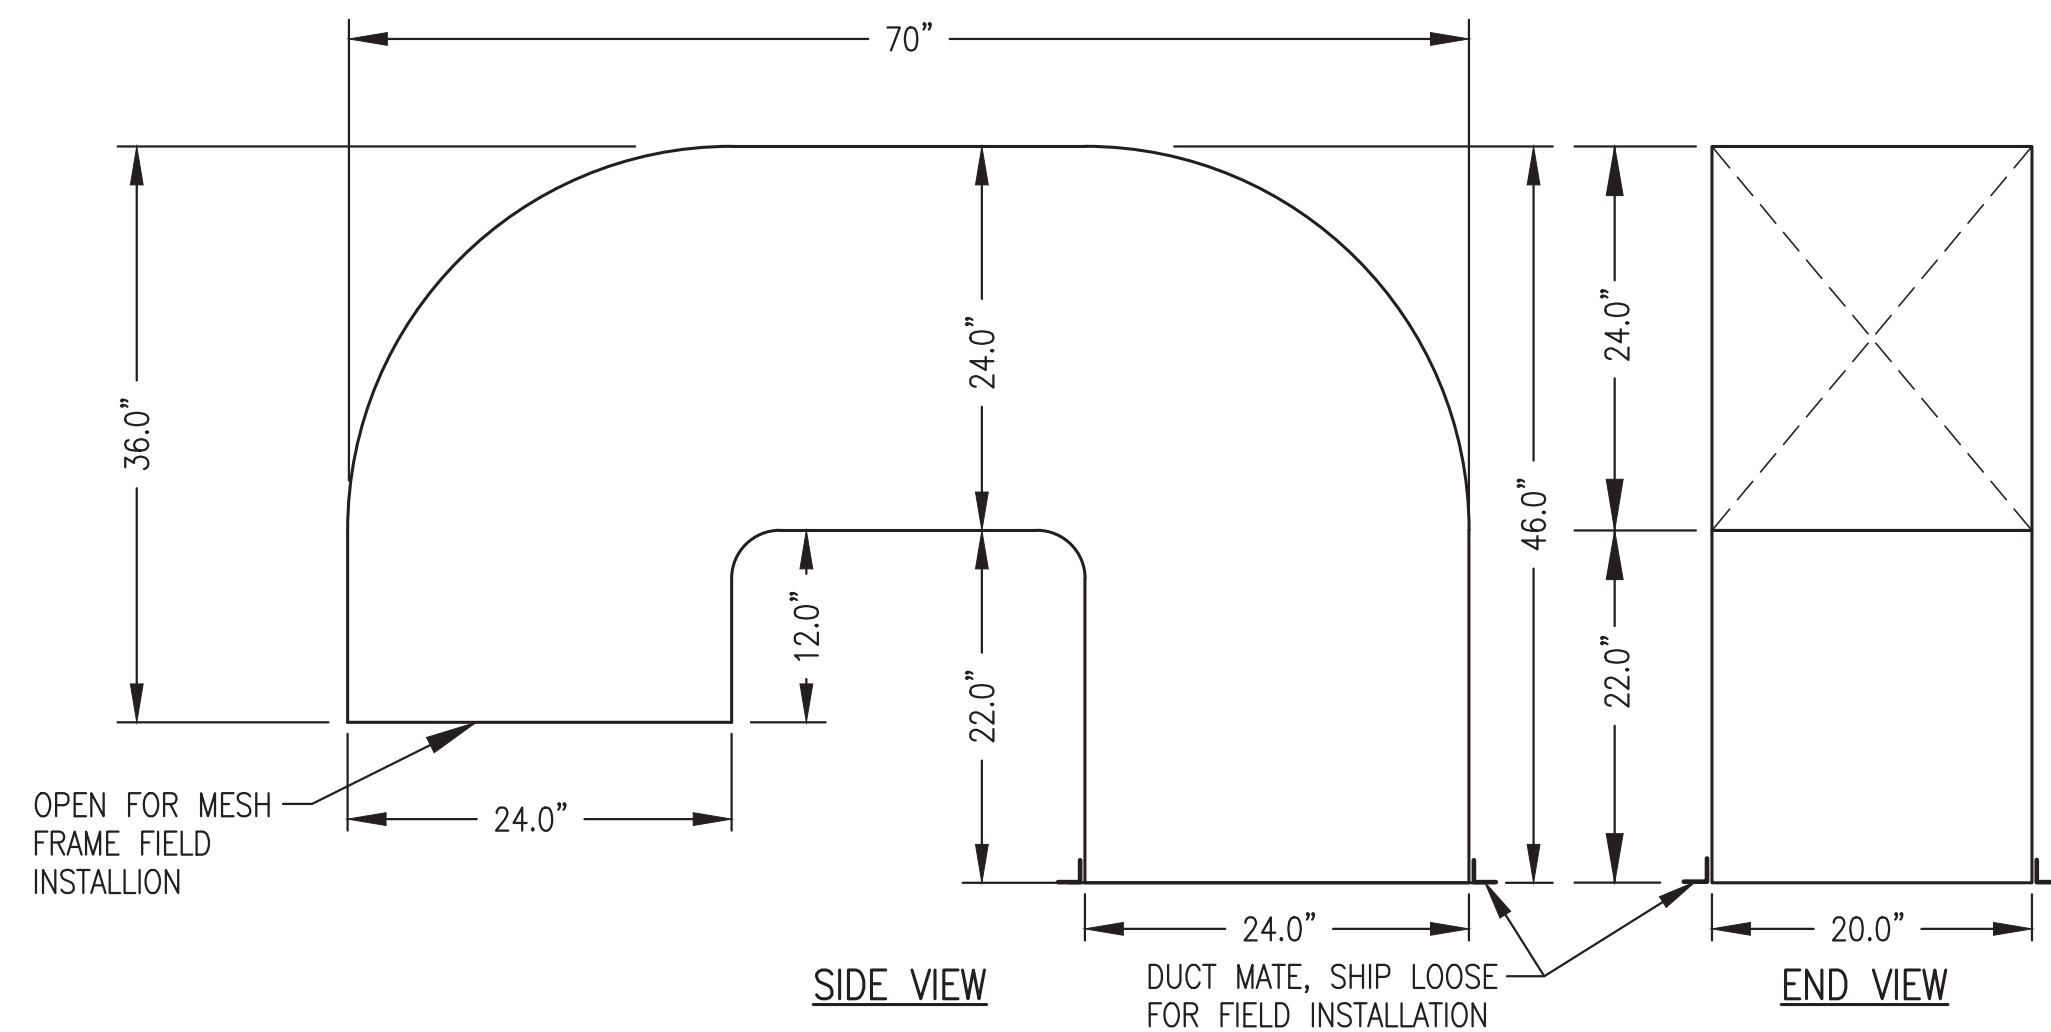


- NOTES:
- 1) FABRICATE 3 IDENTICAL DUCTS FROM MIN 18 GAUGE GALV SHEET METAL WITH SEALED MECHANICAL JOINTS OR AT CONTRACTORS OPTION 0.090" THICK TYPE 5052 ALUMINUM WITH ALL WELDED SEAMS.
  - 2) DUCTS ARE DESIGNED TO FIELD INSTALL BETWEEN TRUSSES. DO NOT ADD JOINTS.

**1** INTAKE DUCT FABRICATION  
M7.2 1"=1'-0"

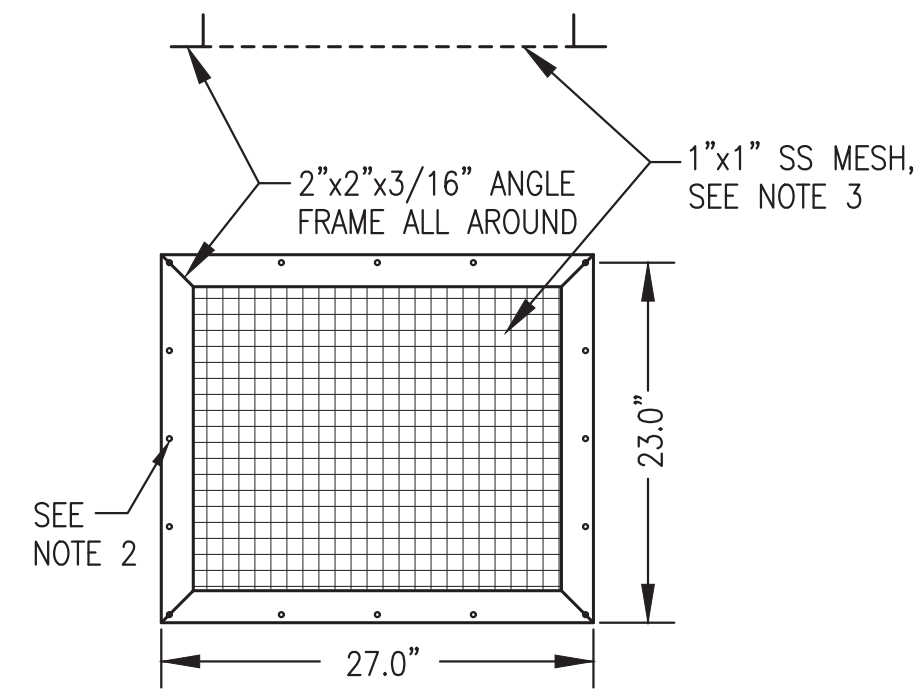


- NOTES:
- 1) FABRICATE 3 IDENTICAL AIR INTAKE MESH FRAMES.
  - 2) FABRICATE FRAME FROM 2"x2"x3/16" ALUMINUM ANGLE WITH MITERED AND WELDED CORNERS AND 1/4" HOLES AT 6" O.C. ALL AROUND, 1/2" FROM OUTSIDE EDGE OF FRAME.
  - 3) INSTALL 1"x1" STAINLESS STEEL WIRE MESH IN HEMMED STAINLESS STEEL FRAME AND FASTEN TO ANGLE FRAME WITH STAINLESS STEEL SCREWS ALL AROUND.

**2** INTAKE MESH FRAME  
M7.2 1"=1'-0"

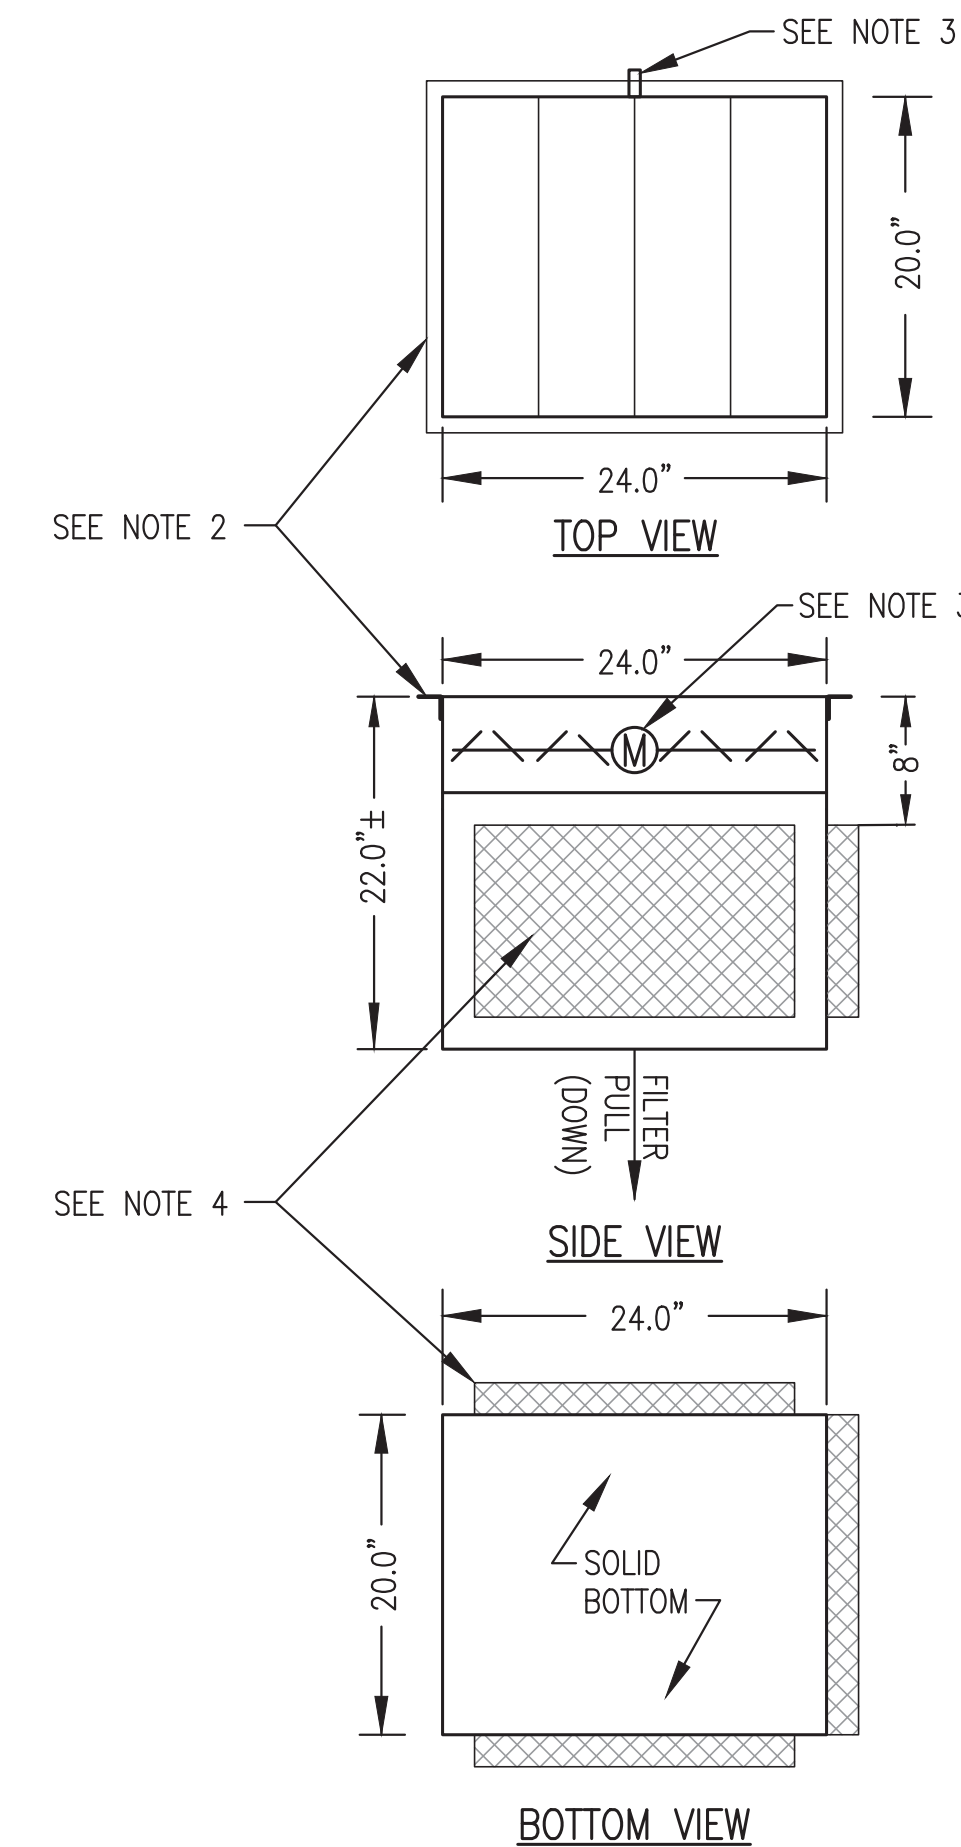


- NOTES:
- 1) FABRICATE 4 IDENTICAL VENTILATION INTAKE ASSEMBLIES.
  - 2) SHOP MOUNT DUCTMATE FLANGE.
  - 3) PROVIDE MIN 3" DAMPER ROD EXTENSION ON SIDE INDICATED AND FABRICATE SHEET METAL STAND-OFF BRACKET TO FULLY SUPPORT THE ACTUATOR FROM THE DAMPER FRAME. SEE PLAN VIEW FOR DAMPER ACTUATOR ORIENTATION.
  - 4) INSTALL FRAME FOR REMOVABLE 20"x12"x2" MERV 8 FILTERS. FABRICATE FROM "C" CHANNEL THREE SIDES WITH LATCHING HINGED COVER ON BOTTOM TO ALLOW FILTERS TO SLIDE DOWN FOR REMOVAL. ON 20" SIDE EXTEND FILTER FRAME BEYOND DUCT EACH WAY AS REQUIRED.

**3** INTAKE AIR DAMPER FABRICATION  
M7.2 1"=1'-0"

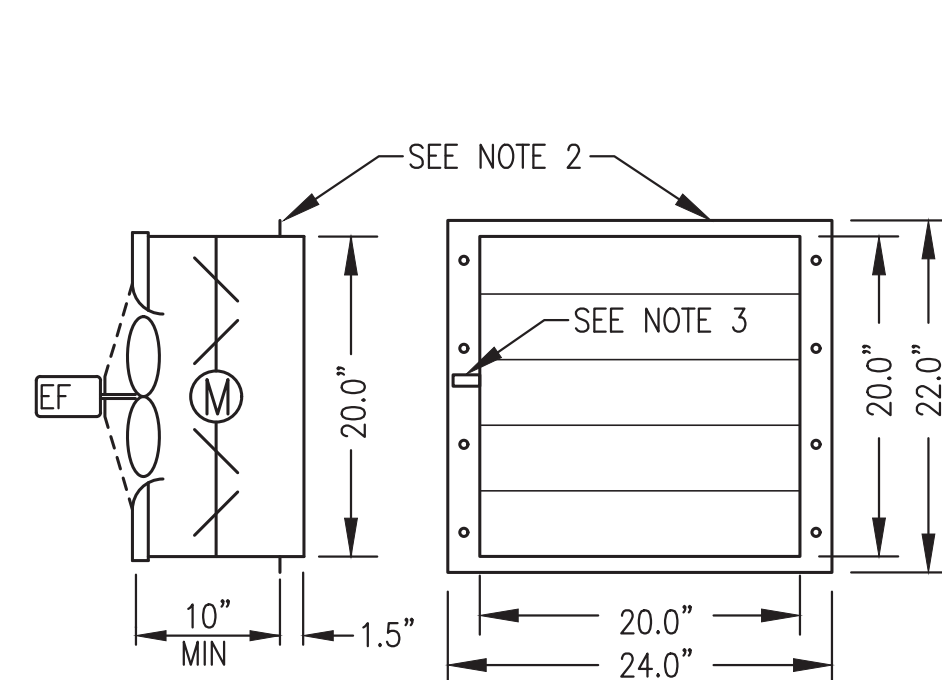

- NOTES:
- 1) FABRICATE 2 IDENTICAL ASSEMBLIES COMPLETE WITH FAN AND DAMPER MOUNTED AND SEALED TO DUCT.
  - 2) PROVIDE 2" WIDE MOUNTING FLANGE ON SIDES WITH 1/4" HOLES AT 5" O.C. PROVIDE 1" MOUNTING FLANGE ON TOP AND BOTTOM WITHOUT HOLES.
  - 3) PROVIDE MIN 3" DAMPER ROD EXTENSION ON THE LEFT SIDE AND FABRICATE SHEET METAL STAND-OFF BRACKET TO FULLY SUPPORT THE ACTUATOR FROM THE DAMPER FRAME.


**4** EXHAUST FAN ASSEMBLY FABRICATION  
M7.2 1"=1'-0"

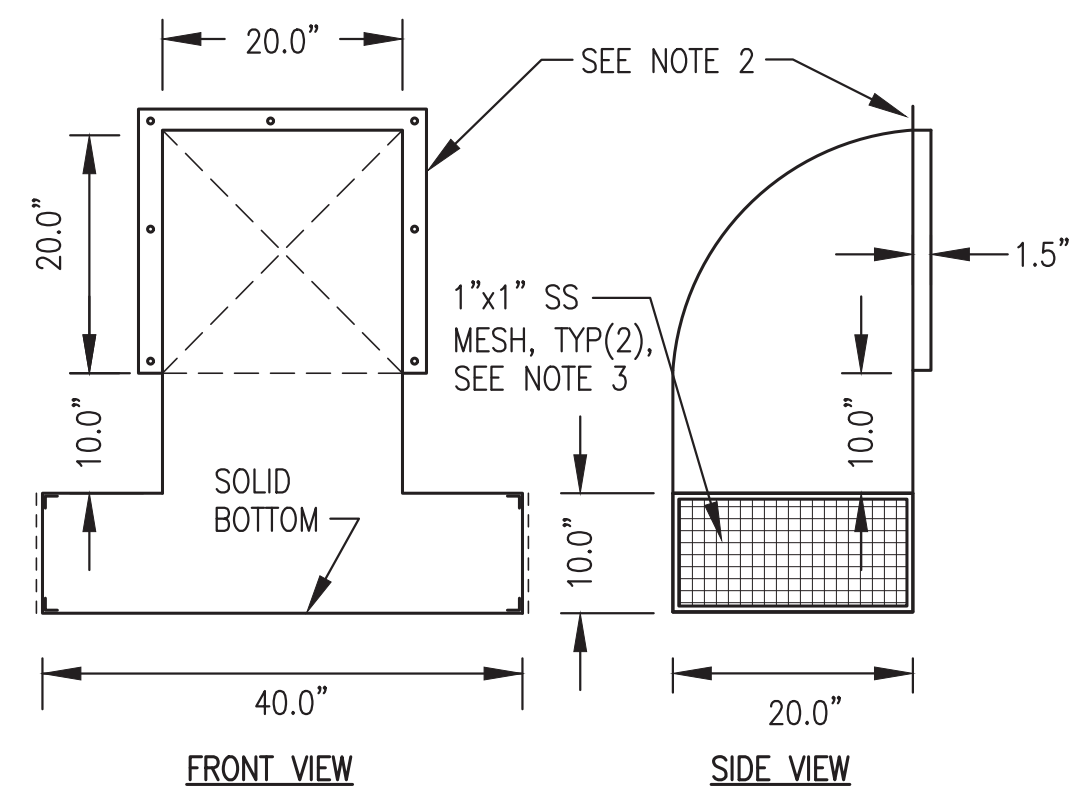

- NOTES:
- 1) FABRICATE HOODS FROM 0.090" THICK TYPE 5052 ALUMINUM WITH ALL WELDED SEAMS.
  - 2) PROVIDE 2" WIDE MOUNTING FLANGE ON TOP & SIDES WITH 1/4" HOLES AT 9" O.C.
  - 3) INSTALL 1"x1" STAINLESS STEEL WIRE MESH IN HEMMED STAINLESS STEEL FRAME AND FASTEN TO ANGLE FRAME WITH STAINLESS STEEL SCREWS ALL AROUND, TYP(2).


**5** EXHAUST HOOD FABRICATION  
M7.2 3/4"=1'-0"

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: SHEET METAL FABRICATION DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_M2-M7		SHEET:	
PROJECT NUMBER:		M7.2	

Gray Stassel Engineering, Inc.  
P.O. 111405, Anchorage, AK 99511 (907)349-0100

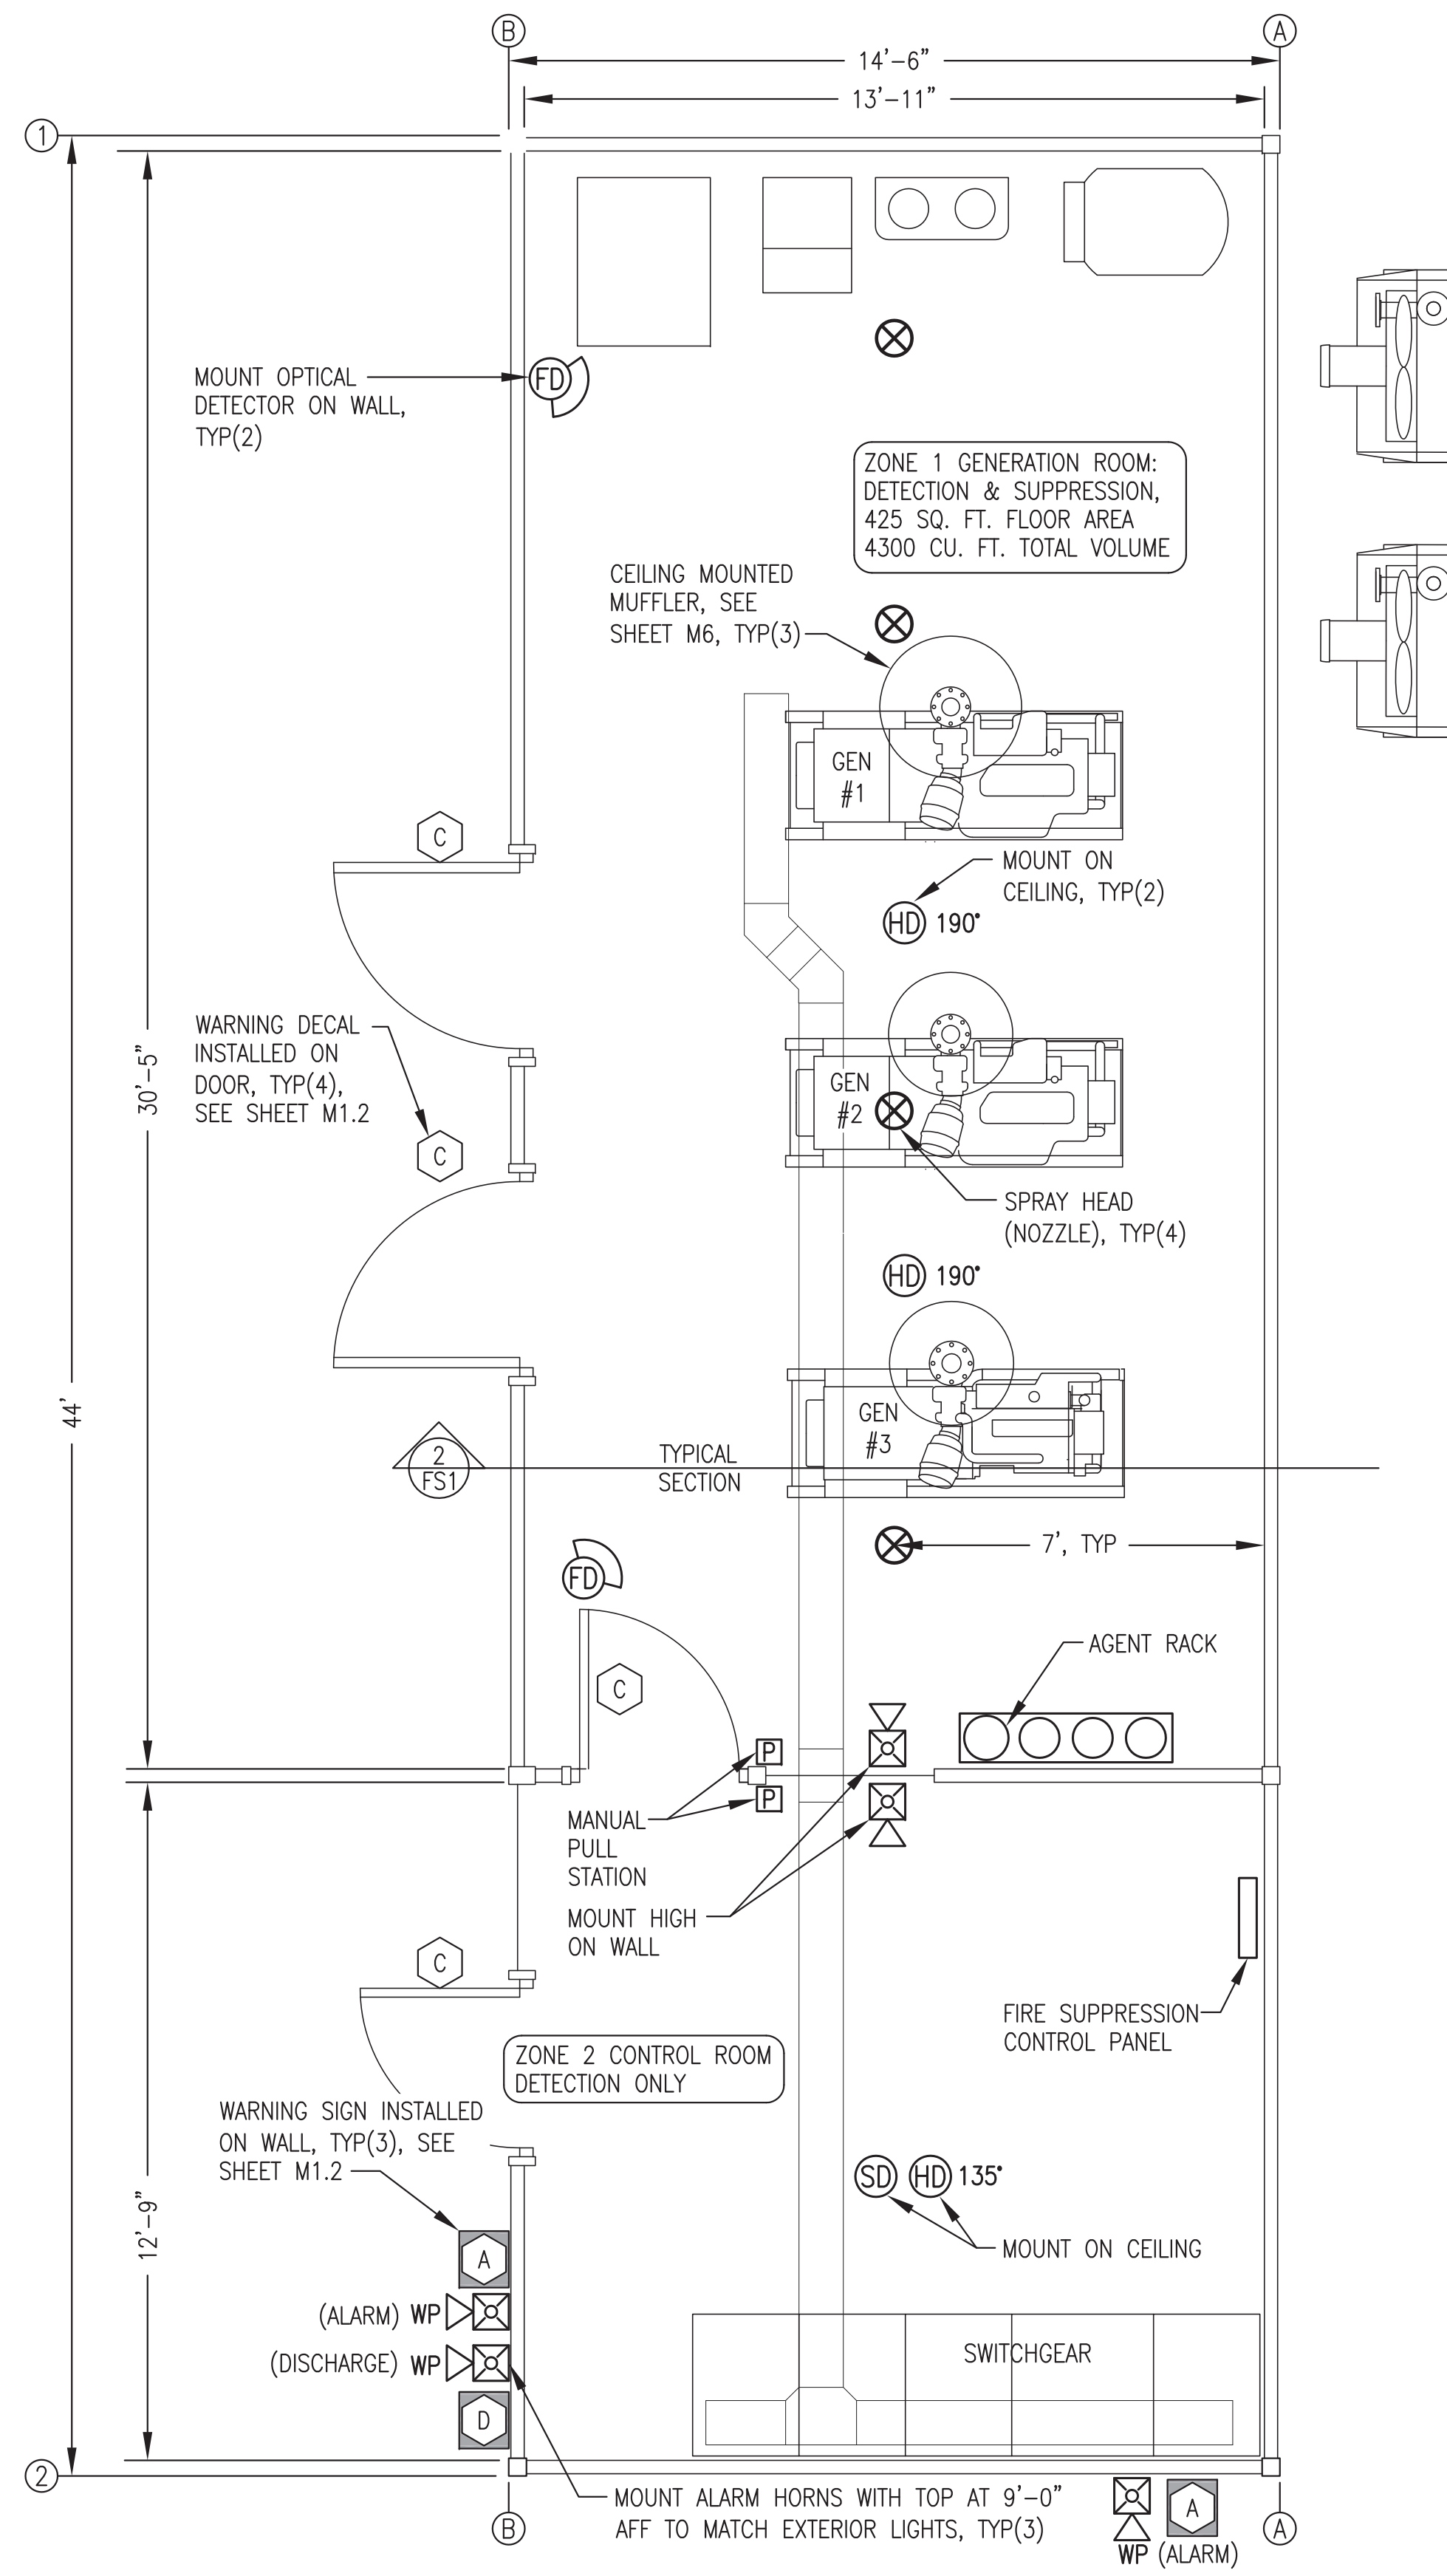

**1** FIRE SUPPRESSION SYSTEM PLAN  
3/8"=1'-0"

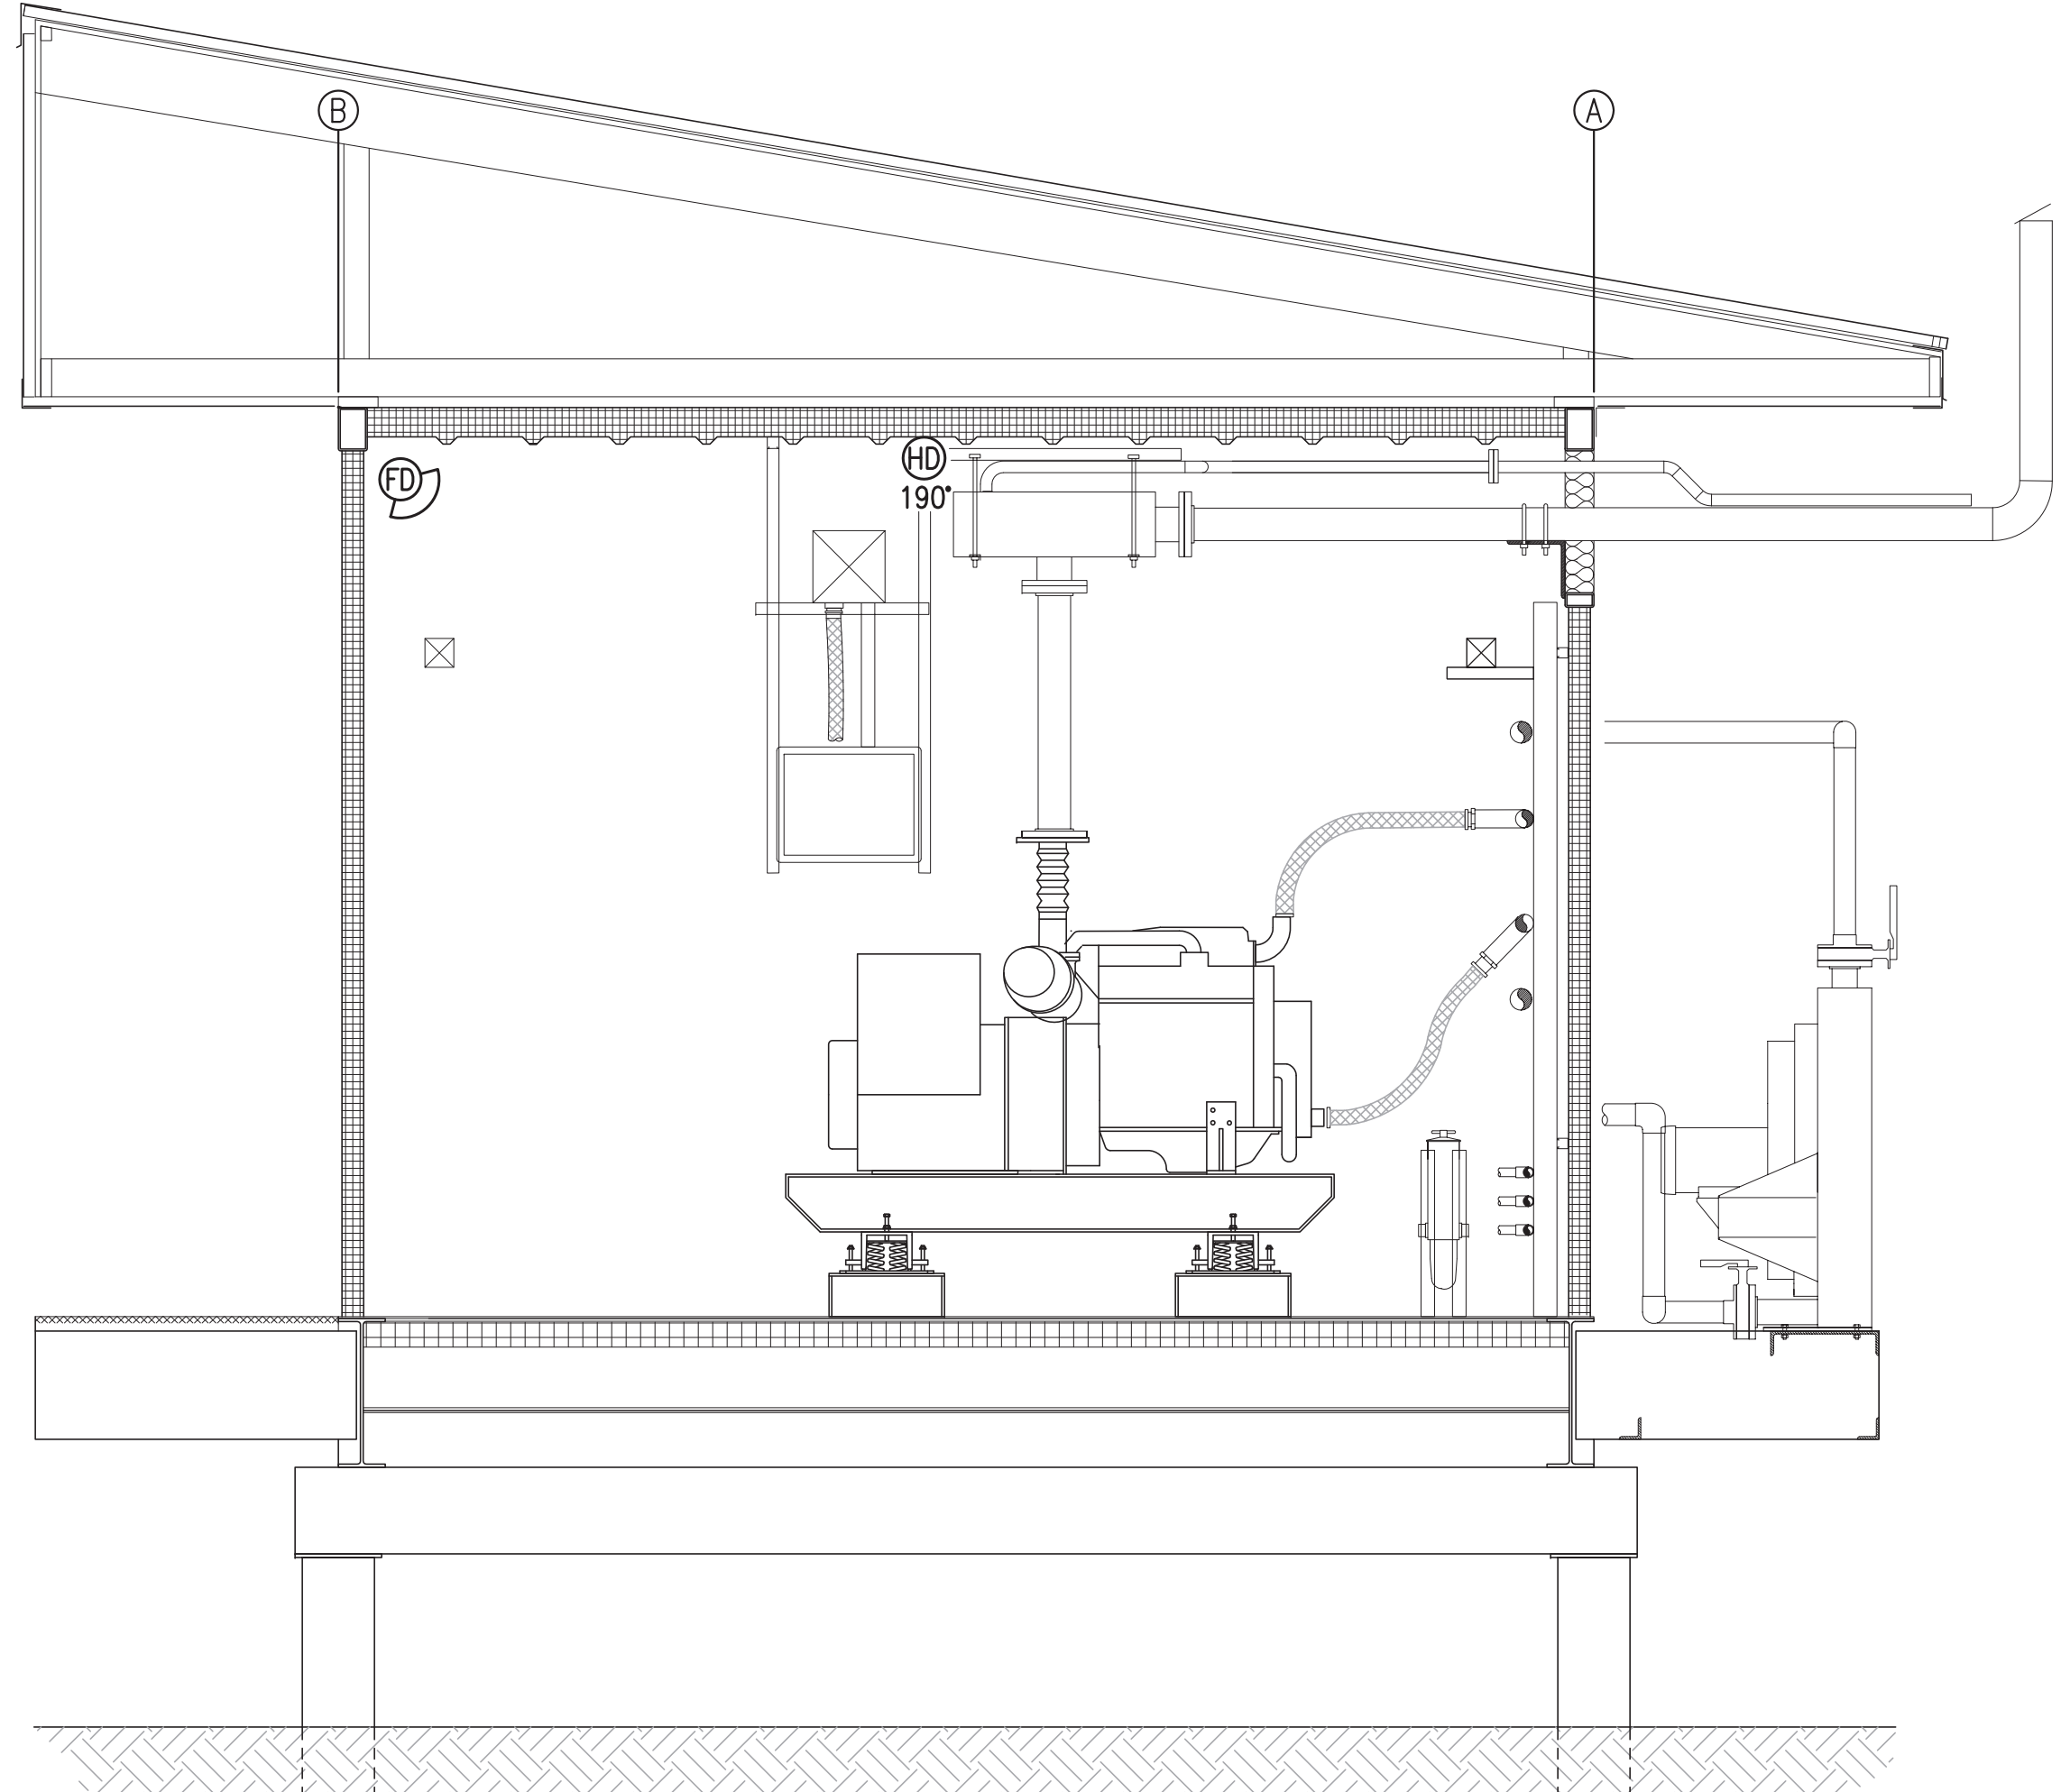

**2** TYPICAL SECTION THROUGH BUILDING  
3/8"=1'-0"

**FIRE SUPPRESSION SYMBOL LEGEND**

SYMBOL	DESCRIPTION	SYMBOL	DESCRIPTION
HD 135°	NORMAL TEMP. (135°F) DETECTOR	P	MANUAL PULL STATION
HD 190°	HIGH TEMP. (190°F) DETECTOR	WP	INTERIOR ALARM HORN/STROBE
FD	FLAME (OPTICAL) DETECTOR	WP	EXTERIOR ALARM HORN/STROBE
SD	SMOKE (IONIZATION) DETECTOR		

**FIRE SUPPRESSION PLACARD SCHEDULE (SEE SHEET M1.2)**

SYMBOL	DESCRIPTION
A	"FIRE ALARM"
C	"CAUTION, ROOM PROTECTED BY WATER MIST FIRE PROTECTION SYSTEM, IN CASE OF FIRE KEEP DOOR CLOSED AND DO NOT ENTER"
D	"FLASHING LIGHT MEANS FIRE SUPPRESSION AGENT HAS DISCHARGED"

**FIRE SUPPRESSION WIRE SCHEDULE**

SYMBOL	CIRCUIT DESCRIPTION	WIRE TYPE	WIRE COLOR
A	24V DC POWER	#14 AWG SOLID	RED & BLACK
B	DETECTION CIRCUITS	#14 AWG SOLID	BLUE & YELLOW
C	ANNUNCIATION ALARM	#14 AWG SOLID	BROWN & ORANGE
D	ANNUNCIATION DISCHARGE	#14 AWG SOLID	WHITE, & GRAY
E	24V DC AUX POWER	#14 AWG SOLID	RED & BLACK WITH GRAY STRIPE

**GENERAL NOTES:**

- INTERIOR FINISH OF ALL WALLS AND CEILING METAL SIDING. INTERIOR FINISH OF FLOOR WELDED STEEL PLATE. CEILING HEIGHT IN ALL ROOMS 10'-2" ABOVE FINISHED FLOOR.
- ALL DOORS SELF-CLOSING WITH GASKETS. ALL BUILDING PIPING AND CONDUIT PENETRATIONS SEALED LIQUID TIGHT. ALL BUILDING DUCT PENETRATIONS EQUIPPED WITH MOTORIZED DAMPERS THAT CLOSE ON GENERATOR SHUT DOWN.

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: FIRE SUPPRESSION SYSTEM PLAN, SECTION, LEGEND, & NOTES			
DRAWN BY: BCG		SCALE: AS NOTED	
DESIGNED BY: BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_FS1		SHEET: FS1 OF 1	
PROJECT NUMBER:			
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

EQUIPMENT REQUIREMENTS FOR APPROVED EQUALS (APPLIES TO ALL SCHEDULES):  
 SPECIFIC PARTS MANUFACTURER AND MODEL SELECTED NOT ONLY TO MEET PERFORMANCE FUNCTION BUT ALSO TO COORDINATE AND INTERFACE WITH OTHER DEVICES AND SYSTEMS. APPROVED EQUAL SUBSTITUTIONS WILL BE ALLOWED ONLY BY ENGINEER'S APPROVAL. TO OBTAIN APPROVAL, SUBMITTALS MUST CLEARLY DEMONSTRATE HOW SUBSTITUTE ITEM MEETS OR EXCEEDS SPECIFIED ITEM QUALITY AND PERFORMANCE CHARACTERISTICS AND ALSO COMPLIES WITH MECHANICAL AND/OR ELECTRICAL CONNECTIONS AND PHYSICAL LAYOUT REQUIREMENTS.

**ELECTRICAL EQUIPMENT SCHEDULE**

SYMBOL	SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL
1	DAY TANK ALARM HORN/STROBE	MULTI-TONE ALARM WITH STROBE, 115V, NEMA 3R, WEATHER RESISTANT SURFACE MOUNT BELL BOX	WHEELLOCK MT4-115-WH-VNS
2	DIGITAL THERMOSTAT	MULTIPLE OUTPUT MODULATING DIGITAL THERMOSTAT	HONEYWELL TB7980B
3	NOT USED	NOT USED	NOT USED
4	EXTERIOR LIGHT	AREA LIGHT, WIDE DISPERSION WALL PACK WITH PHOTO CONTROL. LED, 17.7W, 120-277V DRIVER	HUBBELL NRG-356L-5K-U-PC
5	EMERGENCY LIGHT	WHITE PLASTIC ENCLOSURE, 120-347V INPUT, DUAL 5.3W LED LAMPS, LITHIUM IRON PHOSPHATE BATTERY	LITHONIA EML6L UVOLT LTP SRDT
6	EMERGENCY/EXIT LIGHT COMBO	WHITE PLASTIC ENCLOSURE, RED EXIT SIGN, 277/120V INPUT, DUAL 1.5W 9.6V LED LAMPS. OPTIONAL HIGH OUTPUT NI-CAD BATTERY	LITHONIA LHQM LED R HO
7	EMERGENCY EXIT REMOTE LIGHT	REMOTE LAMP FIXTURE, DUAL HEAD, RATED FOR EXTERIOR INSTALLATION IN DAMP/WET LOCATIONS, 1.5W 9.6V LED LAMPS.	LITHONIA ELA T QWP L0309
8	INTERIOR LIGHT	SURFACE MOUNTED LED STRIPLIGHT FIXTURE, 48" LONG, 34W, 5000K WITH SNAP ON FROSTED DIFFUSER	LITHONIA L1N-L48-5000LM-FST
9	TIMER SWITCH	0-5 MINUTE, 120V, 20A, 1HP RATED, INSTALL IN 4"x4" PRESSED STEEL BOX WITH METAL COVER.	INTERMATIC FF5M
10	LIGHT SWITCH	SINGLE POLE SNAP SWITCH, 120V, 20A, METAL, 1-1/2HP RATED, INSTALL IN 4"x4" STEEL BOX WITH METAL COVER, IVORY.	HUBBELL 1221-1
11	1Ø SMALL MOTOR DISCONNECT	SINGLE POLE SNAP SWITCH WITH RED PILOT LIGHT, 120V, 20A, 1HP RATED, INSTALL IN 4"x4" STEEL BOX WITH METAL COVER	HUBBELL 1221-PL
12	NOT USED	NOT USED	
13	STATION SERVICE TRANSFORMER	DRY TYPE, ENERGY STAR, ENCLOSURE TYPE 1 WITH INTEGRAL WALL MOUNT BRACKETS, 15 KVA, HV 480 DELTA, LV 208Y/120	HAMMOND HPS SENTINEL CAT. NO. SG3A0015KB
14	STATION SERVICE PANELBOARD	COPPER BUS, 3 PHASE, 4 WIRE, 120/208V, 125A MAIN BREAKER, 30 CIRCUITS, BOLT-IN BREAKERS, 20" WIDE NEMA 1 ENCLOSURE, SURFACE MOUNT, NO KNOCKOUTS	SIEMENS TYPE P1 OR SQUARE D TYPE NQ
15	STANDARD RECEPTACLE	SURFACE MOUNT 125V NEMA 5-20R RECEPTACLE. INSTALL IN 4"x4" STEEL BOX WITH METAL COVER	PASS & SEYMOUR 5362W
16	EXTERIOR GFCI RECEPTACLE	125V NEMA 5-20R GFCI RECEPTACLE. MOUNT IN CAST FDA BOX WITH WEATHERPROOF COVER	PASS & SEYMOUR 2095-W
17	BATTERY CHARGER	12/24-VOLT SOLID STATE 20-AMP AUTO-EQUALIZING BATTERY CHARGER FOR 120 VAC INPUT, WITH OPTIONAL HIGH/LOW VOLTAGE, AC POWER FAILURE, & REMOTE SUMMARY ALARM RELAYS	SENS NRG22-20-RCLS OR LEMARCHE ECSR-40/20-12/24V-AV1
18	WELDER/COMPR. RECEPTACLE	NEMA 6-30R, BLACK, 250V, 30A, 2 POLE, WITH GROUND. INSTALL IN DEEP 4"x4" STEEL BOX WITH 2.15"Ø HOLE METAL COVER	PASS & SEYMOUR 3801
19	NOT USED	NOT USED	NOT USED
20	RADIATOR MOTOR DISCONNECT	NON-FUSED LOCKABLE SAFETY SWITCH, NEMA 3R ENCLOSURE, 3PST, 600V, 30A, MIN 5HP RATED	SIEMENS HNF361R OR SQUARE D HU361R
21	24VAC CONTROL TRANSFORMER	120V PRIMARY, 24V SECONDARY, 20VA OUTPUT, 1/2" THREADED HUB MOUNT	FUNCTIONAL DEVICES TR20VA001
22	ENCLOSED POWER RELAY (RIB)	20A, 1HP RATED CONTACT, SPDT, 24VAC COIL, NEMA 1 ENCLOSURE, RED LED PILOT LIGHT	FUNCTIONAL DEVICES RIB2401B
23	SNAP SWITCH WITH THERMAL UNIT	600VAC, 1HP, 16A MANUAL MOTOR STARTER WITH TYPE S, TYPE A, MELTING ALLOY, CLASS 20 THERMAL UNIT	SQUARE D 2510F01 MOTOR STARTER WITH A14.8 THERMAL UNIT
24	ROUTER - HIGH SPEED INTERNET	4-PORT GIGABIT ROUTER, DUAL 2.4 AND 5 GHz WIFI WITH ADJUSTABLE ANTENNAS, 4 GIGABIT LAN, 1 GIGABIT WAN, USB 2.0 AND USB 4.0, MINIMUM 256 MB RAM	ASUS RT-ACI-900P

**ELECTRICAL CONDUCTOR SCHEDULE**

SERVICE/FUNCTION	DESCRIPTION	MANUFACTURER/MODEL	NOTES:
GENERATOR LEADS (ENGINE STARTER CABLES SIMILAR)	HIGH TEMPERATURE, EXTRA FLEXIBLE CABLE, TIN COATED COPPER CONDUCTOR. THERMOSET EPDM INSULATION, UL 3340/3374, MINIMUM 600V, LISTED 150°C FOR NON-FLEXING	COBRA CABLE, BELDEN, OR OMNI	TERMINATE WITH COPPER COMPRESSION LUGS RATED FOR THE FULL AMPACITY OF THE CABLE AT 150°C.
GENERAL USE CONDUCTORS	CLASS B CONCENTRIC STRANDED, SOFT DRAWN COPPER. TYPE XHHW2 INSULATION, 600V AND 90C RATED.		
SHIELDED/TWISTED INSTRUMENT & CONTROL & CANBUS CONDUCTORS	#18 AWG STRANDED TINNED COPPER CONDUCTORS, 600V POLYETHYLENE INSULATION, 100% COVERAGE ALUMINUM FOIL-POLYESTER TAPE SHIELD WITH STRANDED TINNED COPPER DRAIN WIRE & PVC OUTER JACKET	BELDEN PART #'S SINGLE PAIR: #1120A FOUR PAIR: #1049A SINGLE TRIAD: #1121A	GROUND SHIELD DRAIN WIRE AT PANEL END ONLY.
EHTERNET (CAT5e) COMMUNICATION CONDUCTORS	SOLID BARE COPPER CONDUCTORS, 300V FEP INSULATION & JACKET, 100% COVERAGE ALUMINUM FOIL-POLYESTER TAPE SHIELD WITH STRANDED TINNED COPPER DRAIN WIRE	FOUR PAIR #24 BELDEN 1585LC	GROUND SHIELD DRAIN WIRE AT PANEL END ONLY. ROUTE ALL DEVICENET & CAT5e CABLES IN SEPARATE DEDICATED RACEWAY.
<del>AERIAL, SELF-SUPPORTED TELEPHONE CABLE</del>	<del>RUS APPROVED PE-38, AERIAL FIGURE 8 TELEPHONE CABLE</del>	<del>ON SITE TWELVE PAIR #22 AWG</del>	<del>ALL INSTALLATION SHALL CONFORM TO THE APPLICABLE RUS BULLETIN.</del>

COLOR CODING - UNLESS SPECIFICALLY INDICATED OTHERWISE COLOR CODE CONDUCTORS AS FOLLOWS:  
 480-VOLT POWER CONDUCTORS  
 PHASE A - BROWN  
 PHASE B - ORANGE  
 PHASE C - YELLOW  
 NEUTRAL - WHITE WITH YELLOW STRIPE  
 120/208-VOLT POWER CONDUCTORS  
 PHASE A - BLACK  
 PHASE B - RED  
 PHASE C - BLUE  
 NEUTRAL - WHITE  
 24 VOLT DC CONDUCTORS  
 +24VDC - RED or RED WITH GRAY STRIPE  
 -24VDC - BLACK or BLACK WITH GRAY STRIPE  
 CONTROL & INSTRUMENT CONDUCTORS  
 COLOR CODED PER MANUFACTURER'S STANDARD

NOTES:  
 1) FOR NO. 6 AWG AND SMALLER CONDUCTORS COLOR CODING SHALL BE PROVIDED BY USING CONDUCTORS WITH CONTINUOUS COLOR EMBEDDED IN THE INSULATION. FOR ALL CONDUCTORS LARGER THAN NO. 6 SCOTCH 35 MARKING TAPE OR EQUIVALENT MAY BE USED TO COLOR CODE THE CABLE. WHERE MARKING TAPE IS USED THE CABLE SHALL BE IDENTIFIED AT EVERY ACCESSIBLE LOCATION. PROVIDE A MINIMUM OF 2 INCHES OF TAPE AT EACH LOCATION.  
 2) GROUNDING - PROVIDE A SEPARATE GREEN INSULATED EQUIPMENT GROUNDING CONDUCTOR IN EACH RACEWAY. DO NOT USE THE CONDUIT AS AN EQUIPMENT GROUNDING CONDUCTOR. EQUIPMENT GROUNDING CONDUCTORS SHALL BE OF THE SAME TYPE AS THE PHASE CONDUCTORS AND SHALL BE SIZED AS INDICATED ON THE DRAWINGS. CONDUCTORS NOT INDICATED SHALL BE SIZED IN ACCORDANCE WITH THE NATIONAL ELECTRICAL CODE.

**WIRING & DEVICE SYMBOL LEGEND**

SYMBOL	DESCRIPTION
SS-##	HOME RUN TO PANEL & BREAKER(S) INDICATED. SHORT DASH INDICATES HOT CONDUCTOR, LONG DASH INDICATES NEUTRAL CONDUCTOR, CURVED DASH INDICATES GROUND CONDUCTOR. IF NOT SPECIFICALLY INDICATED, PROVIDE 2#12 AWG & 1#12 AWG GROUND.
⊕	ELECTRICAL ITEM - SEE EQUIPMENT SCHEDULE
1/4	MOTOR (HOREPOWER INDICATED)
MD	MOTORIZED DAMPER - SEE MECHANICAL
⊖	125V, 20A, DUPLEX RECEPTACLE
Ⓣ	LINE VOLTAGE THERMOSTAT
ⓄT	DIGITAL THERMOSTAT, MODULATING
Ⓢ	SNAP SWITCH / SMALL MOTOR DISCONNECT
ⓉⓈ	TIMER SWITCH
Ⓧ	GROUND

**INSTRUMENTATION & ENERGY MEASUREMENT LEGEND**

NOTE: SEE SCHEDULES SHEET M1.1 FOR EQUIPMENT SPECIFICATIONS.


SYMBOL	SERVICE/FUNCTION	SYMBOL	SERVICE/FUNCTION
Ⓣ	TEMPERATURE TRANSMITTER	Ⓢ	DAY TANK/HOPPER FLOAT SWITCH
ⓉT	PRESSURE TRANSMITTER	ⓄLS	GLYCOL TANK LEVEL SENSOR PROBE
ⓈM	HEAT RECOVERY FLOW METER	ⓉLM	TANK LEVEL MONITOR PANEL
ⓄCA	GLYCOL TANK LOW COOLANT ALARM	ⓄSP	TANK LEVEL SENSOR PROBE

AS PART OF THE MODULE ASSEMBLY WORK FURNISH AND INSTALL ALL MATERIALS AND EQUIPMENT ON THE SCHEDULES THIS SHEET EXCEPT FOR THOSE ITEMS SPECIFICALLY NOTED "ON SITE".

ITEMS SPECIFICALLY NOTED AS ON-SITE WILL BE FURNISHED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT.

REVISION #1  
 ISSUED FOR  
 CONSTRUCTION  
 JULY 2022





1	UPDATED TO COORDINATE WITH ON SITE DESIGN & NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: ELECTRICAL LEGENDS & SCHEDULES			
DRAWN BY: JTD		SCALE: NO SCALE	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM PP E1		SHEET: E1.1	
PROJECT NUMBER:			
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

**GROUNDING GENERAL NOTES:**

- 1) POWER PLANT GROUNDING GRID PROVIDED BY 4 EACH STEEL HELICAL PILES WELDED TO MAIN STEEL SKID BEAMS. POWER PLANT STRUCTURE IS A CONTINUOUSLY WELDED STEEL MODULE. FUEL TANK GROUNDING IS EQUIVALENT.
- 2) MAKE ALL CABLE CONNECTIONS TO STRUCTURE, SKIDS, OR SUPPORT PEDESTALS WITH COPPER COMPRESSION LUGS AND STAINLESS STEEL BOLTS. DRILL AND TAP STRUCTURAL MEMBERS TO ENSURE FULL CONTACT OF THREADS TO CLEAN BARE STEEL. SEE DETAIL 2/E2, SIMILAR.
- 3) IN FEEDER SECTION PROVIDE #2/0 BARE COPPER JUMPER FROM GROUND BUS TO STEEL FLOOR. SEE DETAIL 2/E2, SIMILAR.

**GROUNDING SHOP/ON-SITE NOTES:**

- 1) ALL WORK SHOWN THIS SHEET TO BE PERFORMED AS PART OF THE SHOP FABRICATION.
- 2) FIELD BONDING (WELDING) OF MODULE AND FUEL TANK TO HELICAL PILES TO BE PERFORMED AS PART OF THE ON-SITE WORK.
- 3) AS PART OF SHOP FABRICATION WORK, TEMPORARILY BOND SWITCHGEAR NEUTRAL BUS TO GROUND BUS FOR LOAD BANK TESTING AND LEAVE IN PLACE.
- 4) AS PART OF ON-SITE WORK LEAVE NEUTRAL TO GROUND BUS BONDING JUMPER IN PLACE AS REQUIRED FOR LOAD BANK TESTING.
- 5) REMOVE JUMPER AFTER LOAD BANK TESTING AND PRIOR TO CONNECTING TO THE GRID FOR COMMISSIONING.

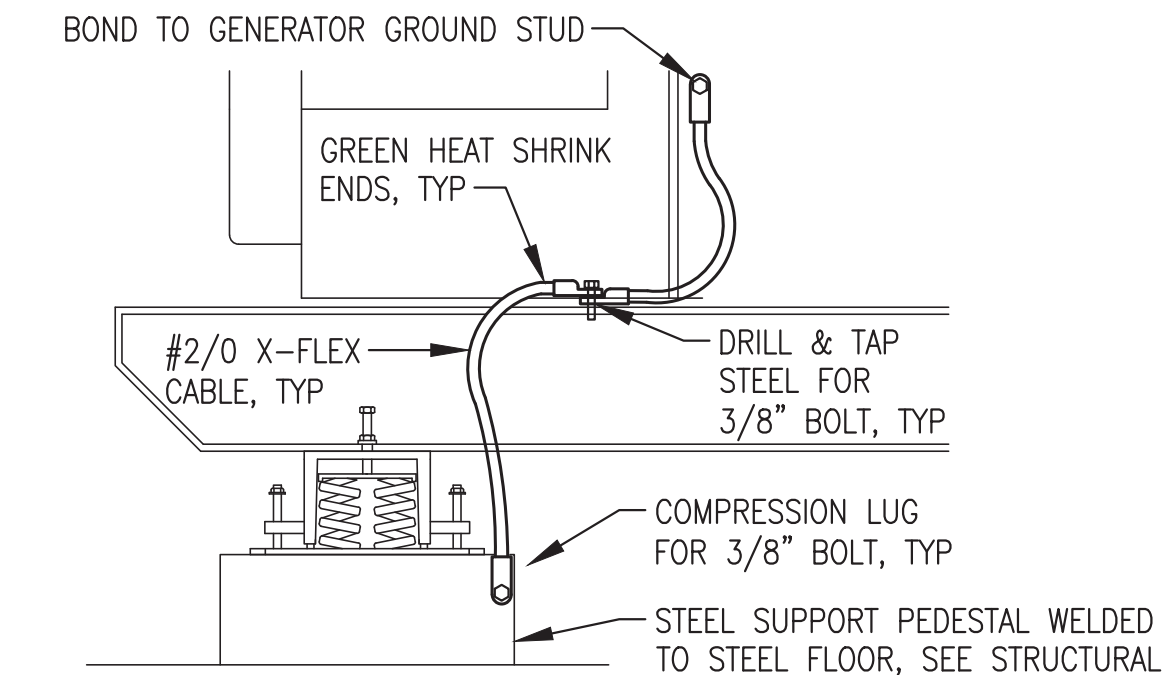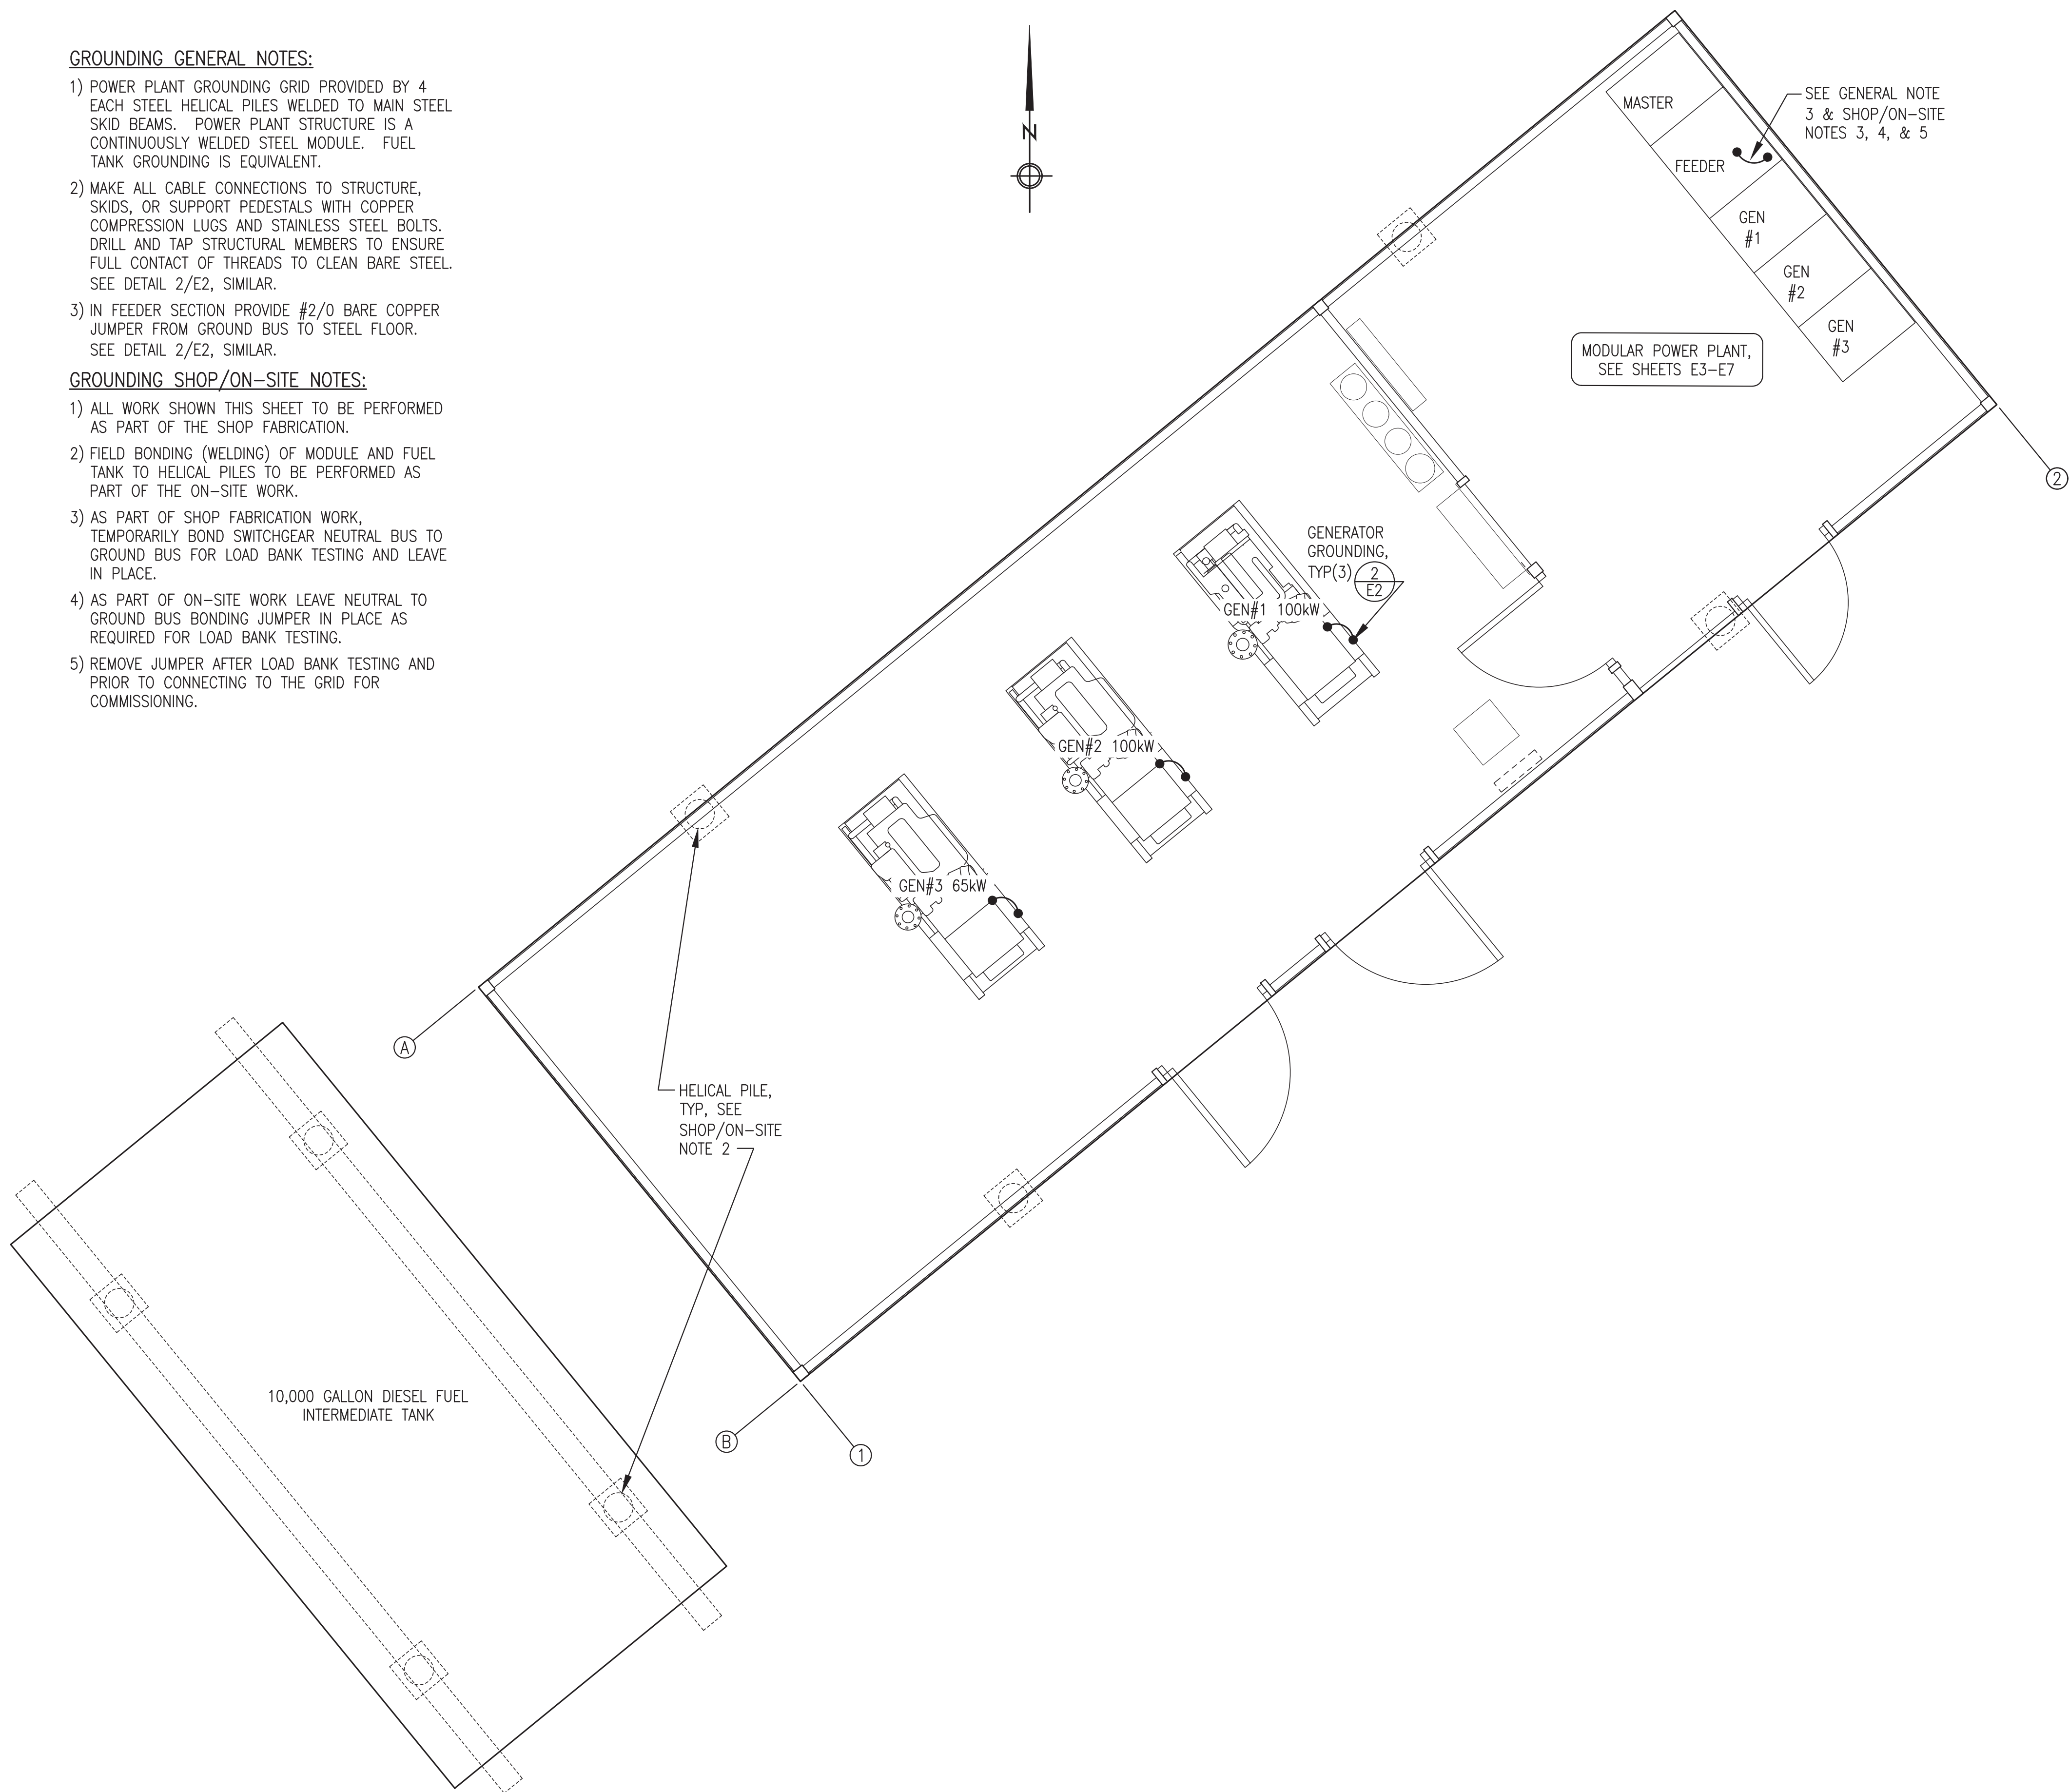


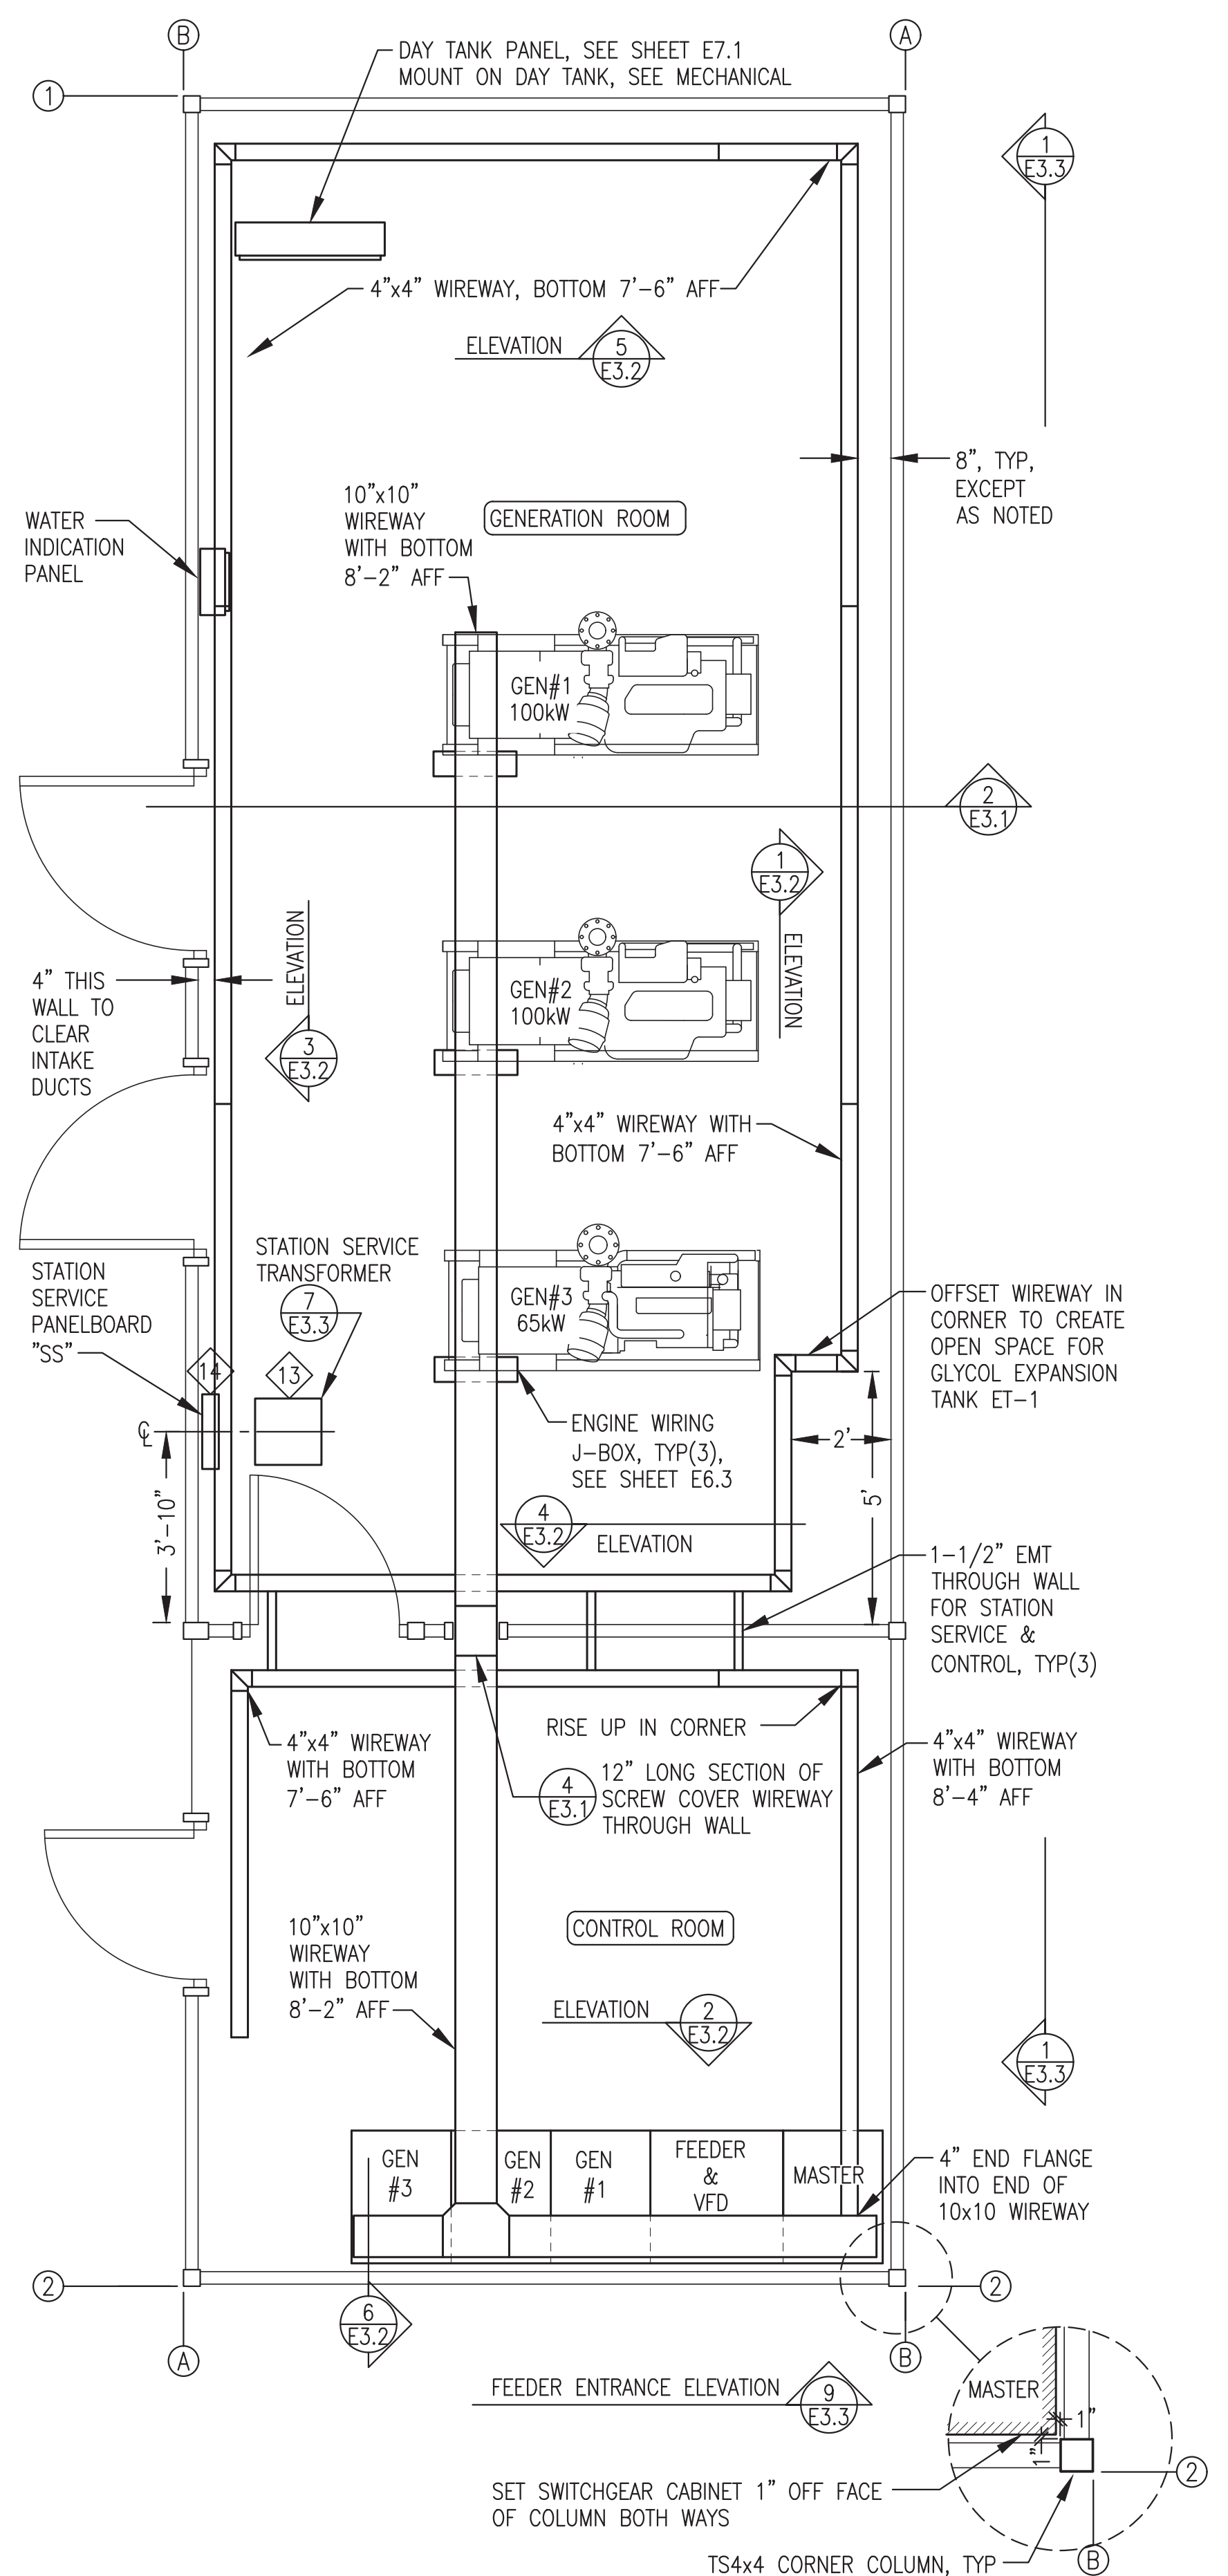
**2**  
**E2** GENERATOR GROUNDING  
NO SCALE

**1**  
**E2** POWER PLANT GROUNDING PLAN  
3/8"=1'-0"


REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH ON SITE DESIGN	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: GROUNDING PLAN & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_E2-E5		SHEET: E2	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			




**1** EQUIPMENT LAYOUT & WIREWAY PLAN  
E3.1 3/8"=1'-0"

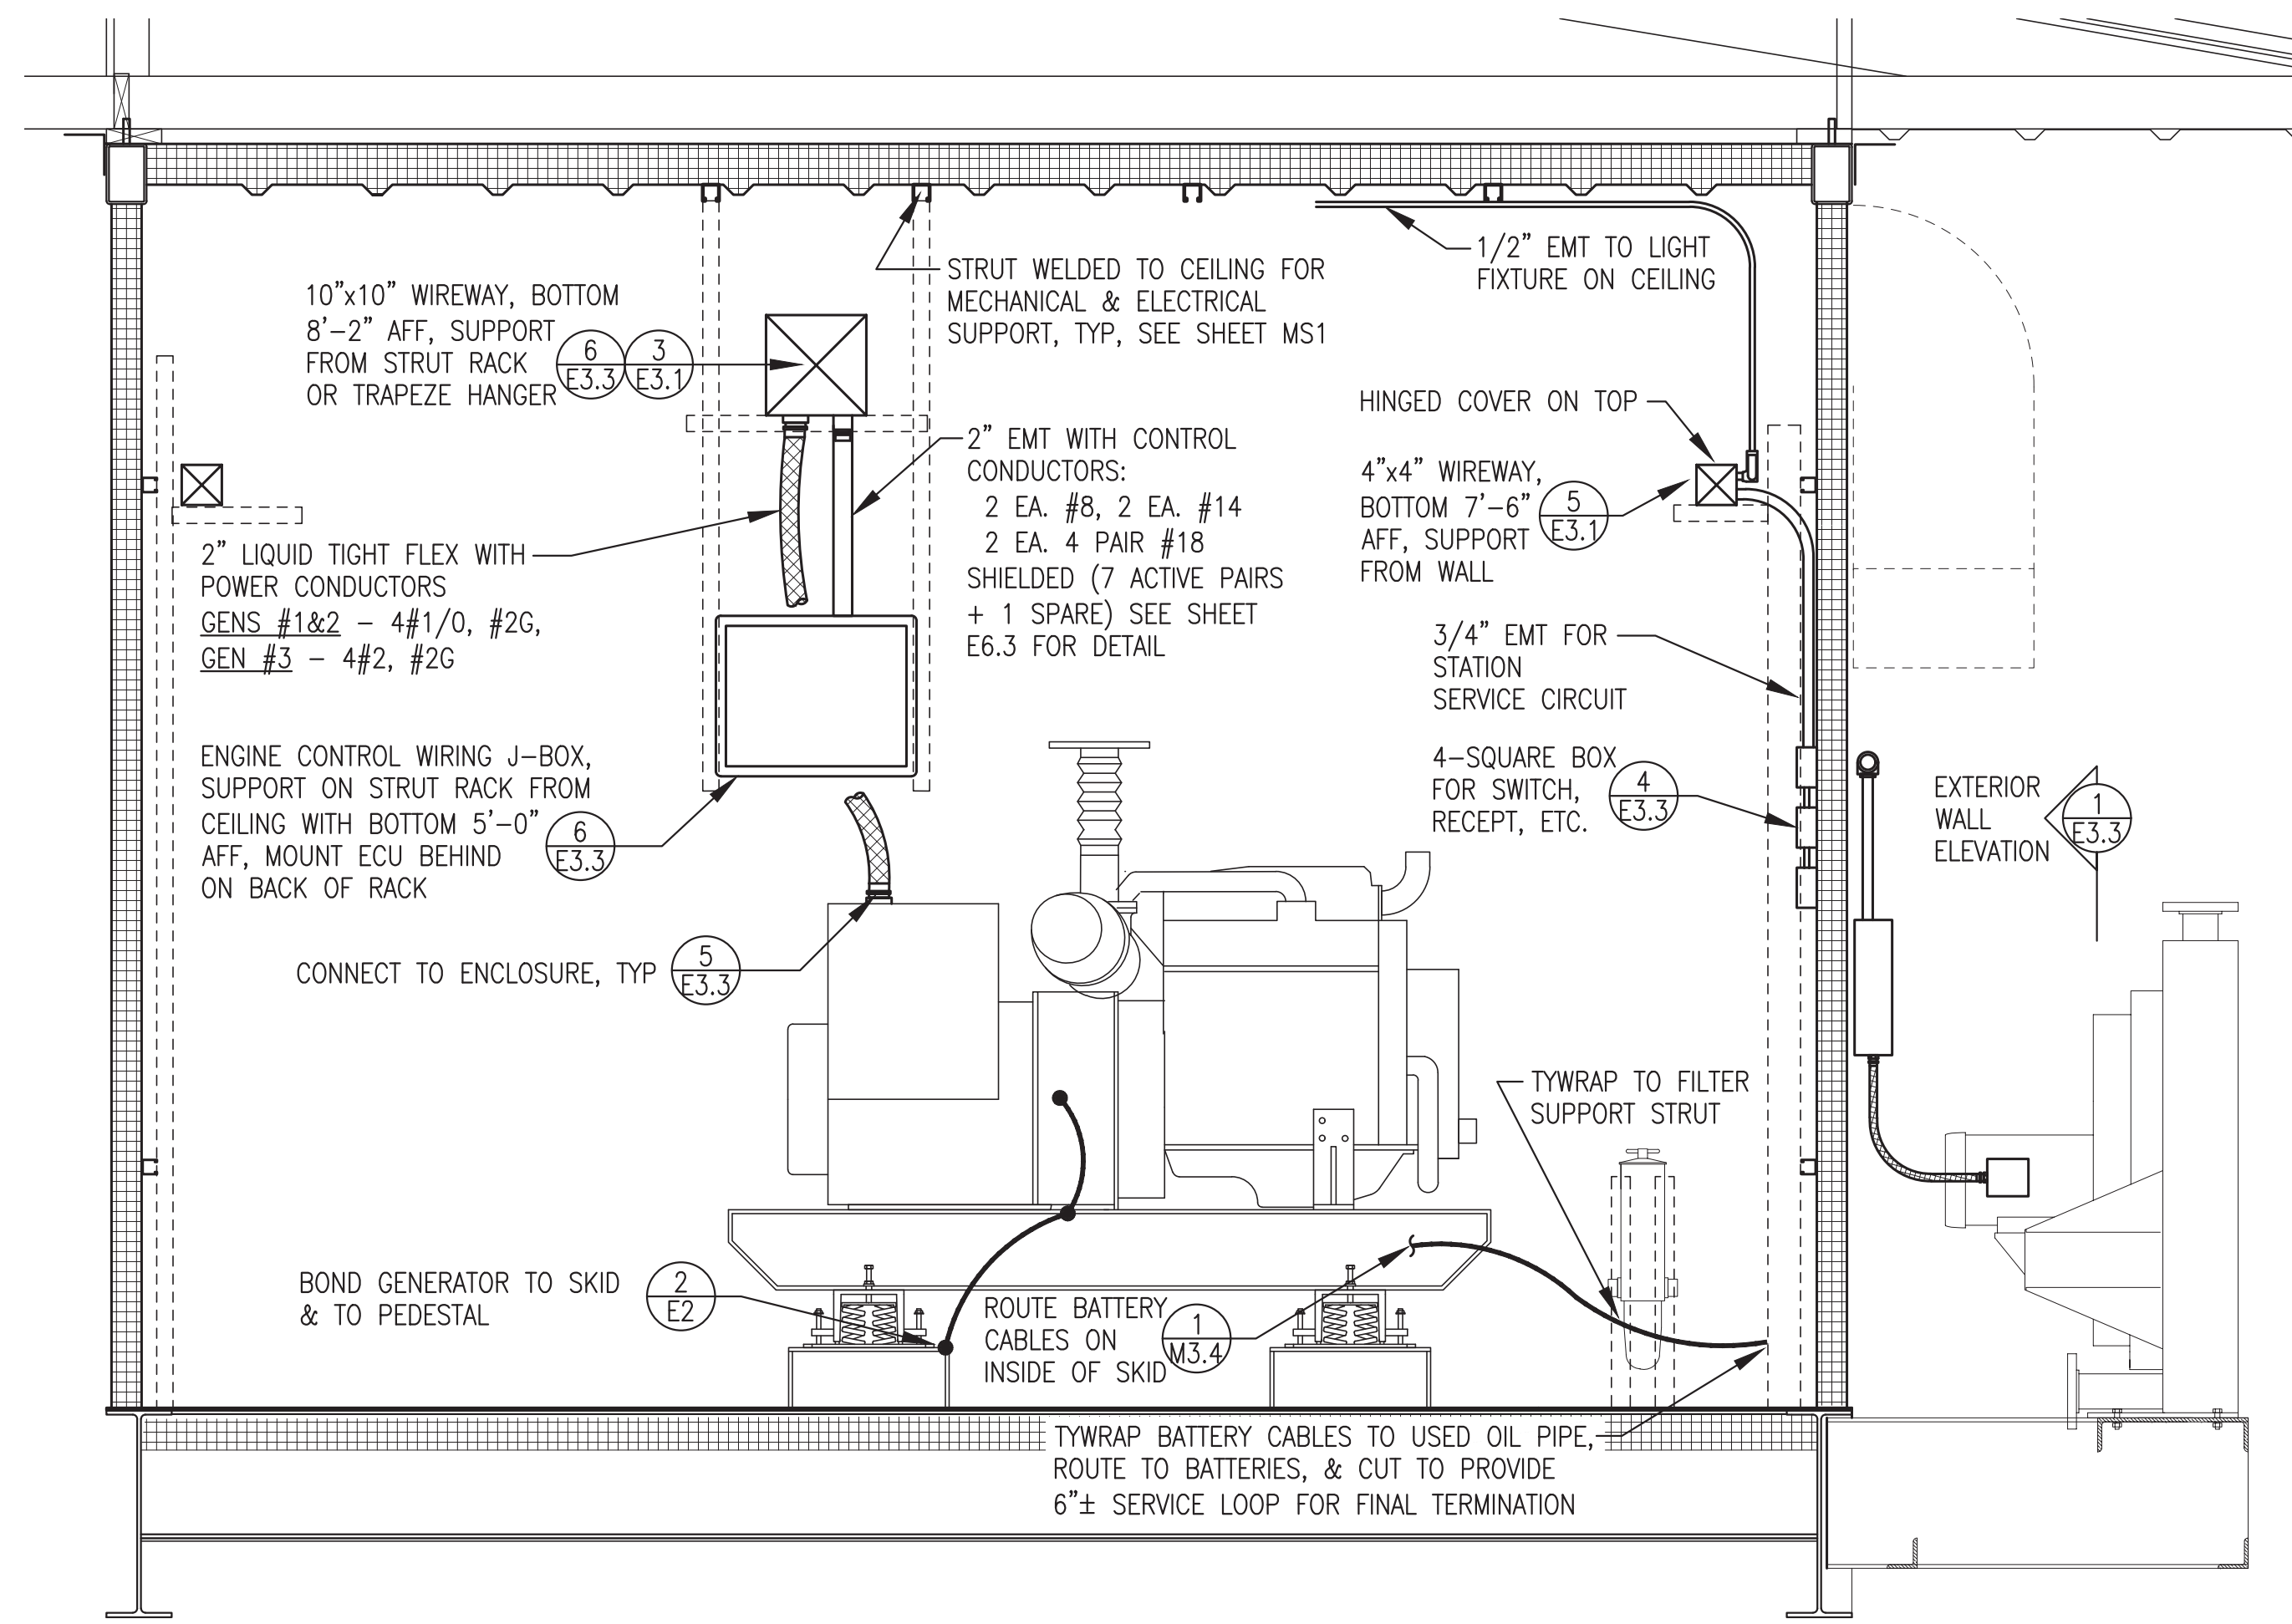


**2** TYPICAL MODULE SECTION  
E3.1 3/4"=1'-0"

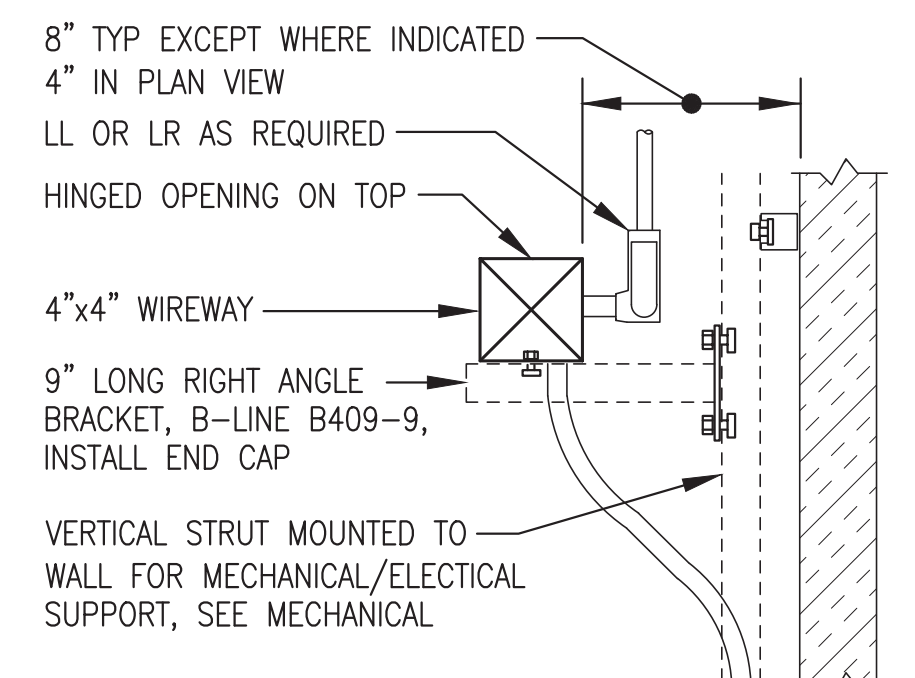

**5** 4" WIREWAY SUPPORT FROM WALL  
E3.1 NO SCALE

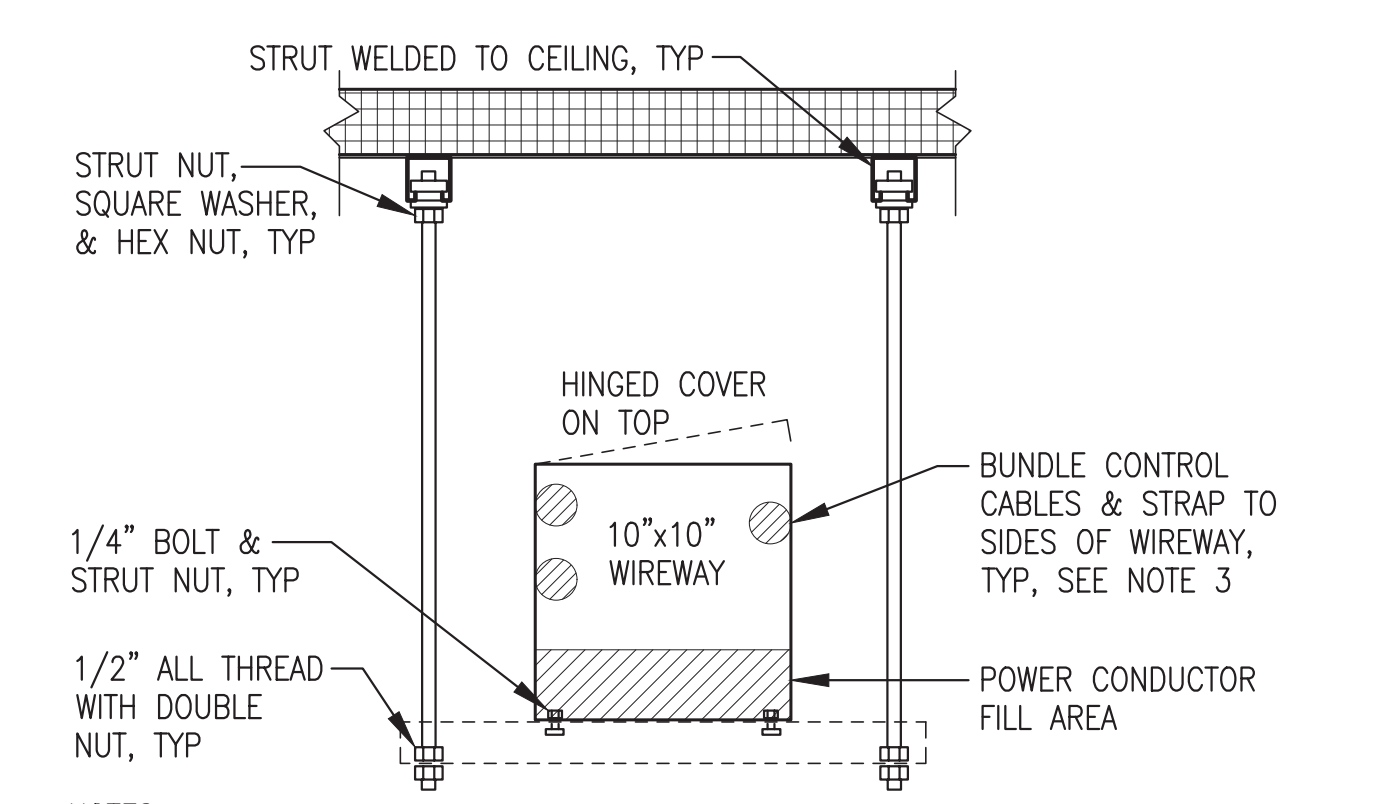

**3** 10" WIREWAY TRAPEZE HANGER  
E3.1 NO SCALE

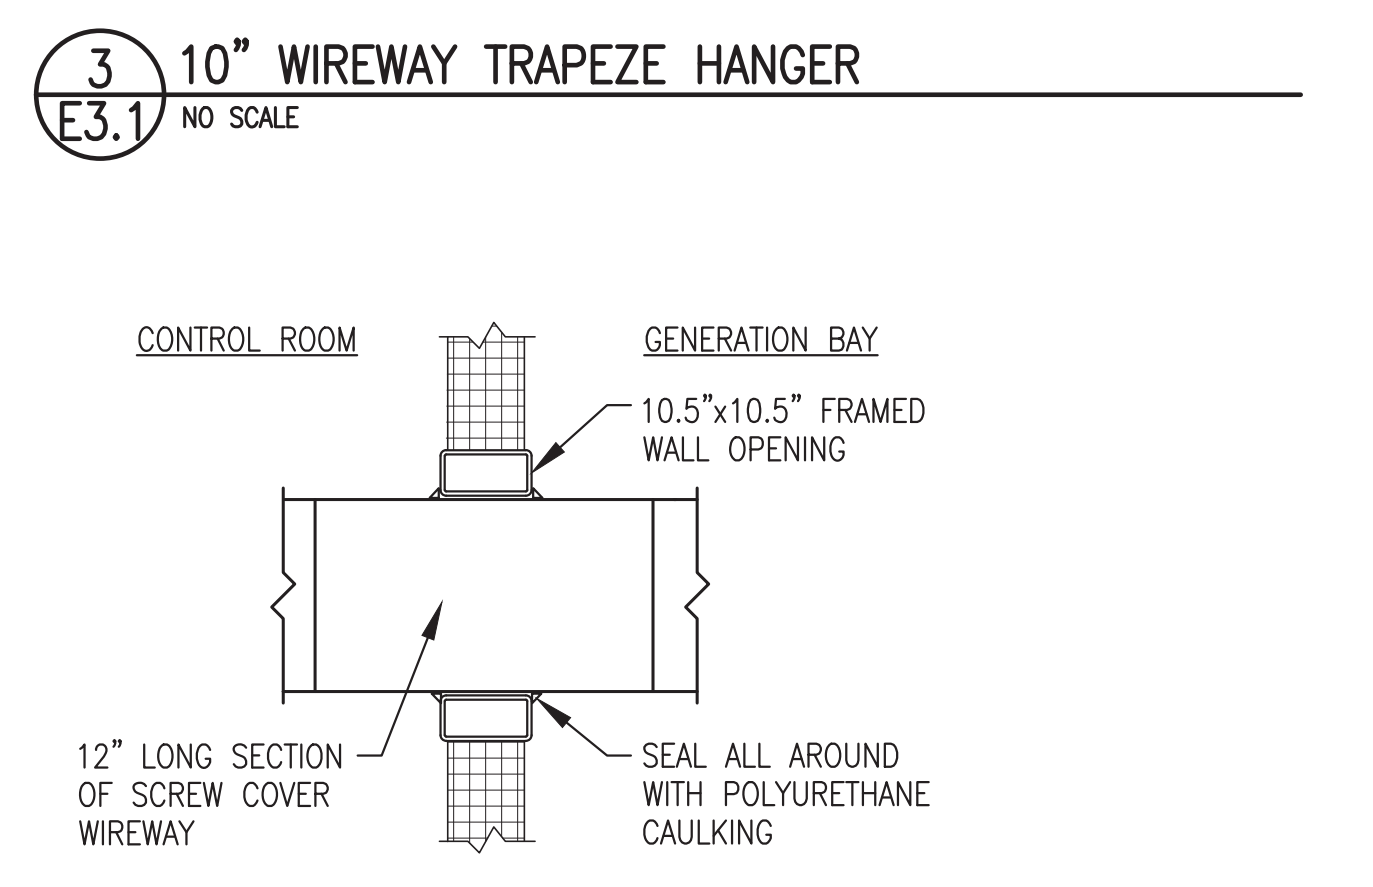


**4** WIREWAY WALL PENETRATION  
E3.1 NO SCALE

ENGINE-GENERATOR SCHEDULE	
GENSET	DESCRIPTION
GEN #1	ENGINE - 148 HP, 100 EKW PRIME, JOHN DEERE 4045AFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 125 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UCI274E.
GEN #2	ENGINE - 148 HP, 100 EKW PRIME, JOHN DEERE 4045AFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 125 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UCI274E.
GEN #3	ENGINE - 99 HP, 65 EKW PRIME, JOHN DEERE 4045TFM85, TIER 3 MARINE. 24 VDC STARTING & CONTROL. GENERATOR - MINIMUM 90 KW CONTINUOUS AT 105°C RISE, NEWAGE/STAMFORD UCI274C.


REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: WIREWAY PLAN, BUILDING SECTION, & DETAILS			
		DRAWN BY: JTD DESIGNED BY: CWV/BCG FILE NAME: RAM_PP_E2-E5 PROJECT NUMBER:	SCALE: AS NOTED DATE: 3/15/22 SHEET: <b>E3.1</b>
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

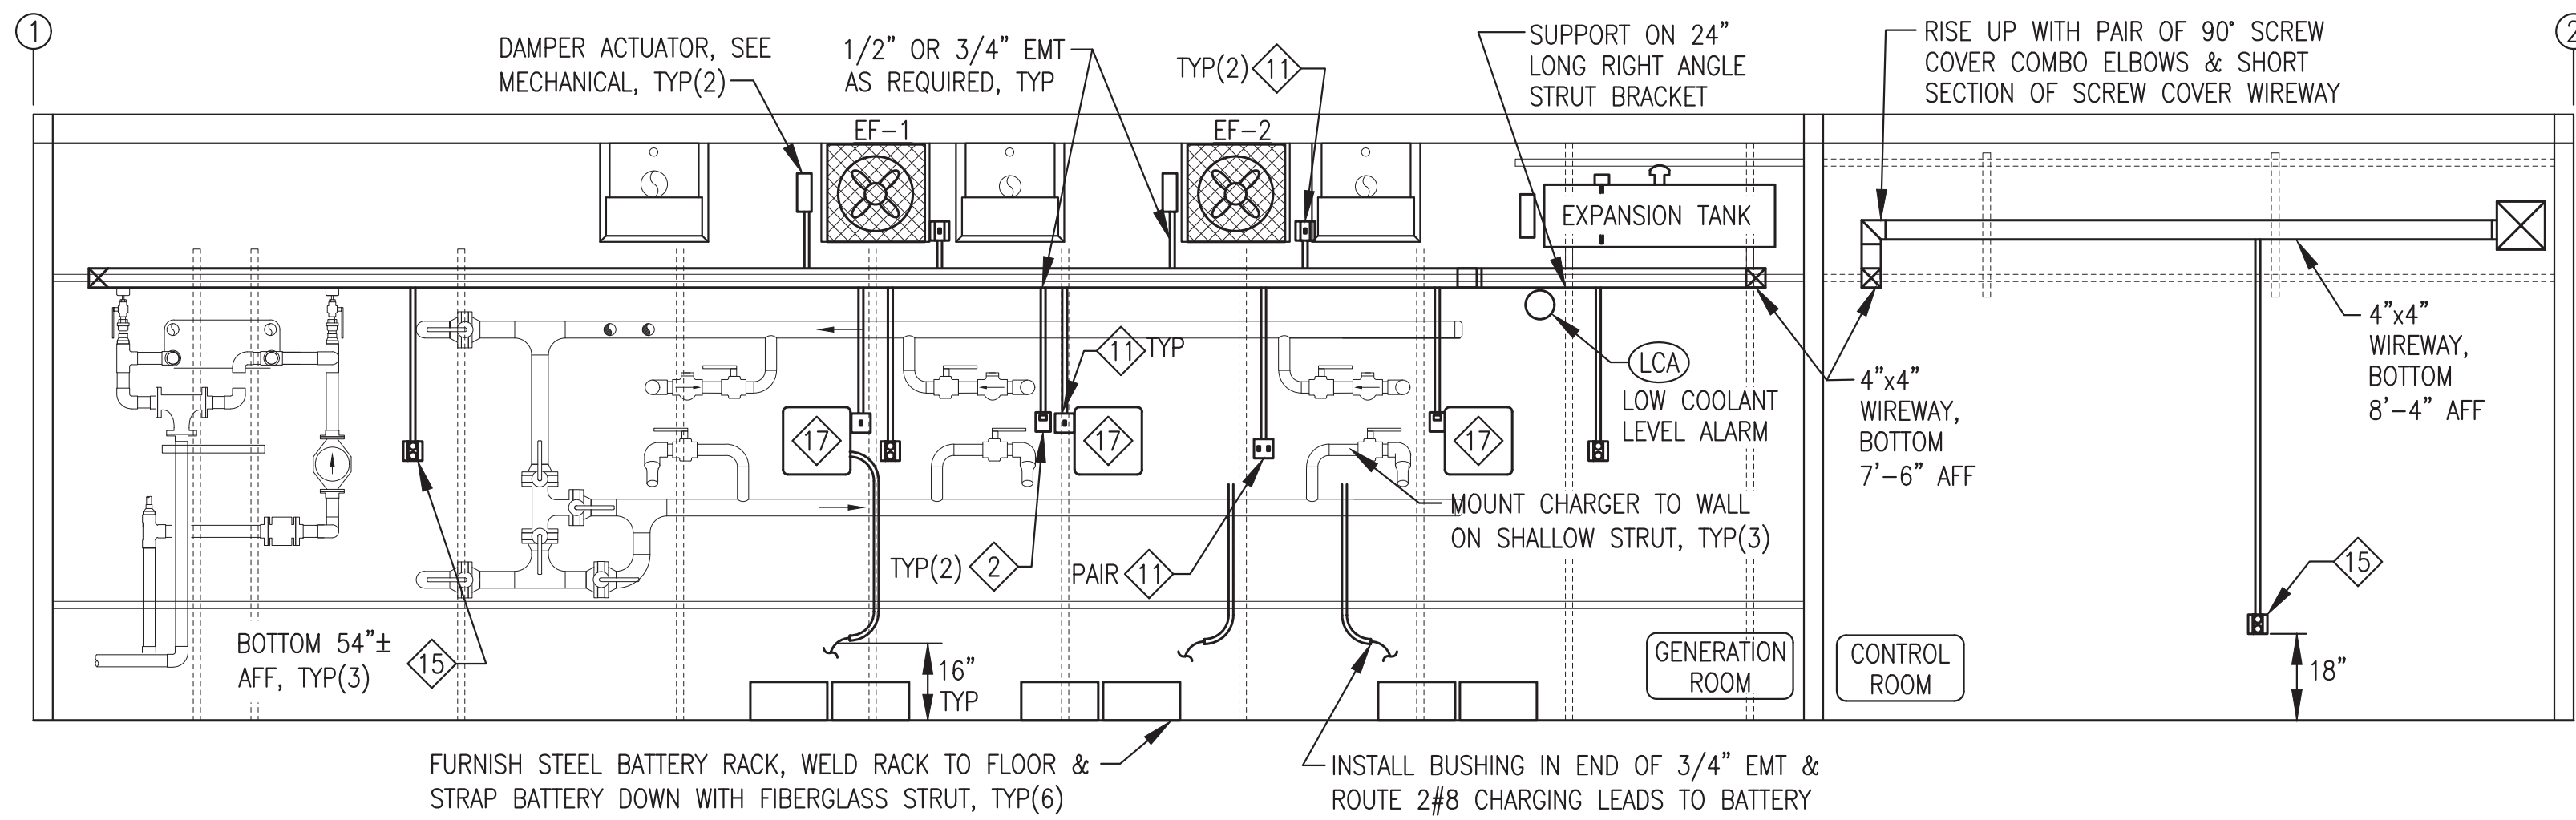


1 WALL ELEVATION AT GRID A  
E3.2 3/8"=1'-0"

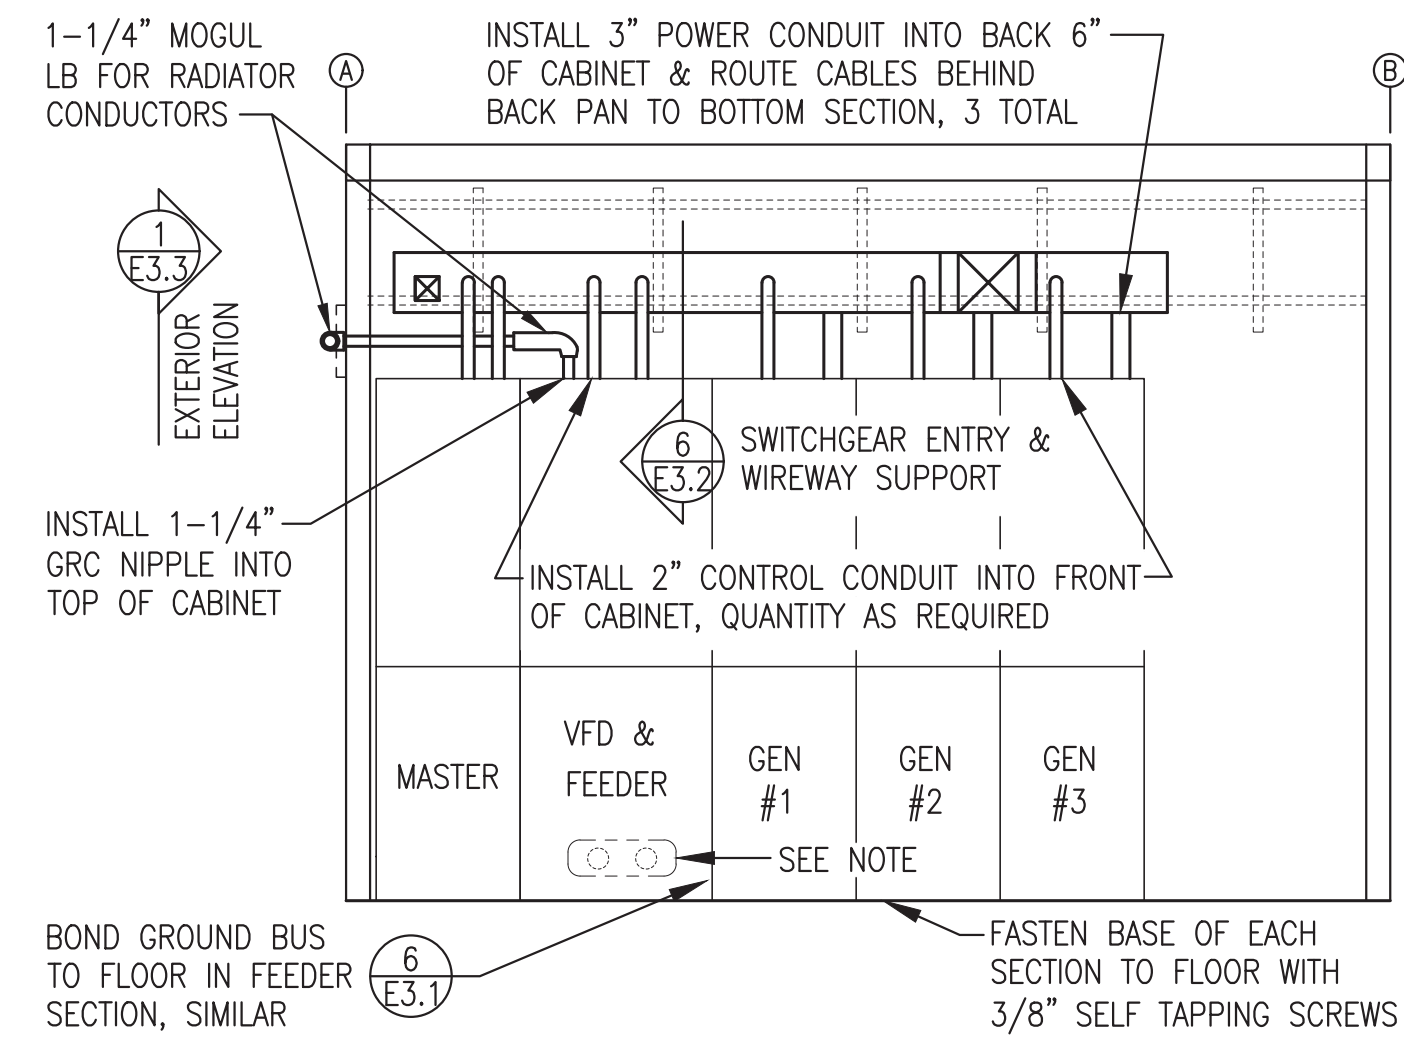


2 WALL ELEVATION AT GRID 2  
E3.2 3/8"=1'-0"

NOTE:  
CENTER OPENING IN BACK  
OF FEEDER/VFD SECTION  
OVER TWO STEEL NIPPLES  
SHOP WELDED IN WALL  
FOR FEEDER CABLE  
ENTRANCE. SEE DETAIL  
9/E3.3.

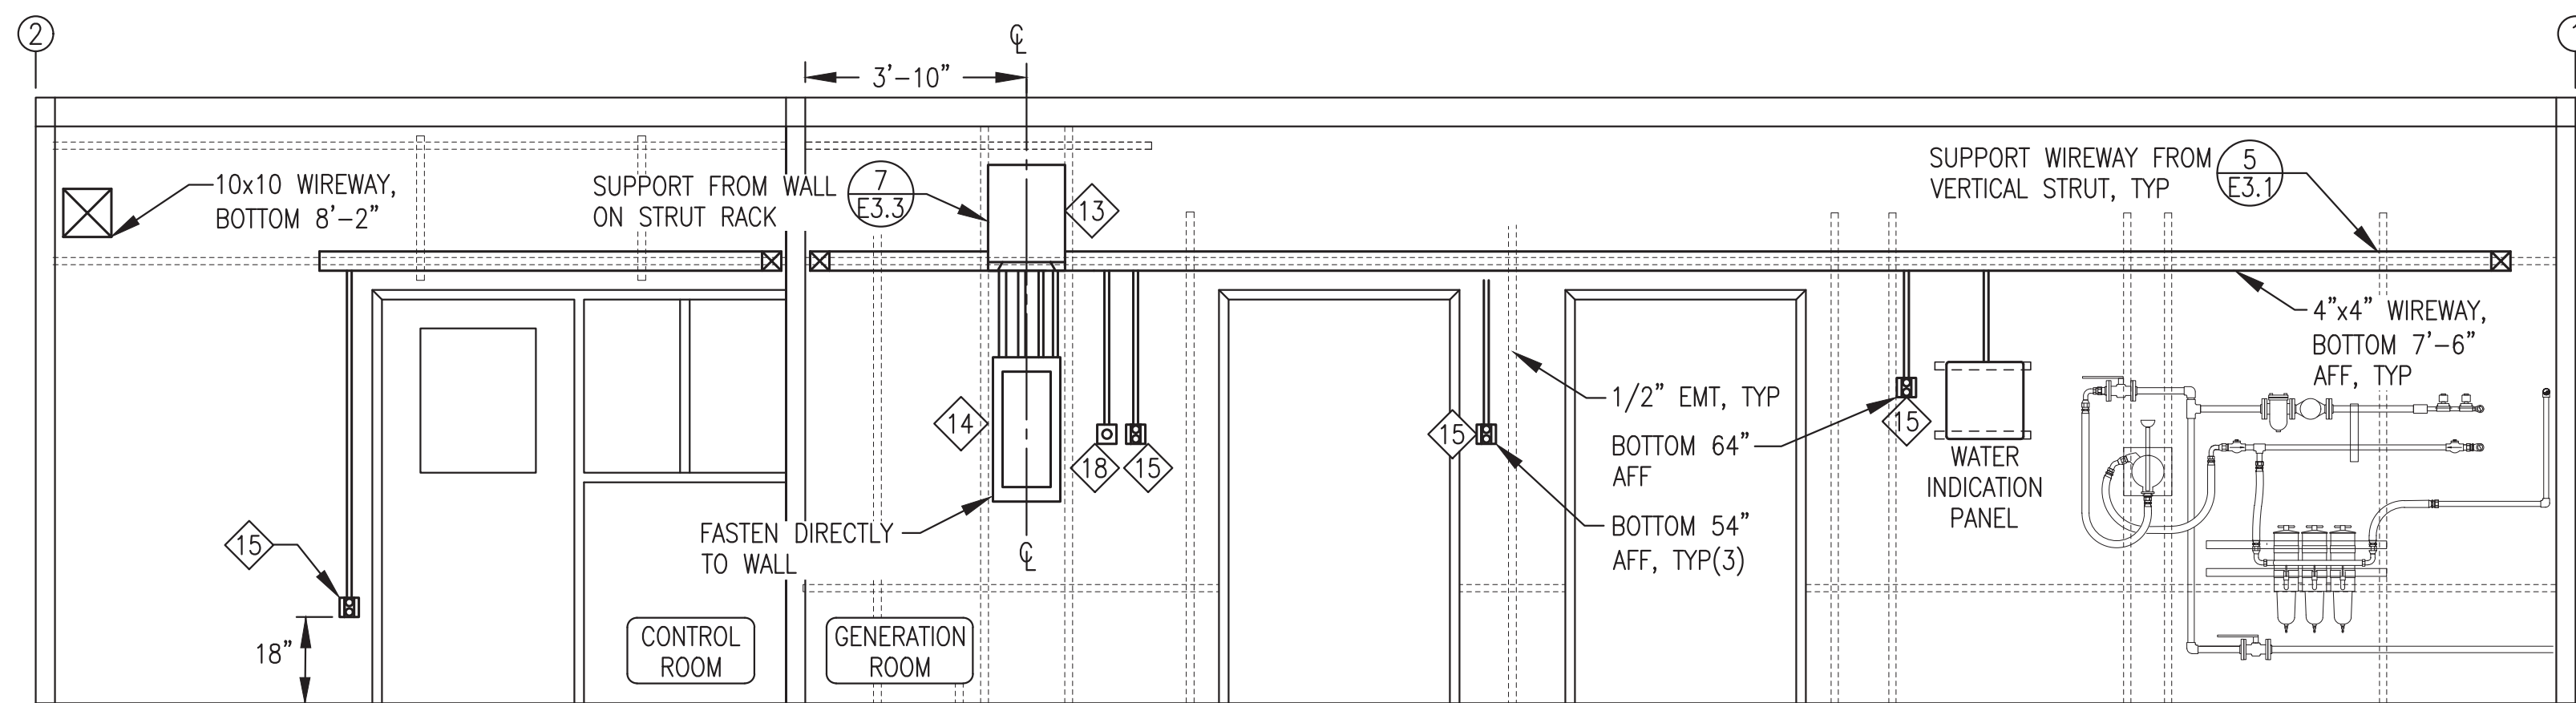


3 WALL ELEVATION AT GRID B  
E3.2 3/8"=1'-0"

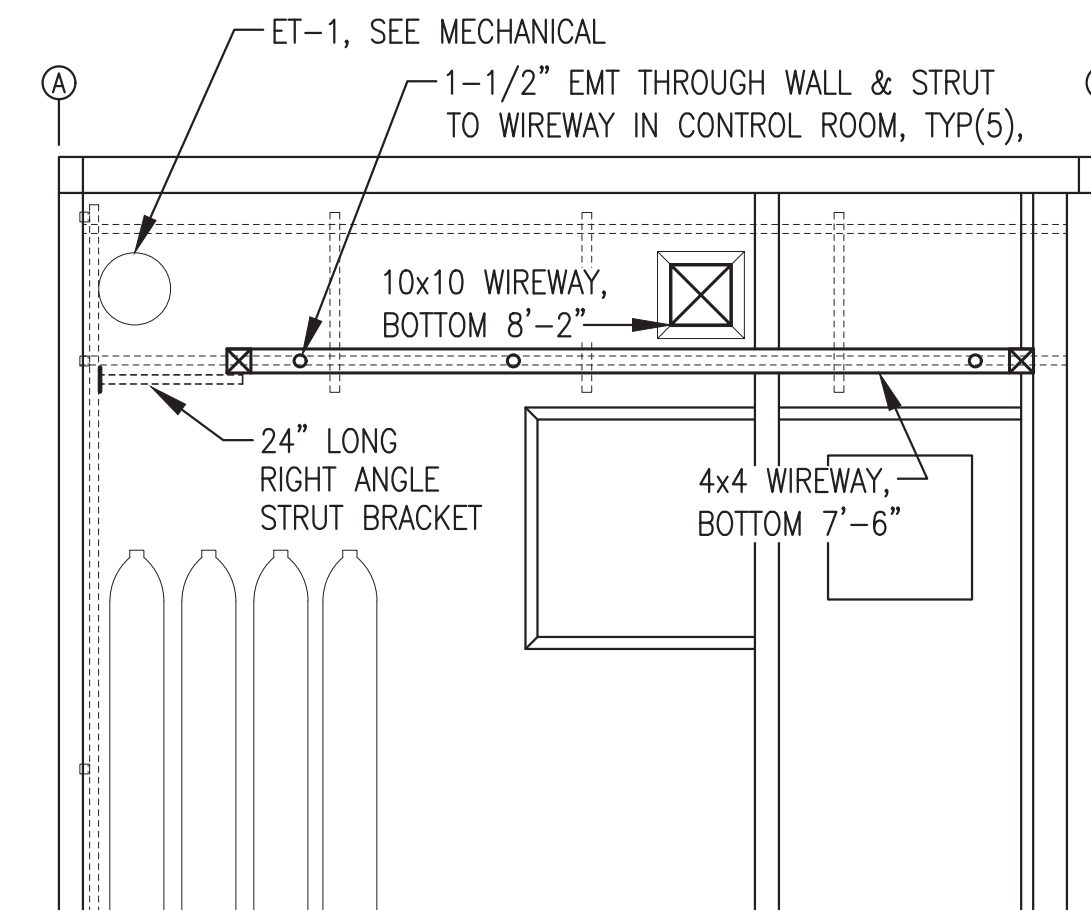


4 INTERIOR WALL ELEVATION  
E3.2 3/8"=1'-0"

GENERAL NOTE:  
WALL ELEVATIONS SHOWN PRIMARILY FOR GENERAL  
LAYOUT OF MAJOR RACEWAY, EQUIPMENT, AND  
DEVICES REQUIRING REGULAR ACCESS FOR  
NORMAL PLANT OPERATIONS. ALL EQUIPMENT,  
DEVICES & INSTRUMENTATION CIRCUITS NOT  
SHOWN FOR CLARITY. SEE PLANS & DETAILS  
FOR COMPLETE ELECTRICAL INSTALLATIONS.

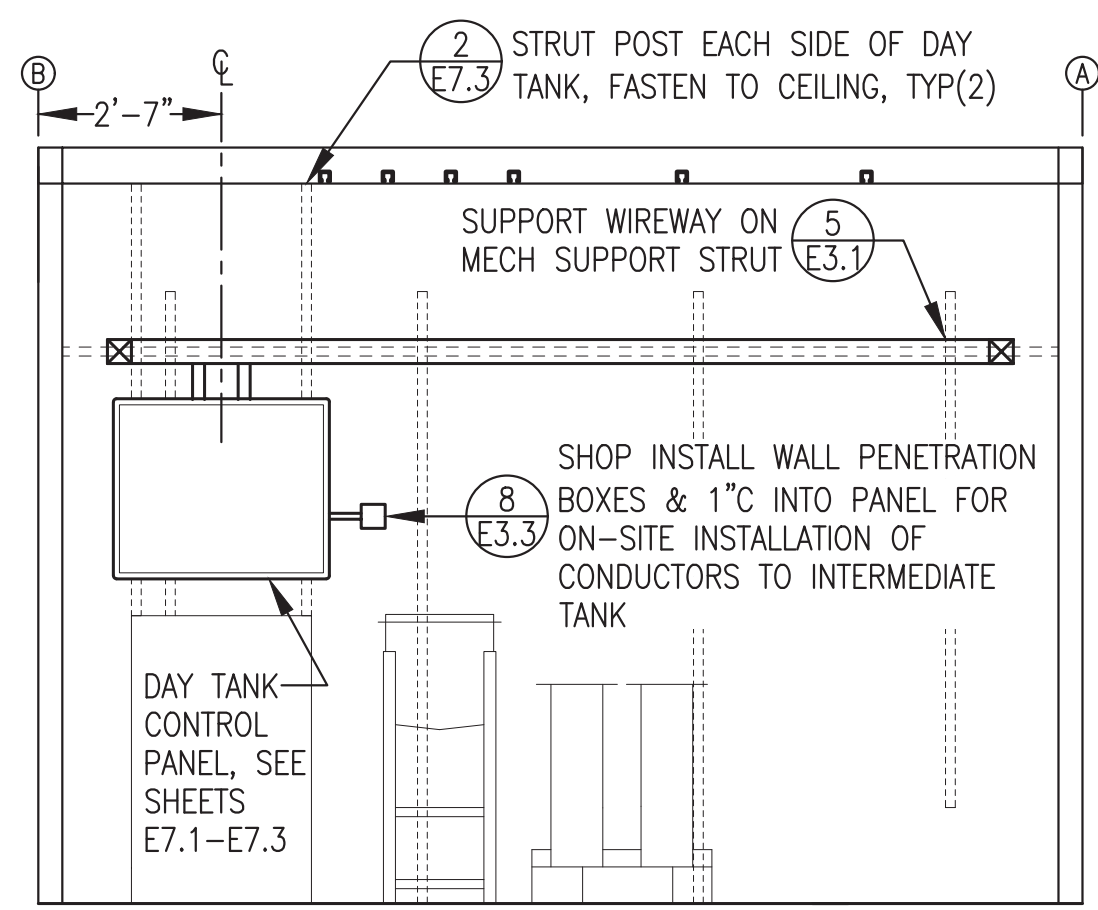


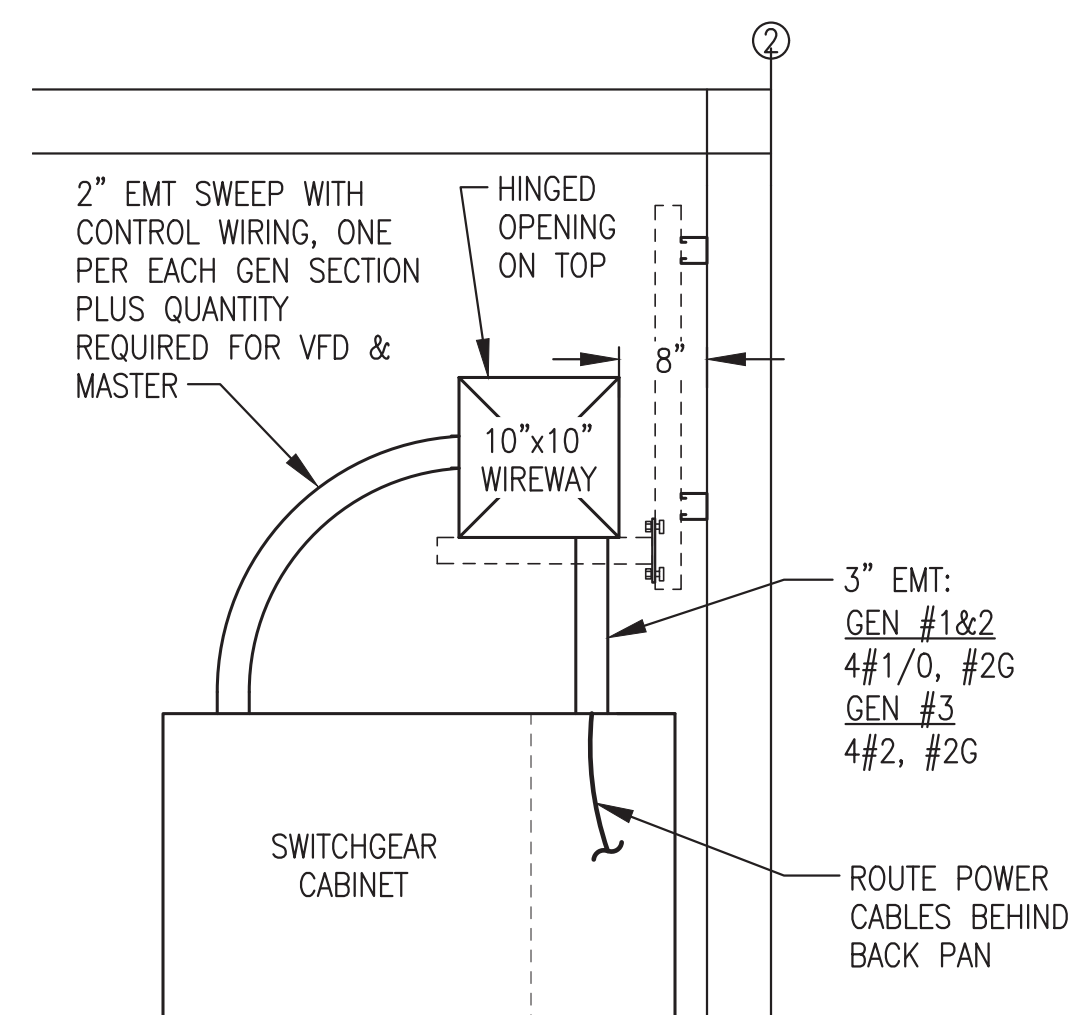

5 WALL ELEVATION AT GRID 1  
E3.2 3/8"=1'-0"




6 SWITCHGEAR ENTRY & WIREWAY SUPPORT  
E3.2 NO SCALE

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT: <b>RAMPART POWER SYSTEM UPGRADE</b>			
TITLE: <b>ELEVATIONS &amp; DETAILS</b>			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP E2-E5		SHEET:	
PROJECT NUMBER:		<b>E3.2</b>	
 <b>Gray Stassel Engineering, Inc.</b> P.O. 111405, Anchorage, AK 99511 (907)349-0100			




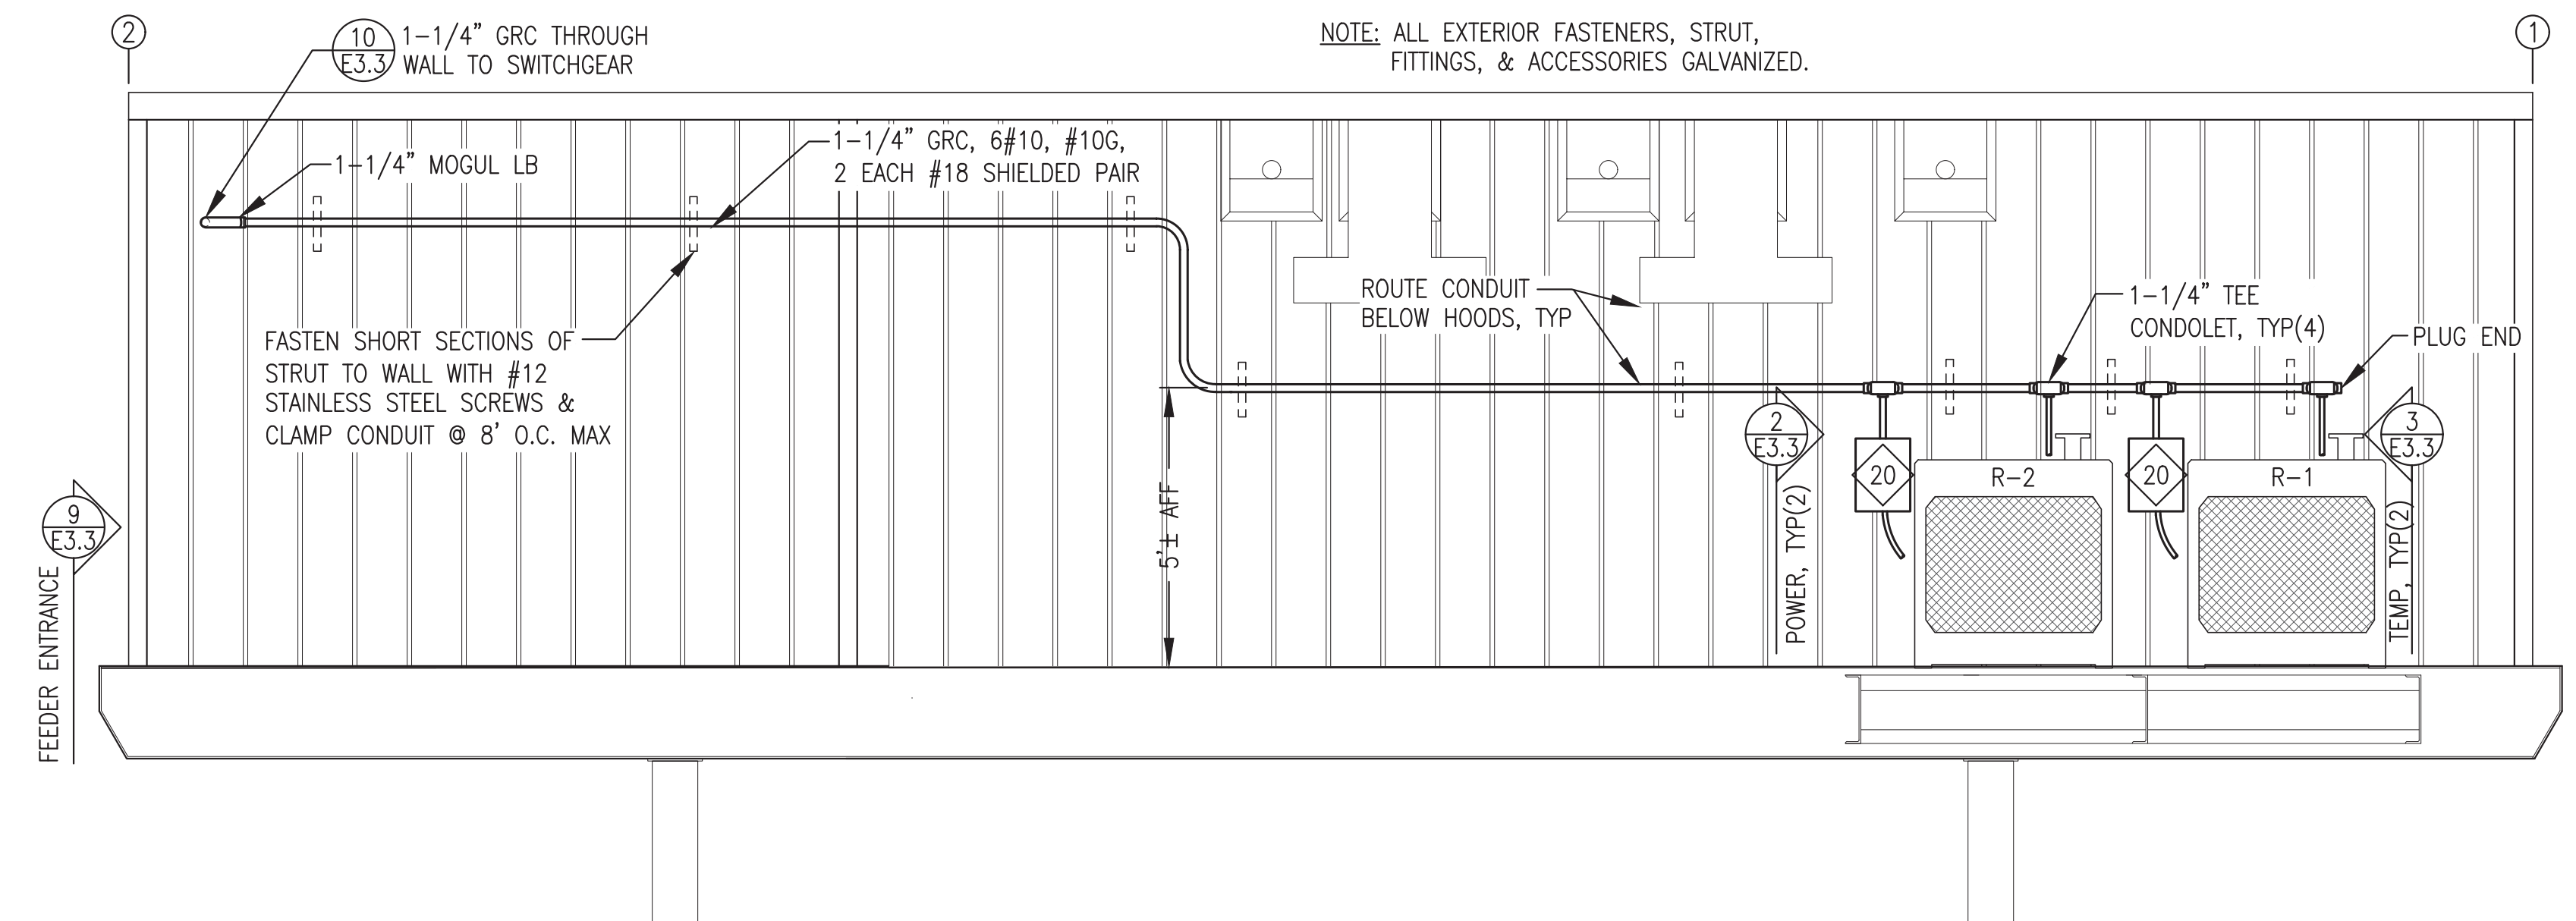

**1** BACK WALL EXTERIOR ELEVATION  
E3.3 3/8"=1'-0"

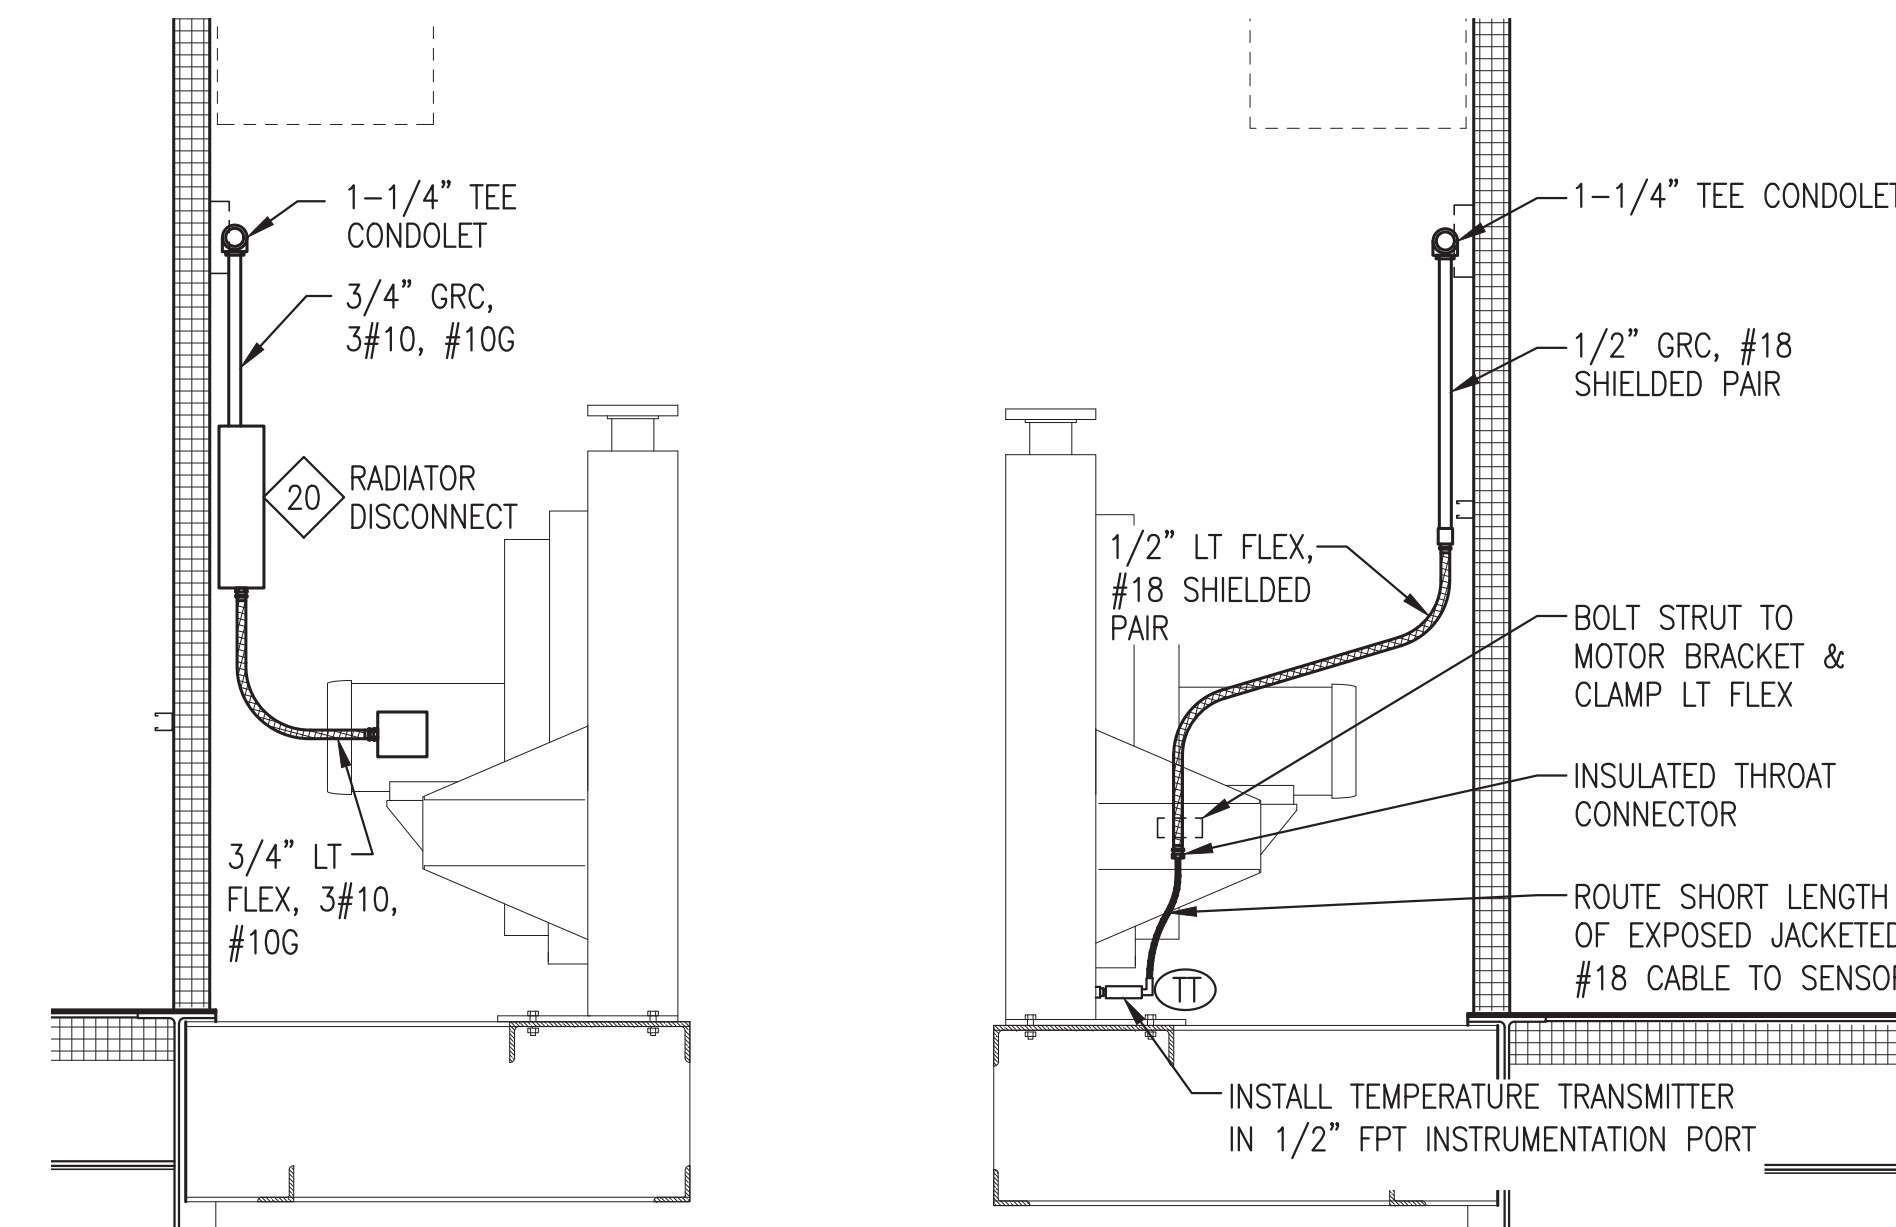


**2** RADIATOR POWER CONNECTION  
E3.3 3/4"=1'-0"

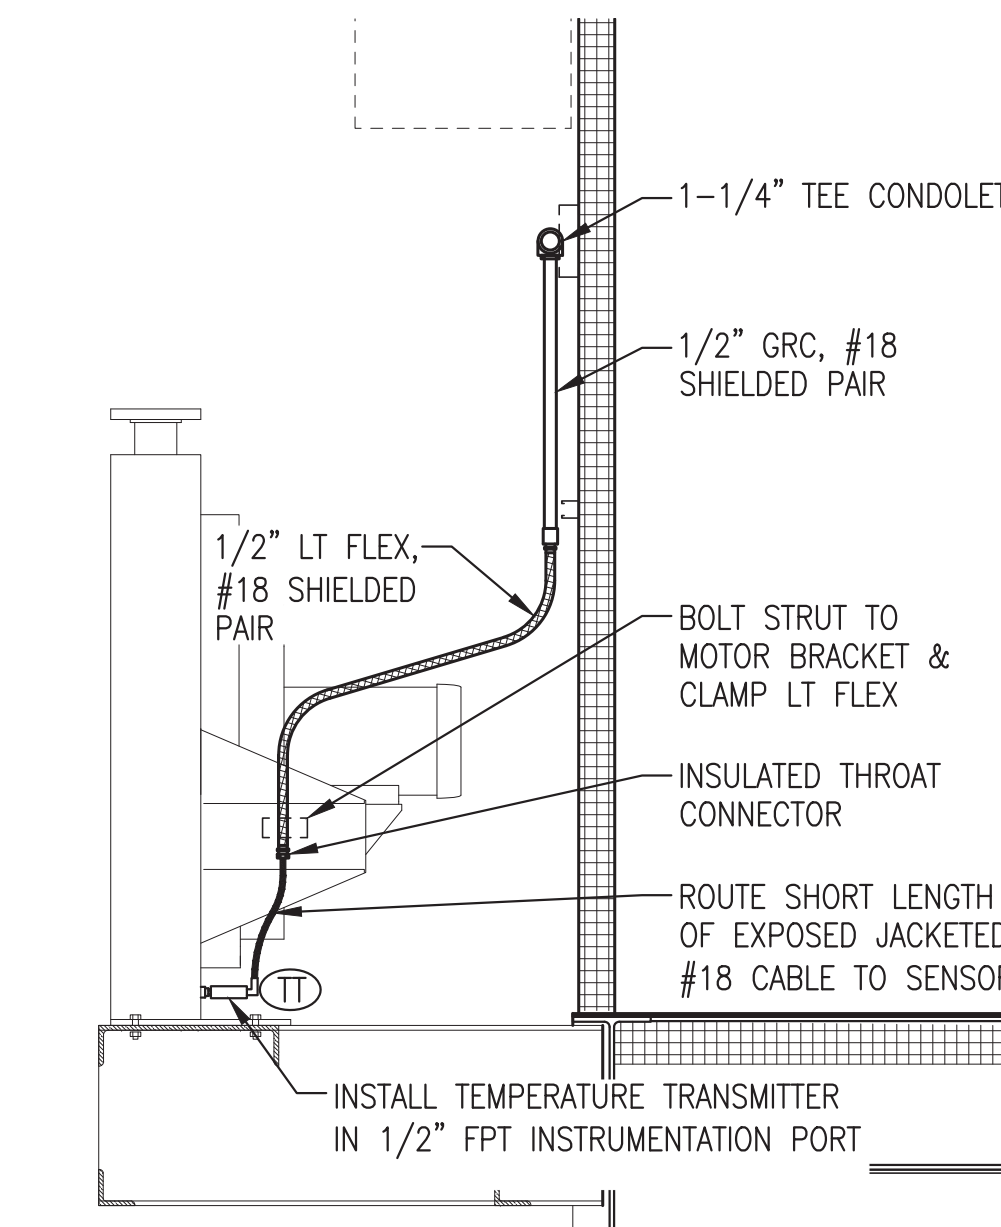


**3** RADIATOR TEMPERATURE TRANSMITTER  
E3.3 3/4"=1'-0"

**RADIATOR SHOP/ON-SITE NOTES:**  
 1) DURING SHOP FABRICATION INSTALL ALL DEVICES AND RACEWAYS AS INDICATED.  
 2) AS PART OF ON-SITE WORK, IF RADIATORS ARE REMOVED FOR SHIPPING DISCONNECT LIQUID TIGHT FLEXES AND SEAL ENDS. COIL AND SECURE CONDUCTORS AND FLEXES FOR SHIPPING.  
 3) AS PART OF ON-SITE WORK REINSTALL AS INDICATED.

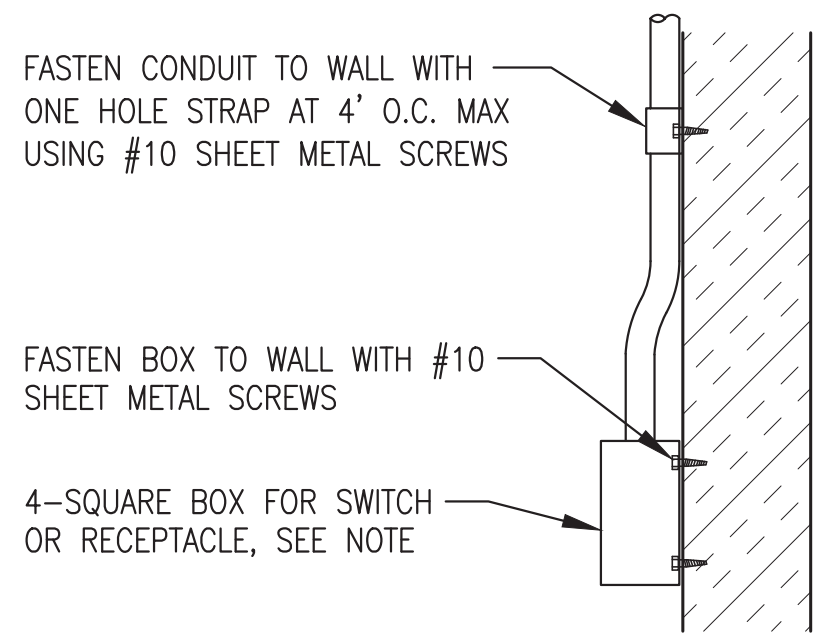


**4** TYPICAL INTERIOR DEVICE MOUNTING  
E3.3 NO SCALE

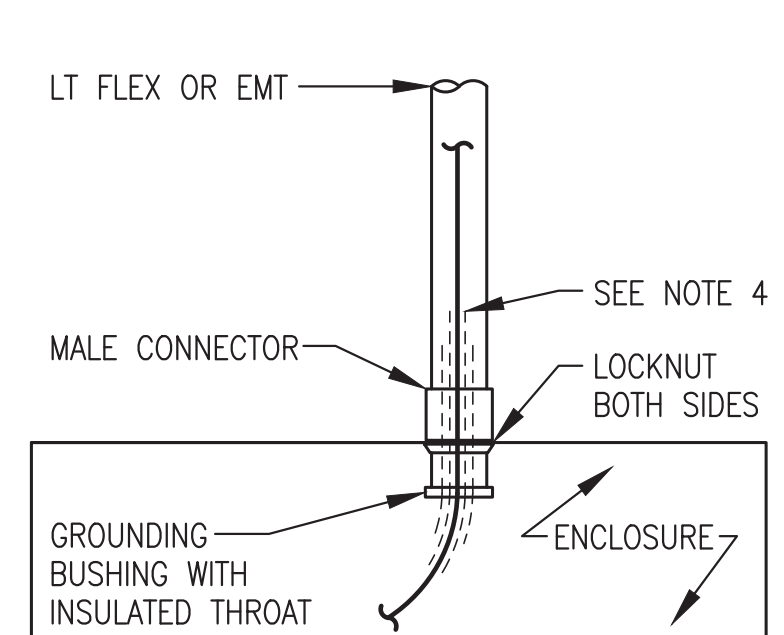


**5** TYP ENCLOSURE CONNECTION  
E3.3 NO SCALE


**NOTES:**  
 1) THIS DETAIL APPLIES TO CONNECTIONS TO WIREWAY, GENERATOR ENCLOSURES, SWITCHGEAR, AND PANELS.  
 2) AT A MINIMUM INSTALL GROUNDING BUSHING ON ALL GENERATOR POWER CONDUIT, COMMUNITY FEEDER CONDUIT, STATION SERVICE FEEDERS, AND WHERE OTHERWISE INDICATED OR REQUIRED. BOND GROUNDING BUSHING TO EQUIPMENT GROUNDING CONDUCTOR.  
 3) INSTALL PLASTIC BUSHING WHERE GROUNDING BUSHING IS NOT REQUIRED.  
 4) ON GENERATOR ENCLOSURES PROTECT CABLES FROM WEAR BY INSTALLING 2 LAYERS OF HEAVY WALL HEAT SHRINK. BASE LAYER 12" LONG & SECOND LAYER 8" LONG, CENTERED IN CONNECTOR.

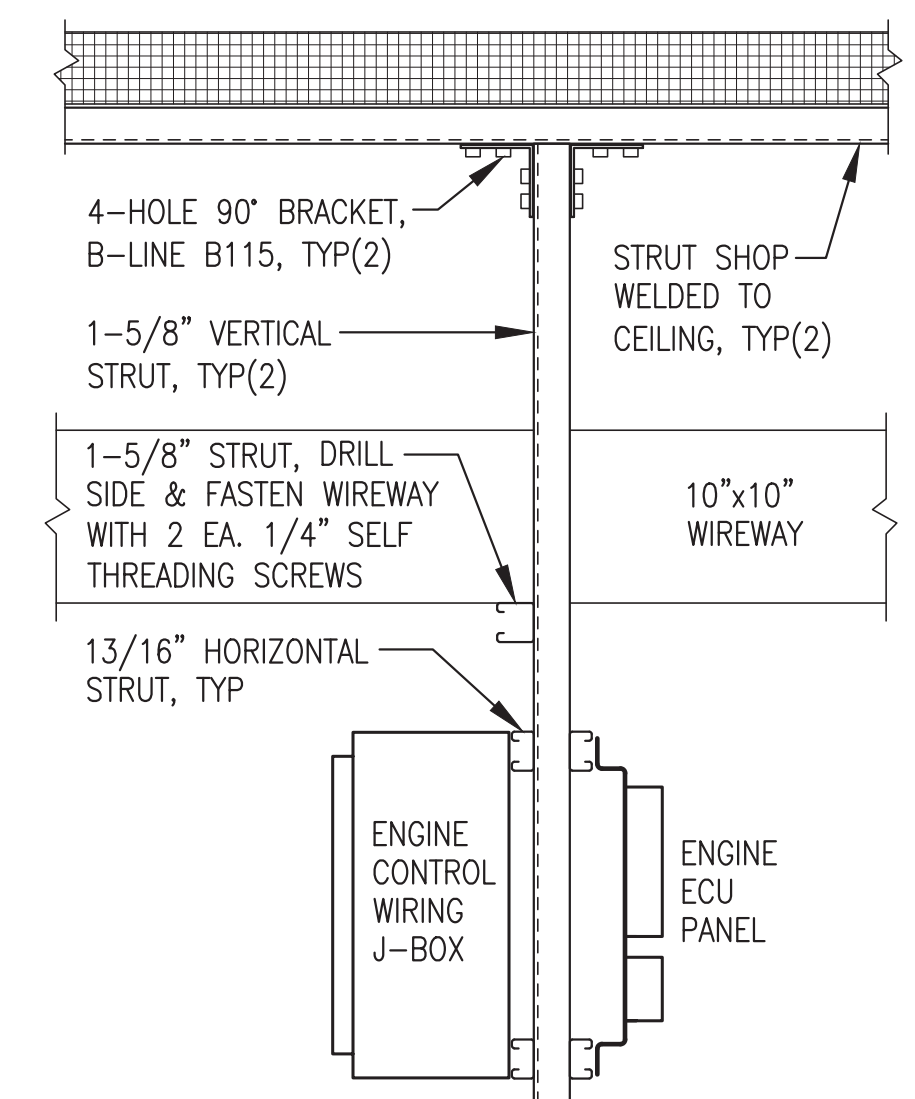


**6** ENGINE WIRING J-BOX SUPPORT  
E3.3 NO SCALE

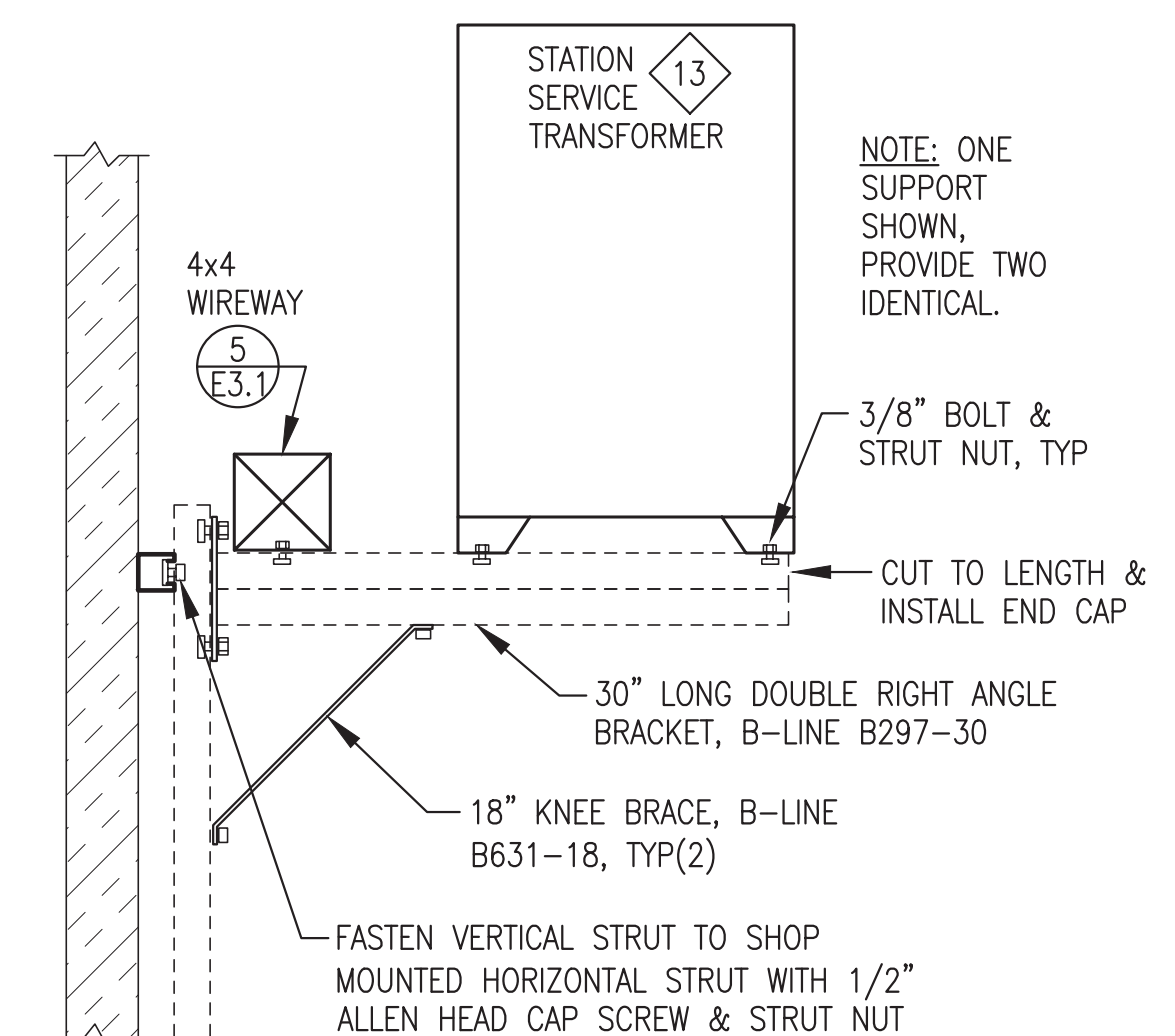


**7** STATION SERVICE TRANSFORMER SUPPORT  
E3.3 NO SCALE

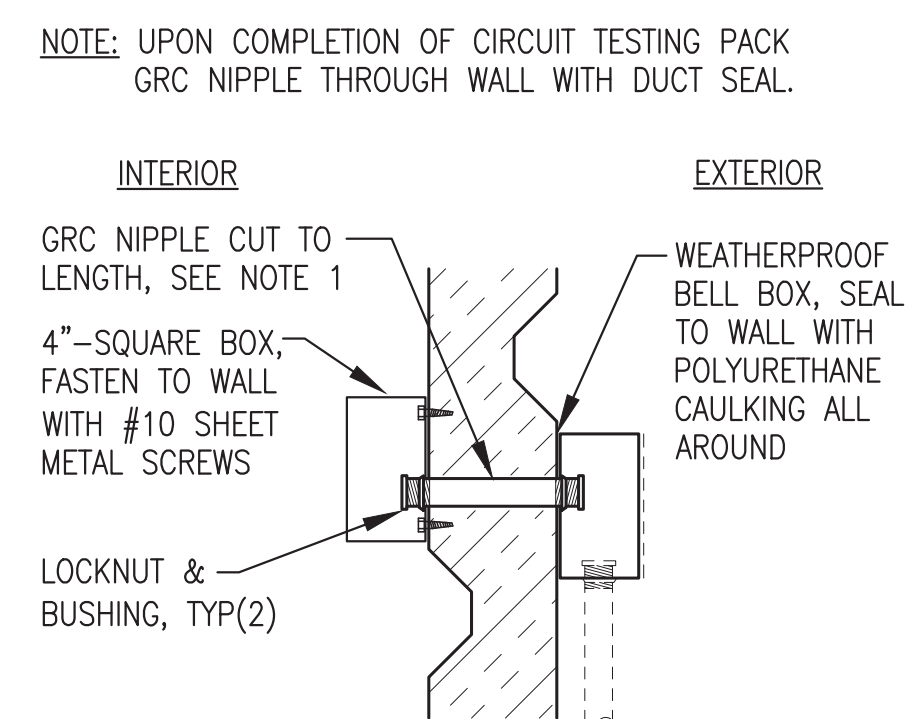

**8** TYP EXTERIOR WALL-MOUNT DEVICE  
E3.3 NO SCALE

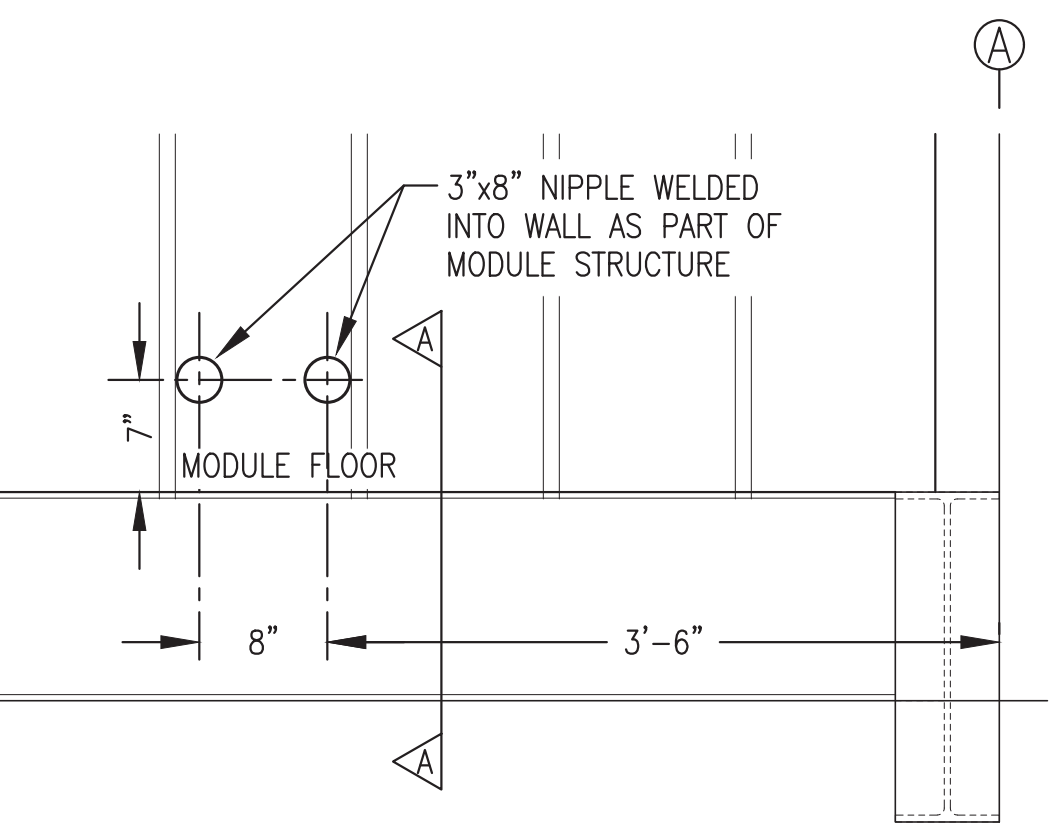


**9** FEEDER ENTRANCE DETAIL  
E3.3 1"=1'-0"

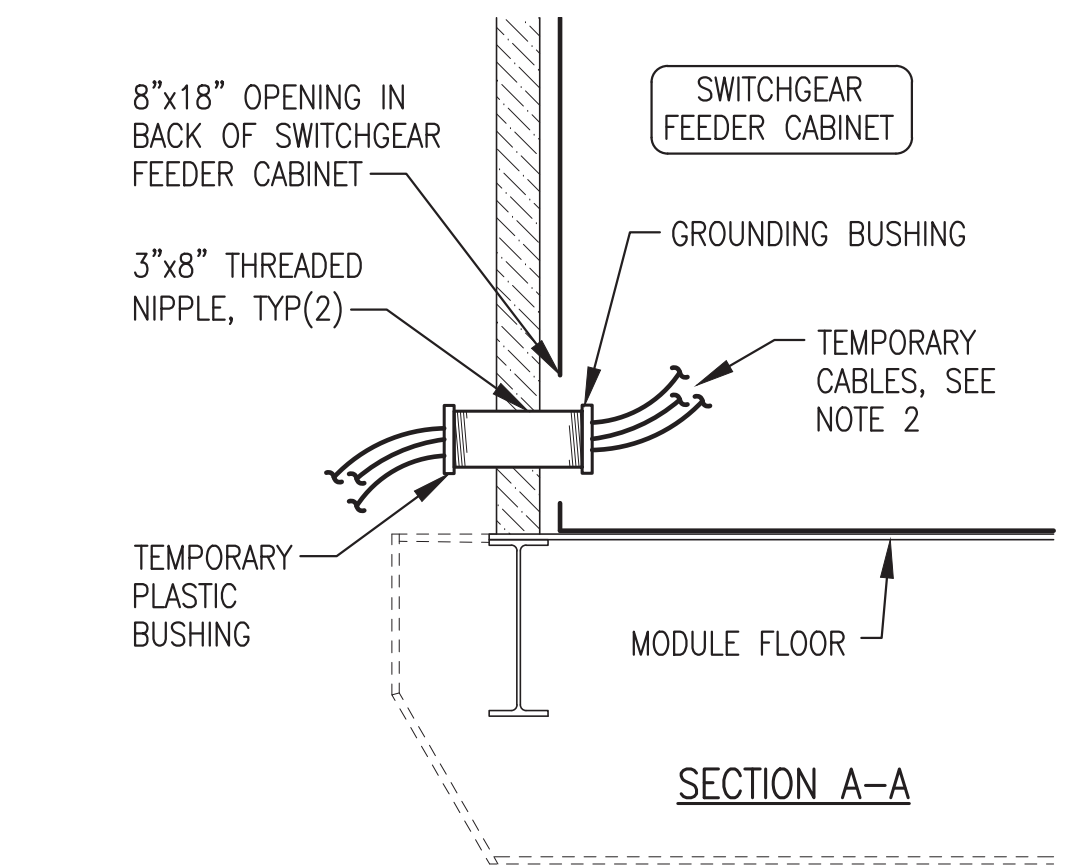

**10** TYP CONDUIT WALL PENETRATION  
E3.3 NO SCALE

**FEEDER SHOP/ON-SITE NOTES:**  
 1) DURING SHOP FABRICATION INSTALL TEMPORARY FEEDER CABLES THROUGH ONE NIPPLE AS SHOWN. SPARE NIPPLE TO REMAIN CAPPED.  
 2) ROUTE TEMPORARY CABLES TO LOAD BANK FOR TESTING. AFTER TESTING INSTALL THREADED CAP ON EXTERIOR END OF NIPPLE.  
 3) INSTALL FEEDER TO TRANSFORMER AS PART OF ON-SITE WORK, SEE SHEET E1.6 FOR CONTINUATION.  
 4) UPON COMPLETION OF TESTING PACK GRC NIPPLES THROUGH WALL WITH DUCT SEAL.

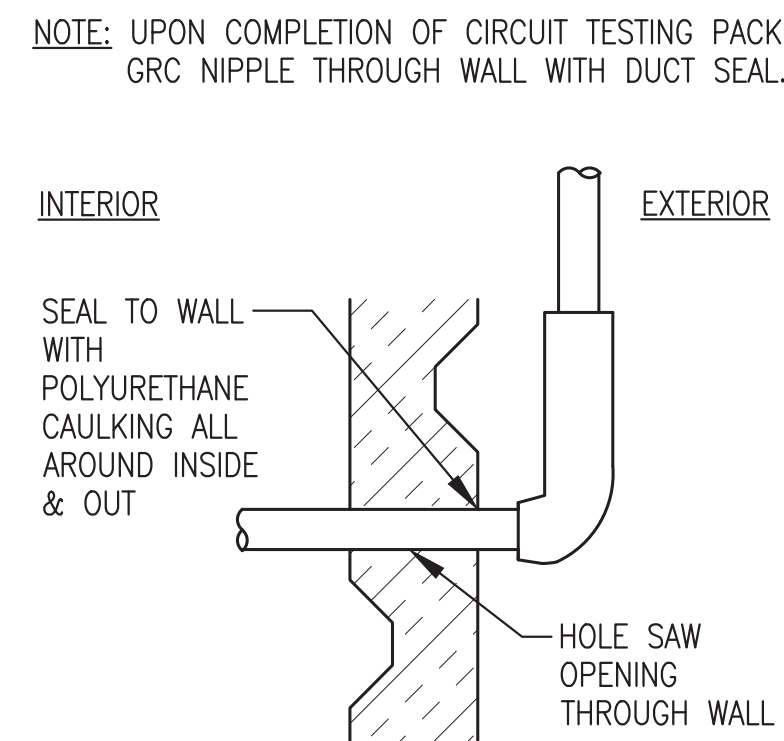


**REVISION #1  
 ISSUED FOR  
 MODULE  
 CONSTRUCTION  
 JULY 2022**




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: ELEVATIONS & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: CWM/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_E2-E5		SHEET: E3.3	
PROJECT NUMBER:			


**Gray Stassel Engineering, Inc.**  
 P.O. 111405, Anchorage, AK 99511 (907)349-0100

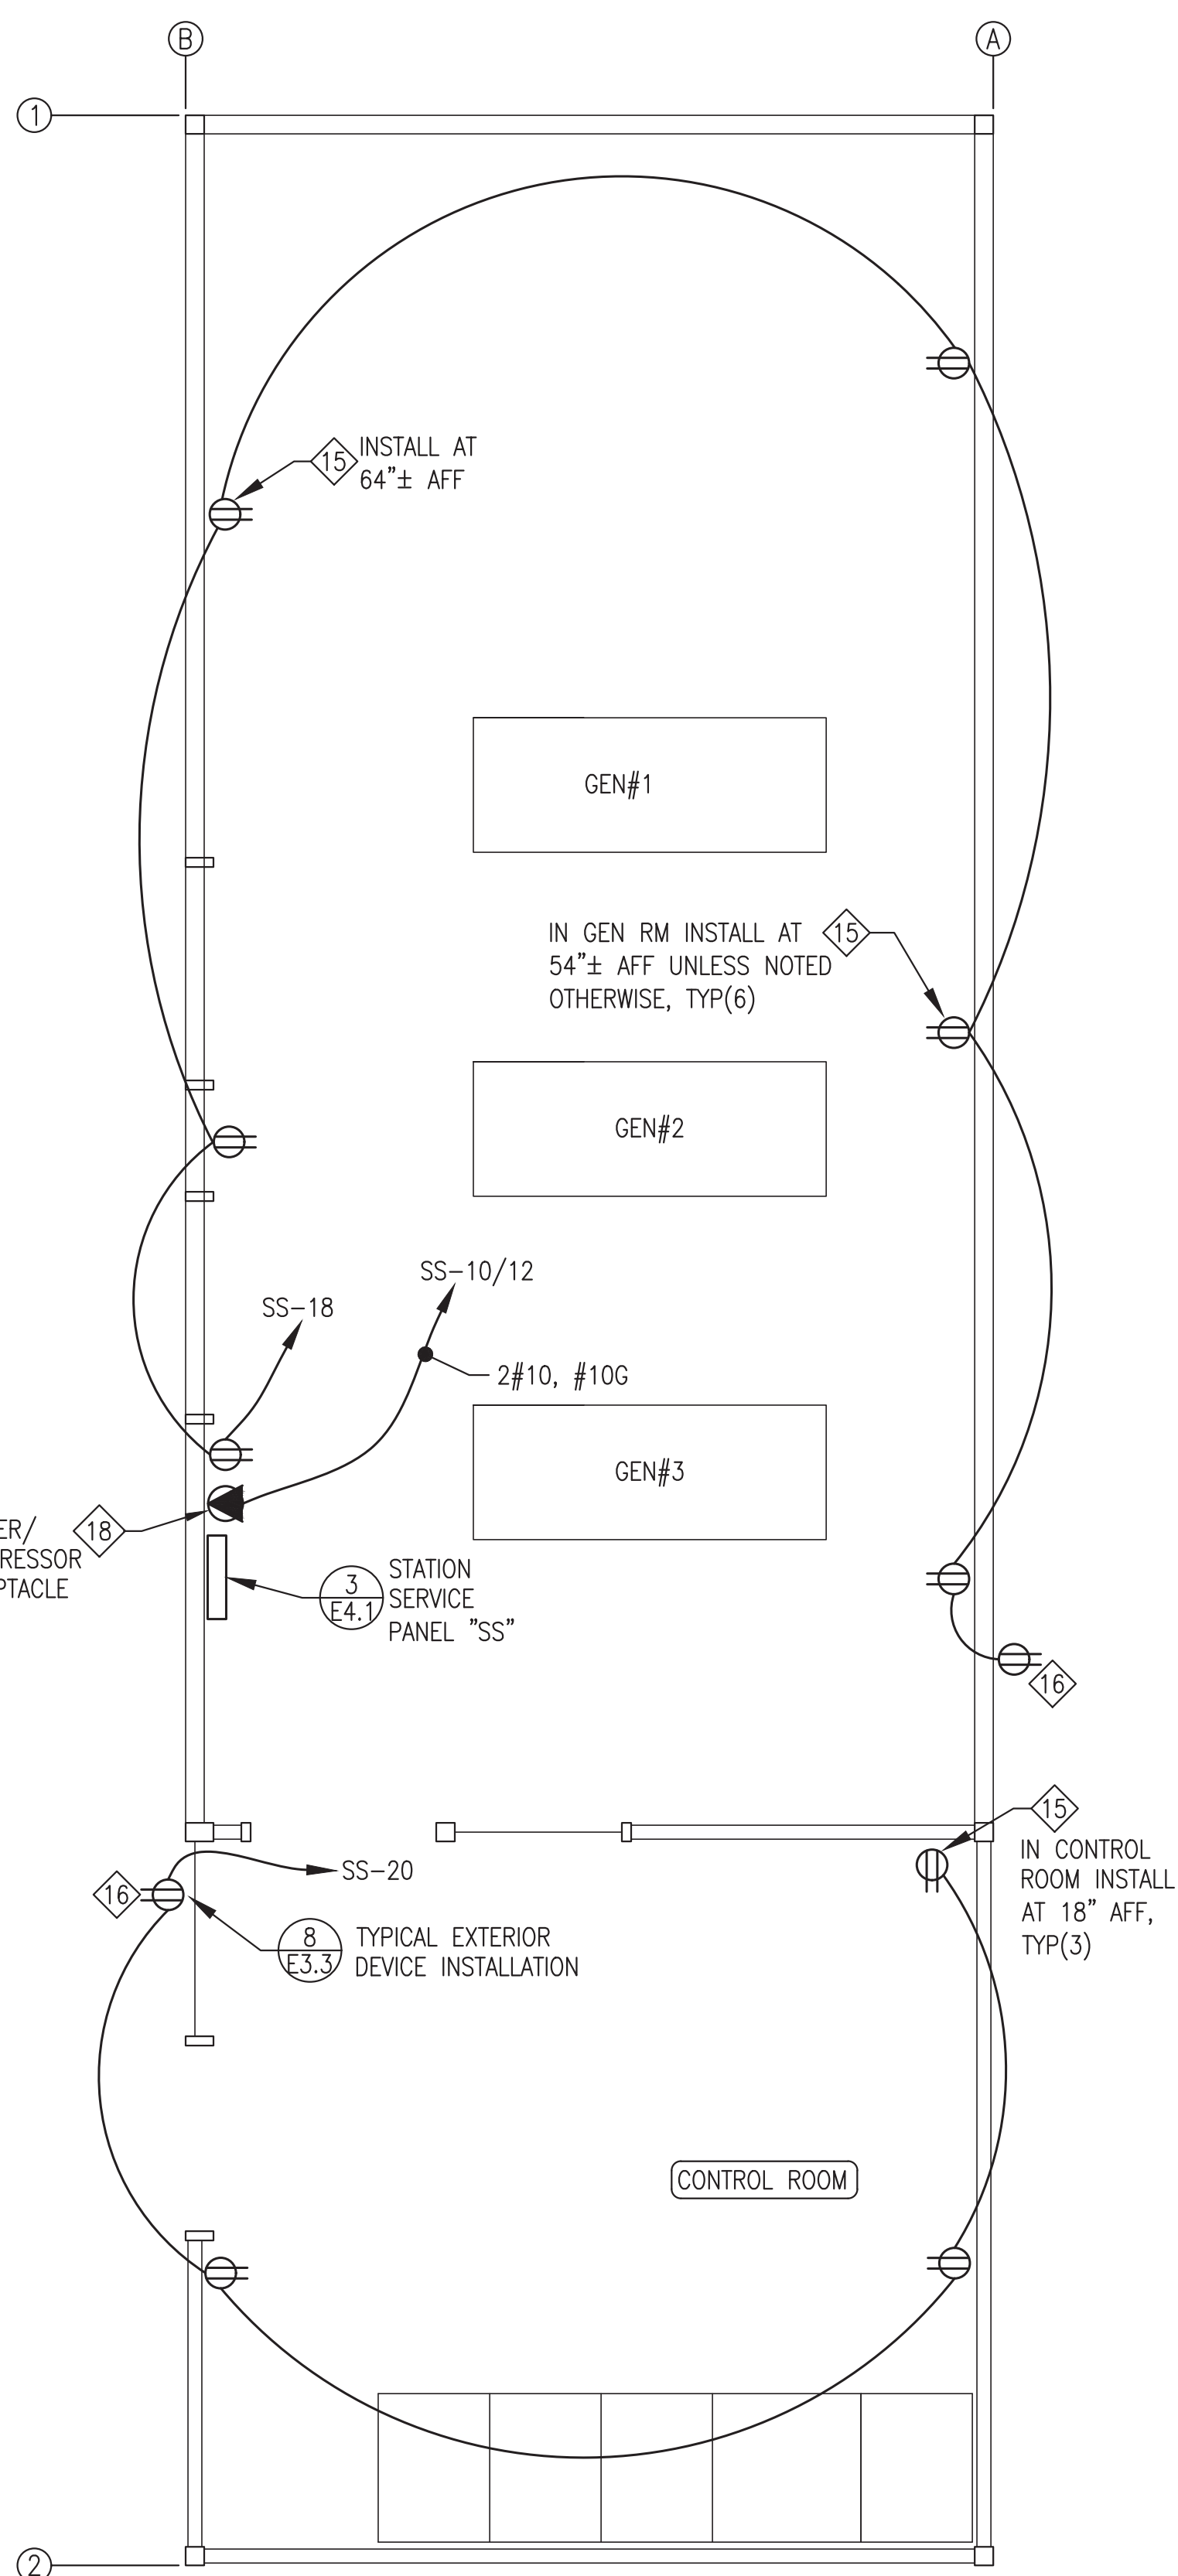

NOTES:  
 1) ALL WIRING RUNS 2#12, #12G UNLESS SPECIFICALLY NOTED OTHERWISE.

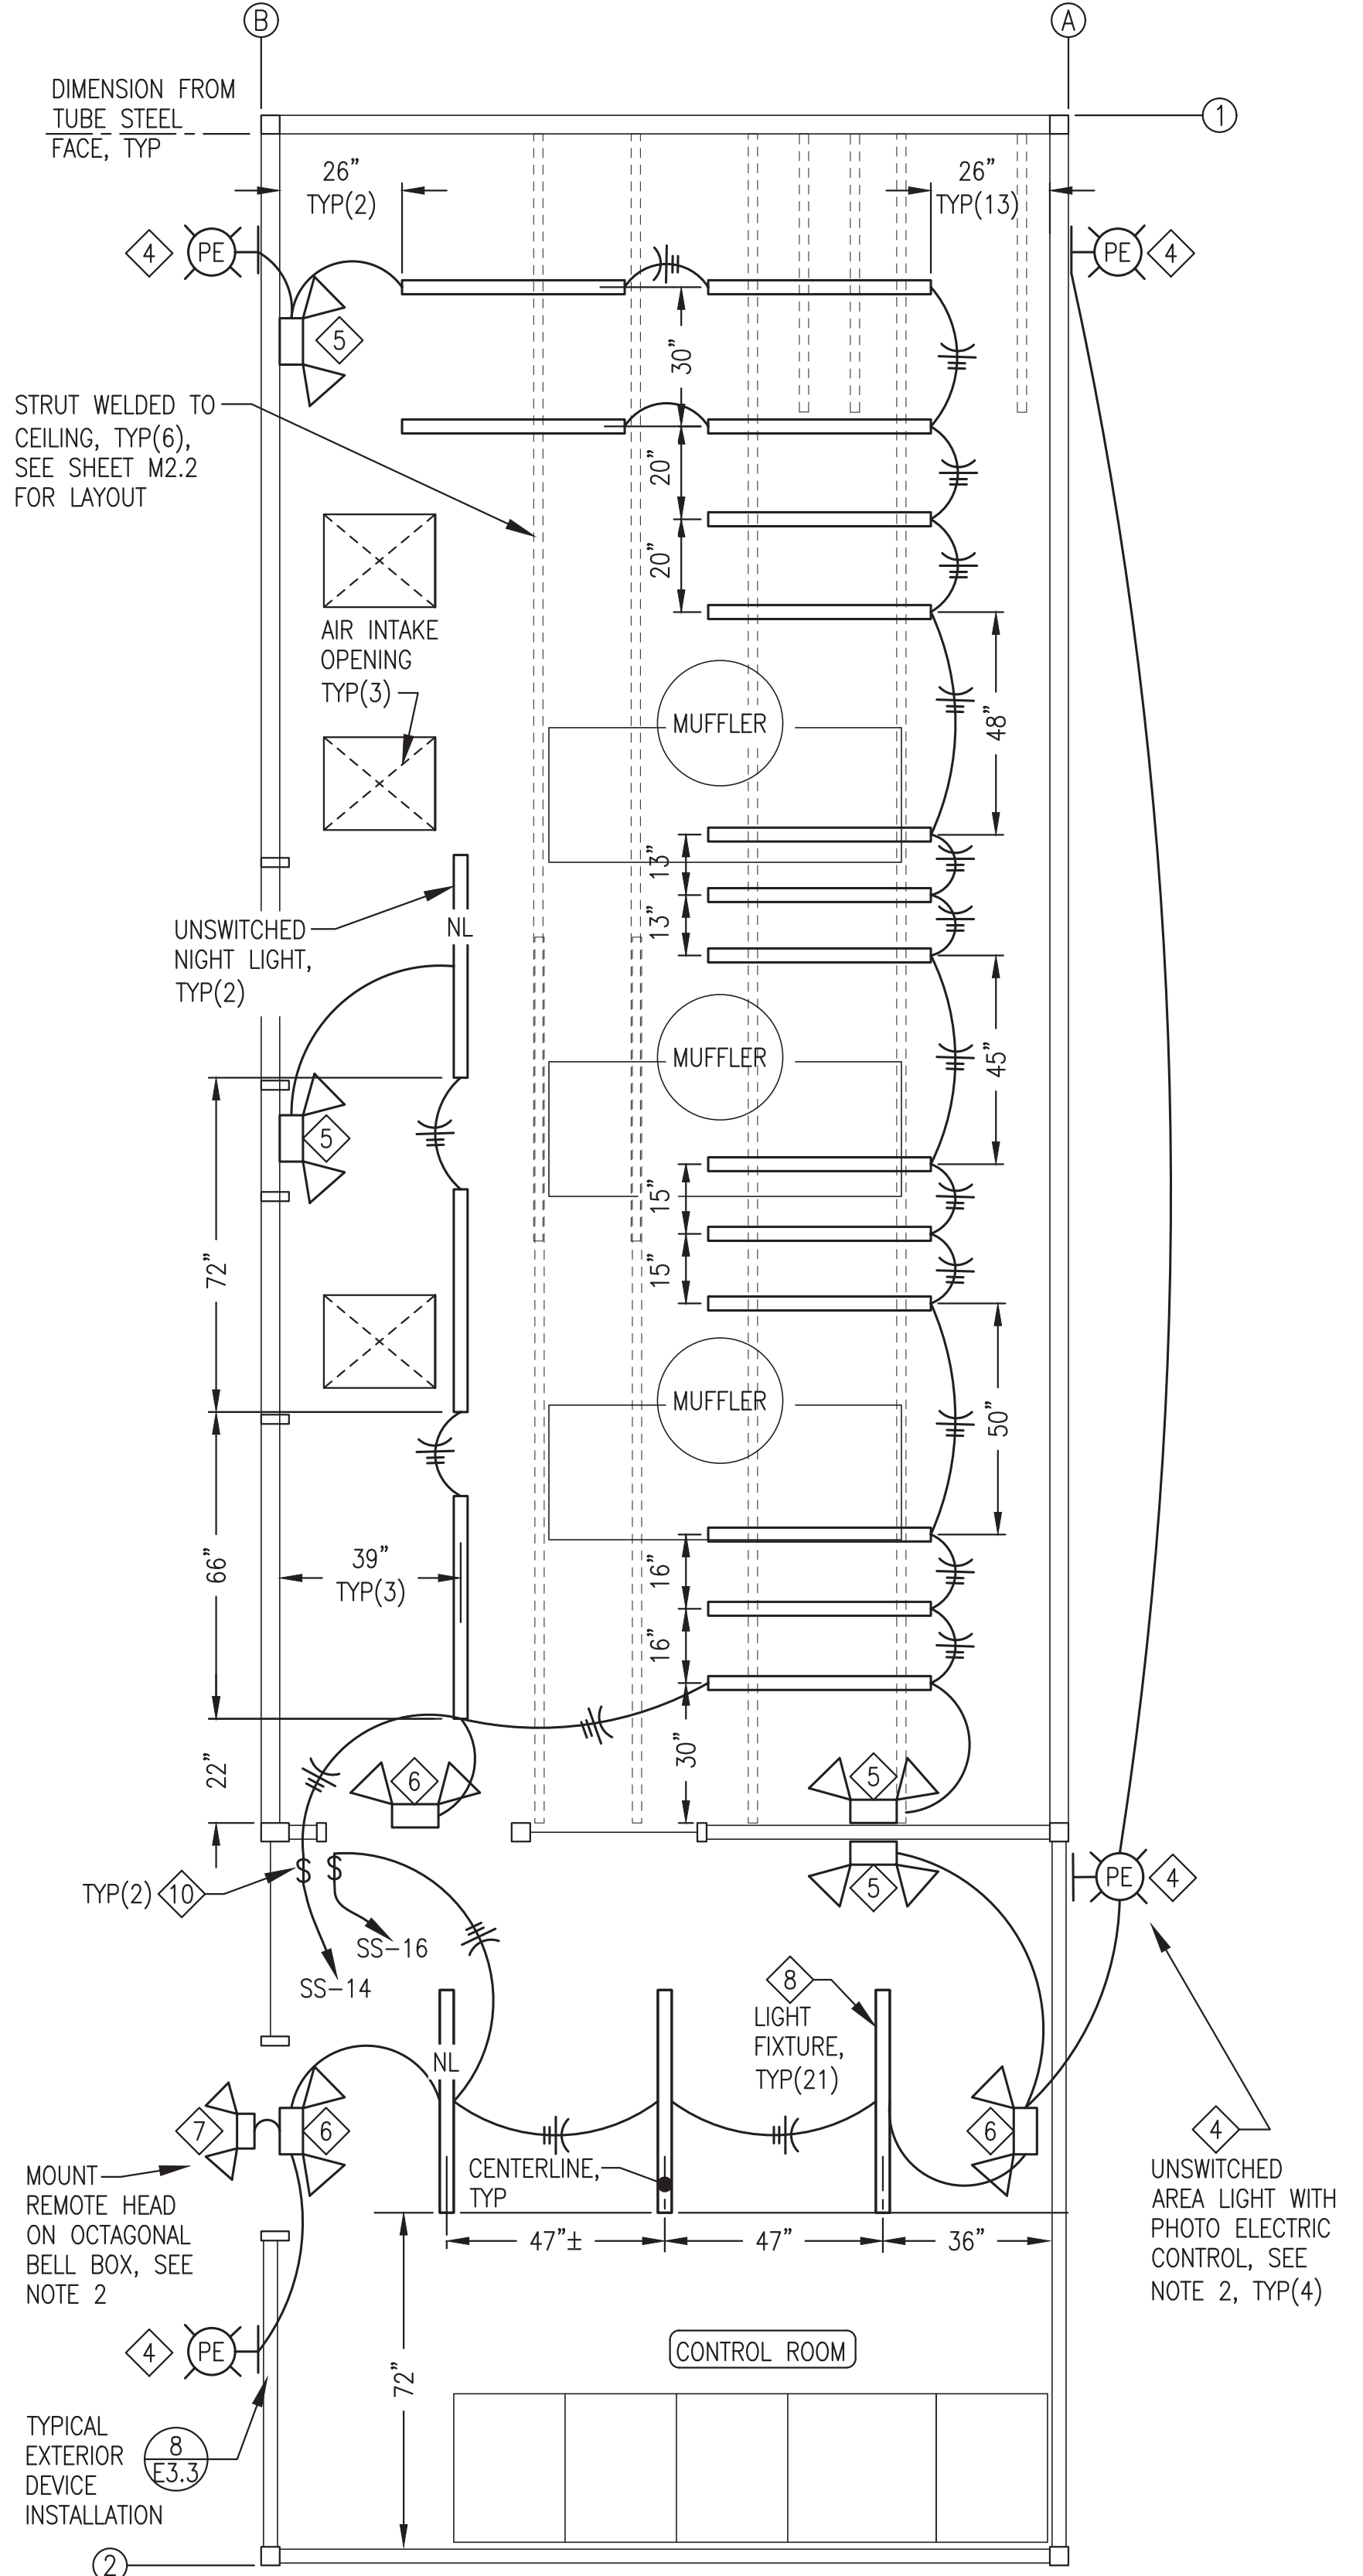

NOTES:  
 1) ALL WIRING RUNS 2#12, #12G UNLESS SPECIFICALLY NOTED OTHERWISE.  
 2) MOUNT EXTERIOR AREA AND EMERGENCY LIGHTS WITH TOP 9'-0" AFF.  
 3) FASTEN INTERIOR LIGHTS TO CEILING WITH #12 SHEET METAL SCREWS EXCEPT WHERE LIGHTS CROSS STRUT USE 1/4" BOLTS & STRUT NUTS, TYP

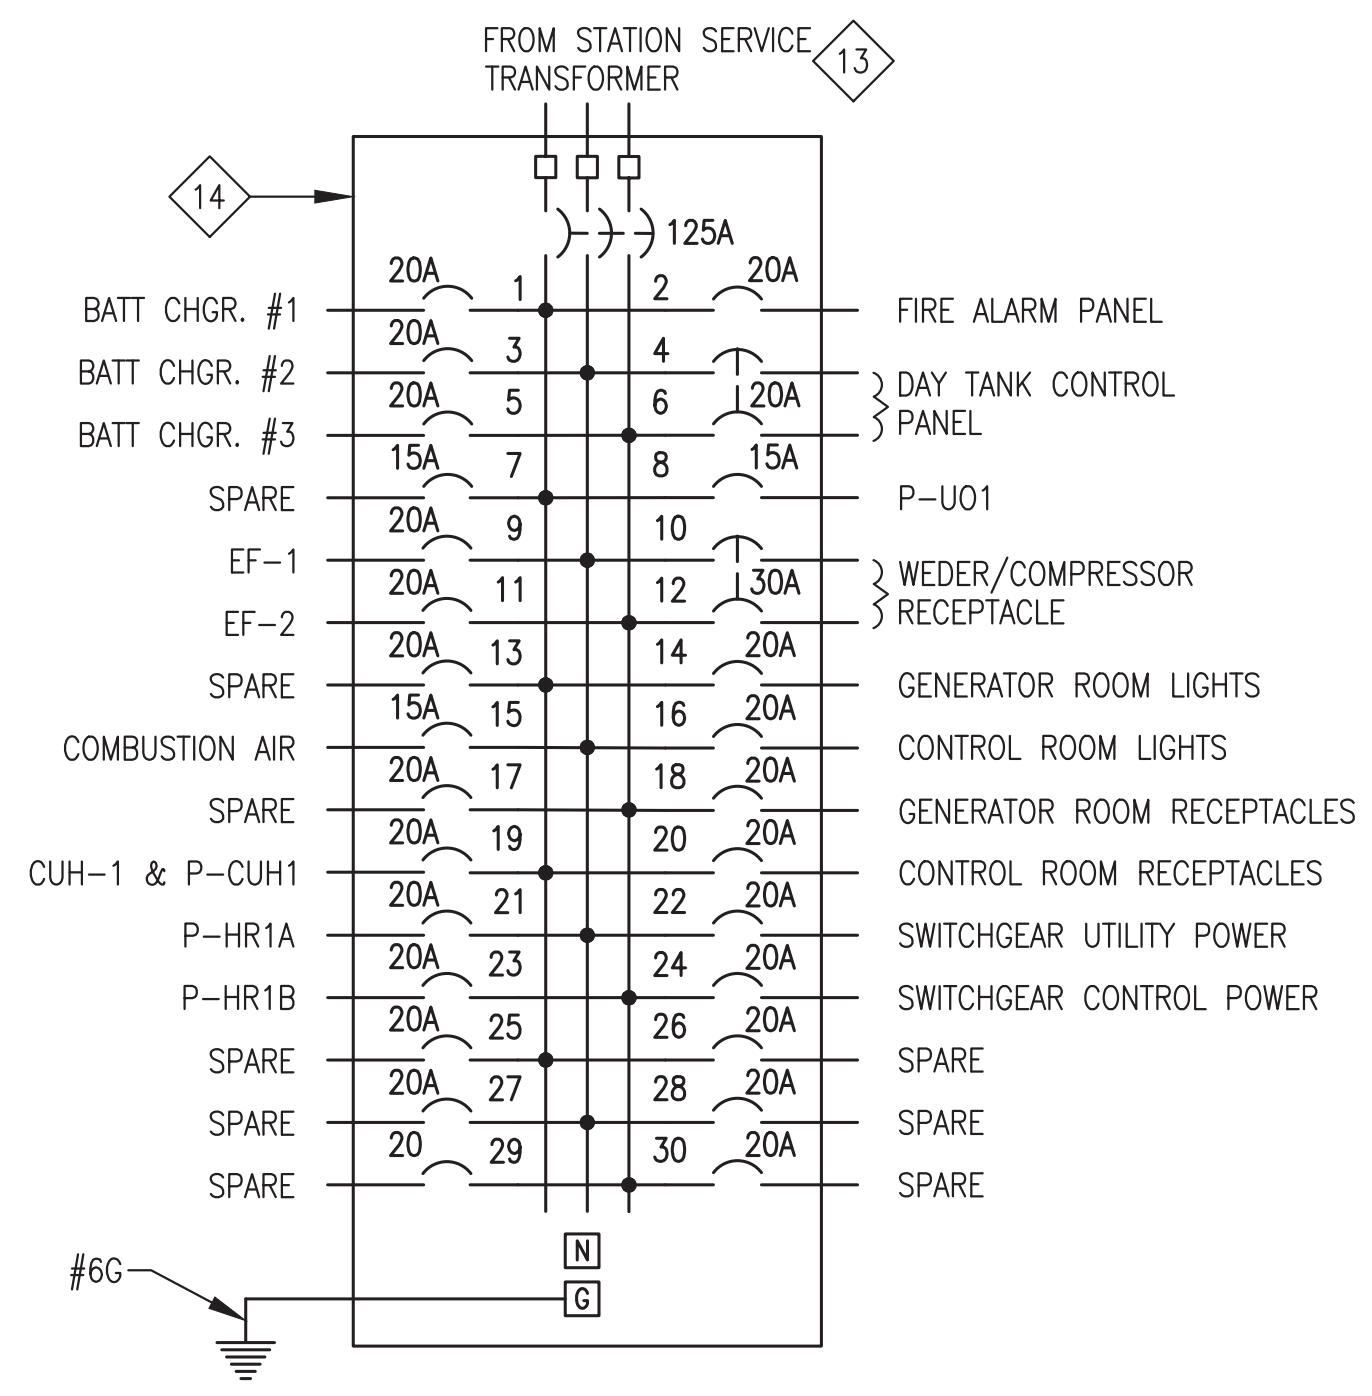

3 STATION SERVICE PANEL "SS"  
 E4.1 NO SCALE


1 RECEPTACLE PLAN  
 E4.1 3/8"=1'-0"

2 LIGHTING PLAN  
 E4.1 3/8"=1'-0"

REVISION #1  
 ISSUED FOR  
 MODULE  
 CONSTRUCTION  
 JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: RECEPTACLE & LIGHTING PLANS & PANELBOARD			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_E2-E5		SHEET:	
PROJECT NUMBER:		E4.1	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

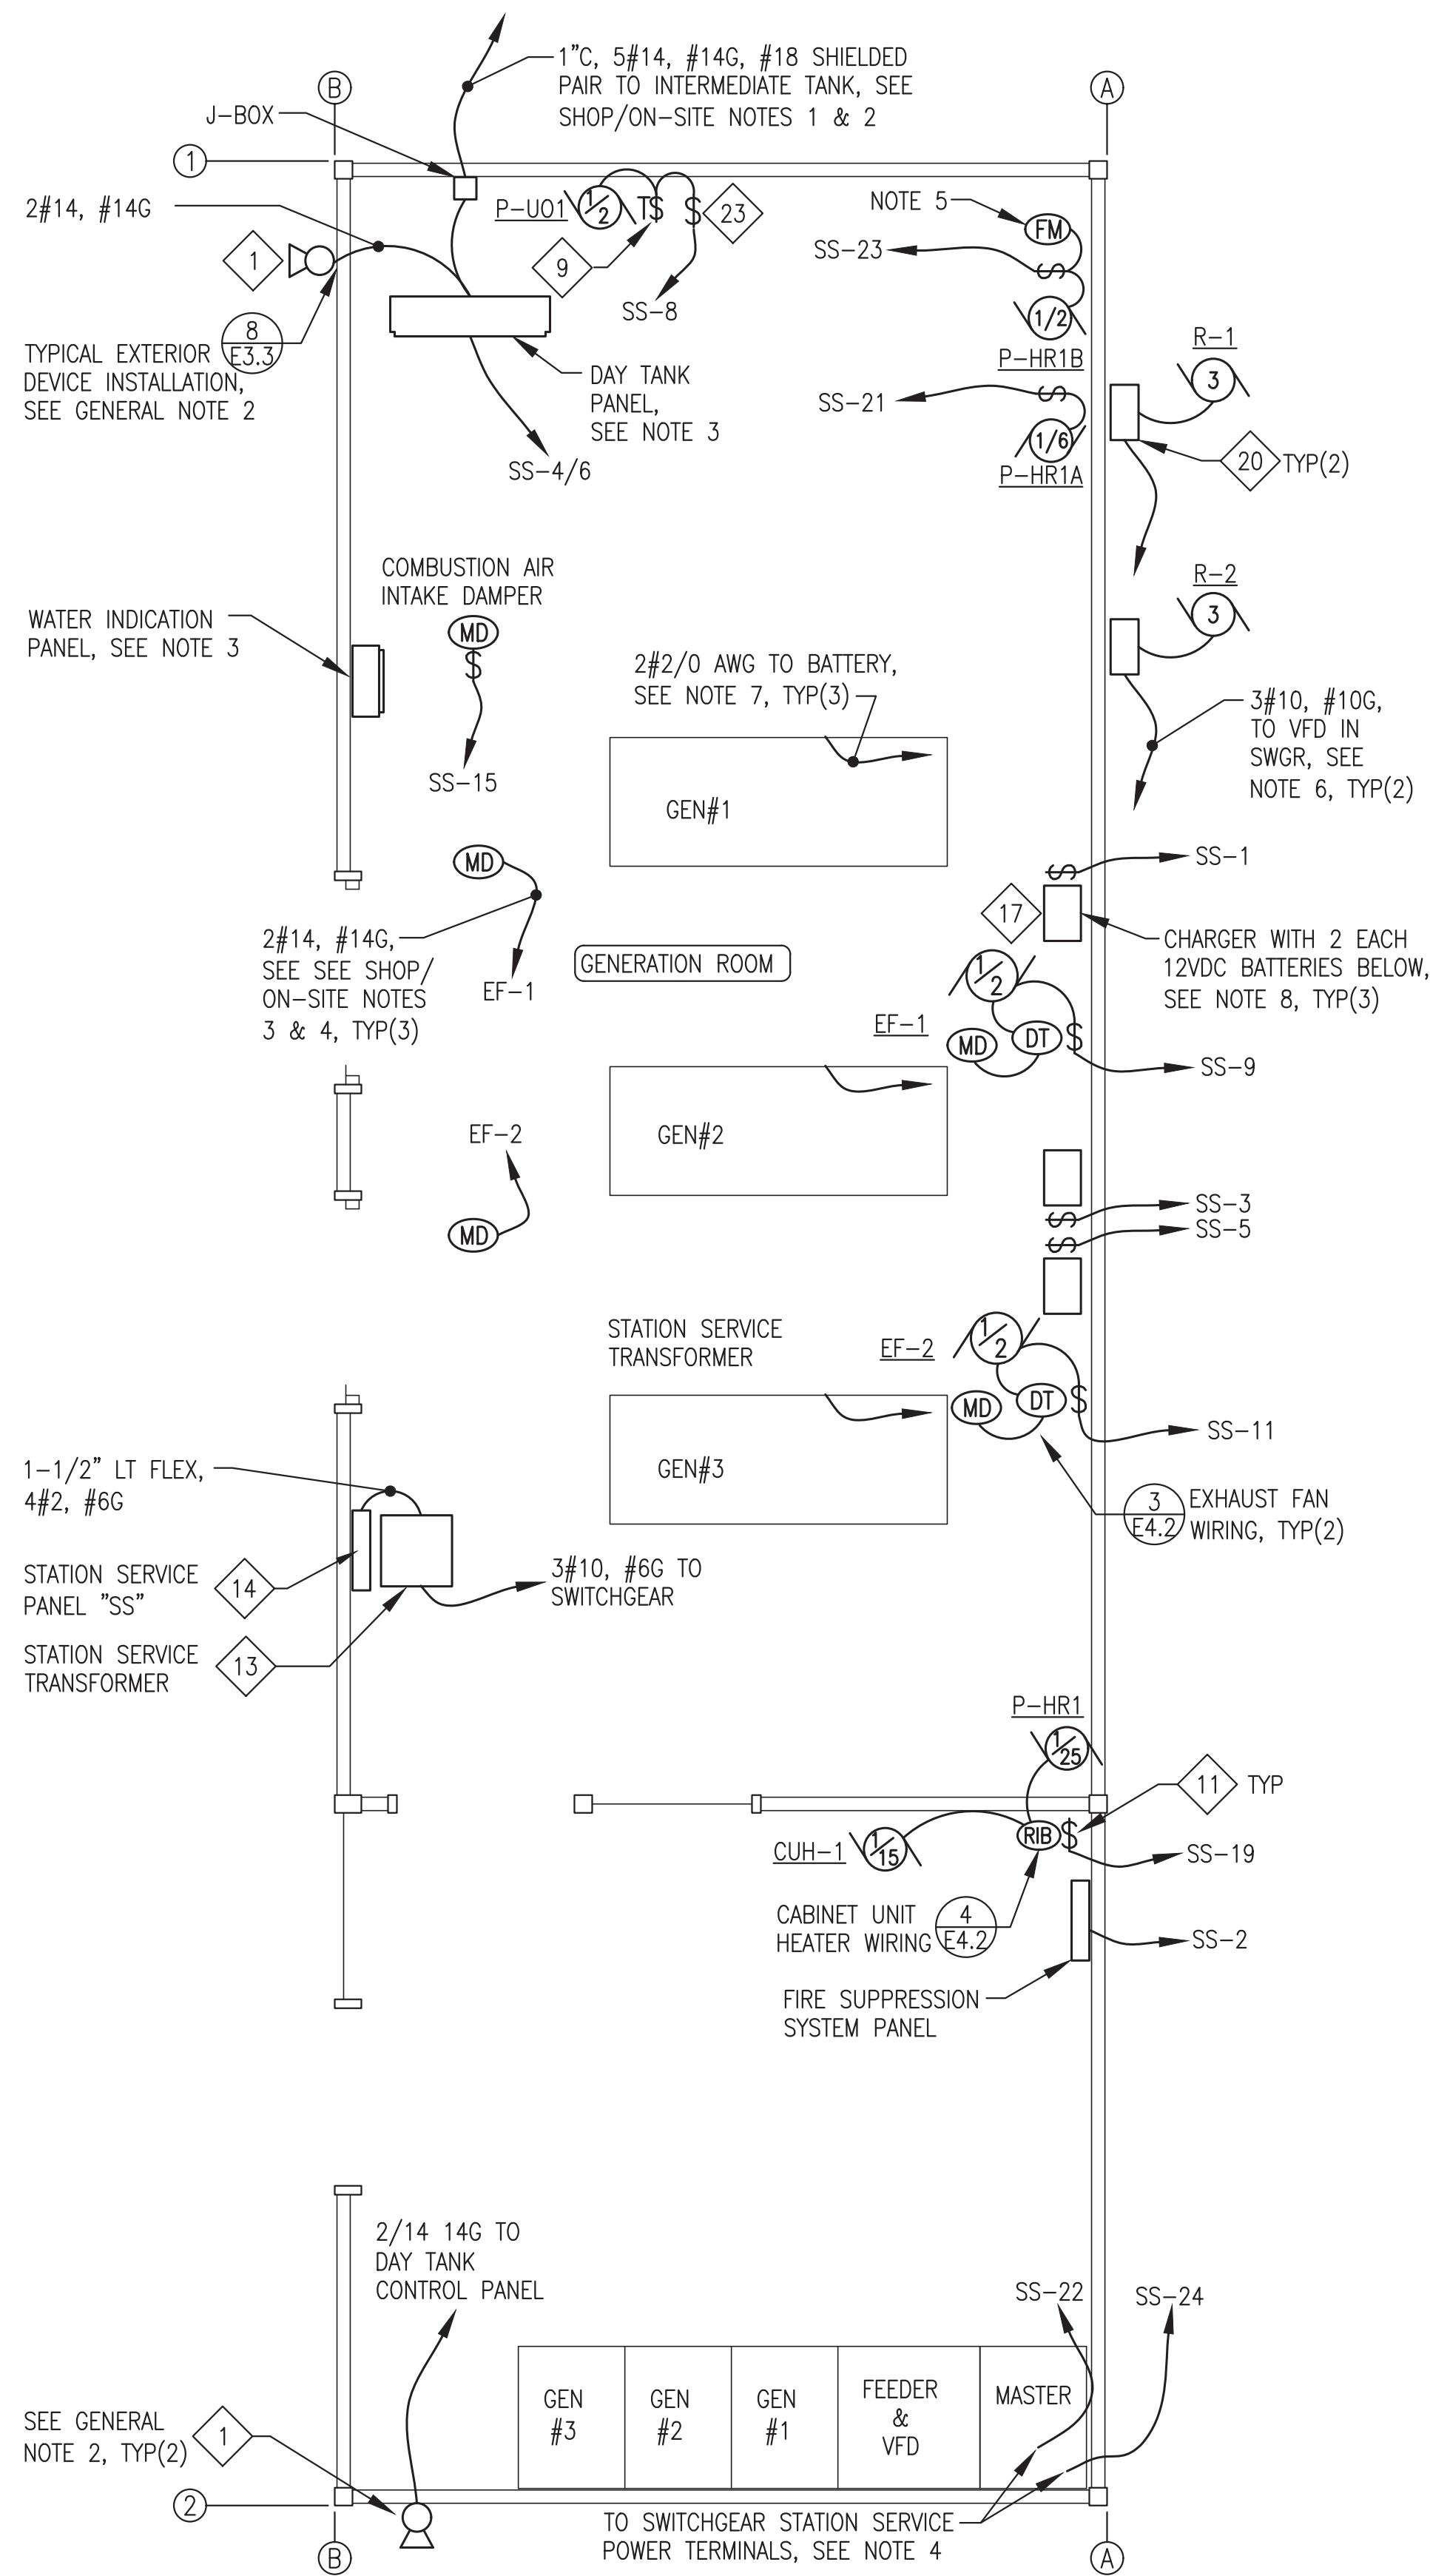

**1** STATION SERVICE PLAN  
E4.2 3/8"=1'-0"


**STATION SERVICE GENERAL NOTES:**

- 1) ALL WIRING RUNS 2#12, #12G UNLESS SPECIFICALLY NOTED OTHERWISE.
- 2) MOUNT ALARMS HORNS WITH TOP AT 9'-0" AFF TO MATCH EXTERIOR LIGHTS, SEE SHEET E4.1
- 3) SEE SHEETS E7.1-E7.4 FOR DAY TANK AND WATER INDICATION PANEL DESIGN AND WIRING TERMINATIONS. ALL ACCESSORIES NOT SHOWN ON PLANS. SEE LOGIC DIAGRAMS FOR ADDITIONAL DETAIL.
- 4) SEE SWITCHGEAR SHOP DRAWINGS FOR TERMINATION OF ALL POWER AND CONTROL WIRING.
- 5) INSTALL FLOW METER FOR HEAT RECOVERY MONITORING WHERE SHOWN ON HEAT RECOVERY PIPING ISOMETRIC 2/M4.2. PROVIDE POWER FROM P-HR1B DISCONNECT.
- 6) ROUTE RADIATOR VFD POWER CONDUCTORS IN SEPARATE EXTERIOR CONDUIT, SEE ELEVATION 1/E3.3. DO NOT ROUTE IN WIREWAY. NOTE THAT CONDUCTORS ARE OVSIZED FOR 80% DE-RATE AND PROVIDED WITH 15A BREAKER IN SWITCHGEAR.
- 7) ROUTE BATTERY CABLES TO FRONT OF SKID SUPPORTED WITH CUSHIONED CLAMPS, SEE SHEET M3.4. ROUTE FROM SKID DIRECTLY UNDER FUEL HOSES TO WALL AND TYWRAP CABLES TO USED OIL PIPE ALONG WALL, SEE DETAIL 2/E3.1. CUT TO PROVIDE 6"± SERVICE LOOP FOR FINAL TERMINATION ON BATTERIES.
- 8) MOUNT BATTERY CHARGER TO WALL ON SHALLOW STRUT AND INSTALL BATTERIES IN RACK ON FLOOR BELOW, SEE ELEVATION 1/E3.2.


**STATION SERVICE SHOP/ON-SITE NOTES:**

- 1) DURING SHOP FABRICATION INSTALL WALL PENETRATION AND CONDUIT INTO DAY TANK PANEL. SEE ELEVATION 5/E3.2.
- 2) AS PART OF ON-SITE WORK INSTALL CONDUIT AND CONDUCTORS TO INTERMEDIATE TANK, SEE SHEET E1.6.
- 3) DURING SHOP FABRICATION INSTALL CEILING MOUNTED BOX ADJACENT TO DAMPER ACTUATOR AND TEMPORARILY CONNECT DAMPER TO VERIFY OPERATION.
- 4) AS PART OF ON-SITE WORK INSTALL CONDUIT AND CONDUCTORS TO DAMPER ACTUATOR. SEE SHEET M7.


MAKE THE FOLLOWING SETTINGS ON DIGITAL THERMOSTAT:  
 APPLICATION = 0 (INTERNAL SENSOR)  
 OUTPUT 1 = 0 (COOL/0-10V)  
 OUTPUT 2 = 0 (NOT USED)  
 OUTPUT 3 = 0 (NOT USED)  
 OUTPUT 3 ACTIVATION = 0 (100%)  
 NSB VALUE = 3 (6'F)  
 OUTPUT 1 MIN = 0 (0%)  
 MAX SETPOINT = 90'F  
 MIN SETPOINT = 50'F

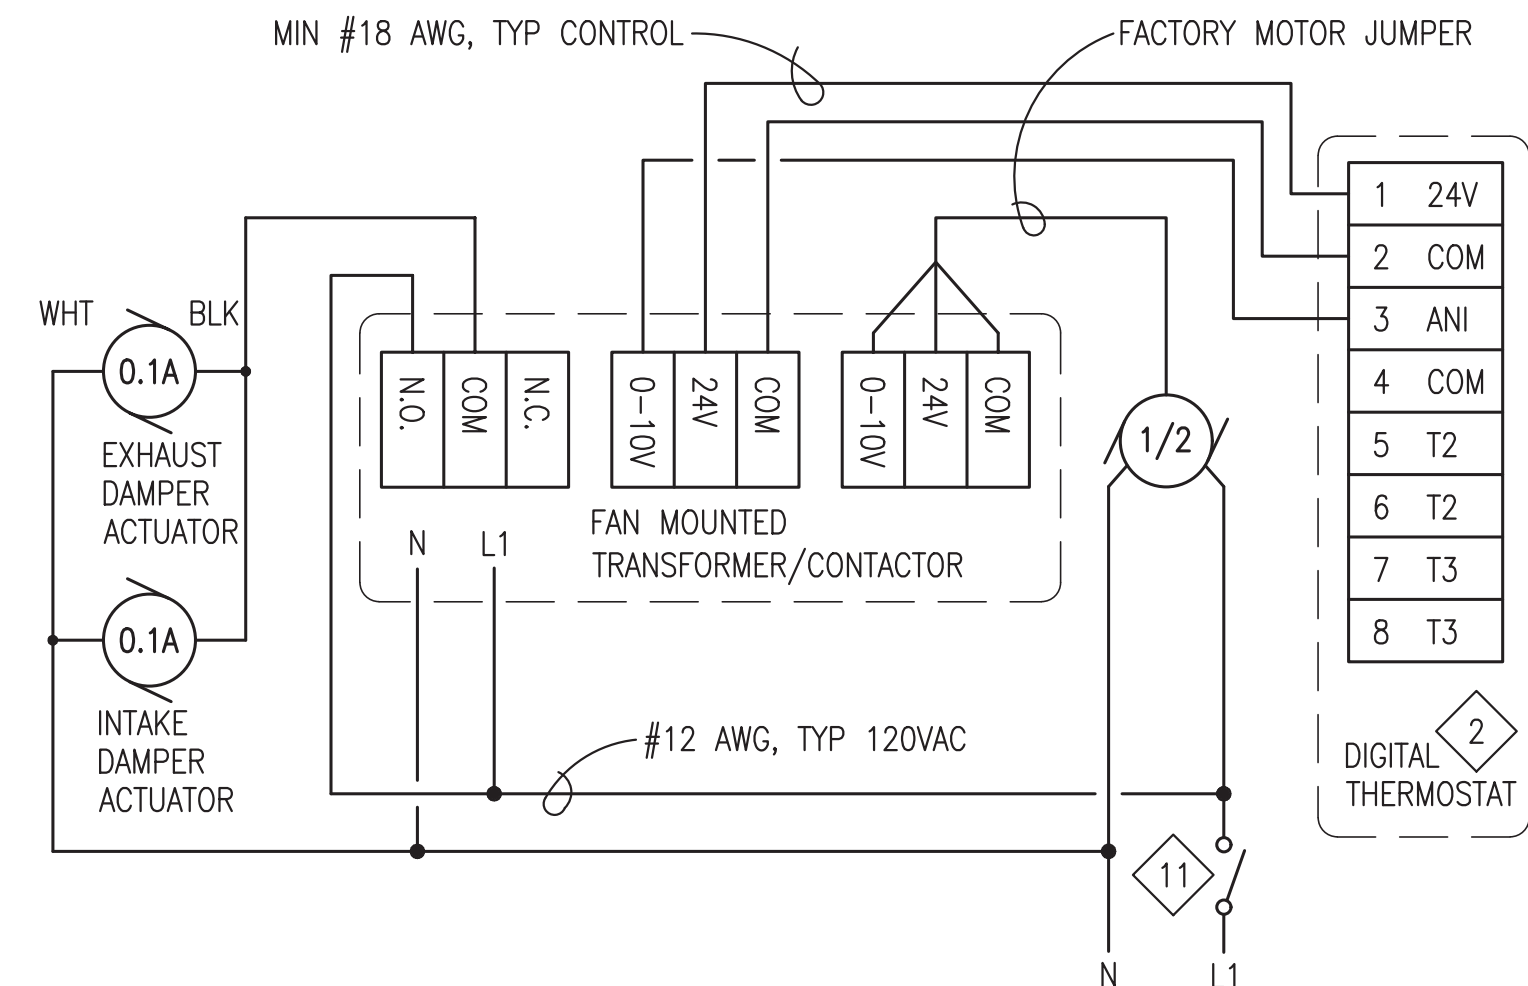

**3** EXHAUST FAN WIRING DIAGRAM  
E4.2 NO SCALE

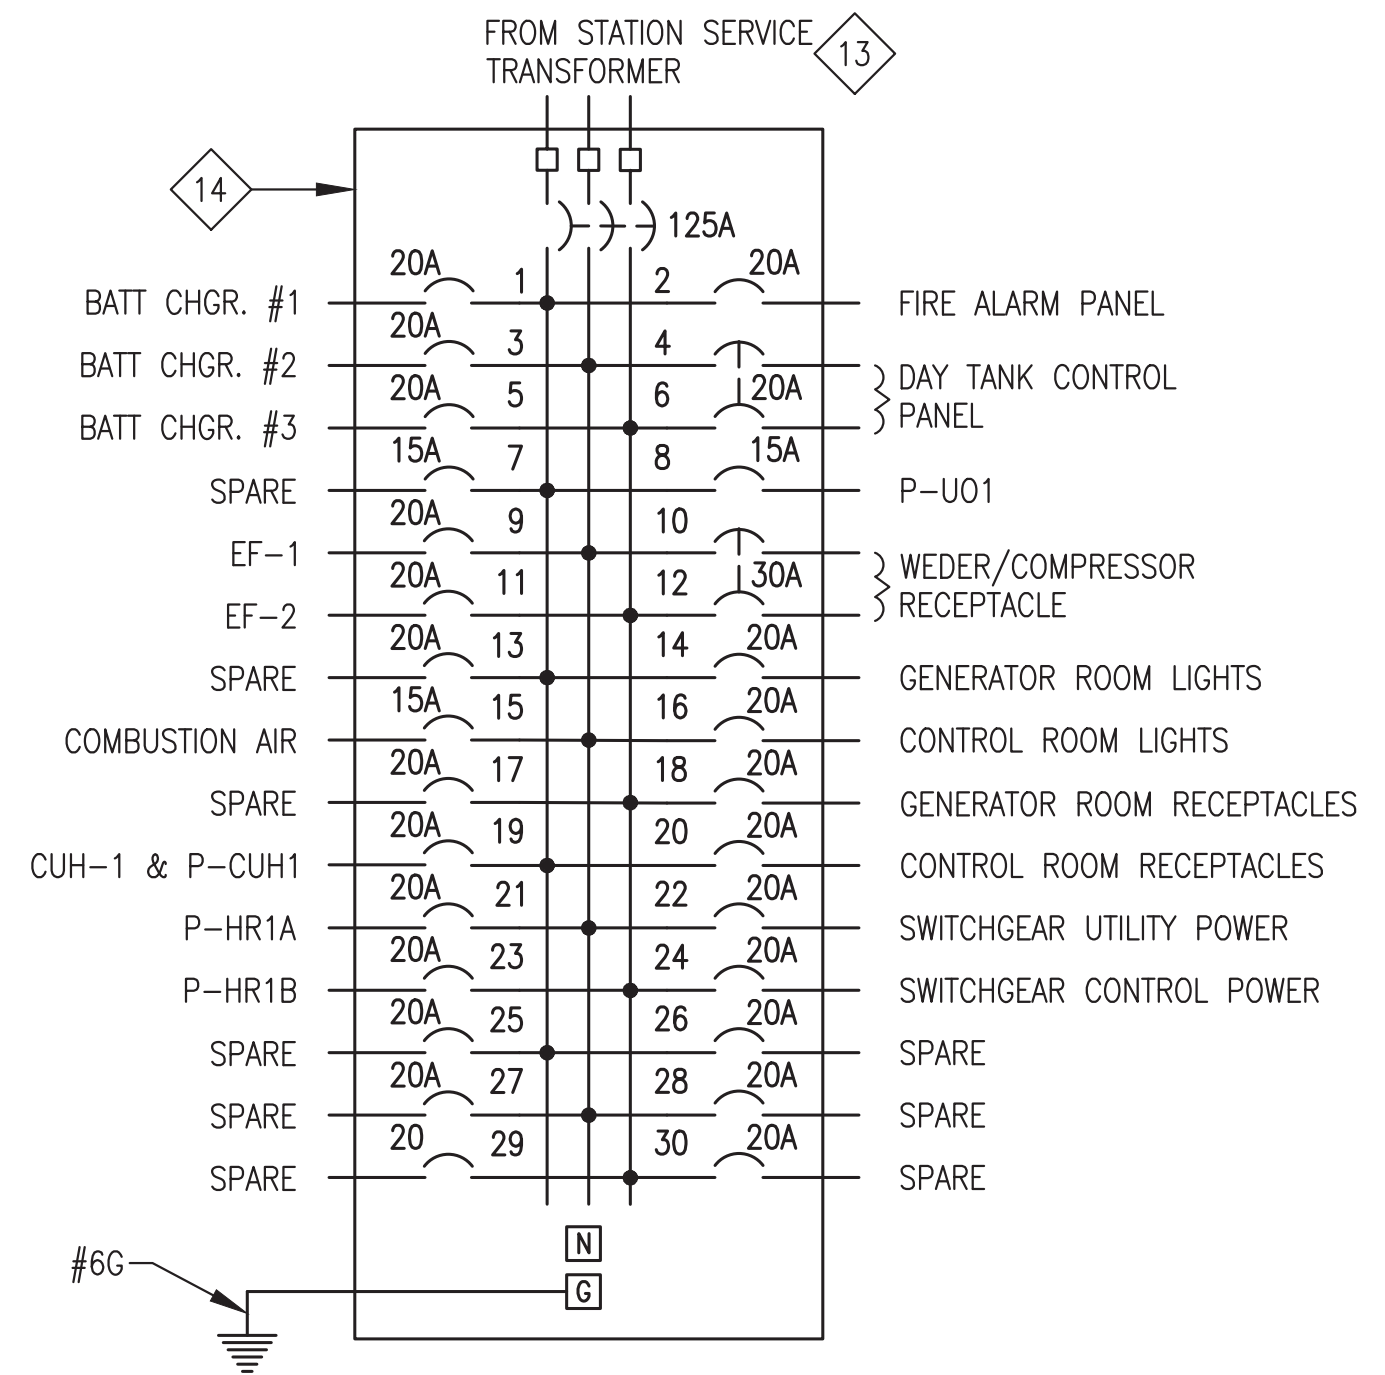


**2** STATION SERVICE PANEL "SS"  
E4.2 NO SCALE

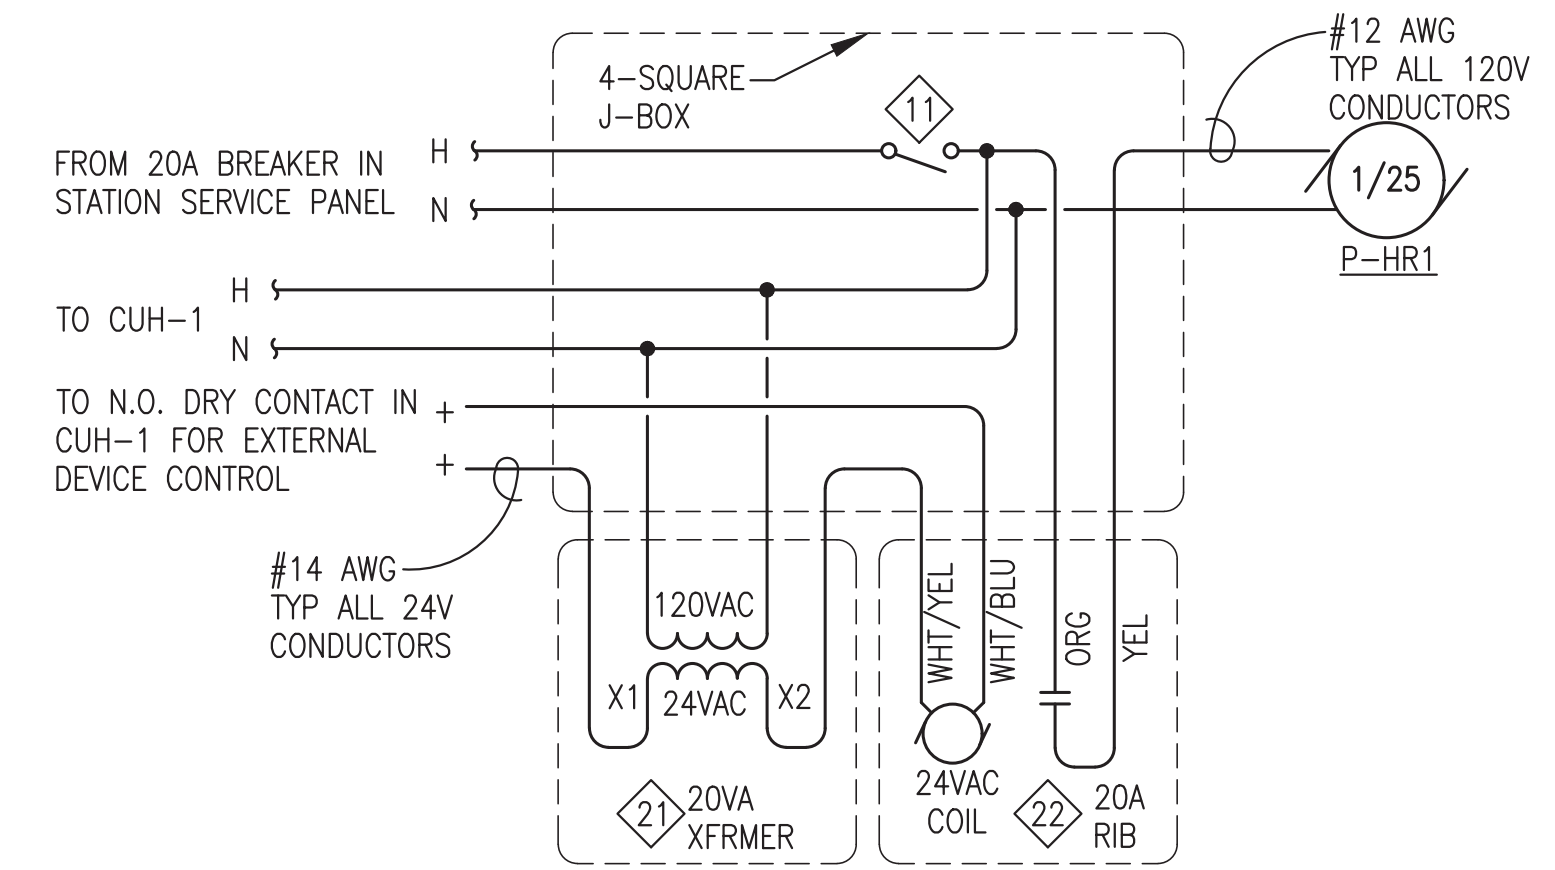


**4** CUH-1 WIRING DIAGRAM  
E4.2 NO SCALE

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: STATION SERVICE PLAN, DETAILS, & PANELBOARD			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP E2-E5		SHEET:	
PROJECT NUMBER:		<b>E4.2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

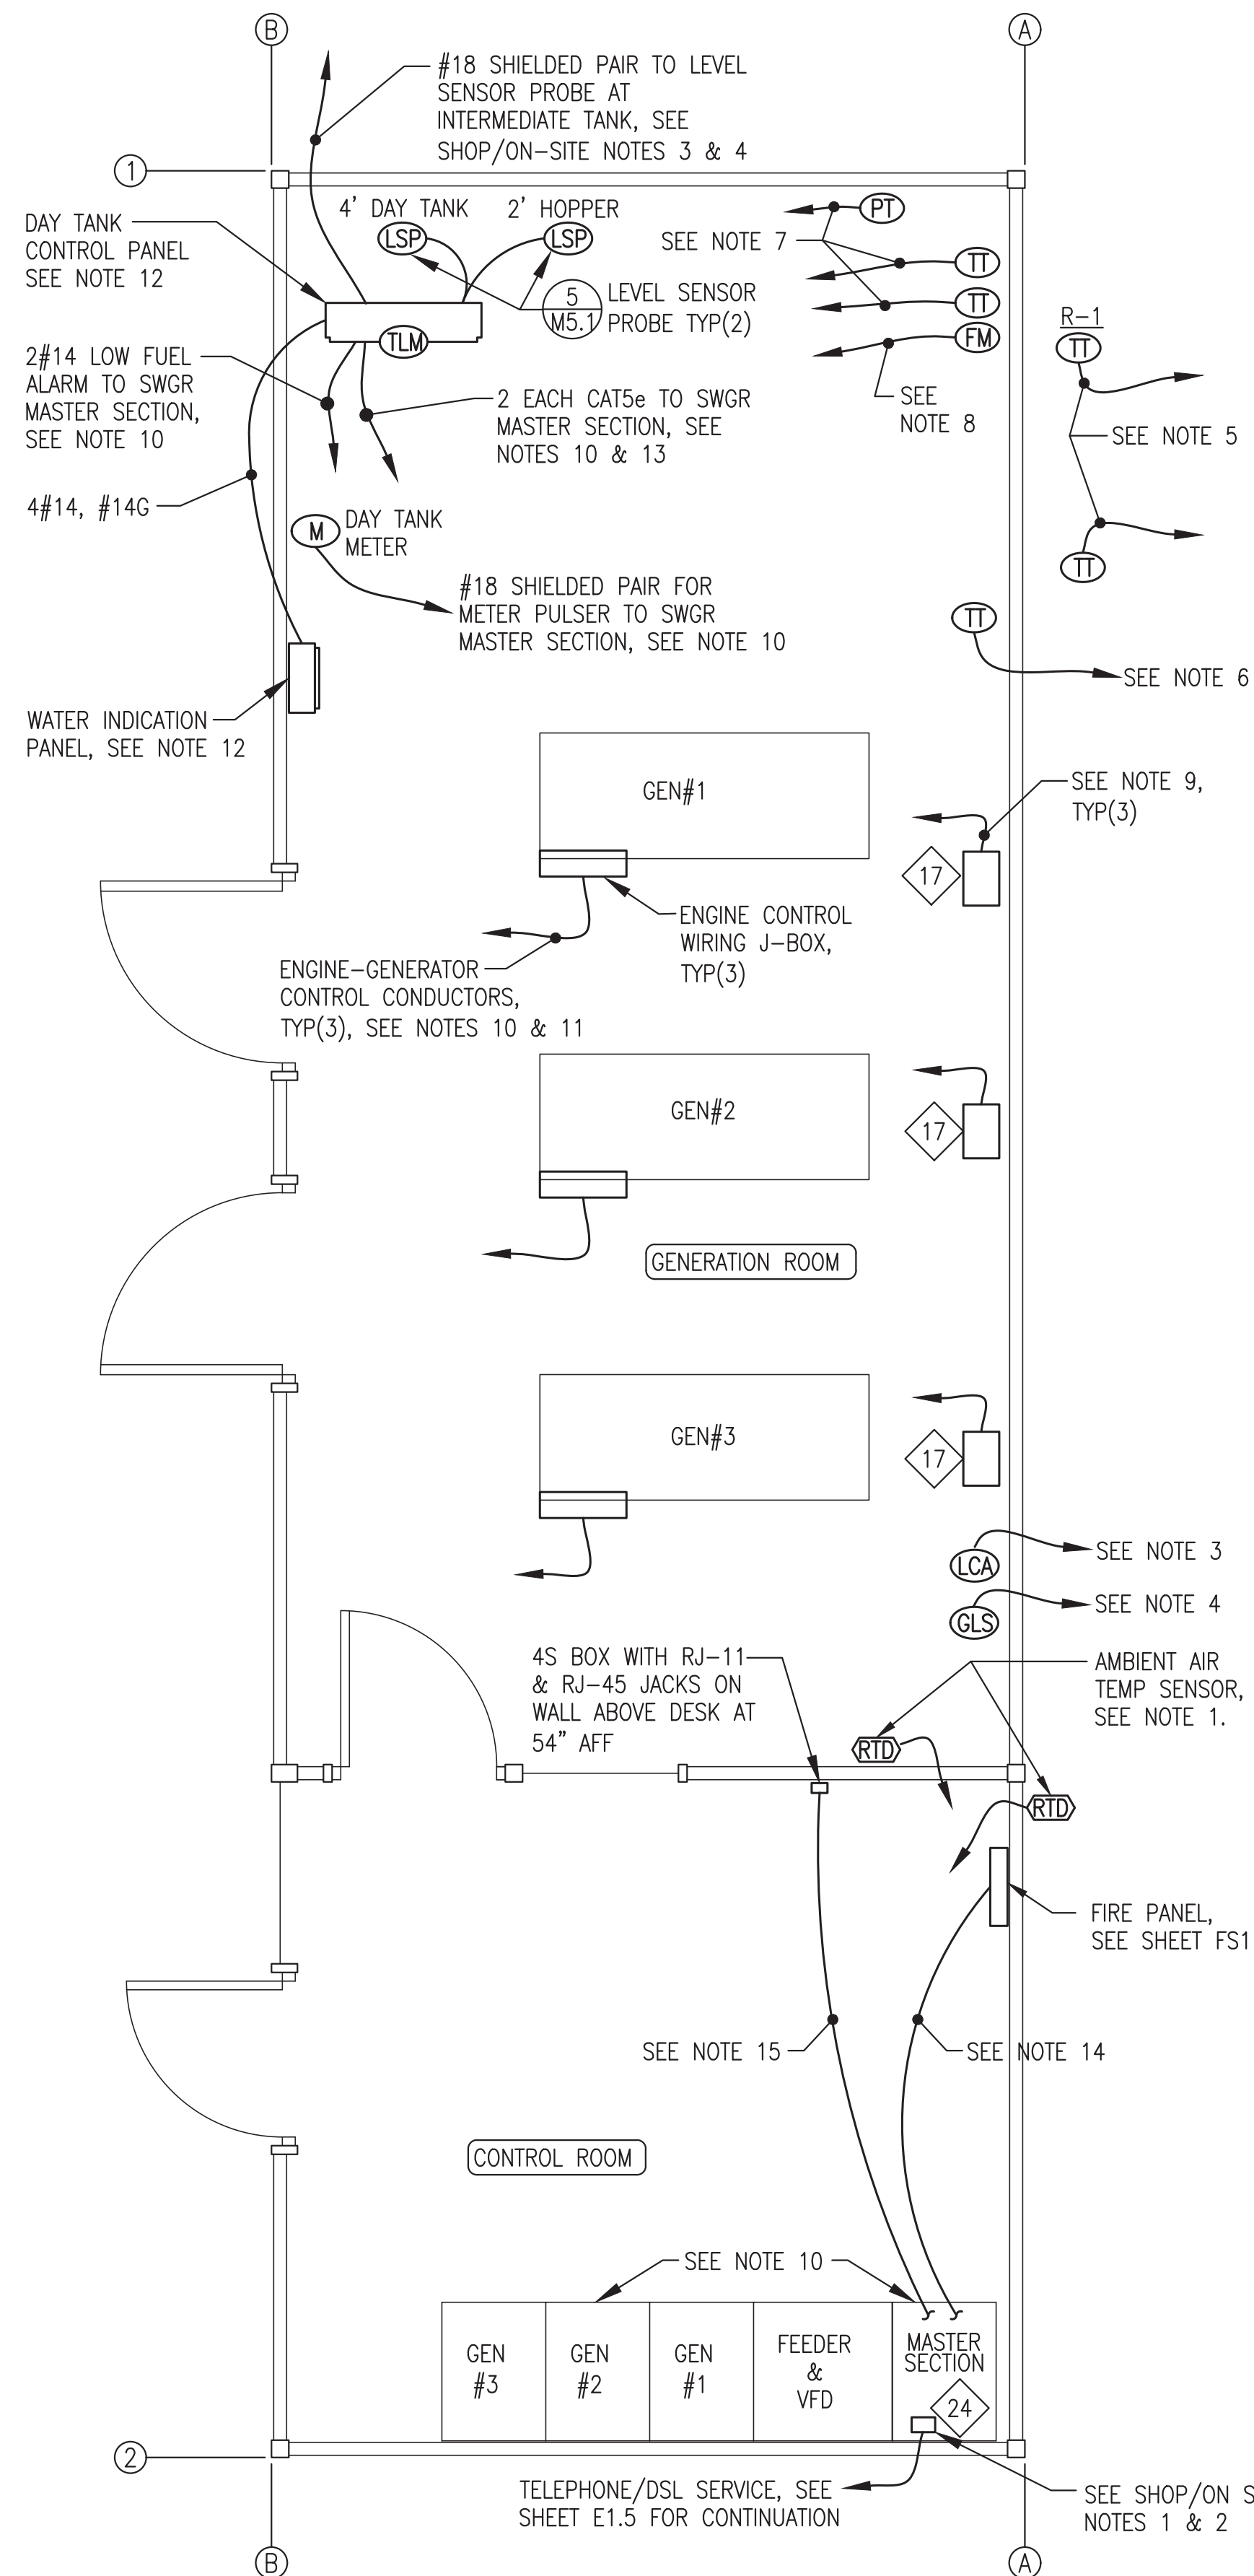


**INSTRUMENTATION & DATA PLAN NOTES:**

- RTD TEMPERATURE SENSOR PROVIDED WITH SWITCHGEAR. ROUTE #18 SHIELDED PAIR TO SWITCHGEAR MASTER SECTION. SEE DETAIL 3/E5 AND NOTE 10.
- INSTALL DSL MODEM AND INTERNET ROUTER ON TOP OF MASTER SECTION IN RACK OR CABINET. CONNECT MODEM TO ROUTER AND TO TELEPHONE LINE. CONNECT ROUTER TO ETHERNET SWITCH INSIDE MASTER SECTION. CONNECT BOTH TO 120VAC UPS. SEE NOTE 10 AND SHOP/ON SITE NOTES 1 AND 2.
- LOW COOLANT LEVEL ALARM SWITCH INSTALLED AT EXPANSION TANK, SEE MECHANICAL. CONNECT TO N.C. SWITCH (WHITE & RED) AND ROUTE 2#14 TO SWITCHGEAR MASTER SECTION. SEE NOTE 10.
- GLYCOL LEVEL SENSOR PROBE INSTALLED IN EXPANSION TANK, SEE MECHANICAL. ROUTE #18 SHIELDED PAIR TO SWITCHGEAR. SEE NOTE 10.
- INSTALL TEMP TRANSMITTER IN EACH RADIATOR, SEE DETAIL 3/E3.3. ROUTE #18 SHIELDED PAIR FROM EACH TO SWITCHGEAR VFD SECTION. SEE ELEVATION 1/E3.3 AND NOTE 10.
- INSTALL COOLANT RETURN TEMP TRANSMITTER IN PIPING MAIN WHERE SHOWN ON COOLING PIPING ISOMETRIC 1/M4.2. ROUTE #18 SHIELDED PAIR TO SWITCHGEAR MASTER SECTION, SEE NOTE 10.
- INSTALL TWO TEMP TRANSMITTERS AND ONE PRESSURE TRANSMITTER FOR HEAT RECOVERY MONITORING WHERE SHOWN ON HEAT RECOVERY PIPING ISOMETRIC 2/M4.2. ROUTE #18 SHIELDED PAIR FROM EACH TO SWITCHGEAR MASTER SECTION. SEE NOTE 10.
- INSTALL FLOW METER FOR HEAT RECOVERY MONITORING WHERE SHOWN ON HEAT RECOVERY PIPING ISOMETRIC 2/M4.2. ROUTE #18 SHIELDED PAIR TO SWITCHGEAR MASTER SECTION. SEE NOTE 10.
- ROUTE 2#14 FROM BATTERY CHARGER ALARM CONTACTS TO ASSOCIATED SWITCHGEAR GENERATOR SECTION, SEE NOTE 10 AND WIRING DIAGRAM 2/E5.
- SEE SWITCHGEAR SHOP DRAWINGS FOR TERMINATION OF ALL INSTRUMENTATION AND DATA WIRING INCLUDING CONTROL POWER.
- ROUTE ENGINE-GENERATOR CONTROL CONDUCTORS TO SWITCHGEAR IN 10x10 WIREWAY WITH POWER CONDUCTORS. SEE DETAIL 2/E3.1, SHEET E6.3, AND NOTE 10.
- SEE SHEETS E7.1-E7.4 FOR DAY TANK AND WATER INDICATION CONTROL PANEL DESIGN AND WIRING TERMINATIONS. ALL ACCESSORIES NOT SHOWN ON PLANS. SEE LOGIC DIAGRAMS FOR ADDITIONAL DETAIL.
- ROUTE CAT5e CONDUCTORS FROM DAY TANK PANEL REMOTE I/O AND TANK LEVEL MONITOR TO ETHERNET SWITCH IN SWITCHGEAR MASTER SECTION. INSTALL IN SEPARATE DEDICATED RACEWAY. DO NOT ROUTE WITH STATION SERVICE OR POWER CONDUCTORS.
- ROUTE CAT5e FOR DATA AND 2#14 FOR GENERATOR SHUT DOWN FROM FIRE PANEL TO SWITCHGEAR MASTER SECTION, SEE SHEET FS1 AND NOTE 10. INSTALL IN SEPARATE DEDICATED RACEWAY, COLOR RED. DO NOT ROUTE WITH STATION SERVICE OR POWER CONDUCTORS.
- ROUTE CAT5e FROM RJ-45 JACK TO ETHERNET SWITCH IN MASTER SECTION. ROUTE TELEPHONE CABLE FROM RJ-11 JACK TO MODEM ON TOP OF MASTER SECTION. INSTALL IN SEPARATE DEDICATED RACEWAY. DO NOT ROUTE WITH STATION SERVICE OR POWER CONDUCTORS.

**INSTRUMENTATION SHOP/ON-SITE NOTES:**


- AS PART OF SHOP FABRICATION INSTALL RACK OR CABINET ON TOP OF MASTER SECTION AND INSTALL INTERNET ROUTER. CONNECT ROUTER TO ETHERNET SWITCH AND TO 120VAC UPS INSIDE MASTER SECTION. SEE NOTE 10.
- AS PART OF ON-SITE WORK INSTALL DSL MODEM ON TOP OF MASTER SECTION IN EXISTING RACK OR CABINET. CONNECT MODEM TO TELEPHONE LINE, TO ROUTER, AND TO 120VAC UPS INSIDE MASTER SECTION. SEE NOTE 10.
- AS PART OF SHOP FABRICATION INSTALL WALL PENETRATION AND CONDUIT INTO DAY TANK PANEL. SEE ELEVATION 5/E3.2.
- AS PART OF ON-SITE WORK INSTALL CONDUIT AND CONDUCTORS TO INTERMEDIATE TANK, SEE SHEET E1.6.

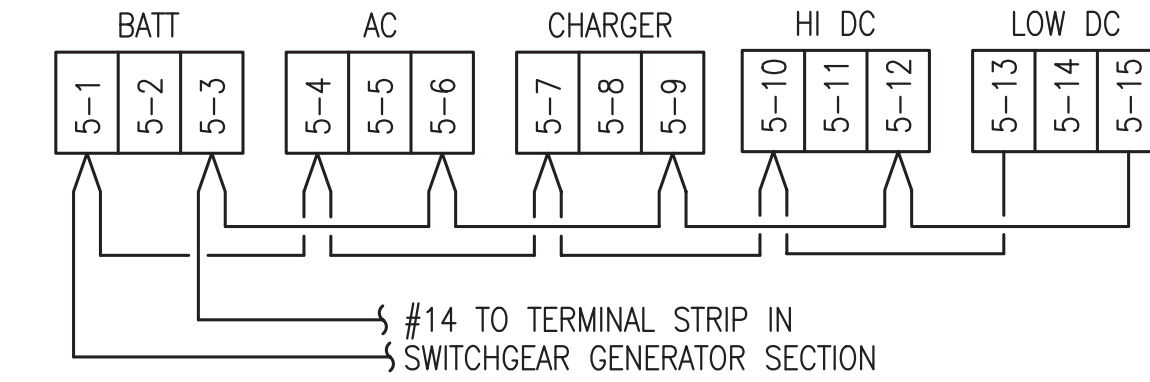

NOTE: PRIOR TO ENERGIZING MAKE THE FOLLOWING SETTINGS ON CHARGER:

- AC LINE VOLTAGE SWITCH TO "115V".
- AUTO BOOST JUMPER TO "NORM".
- FLOAT VOLTAGE JUMPER TO "13.50/27.00" (FOR GEL CELL).
- BATTERY RANGE JUMPER TO "24V".


**2 BATTERY CHARGER ALARM WIRING DIAGRAM**  
NO SCALE

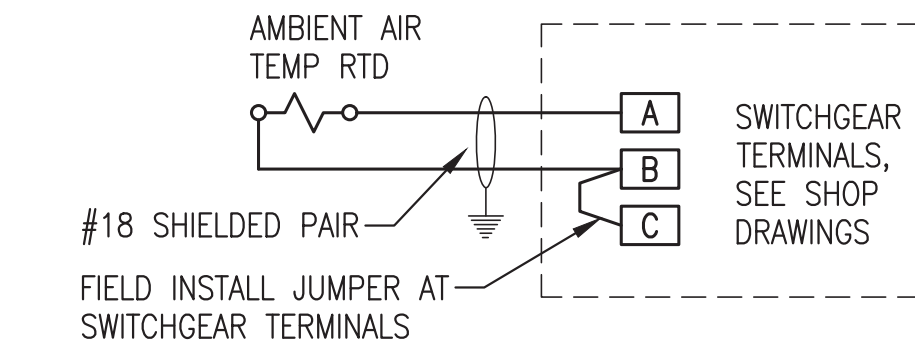



**3 AMBIENT AIR TEMP RTD TERMINATION**  
NO SCALE

**1 INSTRUMENTATION & DATA PLAN**  
3/8"=1'-0"

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT: <b>RAMPART POWER SYSTEM UPGRADE</b>			
TITLE: <b>INSTRUMENTATION &amp; DATA PLAN &amp; DETAILS</b>			
 <b>Gray Stassel Engineering, Inc.</b> P.O. 111405, Anchorage, AK 99511 (907)349-0100		DRAWN BY: JTD DESIGNED BY: CWV/BCG FILE NAME: RAM_PP_E2-E5 PROJECT NUMBER:	SCALE: AS NOTED DATE: 3/15/22 SHEET: <b>E5</b>

Demand Control Table (PLC)				
Demand Control	Generator(s) On Line	On-line kW (Overload)	Level Increase	Level Decrease
Level 1	#3	65	55	---
Level 2	#1 or #2	100	90	45
Level 3	#3 & #1 or #2	165	145	80
Level 4	All	265	---	125


Note : Gen #1 & #2 are equal capacity. Manually select lead unit.

Engine-Generator Alarm Settings (Easygen - EZGN)			
Function	Normal Range	Alarm	Shut Down
Overspeed	1795-1805	----	1900 RPM
Oil Pressure	30-50 PSI	14.5 PSI	10 PSI
Air Filter Vacuum	1-10" H2O	15" H2O	20" H2O
Coolant Temp.	180-200°F	210°F	215°F
Exhaust Temp.	500-850°F	900°F	-----
Under Frequency	59.5-60.5 Hz	----	58.2 Hz
Over Frequency	59.5-60.5 Hz	----	61.8 Hz
Under Voltage	470-490 V	----	432 V
Over Voltage	470-490 V	----	528 V
Reverse Power	0	----	10%


Generator Breaker Settings (Easygen - EZGN)	
Function	Setting
Gen #1 Breaker Trip Setpoint (EZGN Rated Current)	200 A
Gen #2 Breaker Trip Setpoint (EZGN Rated Current)	200 A
Gen #3 Breaker Trip Setpoint (EZGN Rated Current)	150 A
Gen Breaker Level 1 (100%) Time Over Current	3 sec.
Gen Breaker Level 2 (120%) Time Over Current	1 sec.
Gen Breaker Level 3 (250%) Time Over Current	0.4 sec.

Feeder Breaker Settings (Feeder Protection Relay - FPR)	
Function (Note: Element 1 is the only active element)	Setting
T.O.C. Trip Pickup (amps) Note: 5A = 100% of CT rating	5.0
T.O.C. Curve Selection	U4
T.O.C. Time Dial	5.00
E.M Reset delay (Y/N)	N
Constant Time Adder (seconds)	0.00
Minimum Response Time (seconds)	0.00
Maximum Phase T.O.C. Torque Control	1


Radiator VFD Settings	
Function	Setting
Min PID Feedback	20
Max PID Feedback	240
rSL (Wake UP Threshold)	1
PID Reference Temperature	175°F
Proportional Gain	0.93
Integral Gain	0.3
Derivative	0
Minimum Speed	10 Hz.
Low Speed Timeout	10 sec.
Loss of Phase	Ignore

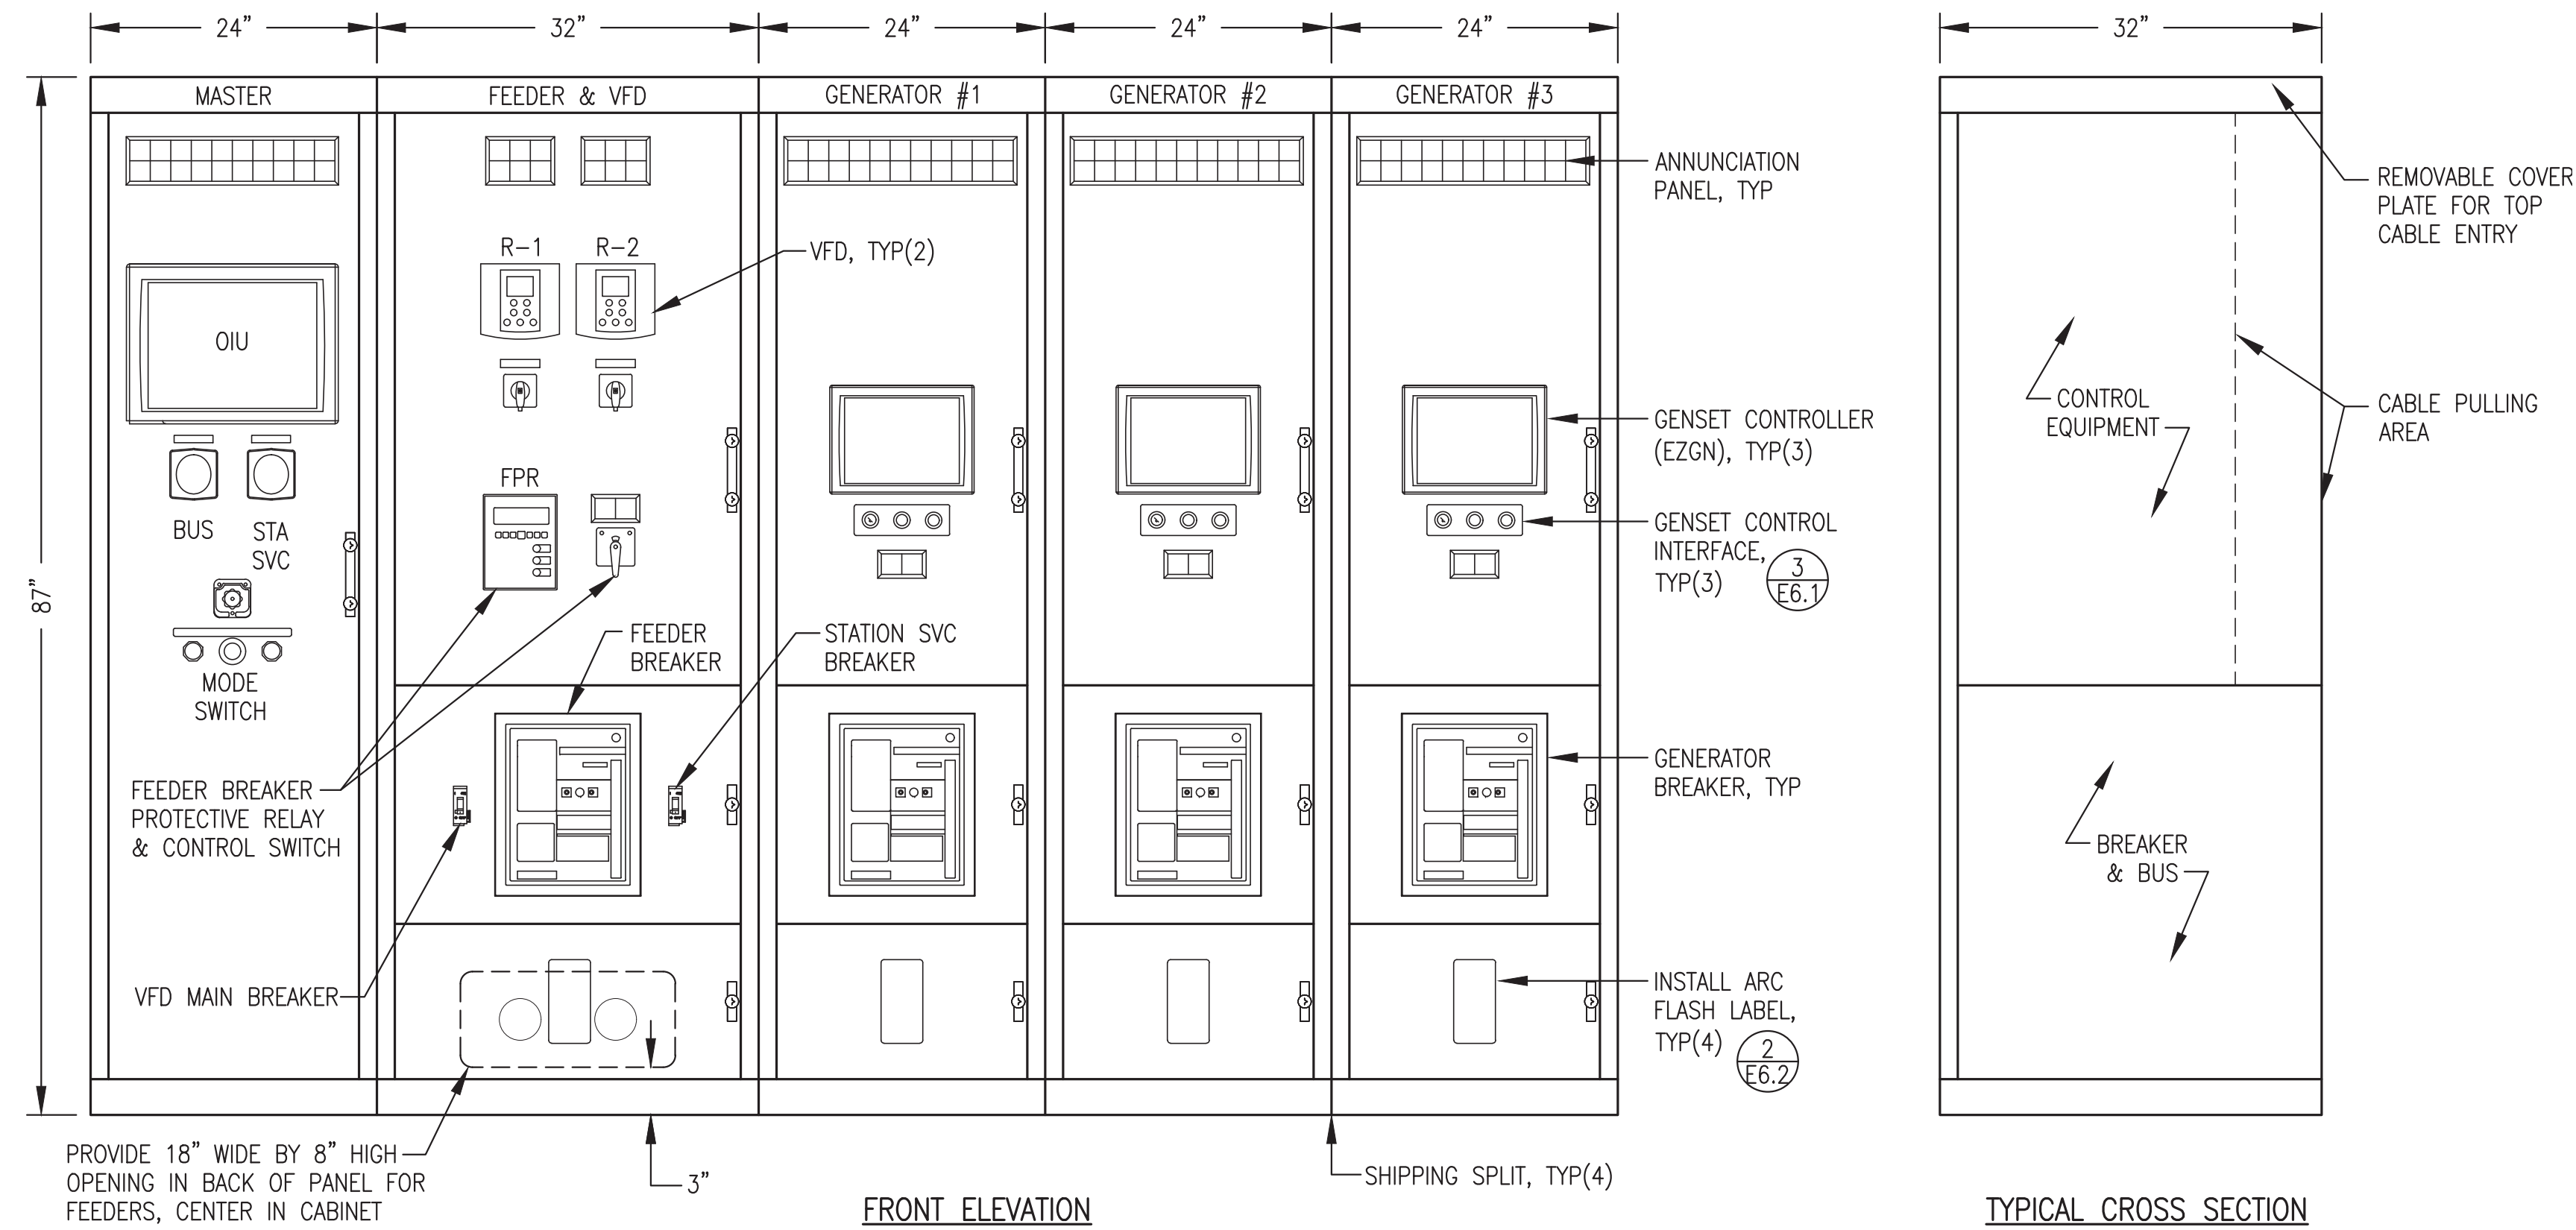


1 SWITCHGEAR ENCLOSURE LAYOUT  
E6.1 NO SCALE

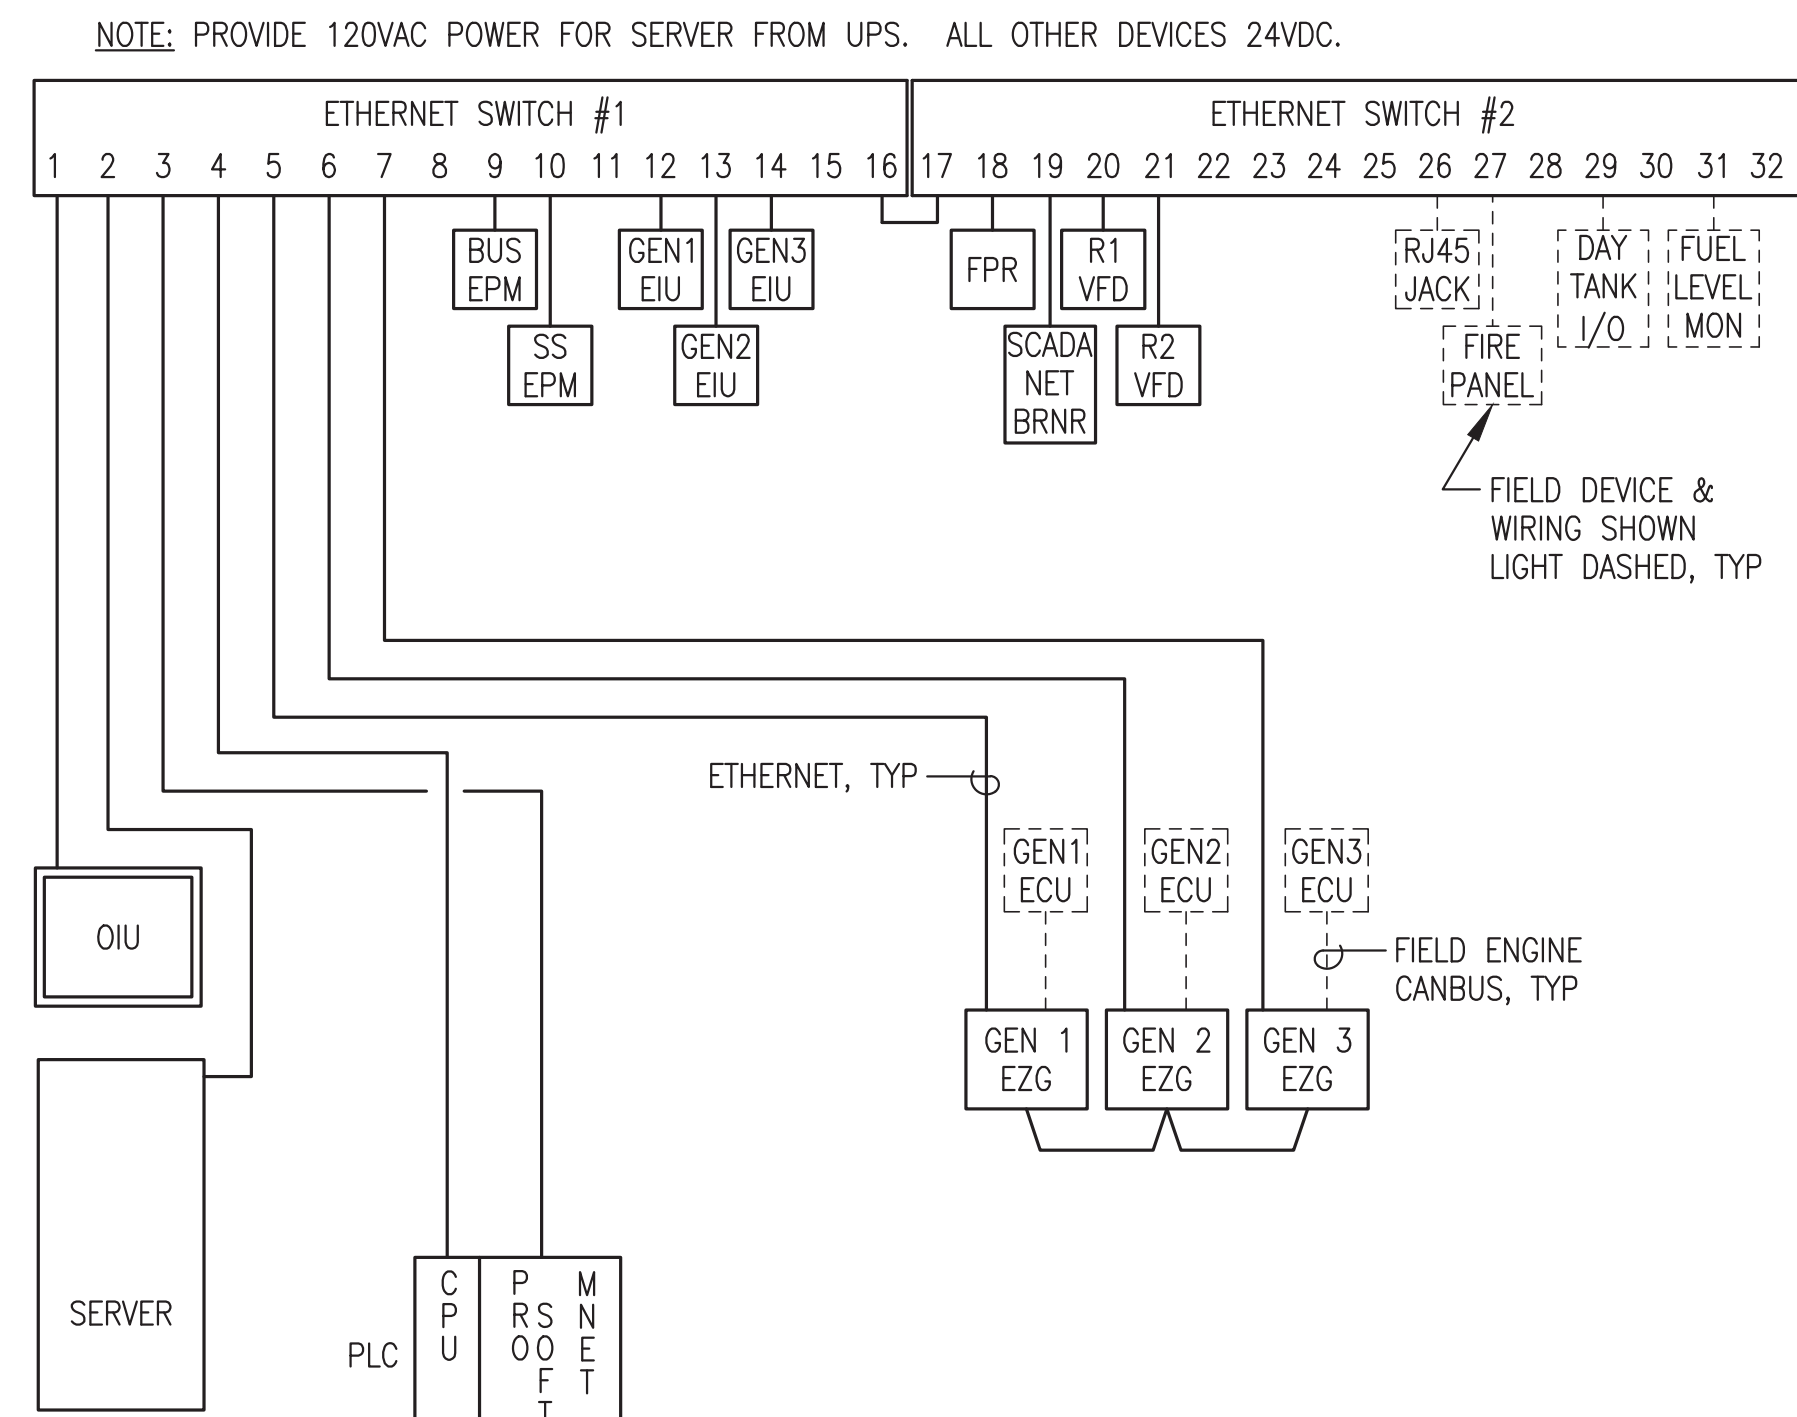

2 COMMUNICATION SCHEMATIC  
E6.1 NO SCALE

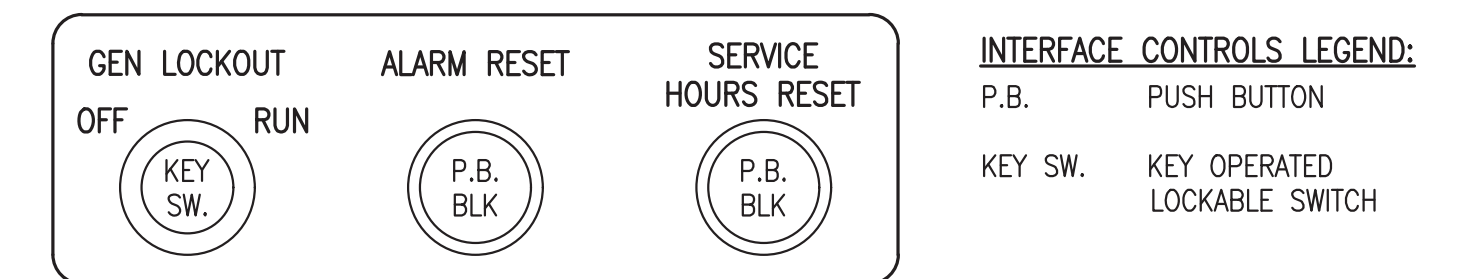


EASYGEN INTERFACE CONTROLS

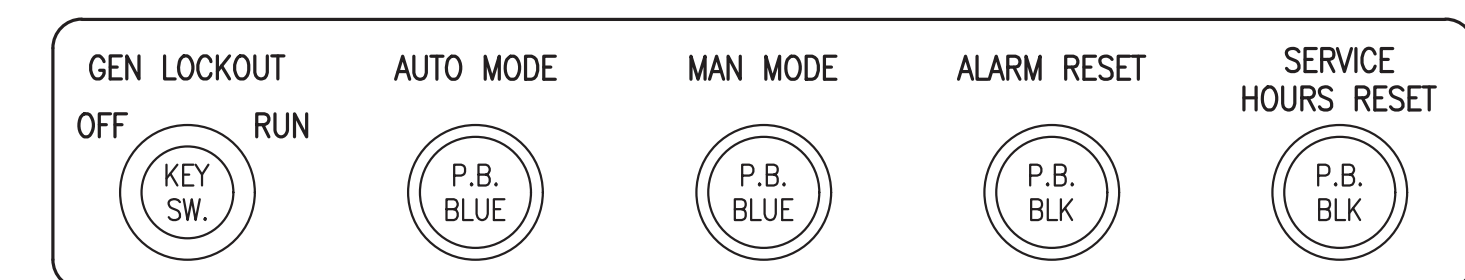


COMAP INTERFACE CONTROLS

3 GENSET CONTROL (EZGN) INTERFACE CONTROLS  
E6.1 NO SCALE

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: SWITCHGEAR ENCLOSURE LAYOUT, SETTING TABLE, & DETAILS			
DRAWN BY: JTD		SCALE: NO SCALE	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM PP E6		SHEET: E6.1	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

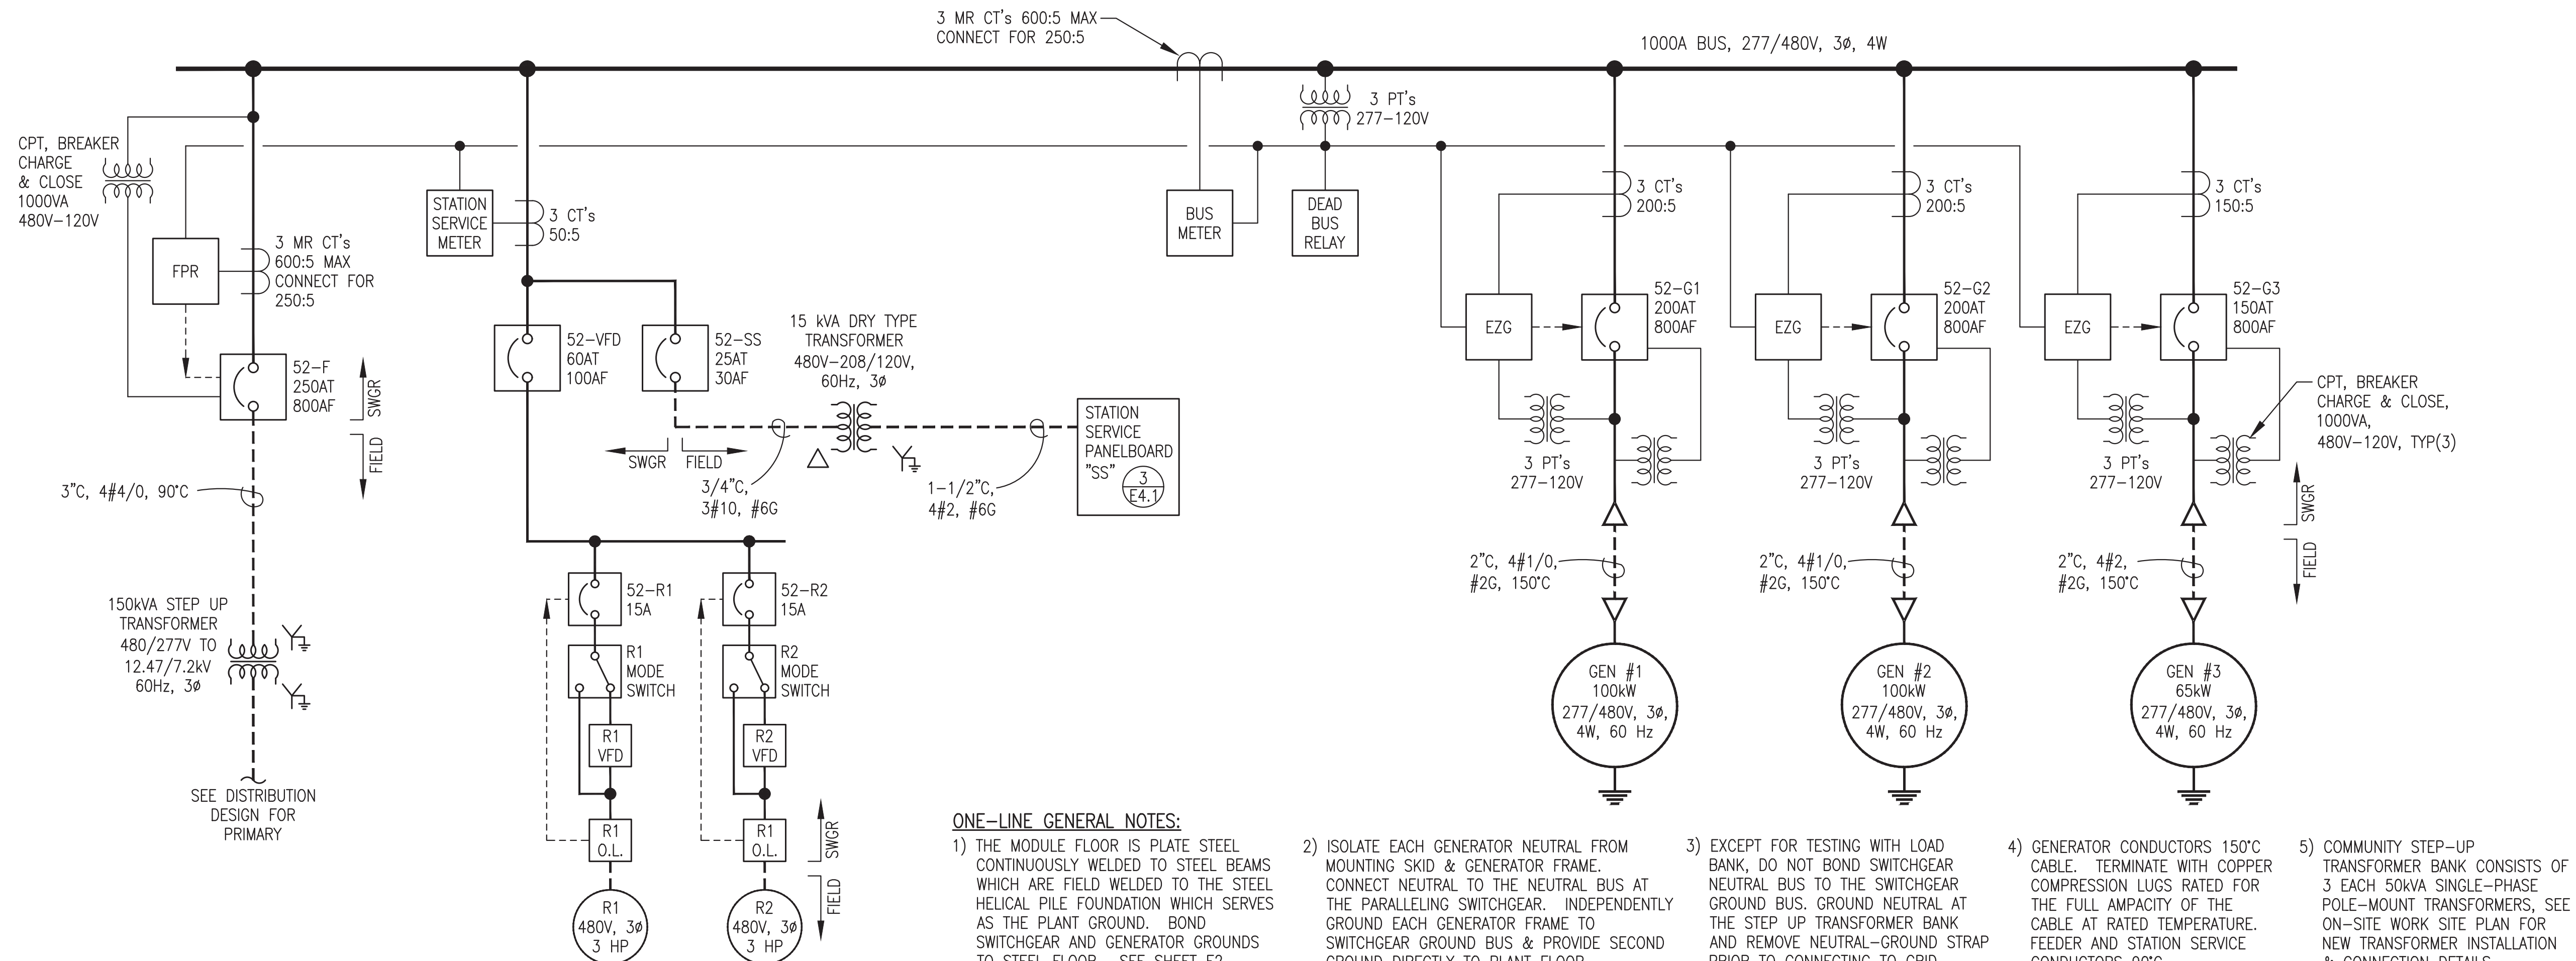

SWITCHGEAR SYMBOL LEGEND	
	TRANSFORMER PT=POTENTIAL XFRMR CPT=CONTROL POWER XFRMR
	CURRENT TRANSFORMER M.R. - INDICATES MULTIRATIO CT'S RATING FACTOR RF=2.0
	CIRCUIT BREAKER AT=AMP TRIP RATING AF=AMP FRAME RATING
	WOODWARD EASYPEN GENSET CONTROLLER
	FEEDER PROTECTION RELAY
	SHOP INSTALLED POWER WIRING/BUS
	FIELD INSTALLED POWER WIRING
	SHOP INSTALLED CONTROL WIRING

**ONE-LINE GENERAL NOTES:**

- 1) THE MODULE FLOOR IS PLATE STEEL CONTINUOUSLY WELDED TO STEEL BEAMS WHICH ARE FIELD WELDED TO THE STEEL HELICAL PILE FOUNDATION WHICH SERVES AS THE PLANT GROUND. BOND SWITCHGEAR AND GENERATOR GROUNDS TO STEEL FLOOR. SEE SHEET E2.
- 2) ISOLATE EACH GENERATOR NEUTRAL FROM MOUNTING SKID & GENERATOR FRAME. CONNECT NEUTRAL TO THE NEUTRAL BUS AT THE PARALLELING SWITCHGEAR. INDEPENDENTLY GROUND EACH GENERATOR FRAME TO SWITCHGEAR GROUND BUS & PROVIDE SECOND GROUND DIRECTLY TO PLANT FLOOR.
- 3) EXCEPT FOR TESTING WITH LOAD BANK, DO NOT BOND SWITCHGEAR NEUTRAL BUS TO THE SWITCHGEAR GROUND BUS. GROUND NEUTRAL AT THE STEP UP TRANSFORMER BANK AND REMOVE NEUTRAL-GROUND STRAP PRIOR TO CONNECTING TO GRID.
- 4) GENERATOR CONDUCTORS 150°C CABLE. TERMINATE WITH COPPER COMPRESSION LUGS RATED FOR THE FULL AMPACITY OF THE CABLE AT RATED TEMPERATURE. FEEDER AND STATION SERVICE CONDUCTORS 90°C.
- 5) COMMUNITY STEP-UP TRANSFORMER BANK CONSISTS OF 3 EACH 50kVA SINGLE-PHASE POLE-MOUNT TRANSFORMERS, SEE ON-SITE WORK SITE PLAN FOR NEW TRANSFORMER INSTALLATION & CONNECTION DETAILS

**1 SWITCHGEAR ONE-LINE DIAGRAM**  
NO SCALE

- ARC FLASH NOTES:**
- 1) PERMANENTLY AFFIX ARC FLASH LABELS TO EACH SECTION WITH 480V POWER AS INDICATED.
  - 2) SCALED PDF IMAGES OF THESE LABELS WILL BE FURNISHED TO THE FABRICATOR UPON REQUEST.

**WARNING**  
07-15-2022

**Arc Flash and Shock Hazard**  
Appropriate PPE Required

Arc Flash Boundary	0.4 ft
Incident Energy (cal/cm <sup>2</sup> )	0.2
Working Distance	18.0 in

Arc-rated long-sleeve shirt and arc-rated pants or arc-rated coverall and/or arc flash suit, Arc-rated face shield, Arc-rated jacket, Hard hat, Arc-rated hard hat liner, Safety glasses, Hearing protection, Leather gloves and Leather work shoes.

Shock Hazard Exposure: 480 V  
Shock Hazard when covers removed

Limited Approach	3.5 ft	Class 00
Restricted Approach	1.0 ft	Insulating Gloves V-rating 500 VAC

**GENERATOR**

**WARNING**  
07-15-2022

**Arc Flash and Shock Hazard**  
Appropriate PPE Required


Arc Flash Boundary	0.4 ft
Incident Energy (cal/cm <sup>2</sup> )	0.2
Working Distance	18.0 in

Arc-rated long-sleeve shirt and arc-rated pants or arc-rated coverall and/or arc flash suit, Arc-rated face shield, Arc-rated jacket, Hard hat, Arc-rated hard hat liner, Safety glasses, Hearing protection, Leather gloves and Leather work shoes.

Shock Hazard Exposure: 480 V  
Shock Hazard when covers removed

Limited Approach	3.5 ft	Class 00
Restricted Approach	1.0 ft	Insulating Gloves V-rating 500 VAC


**FEEDER**

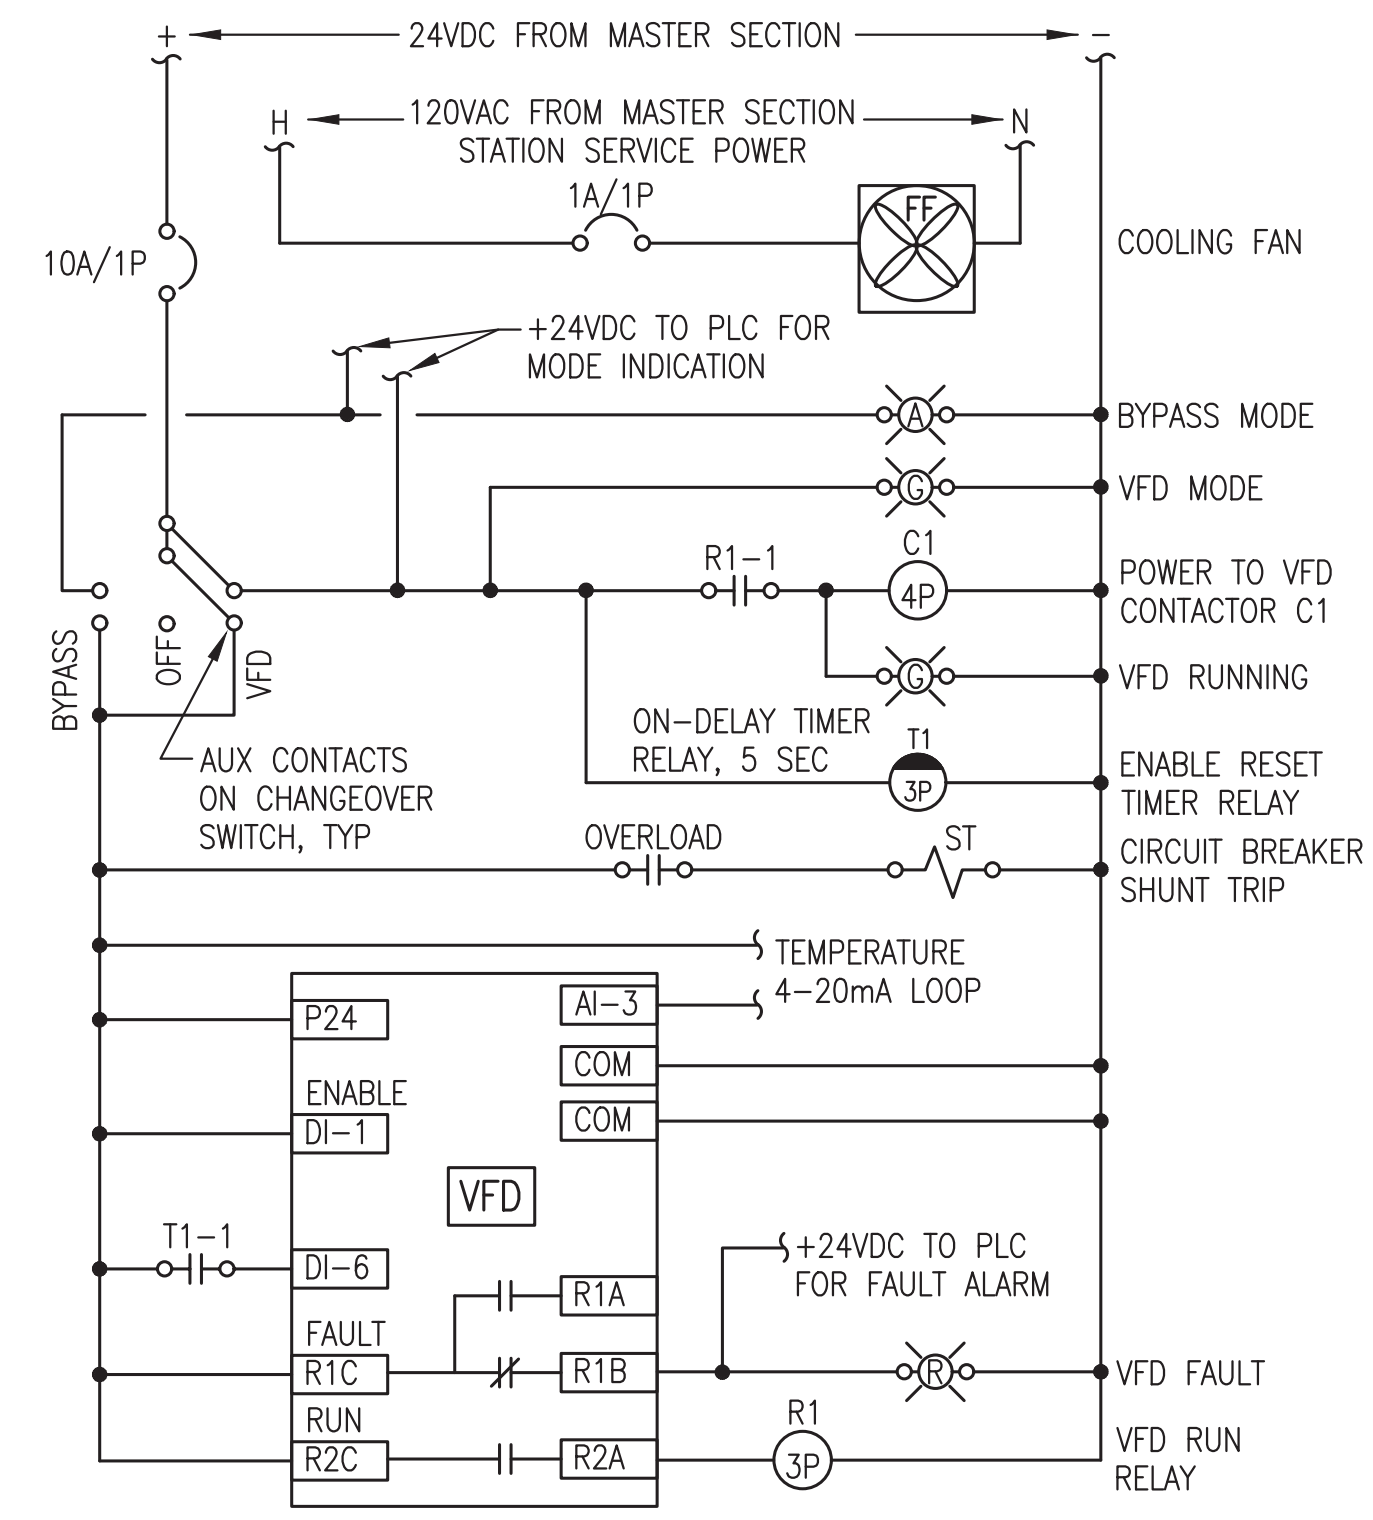


**3 TYPICAL RADIATOR VFD LOGIC DIAGRAM**  
NO SCALE

**2 ARC FLASH LABELS**  
NO SCALE


REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022




1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: SWITCHGEAR ONE-LINE & SCHEMATICS			
DRAWN BY: JTD		SCALE: NO SCALE	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM PP E6		SHEET: E6.2	
PROJECT NUMBER:			
 <b>Gray Stassel Engineering, Inc.</b> P.O. 111405, Anchorage, AK 99511 (907)349-0100			

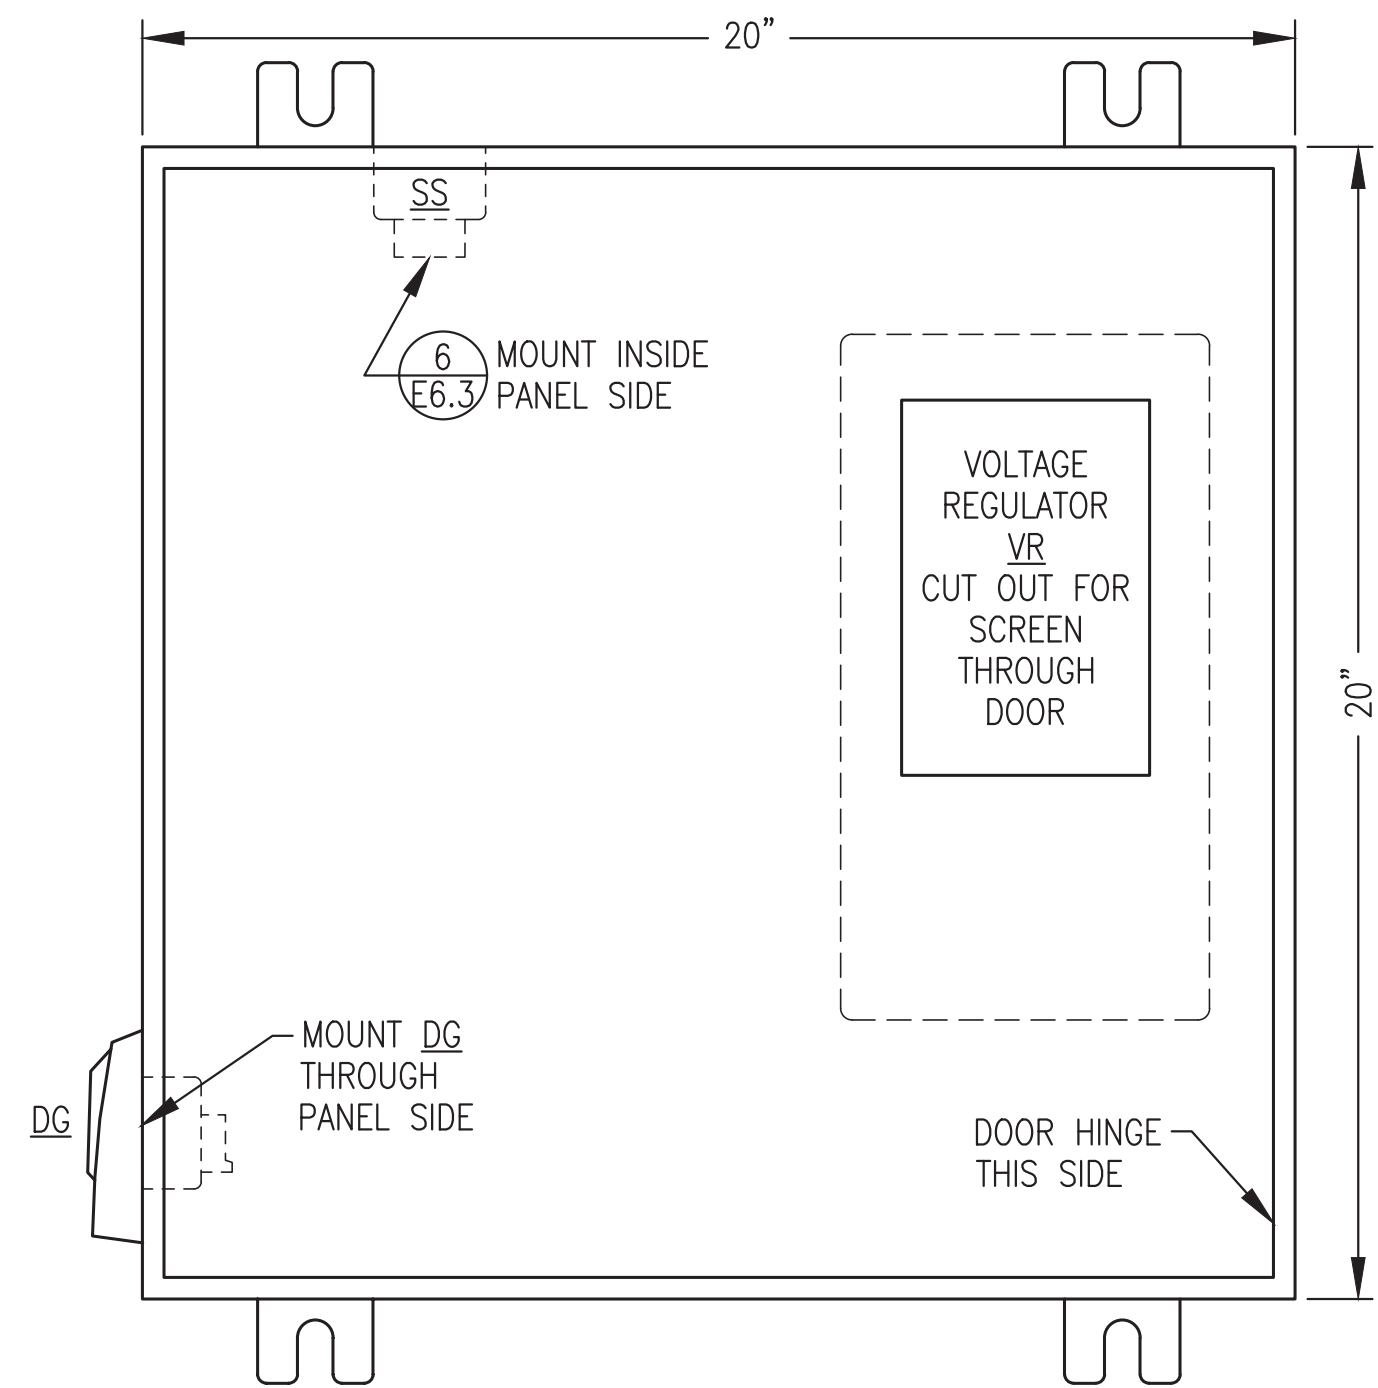


**1** JUNCTION BOX FRONT PANEL LAYOUT  
E6.3 NO SCALE

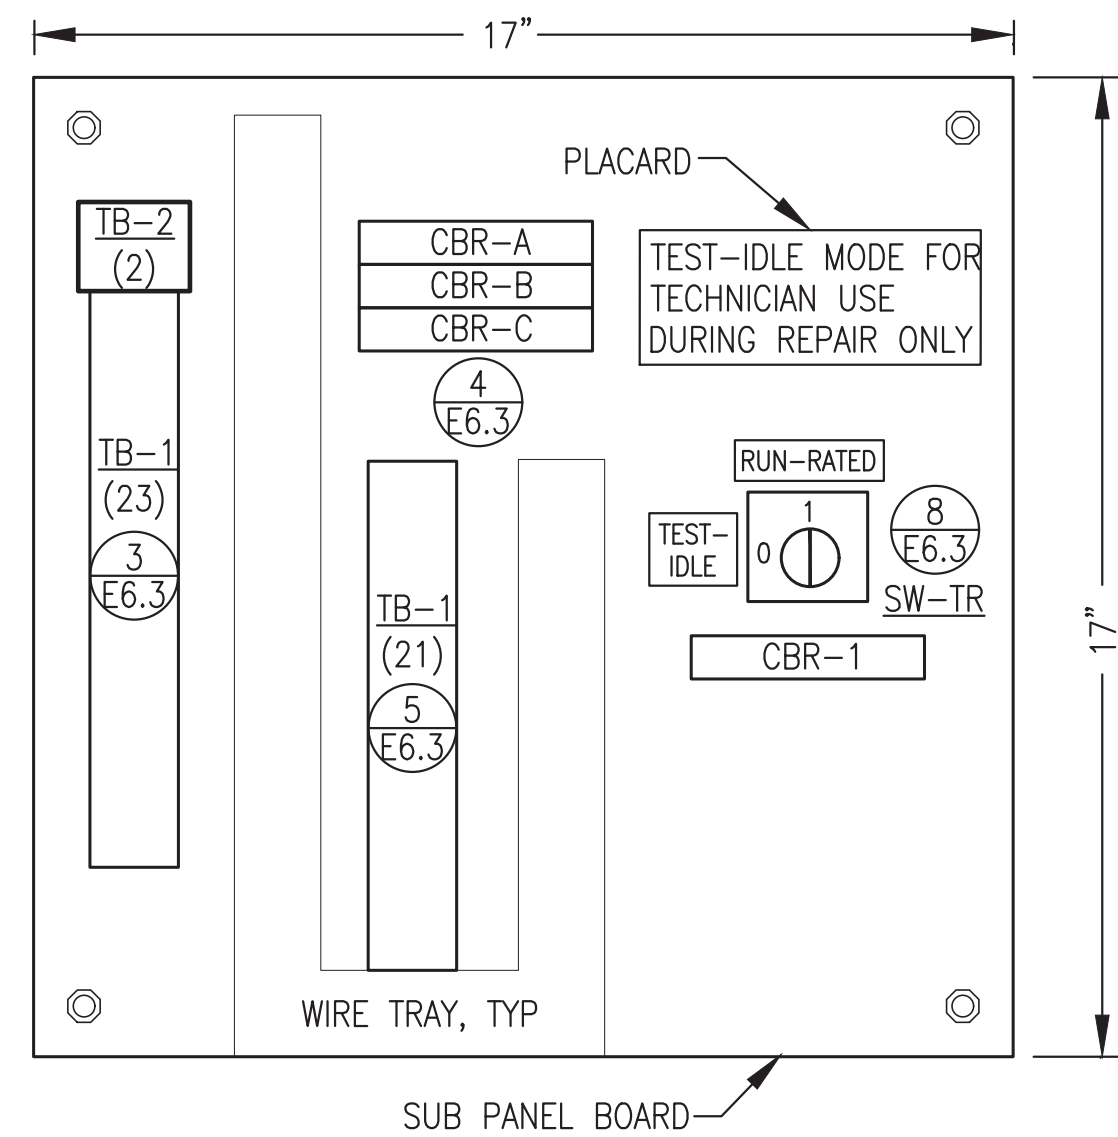

**2** JUNCTION BOX SUB PANEL LAYOUT  
E6.3 NO SCALE




**3** TERMINAL STRIP CONNECTIONS  
E6.3 NO SCALE

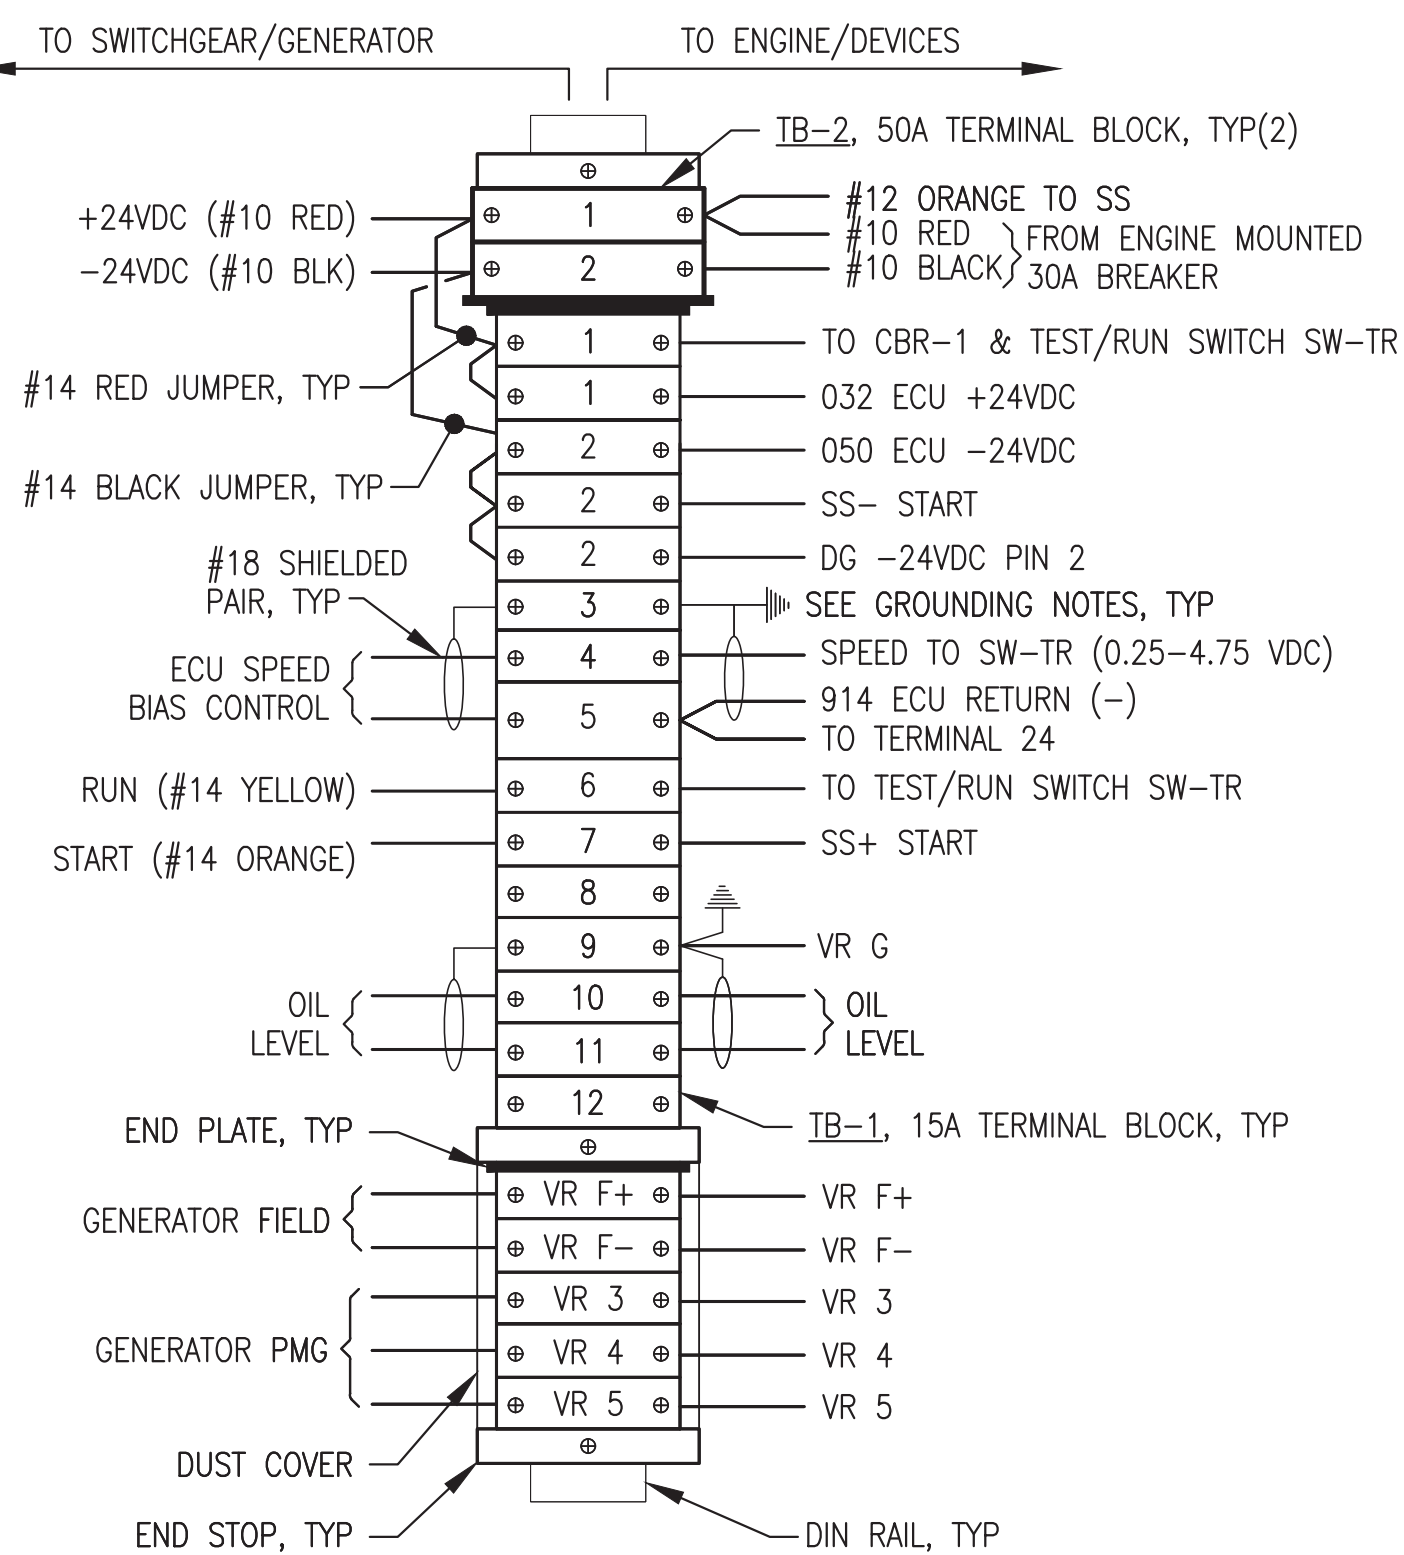

NOTE: TYPICAL JOHN DEERE ECU CONNECTION NUMBERS SHOWN. SEE WIRING HARNESS FOR EACH ENGINE FOR ACTUAL ECU CONNECTIONS.

**3** TERMINAL STRIP CONNECTIONS  
E6.3 NO SCALE

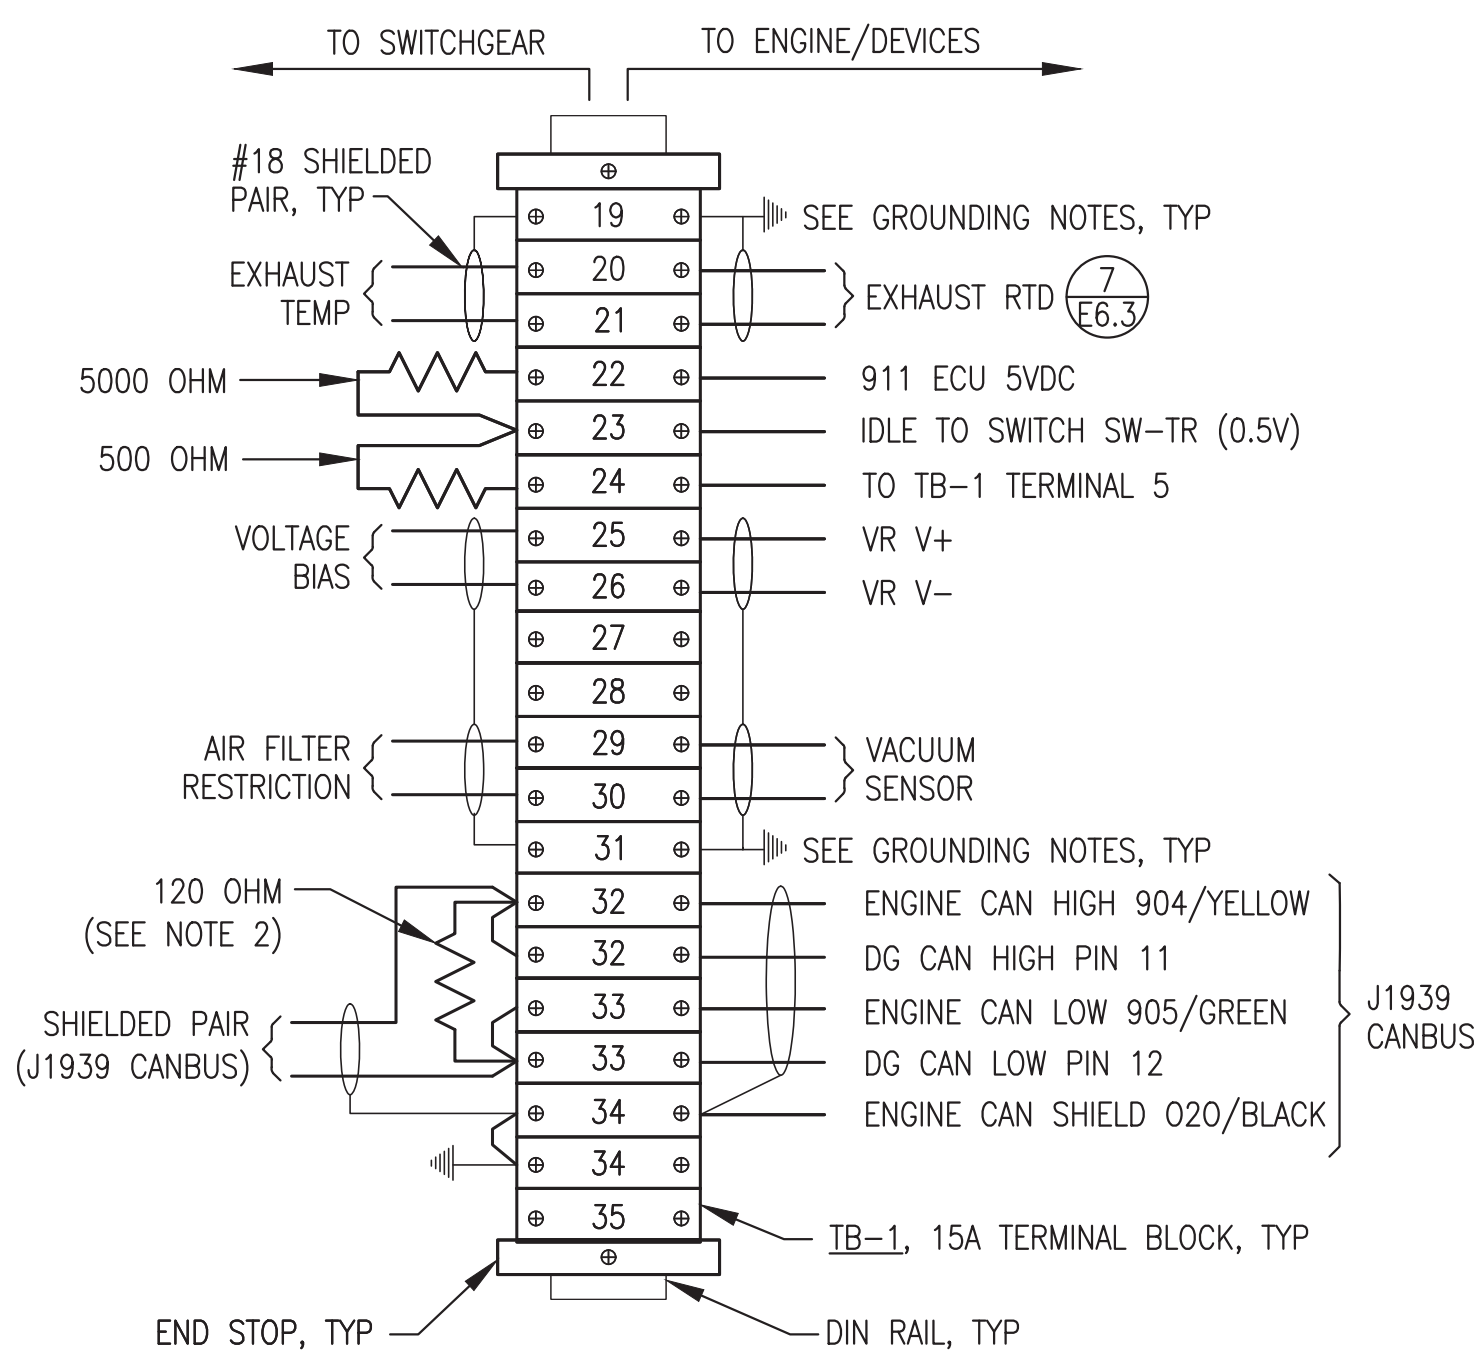

NOTES: 1) ALL RESISTORS 0.25W.  
2) REMOVE RESISTOR IF ENGINE WIRING HARNESS HAS 120 OHM END OF LINE RESISTOR.

**4** CIRCUIT BREAKER CONNECTIONS  
E6.3 NO SCALE

TAG	MANUFACTURER	MODEL	DESCRIPTION
CBR-A/B/C	ALLEN-BRADLEY	1489-M1-C010	RAIL MOUNT CIRCUIT BREAKER, 1P, 1A
CBR-1	ALLEN-BRADLEY	1489-M1-C050	RAIL MOUNT CIRCUIT BREAKER, 1P, 5A
DG	JOHN DEERE	DG-14	DIAGNOSTIC GAUGE WITH HARNESS PROGRAMMED FOR MARINE TIER 3 WITH UNIQUE JOHN DEERE FAULT CODE
ENCL.	HOFFMAN	A20H20ALP	20x20x8" NEMA 12 BACK PANEL
SS	HOFFMAN	A20P20	STARTER AUXILIARY SOLENOID, 24V
SW-TR	ALLEN-BRADLEY	194L-A12-225-2	CHANGEOVER SWITCH, 12A, 2P
	ALLEN-BRADLEY	194L-HE-4A-175	90 DEGREE I-O HANDLE
TB-1	IDEC	BNH15LW	15A DIN RAIL-MOUNT TERMINAL BLOCK
TB-2	IDEC	BNH50W	50A DIN RAIL-MOUNT TERMINAL BLOCK
VR	BASLER	DECS-150 5NS1V1N1S	DIGITAL VOLTAGE REGULATOR


BRAND SPECIFIC NOTE: SPECIFIC PARTS MANUFACTURER AND MODEL SELECTED NOT ONLY TO MEET PERFORMANCE FUNCTION BUT ALSO TO COORDINATE AND INTERFACE WITH OTHER DEVICES AND SYSTEMS. APPROVED EQUAL SUBSTITUTIONS WILL BE ALLOWED ONLY BY ENGINEER'S APPROVAL. TO OBTAIN APPROVAL, SUBMITTALS MUST CLEARLY DEMONSTRATE HOW SUBSTITUTE ITEM MEETS OR EXCEEDS SPECIFIED ITEM QUALITY AND PERFORMANCE CHARACTERISTICS AND ALSO COMPLIES WITH MECHANICAL AND/OR ELECTRICAL CONNECTIONS AND PHYSICAL LAYOUT REQUIREMENTS.

**SHOP FABRICATION NOTES:**


- PROVIDE ASSEMBLY WITH ALL DEVICES AND WIRING INDICATED.
- INSTALL IN A NEMA 12 ENCLOSURE WITH MOUNTING FLANGES AT BACK, A MIN 14 GAUGE INTERIOR BACK PANEL AND HINGED LOCKABLE DOOR. SIZE AS INDICATED.
- PROVIDE DIN RAIL, TERMINAL END PLATES, TERMINAL END STOPS, TERMINAL DUST COVERS AND OTHER MISCELLANEOUS HARDWARE AS REQUIRED TO MATCH TERMINALS. LABEL ALL TERMINALS EXACTLY AS INDICATED ON THE DETAILS.
- ALL WIRE #14AWG EXCEPT WHERE SPECIFICALLY INDICATED OTHERWISE. LABEL BOTH ENDS OF ALL JUMPERS WITH THE ENGINE PANEL TERMINAL NUMBER.
- PROVIDE MECHANICAL GROUND LUGS FASTENED TO BACK PANEL AND GROUNDED TO ENGINE-GENERATOR. GROUND ALL SHIELD DRAIN WIRES TO LUGS AT BACK PANEL ONLY.
- PROVIDE WIRING HARNESSES FOR CONNECTION TO GENERATOR AND TO ENGINE. INSTALL WIRES IN LIQUID TIGHT FLEX OR FLEXIBLE PLASTIC WIRE LOOM AND PROVIDE SERVICE LOOPS IN ACCORDANCE WITH SPECIFICATIONS.
- SHOP TEST EACH NEW ENGINE-GENERATOR WITH ASSOCIATED JUNCTION BOX PERMANENTLY CONNECTED. UPON COMPLETION OF TESTING, COIL WIRING HARNESSES AND SECURE JUNCTION BOX TO GENERATOR FOR SHIPPING.

**FIELD INSTALLATION NOTES:**


- PERFORM ALL FIELD WIRING IN ACCORDANCE WITH SPECIFICATIONS. LABEL BOTH ENDS OF ALL FIELD WIRING WITH THE ENGINE PANEL TERMINAL NUMBER.
- ON SHIELDED CONDUCTORS GROUND ALL SHIELD DRAIN WIRES AT ENGINE J-BOX ONLY. CLIP DRAIN WIRES AT OPPOSITE ENDS.

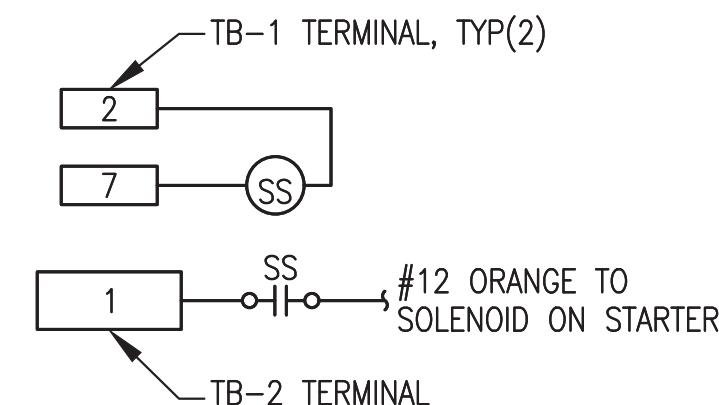

**6** STARTER AUX SOLENOID SS WIRING  
E6.3 NO SCALE

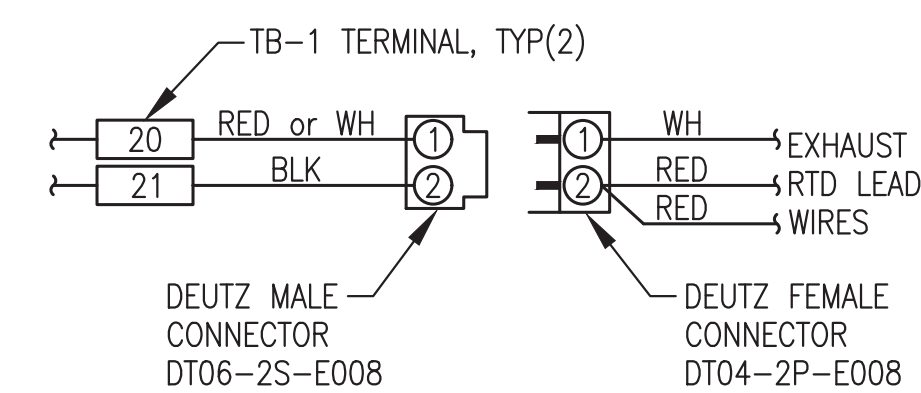


**7** EXHAUST RTD CONNECTOR  
E6.3 NO SCALE

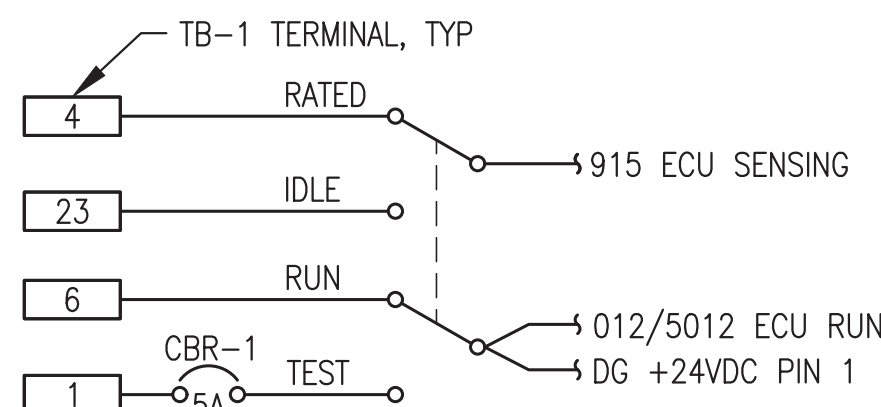


**8** TEST-IDLE/RUN-RATED SWITCH SW-TR WIRING  
E6.3 NO SCALE

ENGINE WIRING JUNCTION BOXES SHOWN HERE WILL BE FURNISHED AS PART OF THE OWNER FURNISHED ENGINE-GENERATORS.


REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: 24VDC ENGINE WIRING JUNCTION BOX			
DRAWN BY: JTD		SCALE: NO SCALE	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM PP E6		SHEET: E6.3	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

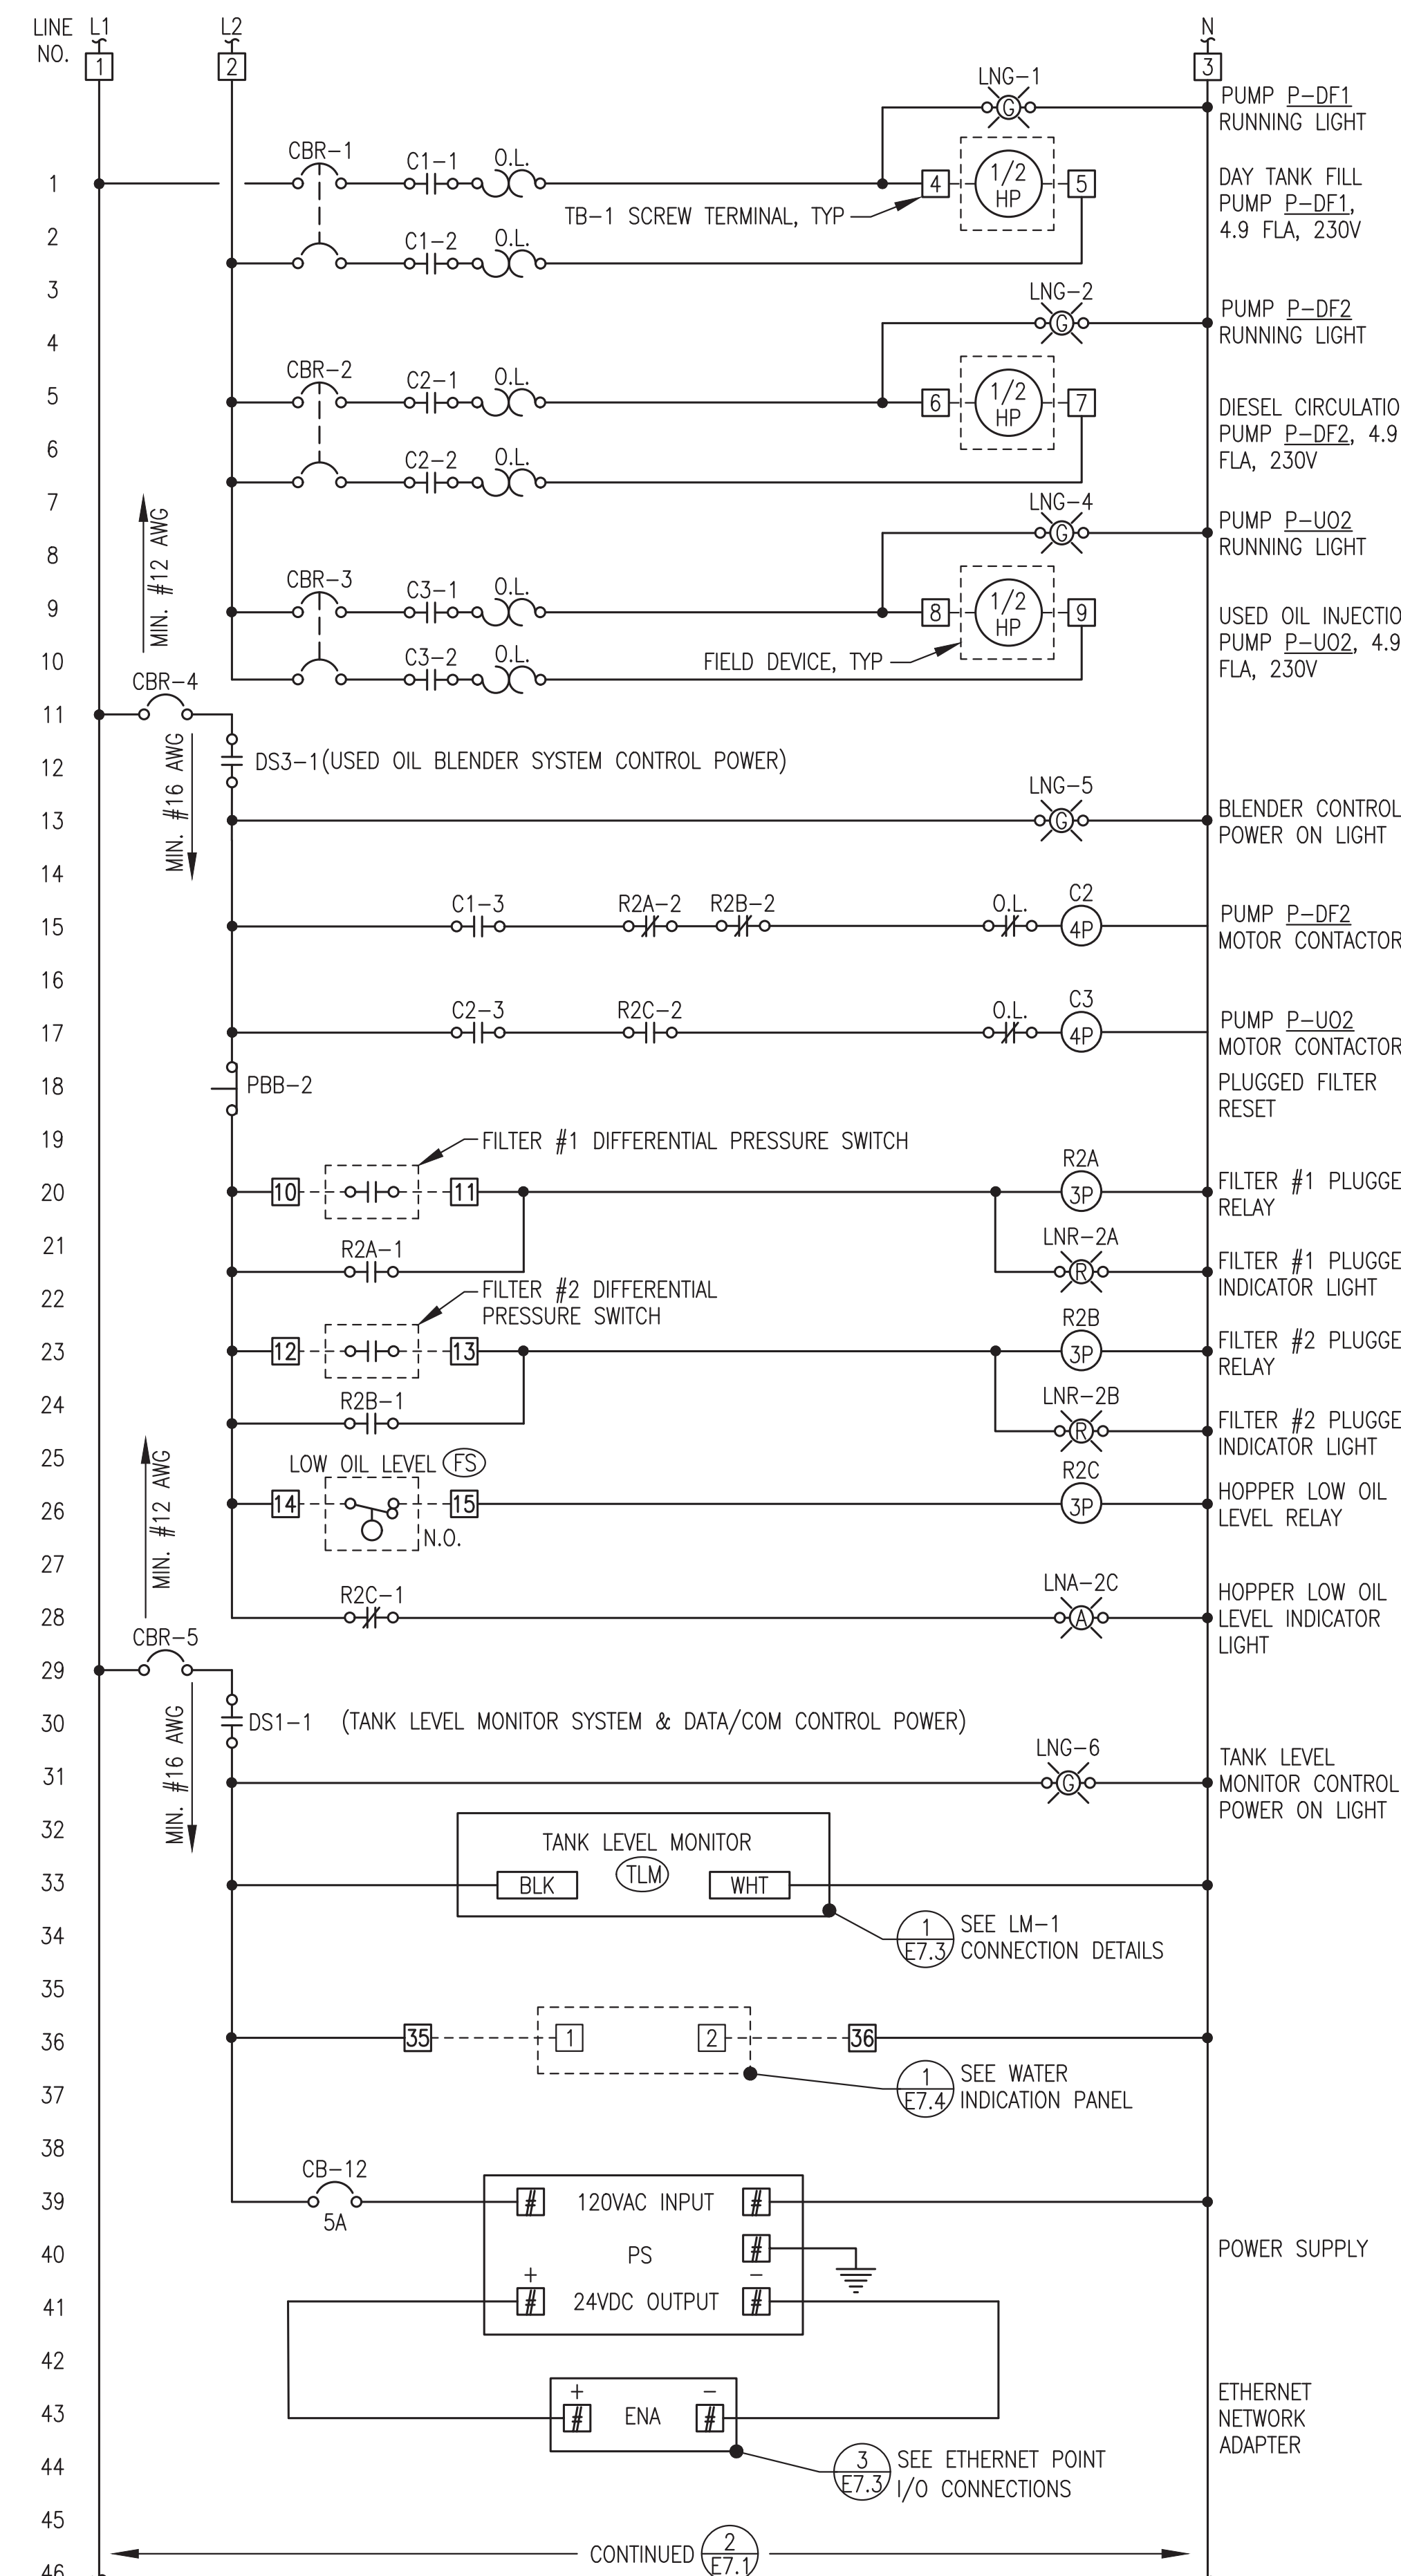

**1** USED OIL BLENDER SYSTEM LOGIC DIAGRAM  
E7.1 NO SCALE

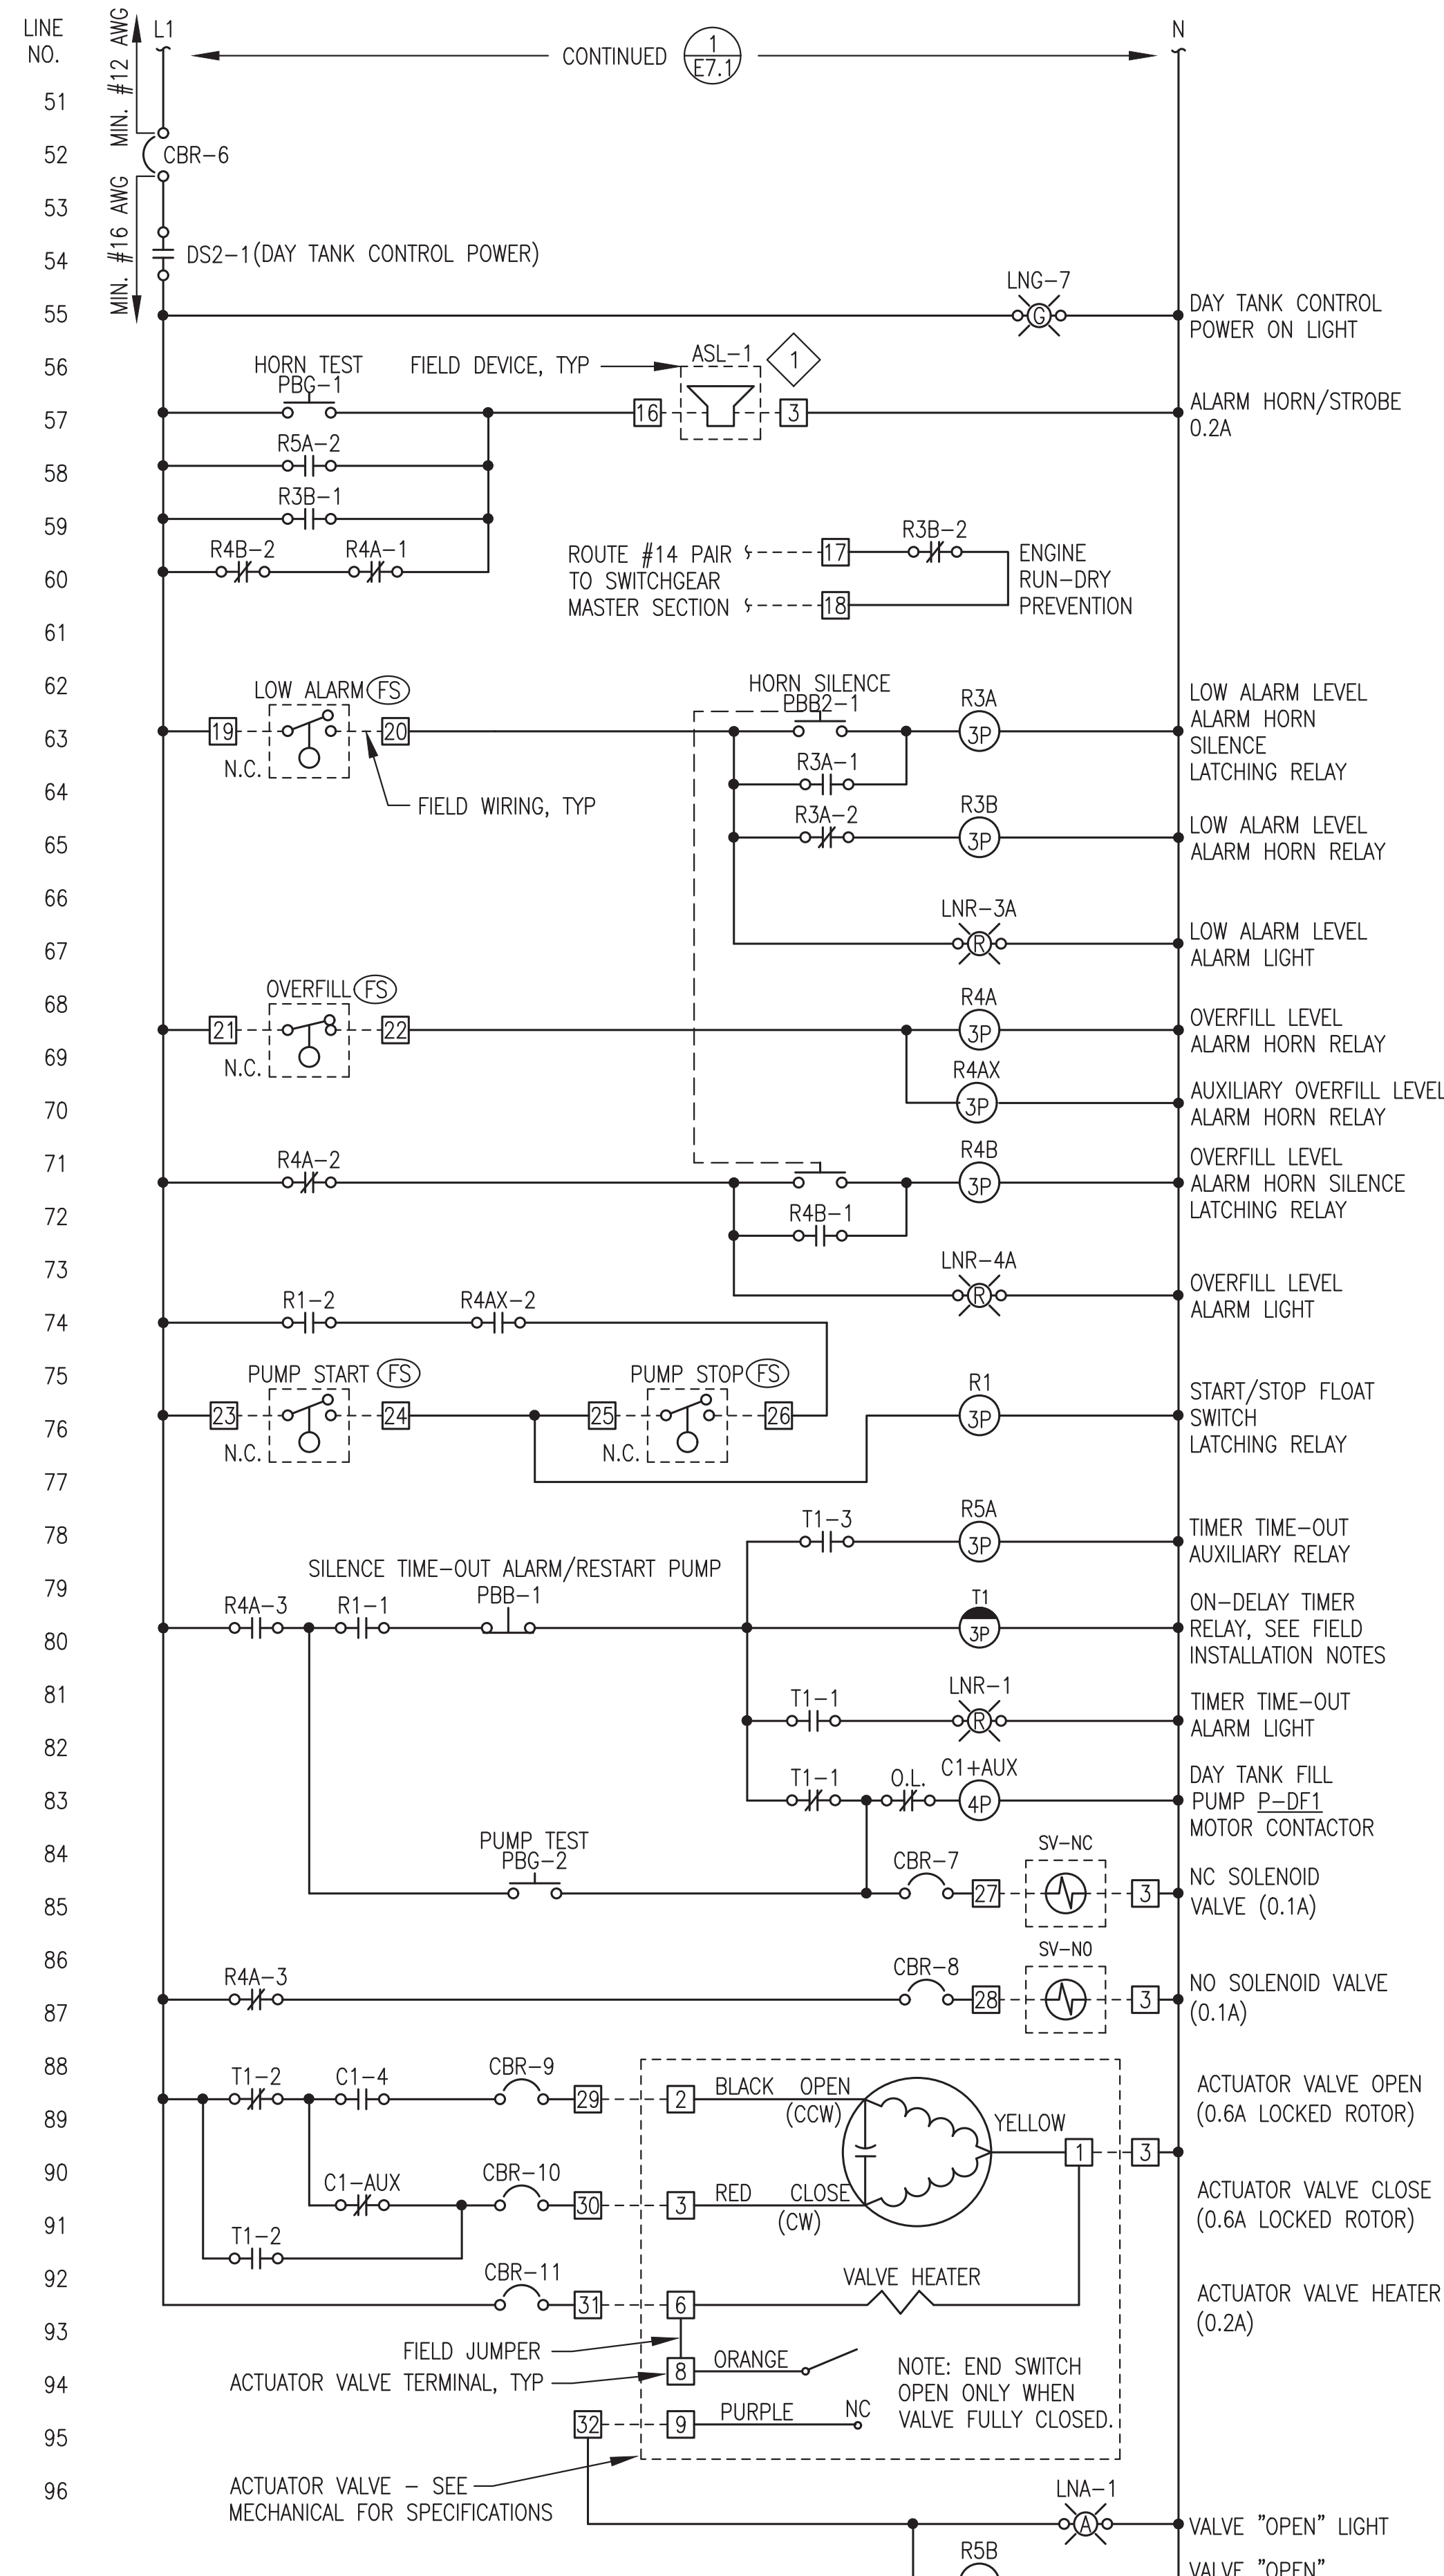


**2** DAY TANK LOGIC DIAGRAM  
E7.1 NO SCALE

BILL OF MATERIALS			
NOTE: ON THIS SHEET AND THE PANEL DRAWINGS THAT FOLLOW SPECIFIC PARTS MANUFACTURER AND MODEL ARE SELECTED NOT ONLY TO MEET PERFORMANCE FUNCTION BUT ALSO TO COORDINATE AND INTERFACE WITH OTHER DEVICES AND SYSTEMS. APPROVED EQUAL SUBSTITUTIONS WILL BE ALLOWED ONLY BY ENGINEER'S APPROVAL. TO OBTAIN APPROVAL, SUBMITTALS MUST CLEARLY DEMONSTRATE HOW SUBSTITUTE ITEM MEETS OR EXCEEDS SPECIFIED ITEM QUALITY AND PERFORMANCE CHARACTERISTICS AND ALSO COMPLIES WITH MECHANICAL AND/OR ELECTRICAL CONNECTIONS AND PHYSICAL LAYOUT REQUIREMENTS.			
TAG	MANUFACTURER	MODEL	DESCRIPTION
AUX C	ALLEN-BRADLEY	100SA11	AUXILIARY CONTACT FOR CONTACTOR, 2 POLE, NO, NC CONTACTOR, 120V COIL, 9A, 4 POLE
CBR-1,2,3	ALLEN-BRADLEY	1489-M2-C150	RAIL-MOUNT CIRCUIT BREAKER, 2 POLE, 15A
CBR-4,5,6,12	ALLEN-BRADLEY	1489-M1-C050	RAIL-MOUNT CIRCUIT BREAKER, 1 POLE, 5A
CBR-7,8,9,10,11	ALLEN-BRADLEY	1489-M1-C010	RAIL-MOUNT CIRCUIT BREAKER, 1 POLE, 1A
DS	ALLEN-BRADLEY	194LE201753	DISCONNECT, 2 POSITION, 3 N.O., 20A, FACE MOUNT
ENA	ALLEN-BRADLEY	194LHC4E1751	KNOB ACTUATOR FOR LOAD SWITCH, ON/OFF, LOCKABLE
Di8	ALLEN-BRADLEY	1734-AENTR	I/O DUAL PORT ETHERNET NETWORK ADAPTER
LNG	ALLEN-BRADLEY	1734-IB8	DIGITAL INPUT MODULE, 24VDC, 8 POINT, SINKING
LNR	ALLEN-BRADLEY	800HQRH2G	GREEN LED PILOT LIGHT, 12-130V, NEMA 4X
LNA	ALLEN-BRADLEY	800HQRH2R	RED LED PILOT LIGHT, 12-130V, NEMA 4X
OL	ALLEN-BRADLEY	800HQRH2A	AMBER LED PILOT LIGHT, 12-130V, NEMA 4X
PBB	ALLEN-BRADLEY	193-1EEDB	OVERLOAD, 230V, 1#, ADJUSTABLE 3.2A-16.0A RANGE
PBB2	ALLEN-BRADLEY	800HAR2D2	MOMENTARY PUSH BUTTON, 1 NO, NEMA 4X, BLACK
PBG	ALLEN-BRADLEY	800HAR2A2	MOMENTARY PUSH BUTTON, 2 NO, NEMA 4X, BLACK
PP	ALLEN-BRADLEY	800HAR1D1	MOMENTARY PUSH BUTTON, 1 NO, NEMA 4X, GREEN
R	PHOENIX CONTACTS	FLPPRJ45/RJ45	ETHERNET PATCH PANEL, RJ45xRJ45, DIN RAIL MOUNT
T	ALLEN-BRADLEY	700HA33A1	3PDT RELAY
	ALLEN-BRADLEY	700HN101	11 PIN SOCKET BASE
	ALLEN-BRADLEY	700HT3	SERIES B TIMING MODULE
	ALLEN-BRADLEY	700HA33A1	3PDT RELAY
	ALLEN-BRADLEY	700HN205	11 PIN RELAY SOCKET BASE FOR TIMER
TB-1,2	ALLEN-BRADLEY	1492CAM1L	35A, 600V, LARGE-HEAD SCREW TERMINALS
(TLM)			TANK LEVEL MONITOR, SEE INSTRUMENTATION SCHEDULE ON SHEET M1.1

LEGEND			
—	PANEL WIRING	---	FIELD WIRING
R#	CONTROL RELAY	R#-#	NORMALLY OPEN CONTACT
T#	TIME DELAY RELAY	SS-#	2-POSITION SELECTOR SWITCH
C#	CONTACTOR	R#-#	NORMALLY CLOSED CONTACT
#	TERMINAL BLOCK	SW-#	NORMALLY OPEN FLOAT SWITCH
CB-#	CIRCUIT BREAKER	SW-#	NORMALLY CLOSED FLOAT SWITCH
O.L.	OVERLOADS	PB-#	NORMALLY OPEN MOMENTARY PUSH BUTTON
		PB-#	NORMALLY CLOSED MOMENTARY PUSH BUTTON
		SV#	SOLENOID VALVE
		ASL-#	ALARM & STROBE LIGHT

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



REV.	DESCRIPTION	DATE	BY
1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG


PROJECT: RAMPART POWER SYSTEM UPGRADE

TITLE: DAY TANK CONTROL PANEL LOGIC DIAGRAM & BILL OF MATERIALS


DRAWN BY: BCG/JTD	SCALE: AS NOTED
DESIGNED BY: CWB/BCG	DATE: 3/15/22
FILE NAME: RAM PP E7	SHEET: E7.1
PROJECT NUMBER:	

Gray Stassel Engineering, Inc.  
P.O. 111405, Anchorage, AK 99511 (907)349-0100




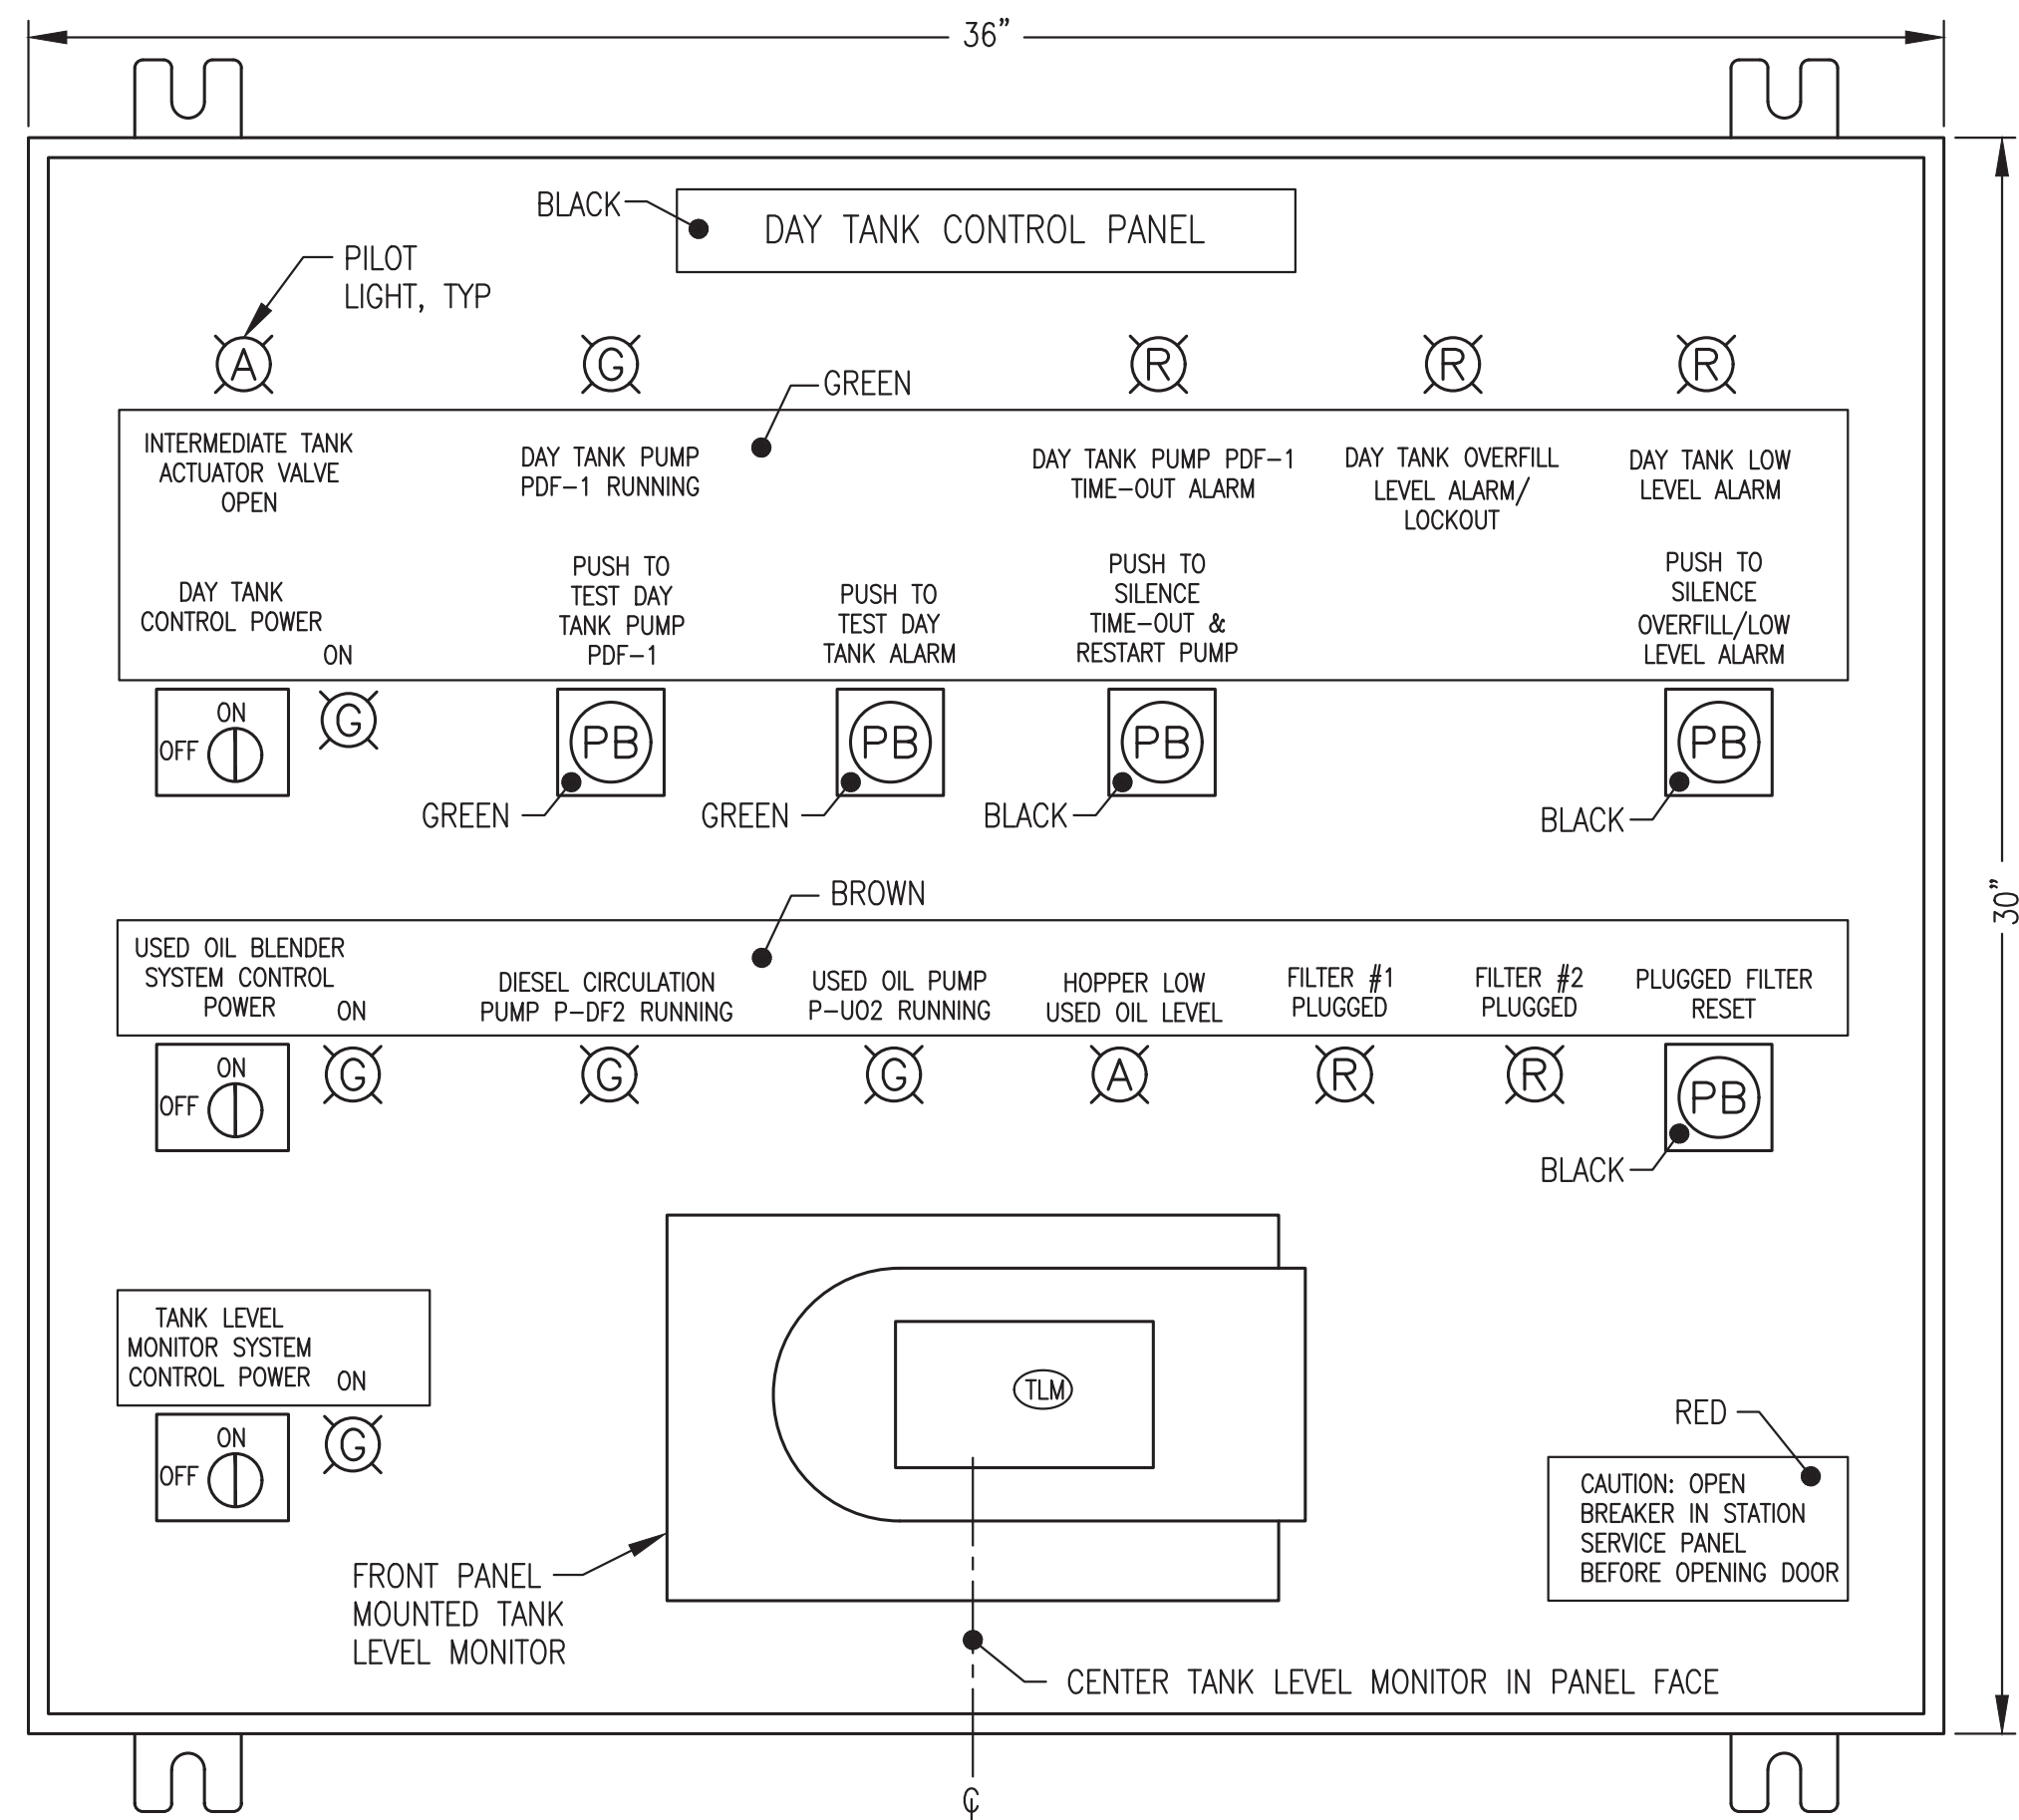

1 FRONT PANEL LAYOUT  
E7.2 NO SCALE

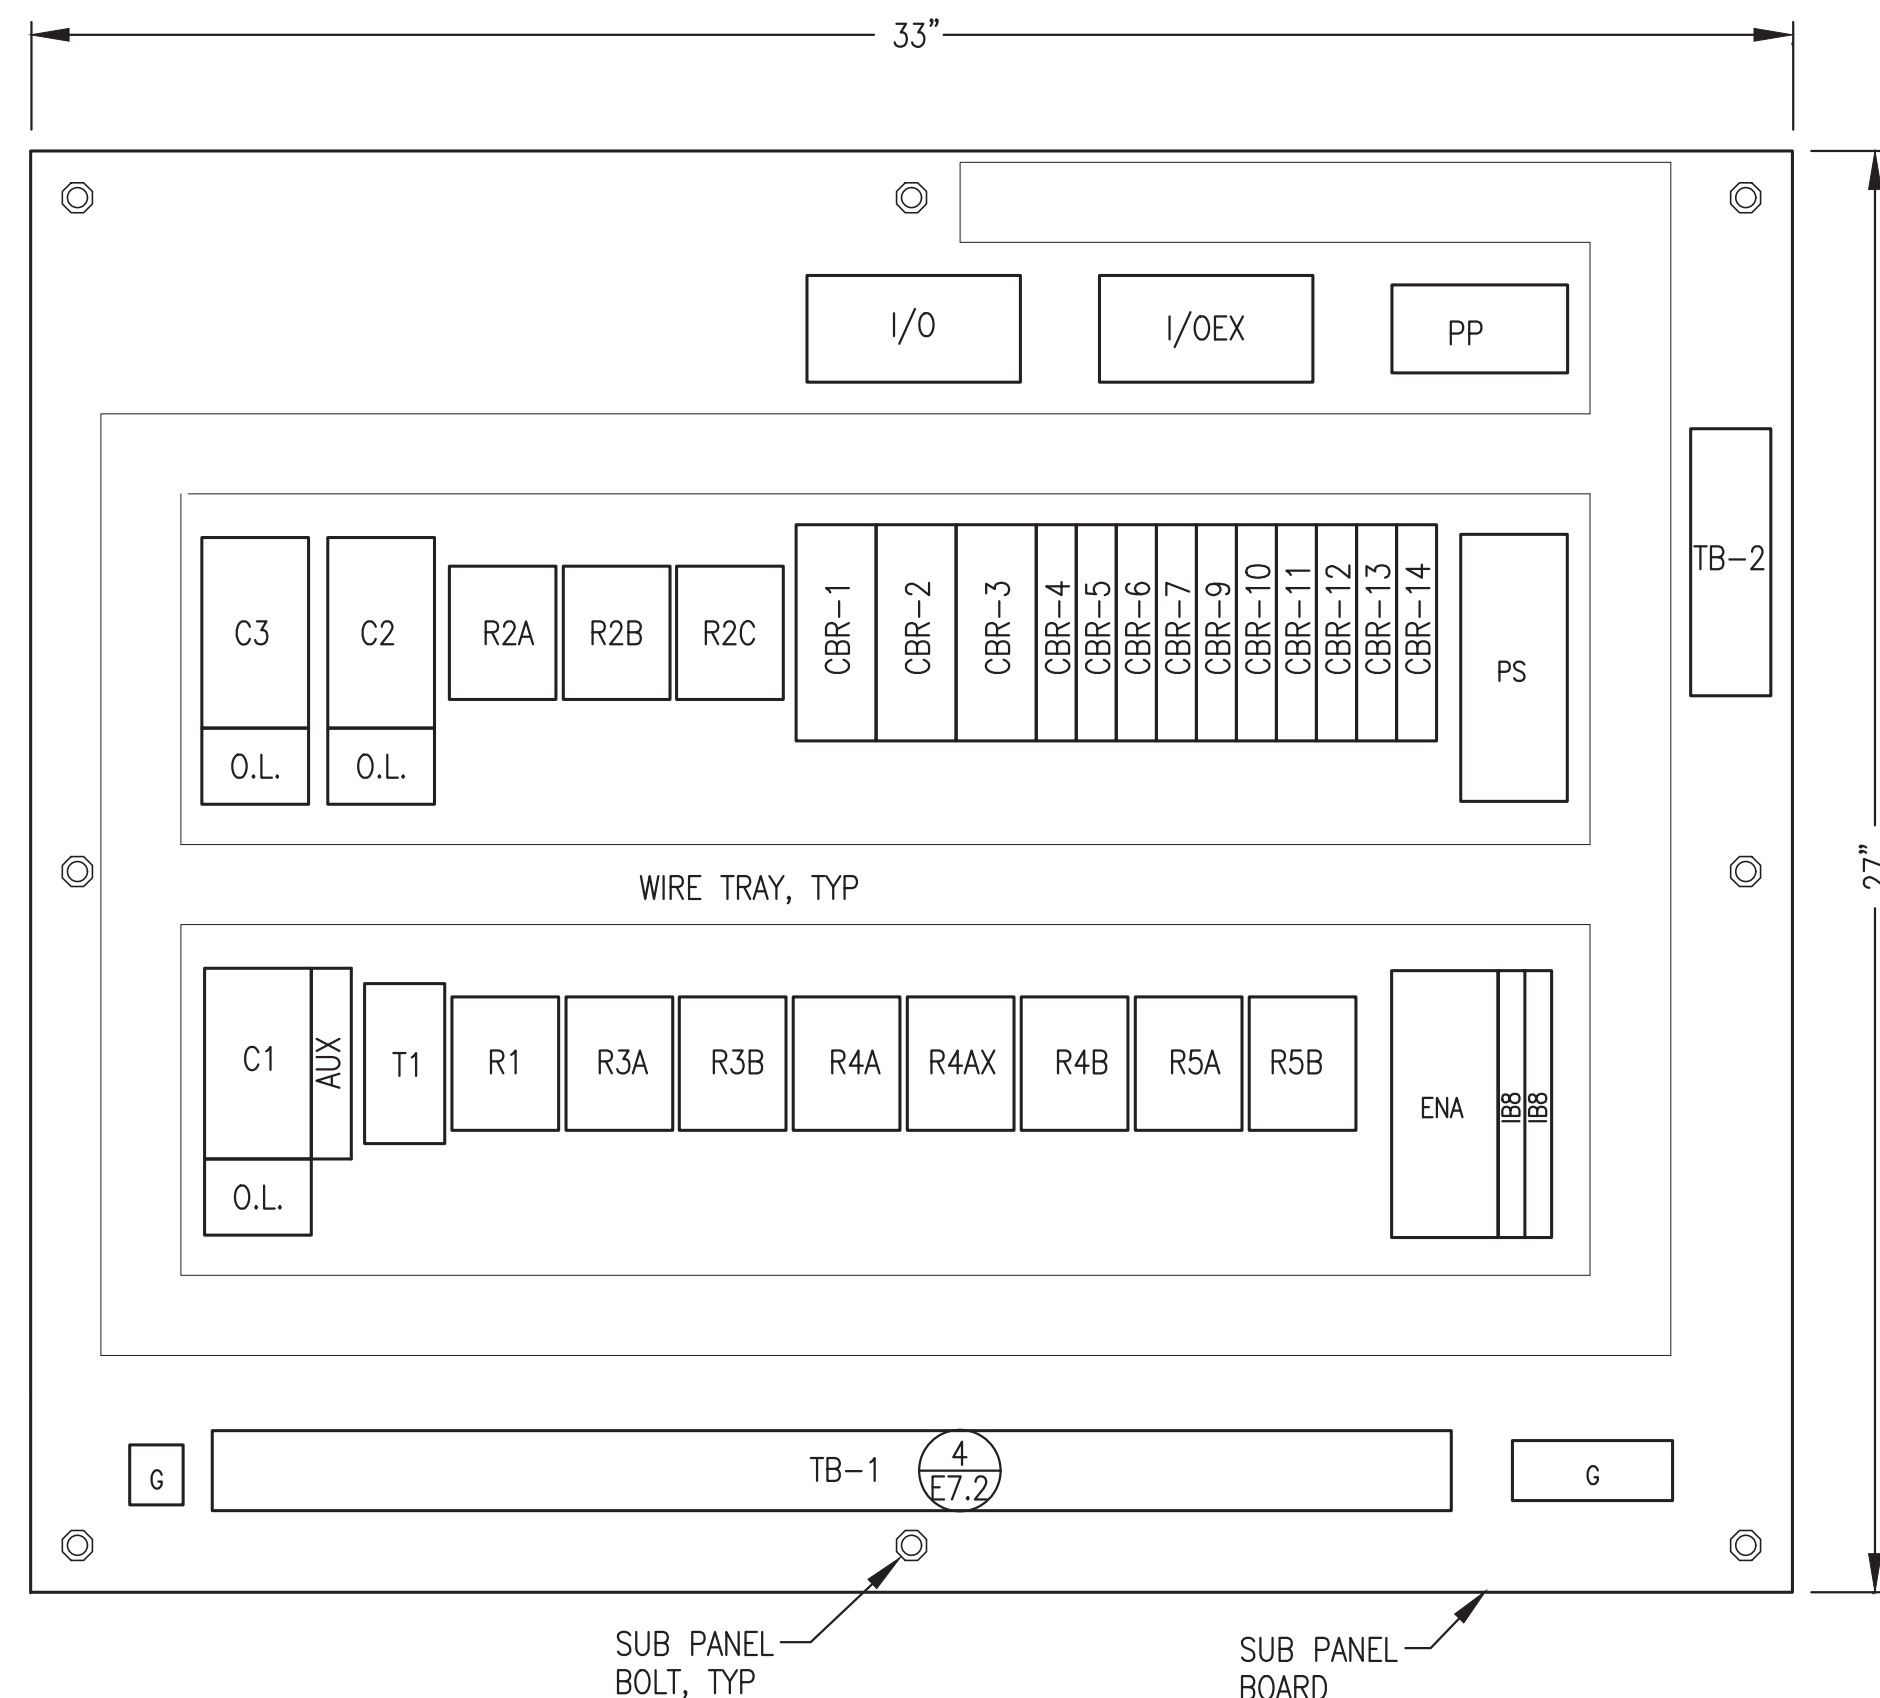


2 SUB PANEL LAYOUT  
E7.2 NO SCALE

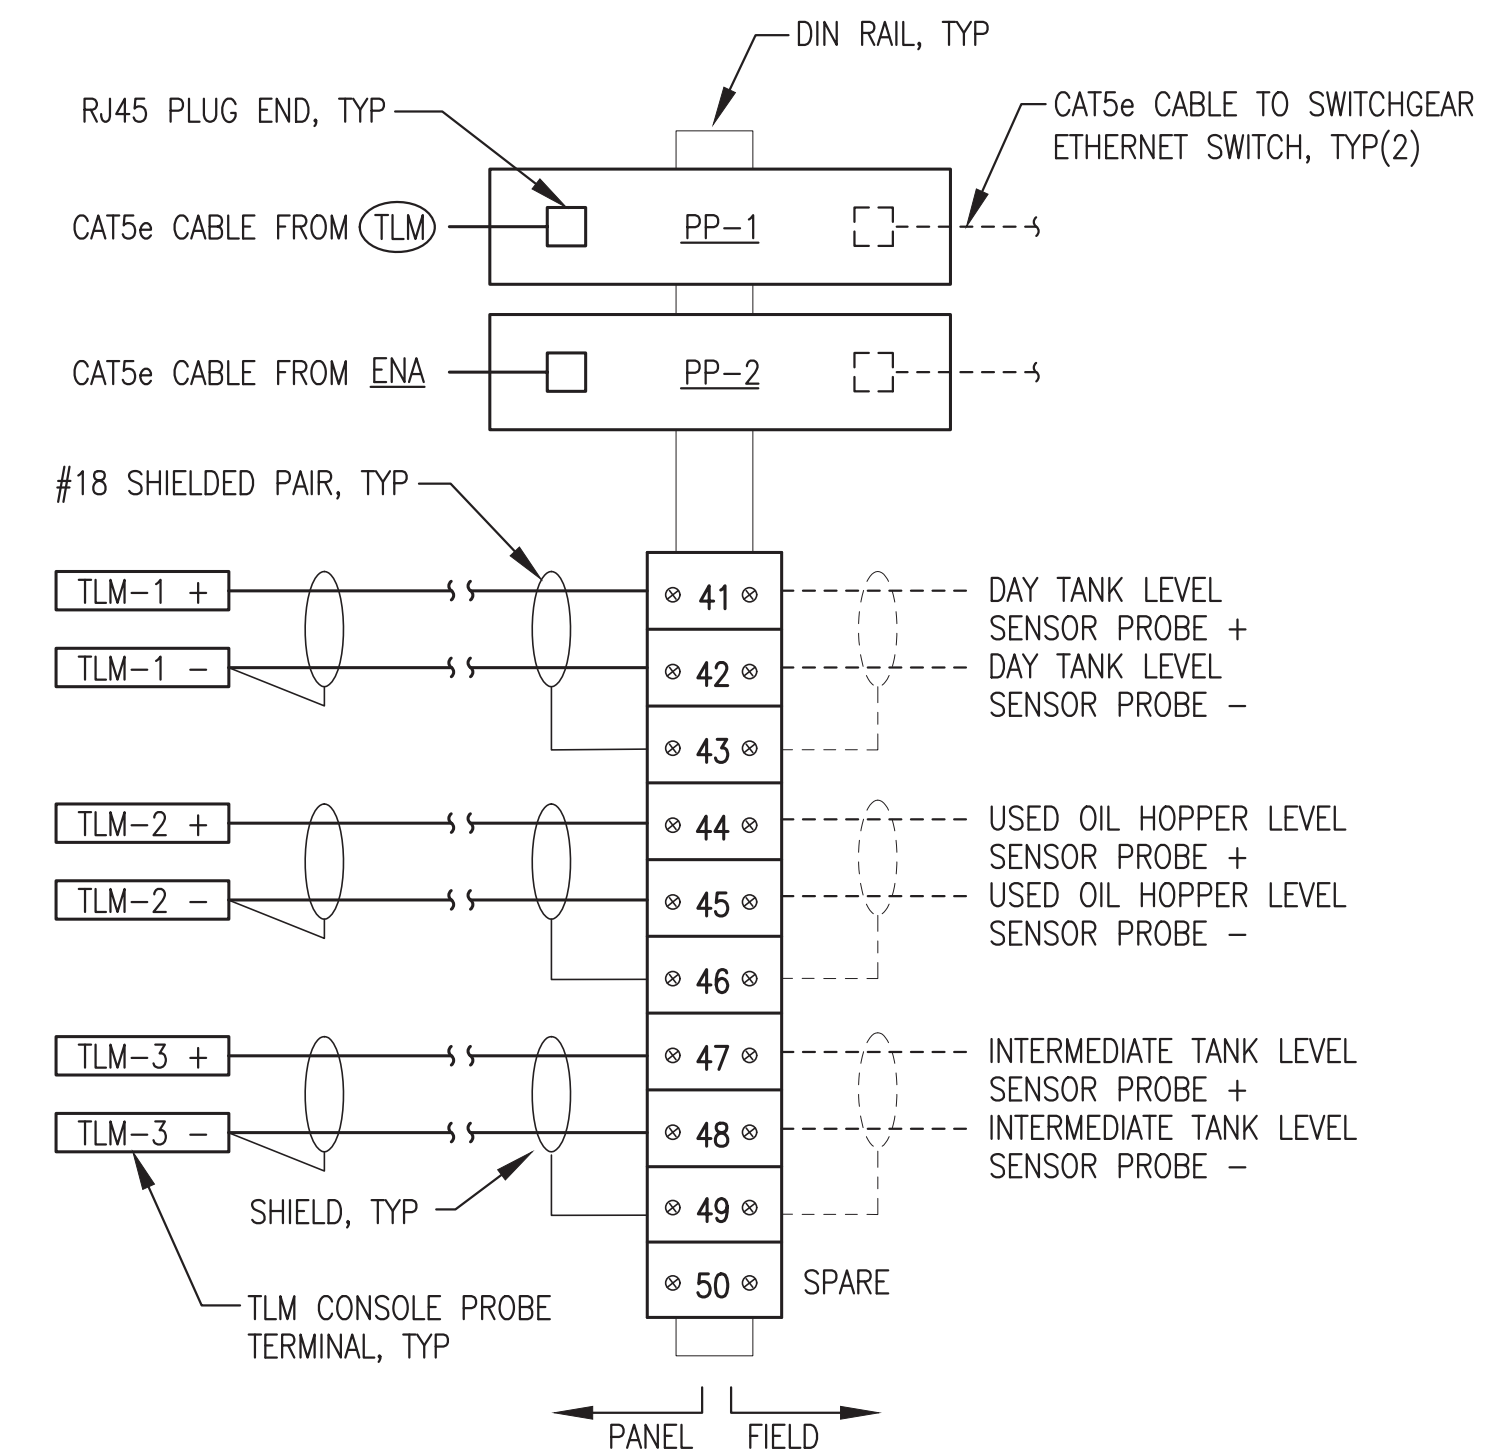

NOTES:

- INSTALL TERMINAL STRIP TB-2 AND ETHERNET PATCH PANEL PP-1 ON VERTICAL DIN RAIL AS SHOWN. LOCATE TERMINAL STRIP IN THE UPPER RIGHT CORNER OF PANEL TO ACCOMMODATE CONDUCTOR ENTRY THROUGH RIGHT SIDE OF PANEL, SEE SUB-PANEL LAYOUT.

3 TB-2 TERM STRIP LAYOUT  
E7.2 NO SCALE

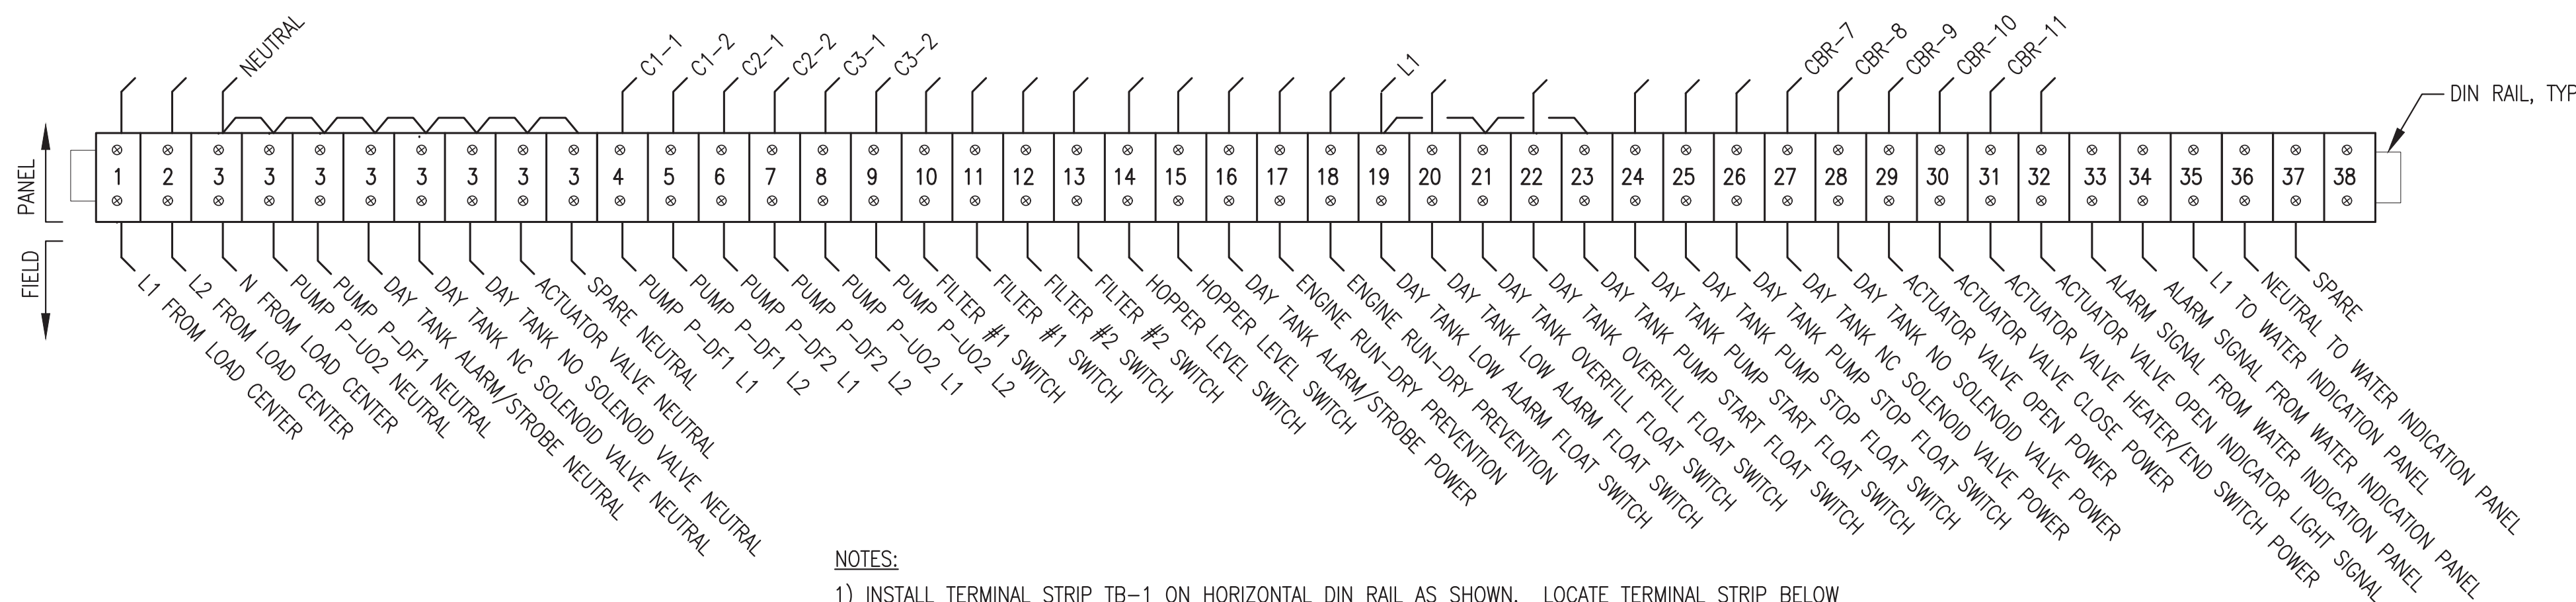


NOTES:

- INSTALL TERMINAL STRIP TB-1 ON HORIZONTAL DIN RAIL AS SHOWN. LOCATE TERMINAL STRIP BELOW PANEL DEVICES TO ACCOMMODATE CONDUCTOR ROUTING FROM CONDUITS CONNECTING TO BOTTOM OF PANEL, SEE SUB-PANEL LAYOUT.
- IN ADDITION TO THE TERMINAL STRIPS SHOWN, PROVIDE 6 EACH 35A SCREW TERMINAL GROUNDING BUS.

4 TB-1 TERMINAL STRIP LAYOUT  
E7.2 NO SCALE

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: DAY TANK CONTROL PANEL LAYOUT & TERMINAL STRIPS			
DRAWN BY: BCG/JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_E7		SHEET: E7.2	
PROJECT NUMBER:			
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

**PANEL NOTES:**

- 1) PROVIDE COMPLETE LISTED PANEL ASSEMBLY WITH ALL DEVICES INDICATED IN LOGIC DIAGRAM EXCEPT FOR FIELD DEVICES. INSTALL IN A NEMA 12 ENCLOSURE WITH 4 EACH INTEGRAL MOUNTING LUGS AT BACK. SEE SHEET E7.2 FOR PANEL LAYOUT DETAILS.
- 2) USE MIN #12 WIRE FOR ALL CIRCUITS UP TO FIRST IN-LINE PANEL BREAKERS (FOR 20A FEED). USE MIN #16 AWG ON ALL 5 AMP CIRCUITS AND MIN #14 AWG WIRE ON ALL 15A CIRCUITS. TAG EACH END OF ALL JUMPERS WITH DEVICE OR TERMINATION DESIGNATOR OF LANDING OF OPPOSITE END OF JUMPER (REVERSE ADDRESS).
- 3) LABEL ALL PANEL DEVICES ON BASE OR BACK PANEL ADJACENT TO ITEM. LABEL REMOTE EQUIPMENT CONNECTIONS AT EACH TERMINAL BLOCK BY THE ITEM TITLE AS SHOWN ON THE FIELD SIDE OF THE TERMINAL STRIP DRAWING. PROVIDE BEVELED EDGE WHITE CORE NAMEPLATES AS SHOWN ON THE PANEL FACE LAYOUT AND SECURE TO PANEL FACE WITH A MINIMUM OF TWO STAINLESS STEEL MOUNTING SCREWS, COLOR AS INDICATED.
- 4) BENCH TEST COMPLETED UNIT. PROVIDE MIN 48 HOURS NOTICE TO ENGINEER TO SCHEDULE OBSERVATION OF BENCH TEST. PROVIDE SWITCHES AND LAMPS TO SIMULATE OPERATION OF ALL FIELD DEVICES.
- 5) DEVICES AND WIRING NOTED AS "FIELD" AND SHOWN WITH DASHED LINES WILL BE FIELD INSTALLED AND ARE NOT PART OF THE PANEL SHOP FABRICATION. FOR BENCH TEST, PROVIDE TEMPORARY DEVICES AND WIRING AS REQUIRED TO SIMULATE FIELD DEVICES.
- 6) POWER TO PANEL PROVIDED FROM DEDICATED 20A 2-POLE CIRCUIT BREAKER IN LISTED LOAD CENTER. SEE FIELD INSTALLATION NOTE #3.

**FIELD INSTALLATION NOTES:**


- 1) SEE MECHANICAL FOR DAY TANK INSTALLATION & PIPING. INSTALL CONTROL PANEL & FIELD DEVICES AS INDICATED TO PROVIDE REDUNDANT HIGH & LOW LIMIT CONTROLS & OVERFILL PROTECTION.
- 2) FIELD WIRING TO FLOAT SWITCHES, SOLENOID VALVES, ACTUATOR VALVE, & ALARM HORN #14 AWG. ALL OTHER FIELD WIRING #12 AWG. LABEL BOTH ENDS OF ALL CONDUCTORS WITH CONTROL PANEL TERMINAL BLOCK TERMINATION NUMBERS. WHEN NOT IN CONDUIT, MAKE JACKETED COM CABLE ENCLOSURE ENTRIES WITH CABLE GLAND CONNECTORS.
- 3) PERFORM ALL FIELD WIRING IN ACCORDANCE WITH ELECTRICAL SPECIFICATIONS ON SHEET E2. PROVIDE POWER TO DAY TANK PANEL FROM DEDICATED 20A 2-POLE CIRCUIT BREAKER IN STATION SERVICE PANELBOARD.
- 4) VERIFY THAT ALL DAY TANK FLOAT SWITCHES ARE ORIENTED FOR N.C. (OPEN ON RISE) OPERATION PRIOR TO INSTALLATION. ALL FLOATS SHOWN ON LOGIC DIAGRAM WITH TANK AT FULL (PUMP STOP) LEVEL. VERIFY THAT THE HOPPER FLOAT SWITCH IS ORIENTED FOR N.O. (CLOSE ON RISE) OPERATION.
- 5) FILL PUMP CAVITIES WITH LUBE OIL PRIOR TO INITIAL OPERATION. VERIFY PROPER ROTATION OF PUMPS. PRIME SYSTEM WITH HAND PRIMING PUMP PRIOR TO BEGINNING DAY TANK FILL.
- 6) FIELD TEST COMPLETED UNIT TO VERIFY ALL CONTROL AND ALARM FUNCTIONS. MANIPULATE FLOAT SWITCHES BY REACHING IN THROUGH ADJACENT 4" BUNG. TEMPORARILY SET TIMING RELAY TO 30 SECONDS TO VERIFY TIME-OUT AND RESET FUNCTIONS.
- 7) SET TIMING RELAY TIME DELAY TO 30 MINUTES (APPROX. 55 GALS. REQUIRED FROM PUMP START TO PUMP STOP LEVEL @ APPROX. 4 GPM). ON THE INITIAL TANK FILL, THE PUMP TEST/RESET BUTTON MAY HAVE TO BE MANUALLY RESET IN ORDER TO GET THE FUEL LEVEL TO WITHIN THE NORMAL OPERATING RANGE. SEE SEQUENCE OF OPERATIONS.

**DAY TANK FILL SEQUENCE OF OPERATIONS:**


- 1) WHEN THE DAY TANK CIRCUIT BREAKER AND CONTROL POWER SWITCH ARE CLOSED, THE POWER LIGHT IS ON AND POWER IS PROVIDED TO THE REMOTE ACTUATOR VALVE HEATER/OPEN LIGHT CIRCUIT.
- 2) WHEN THE DAY TANK IS NOT CALLING FOR FUEL, POWER IS PROVIDED TO THE REMOTE ACTUATOR VALVE CLOSE CIRCUIT. WHEN THE ACTUATOR IS IN THE FULLY CLOSED POSITION, THE CLOSING CIRCUIT IS BROKEN BY INTERNAL ACTUATOR LIMIT SWITCH #2 AND THE REMOTE ACTUATOR VALVE "OPEN" LIGHT IS OFF.
- 3) NORMAL FILL OPERATION - WHEN THE FUEL LEVEL DROPS TO THE "PUMP START" SWITCH, THE TIMER IS STARTED, THE N.C. DAY TANK SOLENOID VALVE OPENS, THE REMOTE ACTUATOR VALVE OPENS & THE VALVE "OPEN" LIGHT TURNS ON, THE DAY TANK PUMP IS ENERGIZED, THE PUMP "ON" LIGHT TURNS ON, AND THE USED OIL BLENDER RUN SIGNAL DRY CONTACT CLOSURES. WHEN THE ACTUATOR IS IN THE FULLY OPEN POSITION, THE OPENING CIRCUIT IS BROKEN BY INTERNAL ACTUATOR LIMIT SWITCH #7 AND THE REMOTE ACTUATOR VALVE "OPEN" LIGHT REMAINS ON. WHEN FUEL REACHES THE "PUMP STOP" FLOAT SWITCH BEFORE THE TIMER TIMES-OUT, THE TIMER IS RESET, THE N.C. DAY TANK SOLENOID VALVE AND REMOTE ACTUATOR VALVE CLOSE, THE REMOTE ACTUATOR VALVE "OPEN" LIGHT TURNS OFF, THE PUMP DE-ENERGIZES, THE PUMP "ON" LIGHT TURNS OFF, AND THE USED OIL BLENDER RUN SIGNAL DRY CONTACT OPENS.
- 4) TIMER OPERATION - IF THE TIMER TIMES-OUT THE N.C. DAY TANK SOLENOID VALVE AND REMOTE ACTUATOR VALVE CLOSE, THE REMOTE ACTUATOR VALVE "OPEN" LIGHT TURNS OFF, THE PUMP DE-ENERGIZES, THE PUMP "ON" LIGHT TURNS OFF, THE USED OIL BLENDER RUN SIGNAL DRY CONTACT OPENS, THE "TIME-OUT" ALARM LIGHT TURNS ON, AND THE TIME-OUT ALARM HORN SOUNDS. PRESSING THE "TIME-OUT ALARM SILENCE / PUMP RESTART" BUTTON RESETS THE TIMER, SILENCES THE ALARM HORN, AND STARTS THE NORMAL FILL OPERATION. SEE FIELD INSTALLATION NOTES FOR TIMER SETTING.
- 5) OVERFILL FUEL LEVEL - IF THE TANK OVERFILLS AND THE FUEL LEVEL REACHES THE "OVERFILL" FLOAT SWITCH, THE N.O. DAY TANK SOLENOID VALVE CLOSES, THE "OVERFILL LEVEL" ALARM LIGHT TURNS ON, THE N.C. DAY TANK SOLENOID VALVE AND REMOTE ACTUATOR VALVE CLOSE, THE VALVE "OPEN" LIGHT TURNS OFF, THE PUMP DE-ENERGIZES, THE PUMP "ON" LIGHT TURNS OFF, THE USED OIL BLENDER RUN SIGNAL DRY CONTACT OPENS, THE "OVERFILL LEVEL" ALARM LIGHT TURNS ON, AND THE ALARM HORN SOUNDS. PRESSING THE LEVEL ALARM HORN "SILENCE" BUTTON SILENCES THE ALARM HORN WHILE LEAVING THE "OVERFILL LEVEL" ALARM LIGHT ON. WHEN THE FUEL LEVEL FALLS BELOW THE "OVERFILL" FLOAT SWITCH, THE "OVERFILL LEVEL" ALARM LIGHT TURNS OFF, THE N.O. DAY TANK SOLENOID VALVE OPENS AND THE ALARM HORN TURNS OFF (IF NOT PREVIOUSLY SILENCED). WHEN THE FUEL LEVEL REACHES THE "PUMP START" FLOAT SWITCH, THE NORMAL FILL OPERATION IS REPEATED.
- 6) LOW FUEL LEVEL - IF THE FUEL LEVEL FALLS BELOW THE "LOW ALARM" FLOAT SWITCH, THE "LOW FUEL LEVEL" ALARM LIGHT TURNS ON, THE ENGINE RUN-DRY PREVENTION DRY CONTACT OPENS, AND THE ALARM HORN SOUNDS. THE LEVEL ALARM HORN "SILENCE" BUTTON SILENCES THE ALARM HORN WHILE LEAVING THE "LOW FUEL LEVEL" ALARM LIGHT ON. WHEN THE FUEL LEVEL RISES ABOVE THE "LOW ALARM" FLOAT SWITCH THE "LOW FUEL LEVEL" ALARM LIGHT TURNS OFF, THE ENGINE RUN-DRY PREVENTION DRY CONTACT CLOSURES, AND THE ALARM HORN TURNS OFF (IF NOT PREVIOUSLY SILENCED).
- 7) PUMP & HORN TEST - MOMENTARY CONTACT BUTTONS ARE PROVIDED TO TEST FUNCTION OF THE DAY TANK PUMP AND ALARM HORN. PRESSING THE "PUSH TO TEST DAY TANK PUMP" BUTTON STARTS THE TIMER, MOMENTARILY OPENS THE N.C. DAY TANK SOLENOID VALVE & ACTUATED BALL VALVE, ENERGIZES THE DAY TANK PUMP, TURNS ON THE DAY TANK PUMP "RUNNING" LIGHT AND CLOSURES THE USED OIL BLENDER RUN SIGNAL DRY CONTACT. THE "PUSH TO TEST DAY TANK PUMP" BUTTON IS LOCKED OUT IF THE DAY TANK IS AT THE OVERFILL LEVEL. PRESSING THE "PUSH TO TEST DAY TANK ALARM" BUTTON MOMENTARILY ENERGIZES THE ALARM HORN/STROBE.

**USED OIL BLENDER SYSTEM SEQUENCE OF OPERATIONS:**


- 1) WHEN THE BLENDER CIRCUIT BREAKER AND CONTROL POWER SWITCH ARE CLOSED; THE GREEN POWER LIGHT IS ON AND POWER IS PROVIDED TO ALL CONTROL DEVICES.
- 2) NORMAL OPERATION - WHENEVER THE DAY TANK FILL SEQUENCE IS INITIATED, BOTH THE DIESEL CIRCULATING PUMP P-DF2 AND THE USED OIL INJECTION PUMP P-U02 RUN AND THE ASSOCIATED GREEN PUMP RUNNING LIGHTS ARE ON.
- 3) PLUGGED FILTER - IF THE DIFFERENTIAL PRESSURE ACROSS A FILTER REACHES THE ALARM SETPOINT, BOTH PUMPS STOP RUNNING AND THE RED FILTER PLUGGED LIGHT FOR THE ASSOCIATED FILTER TURNS ON. THE ALARM LATCHES AND THE SYSTEM WILL NOT OPERATE UNTIL THE PROBLEM IS CORRECTED. AFTER THE FILTER ELEMENT HAS BEEN CHANGED THE BLACK RESET BUTTON MUST BE PRESSED TO RESUME NORMAL OPERATION.
- 4) HOPPER LOW OIL LEVEL - WHEN THE OIL LEVEL FALLS BELOW THE LOW LEVEL FLOAT SWITCH, USED OIL INJECTION PUMP P-U02 STOPS RUNNING AND THE AMBER HOPPER LOW OIL LEVEL LIGHT TURNS ON. PUMP P-U02 WILL NOT OPERATE UNTIL THE USED OIL LEVEL IN THE HOPPER RISES ABOVE THE LOW LEVEL. RESET IS NOT REQUIRED.

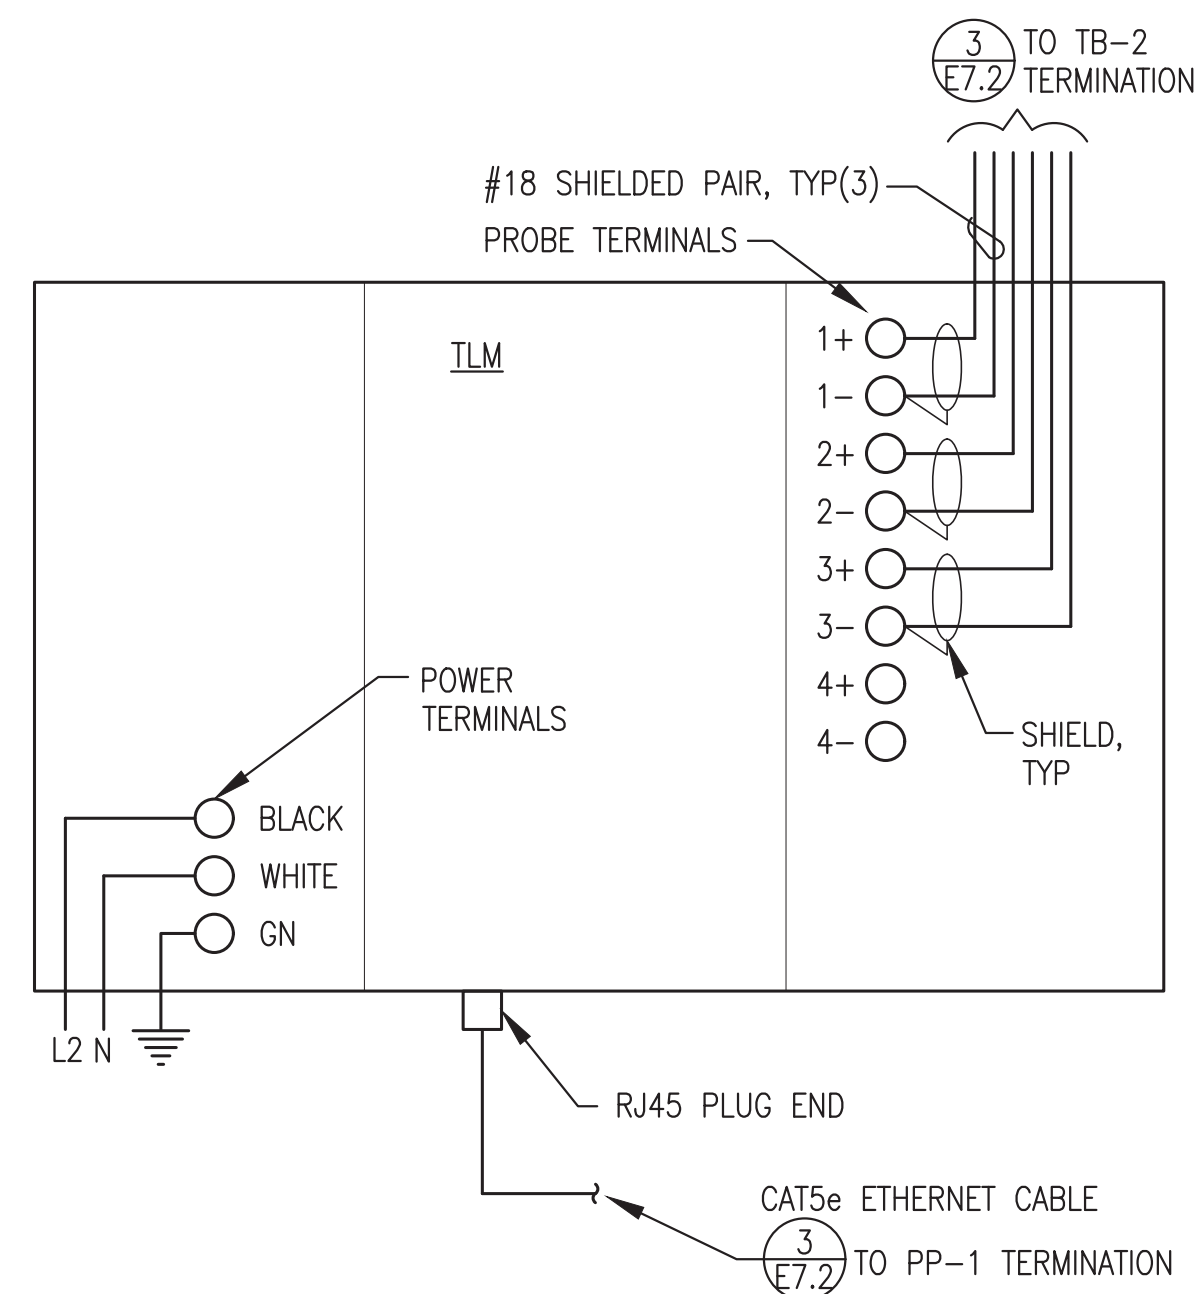

**1 TANK LEVEL MONITOR (TLM) CONSOLE CONNECTIONS**  
NO SCALE

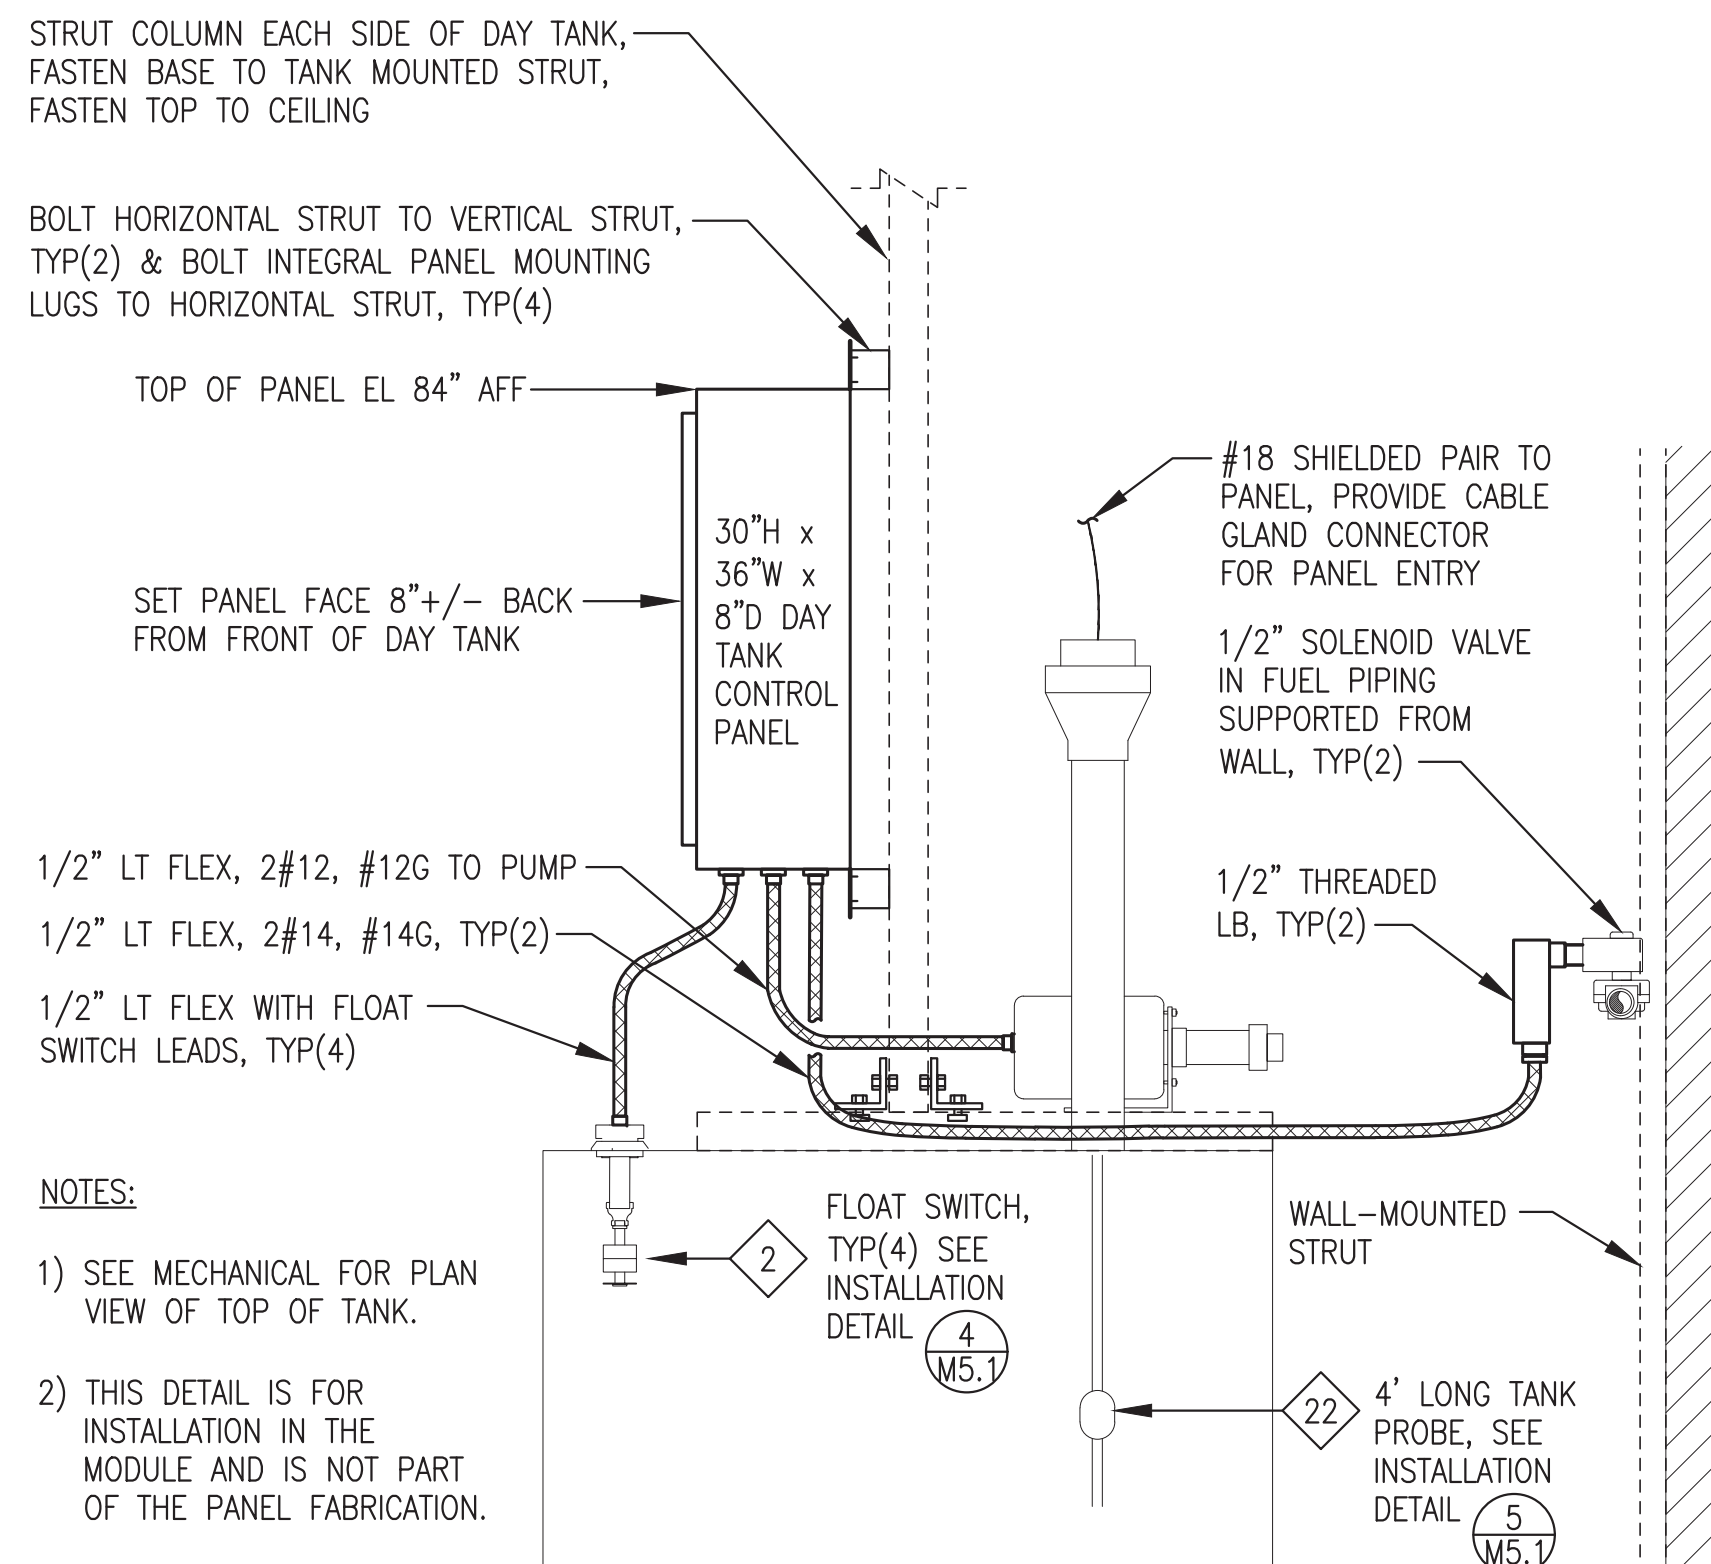


**2 DAY TANK CONTROL PANEL & DEVICE INSTALLATION**  
NO SCALE

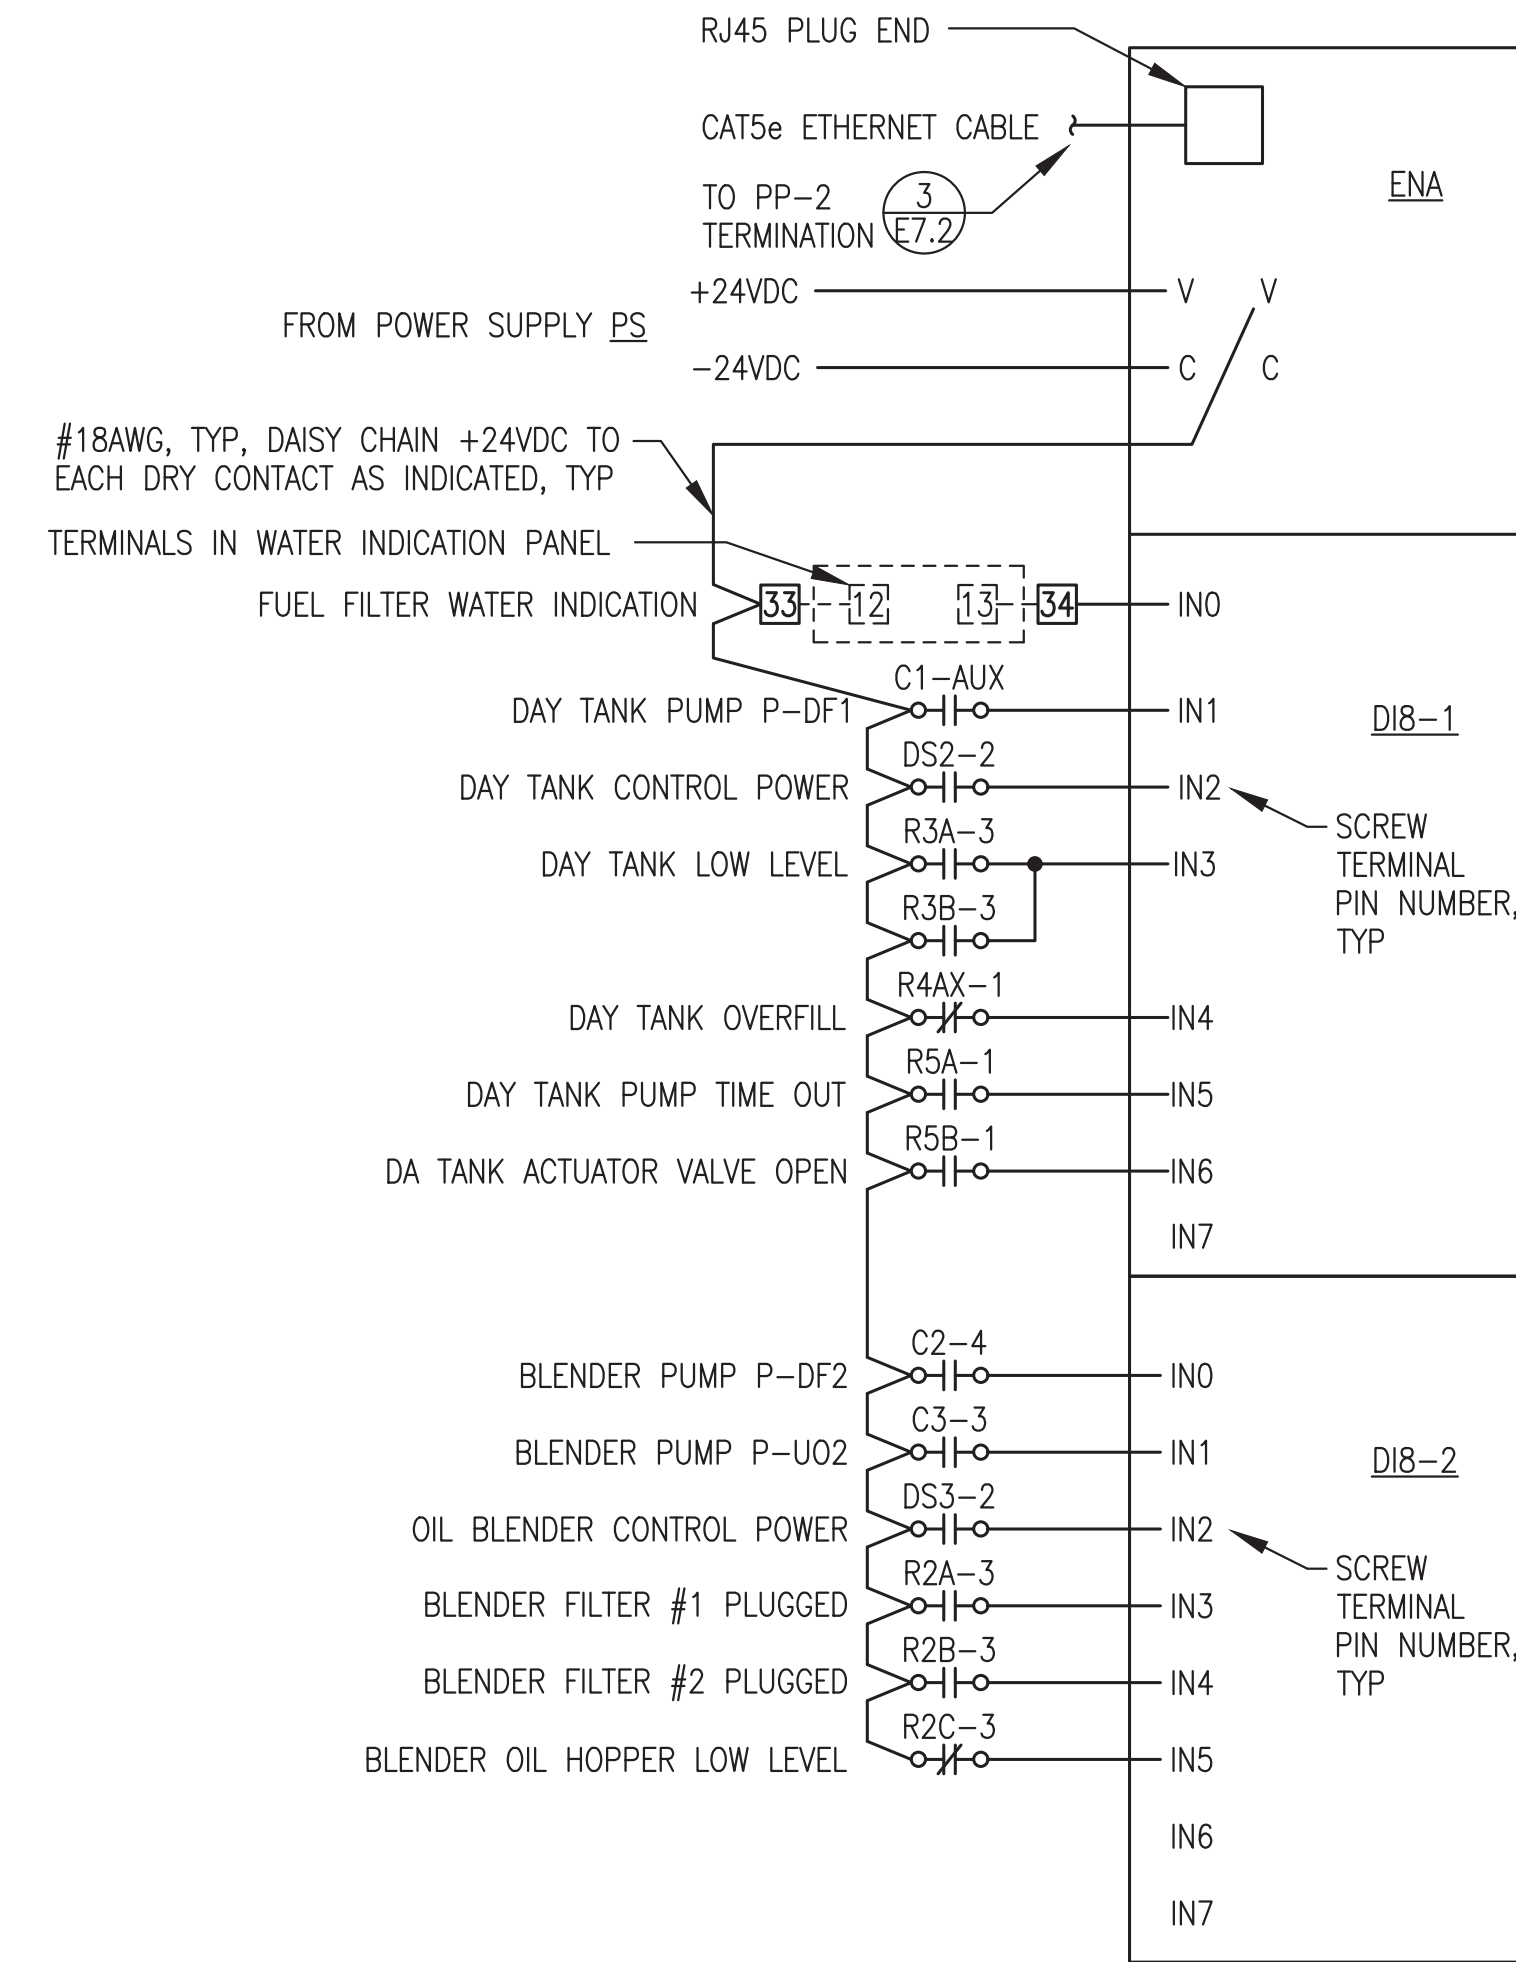


**3 ETHERNET POINT I/O CONNECTIONS**  
NO SCALE


1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: DAY TANK CONTROL PANEL NOTES, SEQUENCE OF OPERATIONS & INTERCONNECT DETAILS			
DRAWN BY: BCG/JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM PP E7		SHEET: E7.3	
PROJECT NUMBER: P.O. 111405, Anchorage, AK 99511 (907)349-0100			

REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022




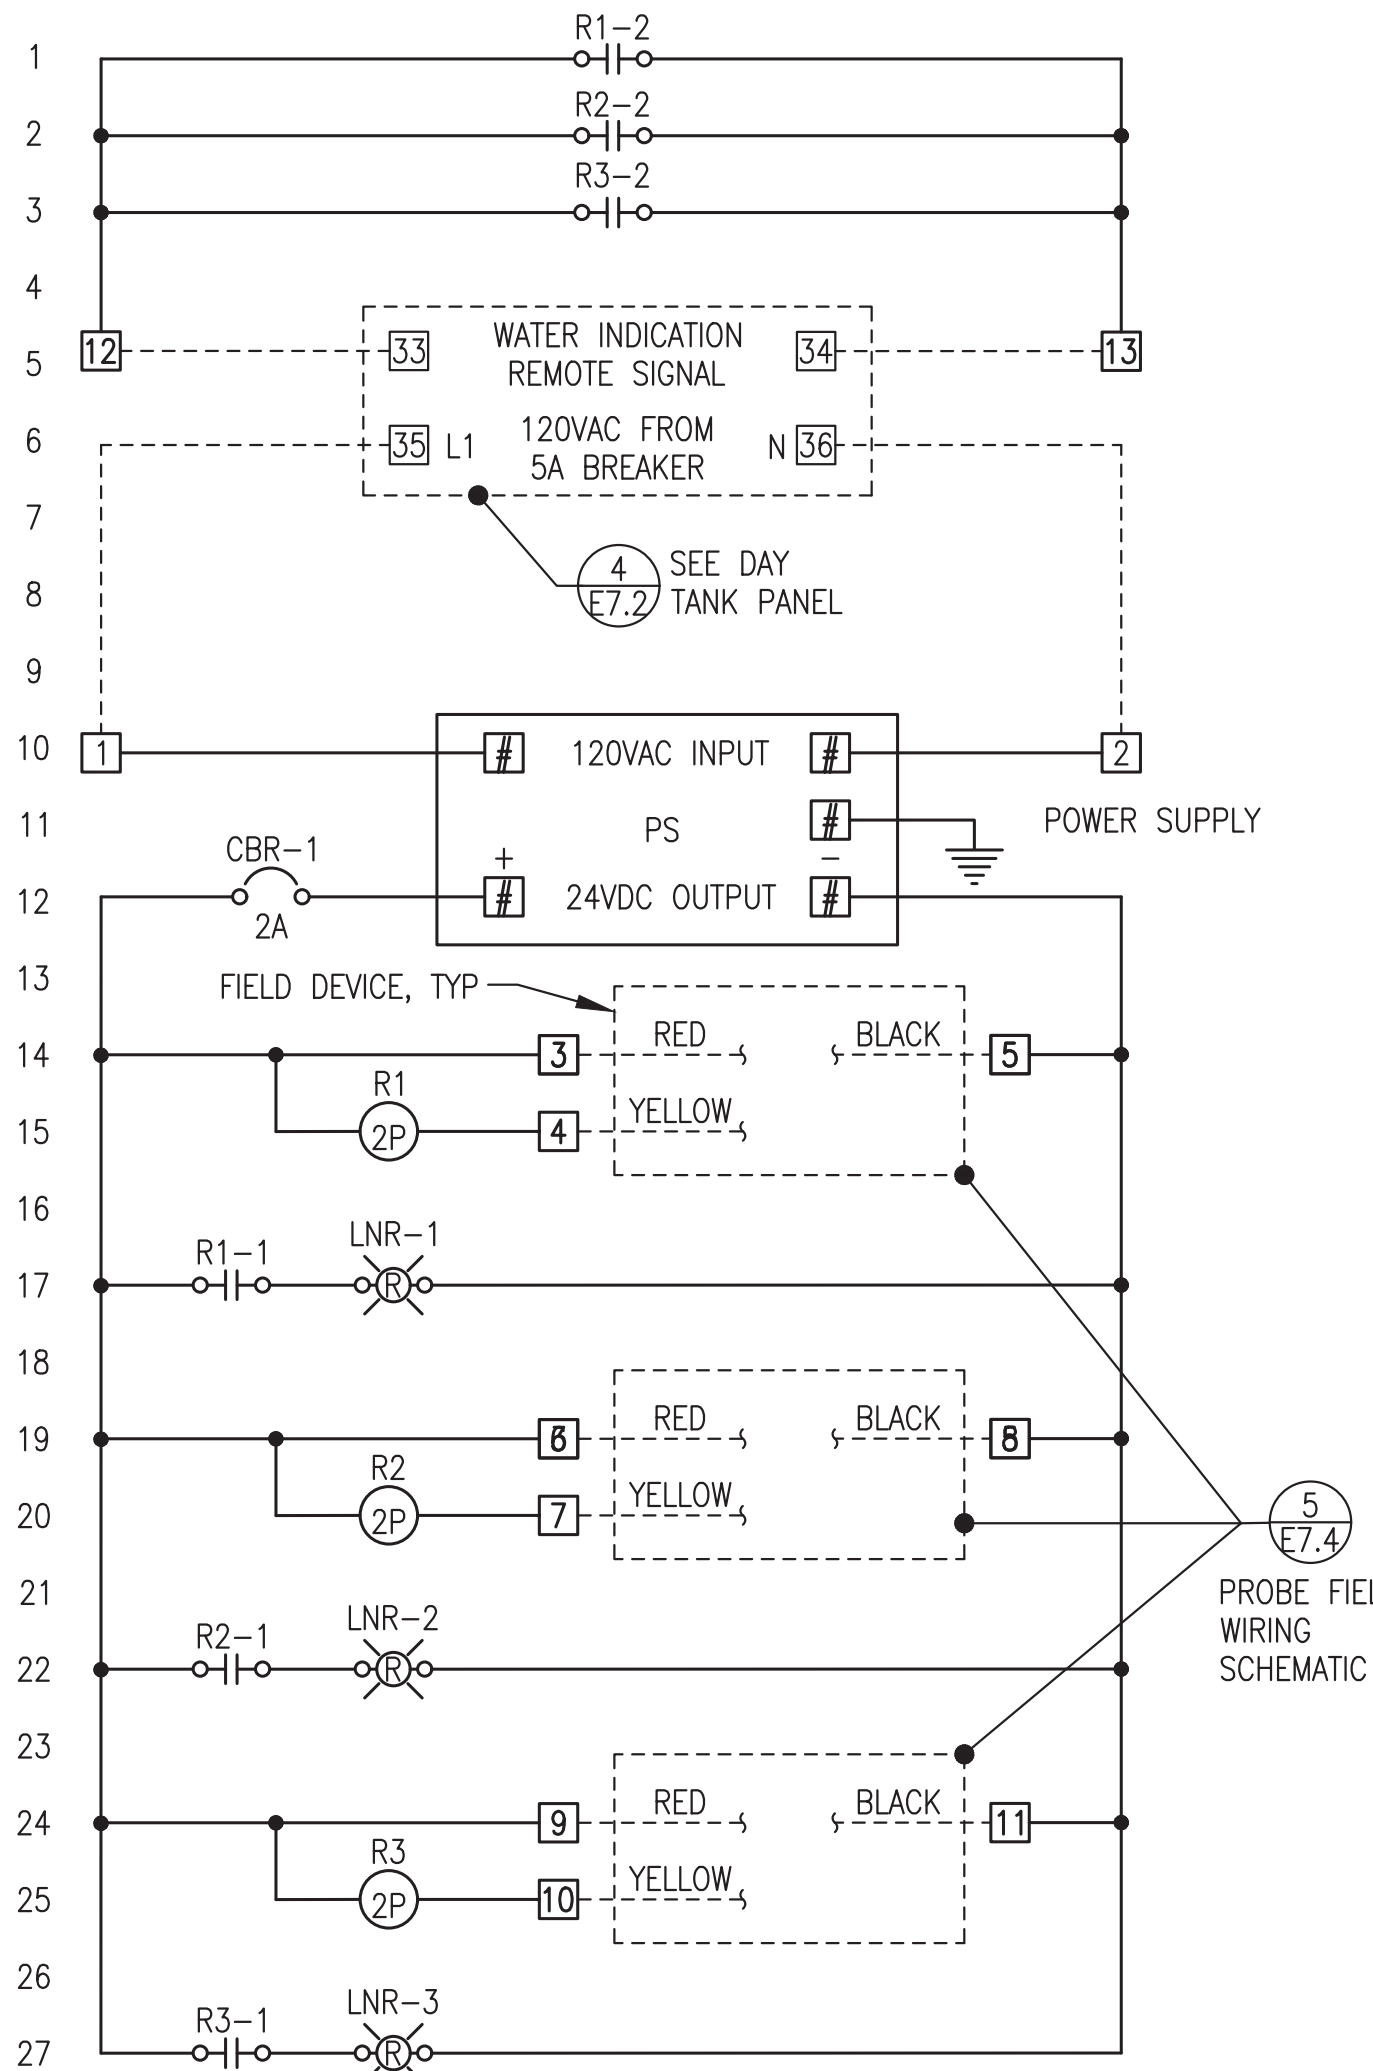

**1** PANEL WIRING DIAGRAM  
E7.4 NO SCALE

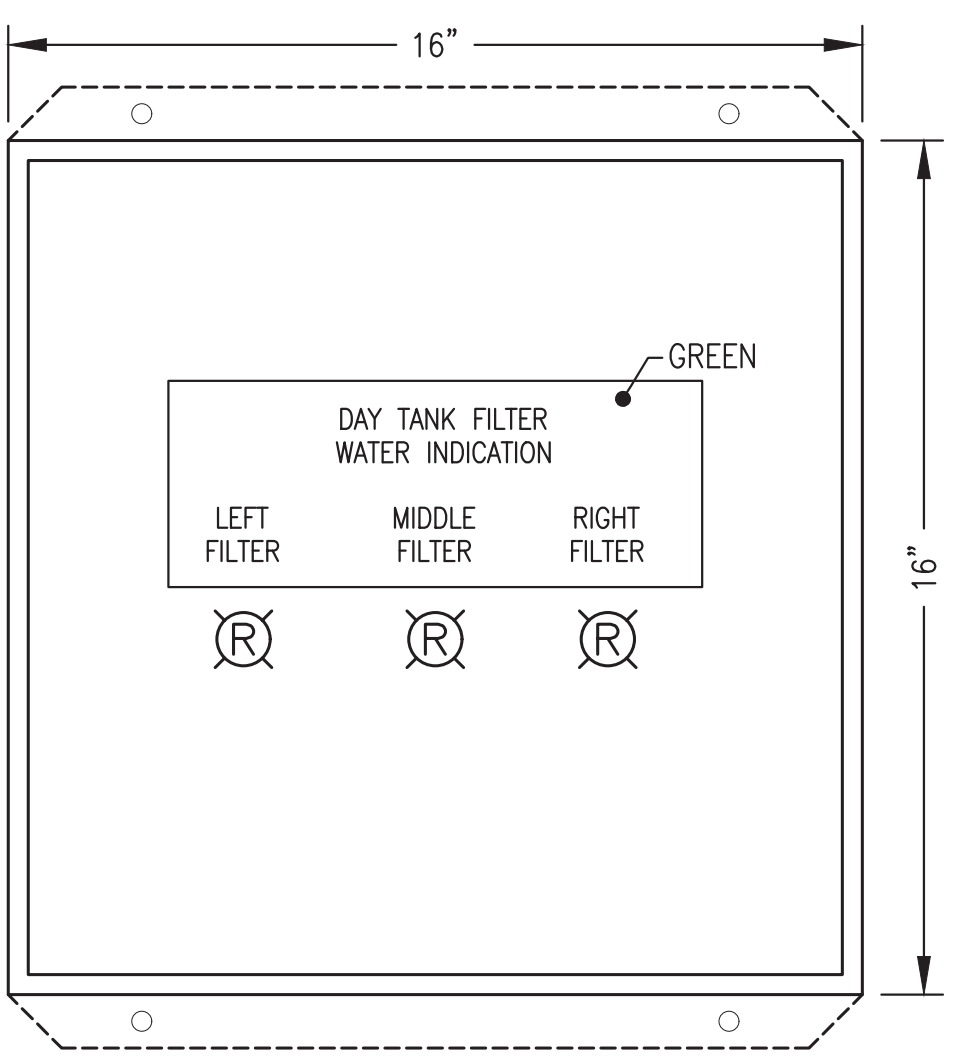

**2** FRONT PANEL LAYOUT  
E7.4 NO SCALE

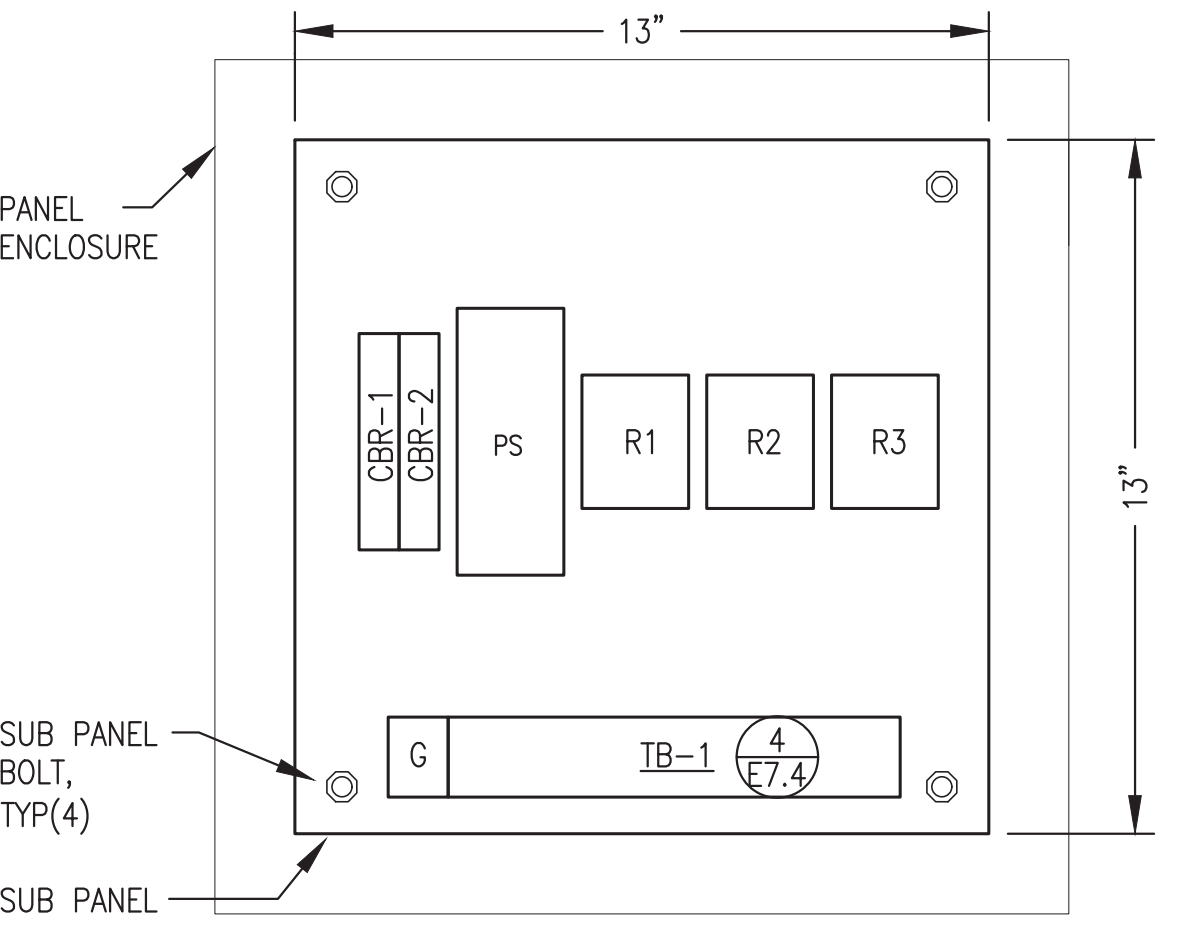


**3** SUB PANEL LAYOUT  
E7.4 NO SCALE

TAG	QTY	MANUFACTURER	MODEL	DESCRIPTION
CBR-1	1	ALLEN-BRADLEY	1489-M1-C020	RAIL-MOUNT CIRCUIT BREAKER, 1 POLE, 2A
LNR	3	ALLEN-BRADLEY	800HQRH2R	RED LED PILOT LIGHT, 12-130V, NEMA 4X
PS	1	PULS	CP.241-S1	5A, 120VAC/24VDC POWER SUPPLY
R	3	ALLEN-BRADLEY	700HA32A1	2PDT RELAY
	3	ALLEN-BRADLEY	700HN100	8 PIN SOCKET BASE
TB	15	ALLEN-BRADLEY	1492CAM1L	35A, 600V, LARGE-HEAD SCREW TERMINALS

**PANEL SHOP FABRICATION NOTES:**


- FURNISH COMPLETE PANEL ASSEMBLY WITH ALL DEVICES INDICATED IN WIRING DIAGRAM AND BILL OF MATERIALS ALONG WITH ALL PANEL DEVICE ACCESSORIES, DIN RAIL, & HARDWARE REQUIRED FOR COMPLETE INSTALLATION.
- INSTALL IN A 16"x16"x8" NEMA 12 STEEL ENCLOSURE WITH INTEGRAL MOUNTING FLANGES AT BACK, A MIN 16 GAUGE INTERIOR BACK PANEL, AND HINGED DOOR. ENCLOSURE COLOR ANSI 61 GRAY AND BACK PANEL COLOR WHITE.
- PROVIDE BEVELED EDGE WHITE CORE NAMEPLATES, FACE COLOR AS INDICATED. SECURE TO PANEL FACE WITH A MINIMUM OF TWO MOUNTING SCREWS.
- CONNECT DEVICES WITH MANUFACTURER PROVIDED CABLES IN ACCORDANCE WITH INSTALLATION INSTRUCTIONS.

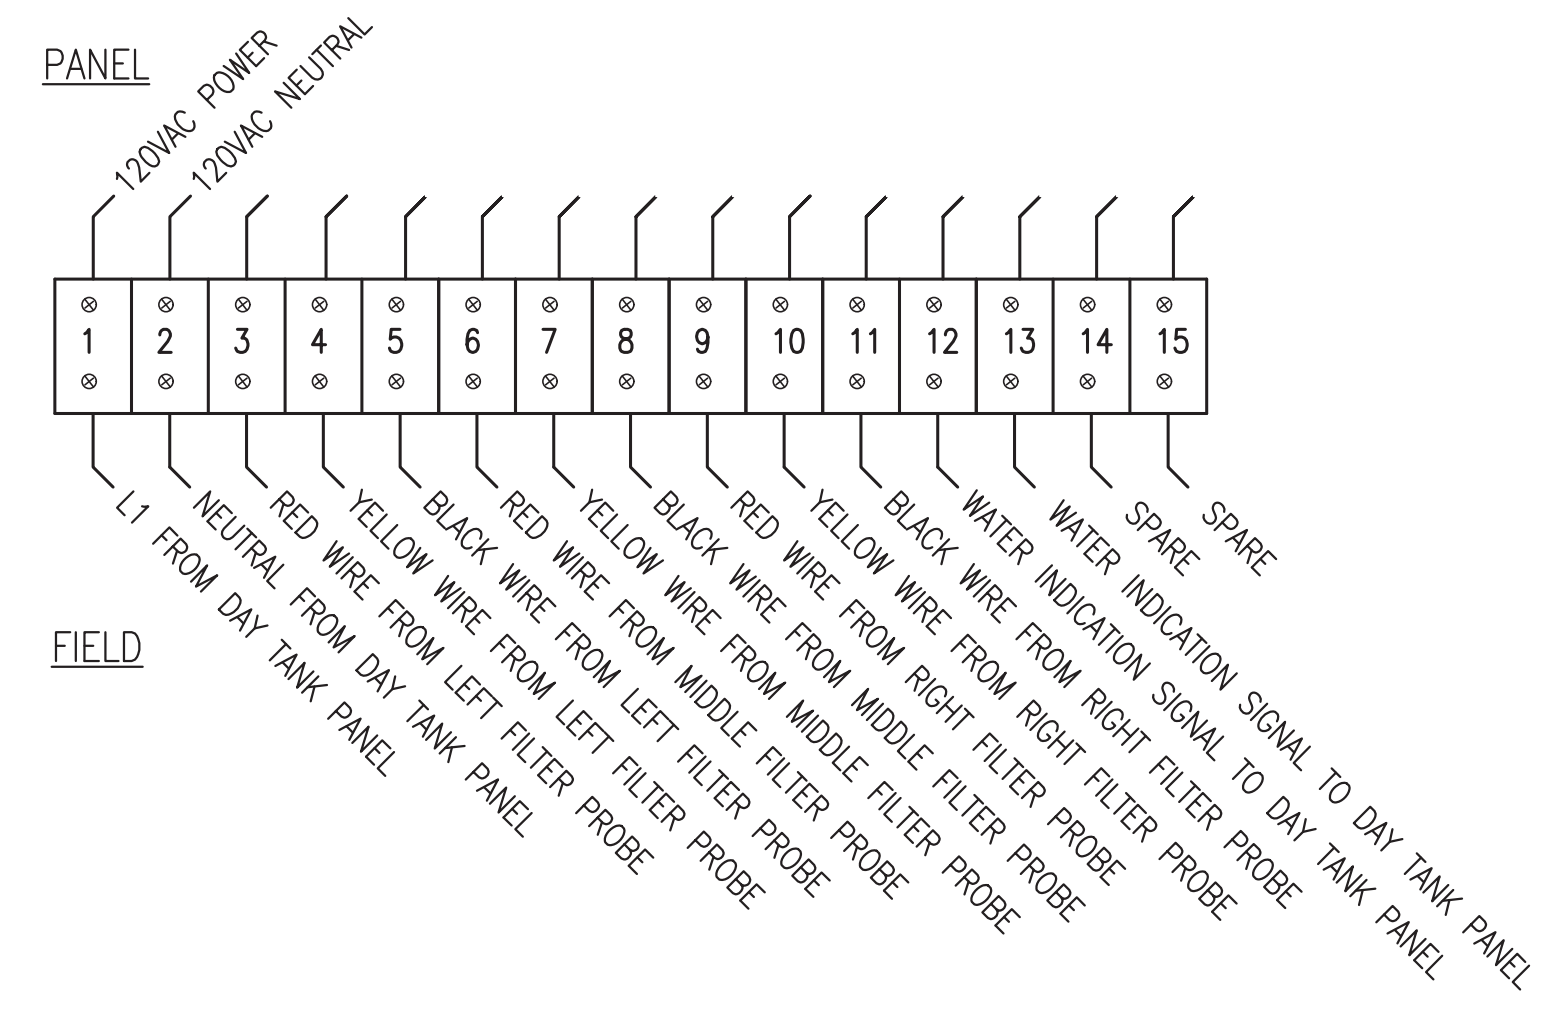

**NOTES:**

- INSTALL TERMINAL STRIP TB-1 HORIZONTALLY AS SHOWN. LOCATE TERMINAL STRIP BELOW WIRE TRAY TO ACCOMMODATE FIELD CONDUCTORS ENTERING BOTTOM OF PANEL, SEE SUB-PANEL LAYOUT.
- IN ADDITION TO THE TERMINAL STRIPS SHOWN, PROVIDE 2 EACH 60A SCREW TERMINAL GROUNDING BUS.

**4** TERMINAL STRIP TB-1 LAYOUT  
E7.4 NO SCALE

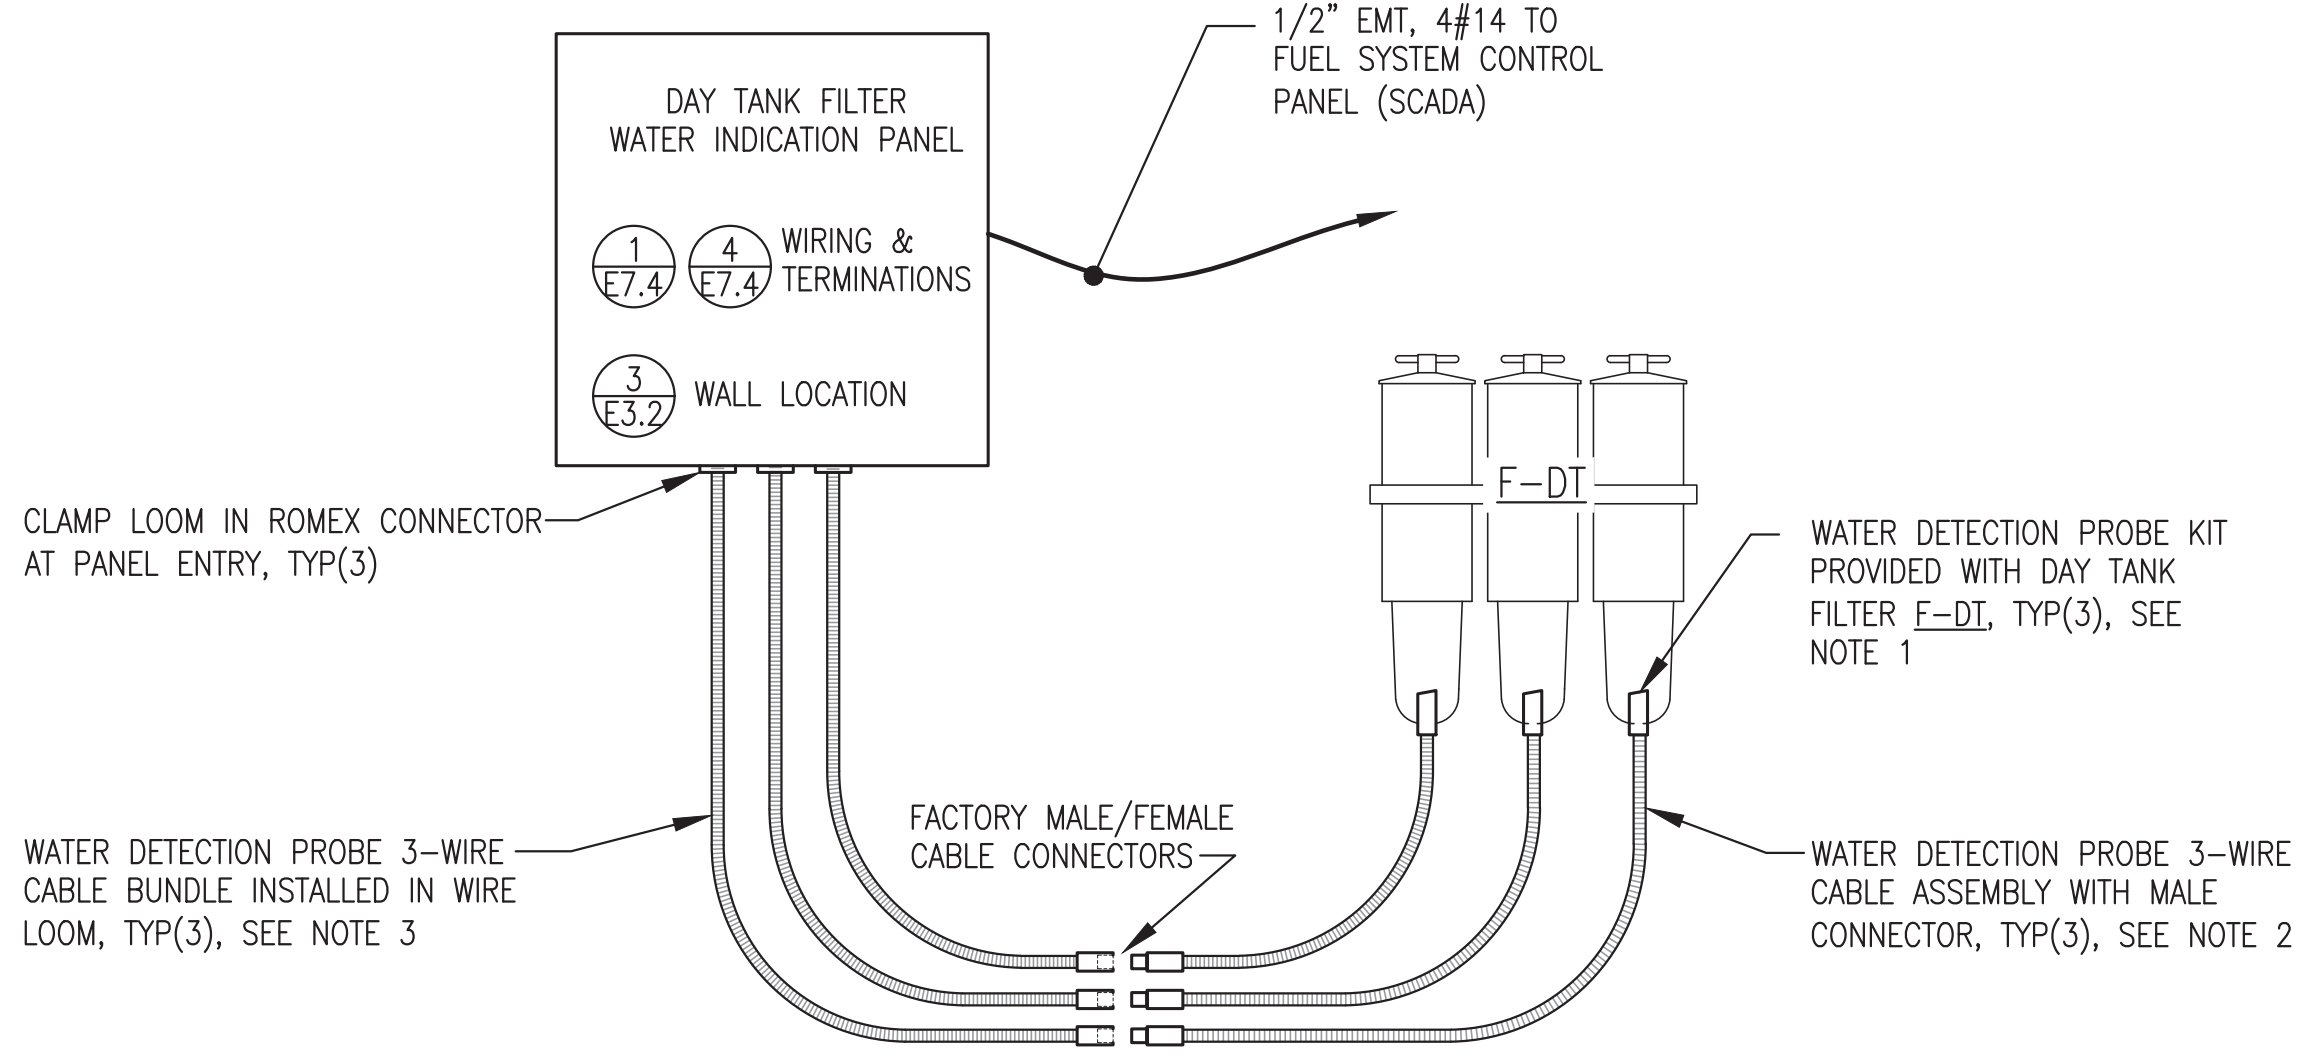


**5** FIELD WIRING SCHEMATIC  
E7.4 NO SCALE


**NOTES:**

- THREE EACH RACOR WATER DETECTION PROBE KITS, MODEL RK30880E, SHIPPED LOOSE WITH 3-FILTER BANK. NOT ALL KIT COMPONENTS USED THIS INSTALLATION. KEEP THREE EACH WATER DETECTION PROBE CABLES WITH MOLDED MALE CONNECTORS AND KEEP THREE EACH 3-WIRE CABLE BUNDLES WITH MOLDED FEMALE CONNECTORS. DISCARD THREE EACH PILOT LIGHTS AND DISCARD THREE EACH MOUNTING PANELS.
- PRIOR TO FLOODING SYSTEM WITH FUEL INSTALL WATER DETECTION PROBES IN EACH FILTER ACCORDING TO MANUFACTURER'S INSTRUCTIONS. ROUTE FACTORY LOOMED CABLES WITH MOLDED FEMALE CONNECTORS BACK TO WALL IN NEAT AND ORGANIZED FASHION FOR CONNECTION TO WIRE EXTENSION CONNECTORS. TYWRAP LOOM TO CONDUIT OR PIPING.
- FACTORY 3-WIRE CABLE BUNDLES FURNISHED WITH MOLDED MALE CONNECTORS. FIELD INSTALL IN 3/8" PLASTIC WIRE LOOM FROM CONNECTOR TO PANEL ENTRY AND ROUTE TO PANEL IN NEAT AND ORGANIZED FASHION. TYWRAP LOOM TO ADJACENT CONDUIT, PIPING, OR STRUT.


REVISION #1  
ISSUED FOR  
MODULE  
CONSTRUCTION  
JULY 2022



1	UPDATED TO COORDINATE WITH NAPASKIAK MODULE	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: DAY TANK FILTER WATER INDICATION PANEL			
DRAWN BY: BCG/JTD		SCALE: AS NOTED	
DESIGNED BY: CWV/BCG		DATE: 3/15/22	
FILE NAME: RAM_PP_E7		SHEET: E7.4	
PROJECT NUMBER:			
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

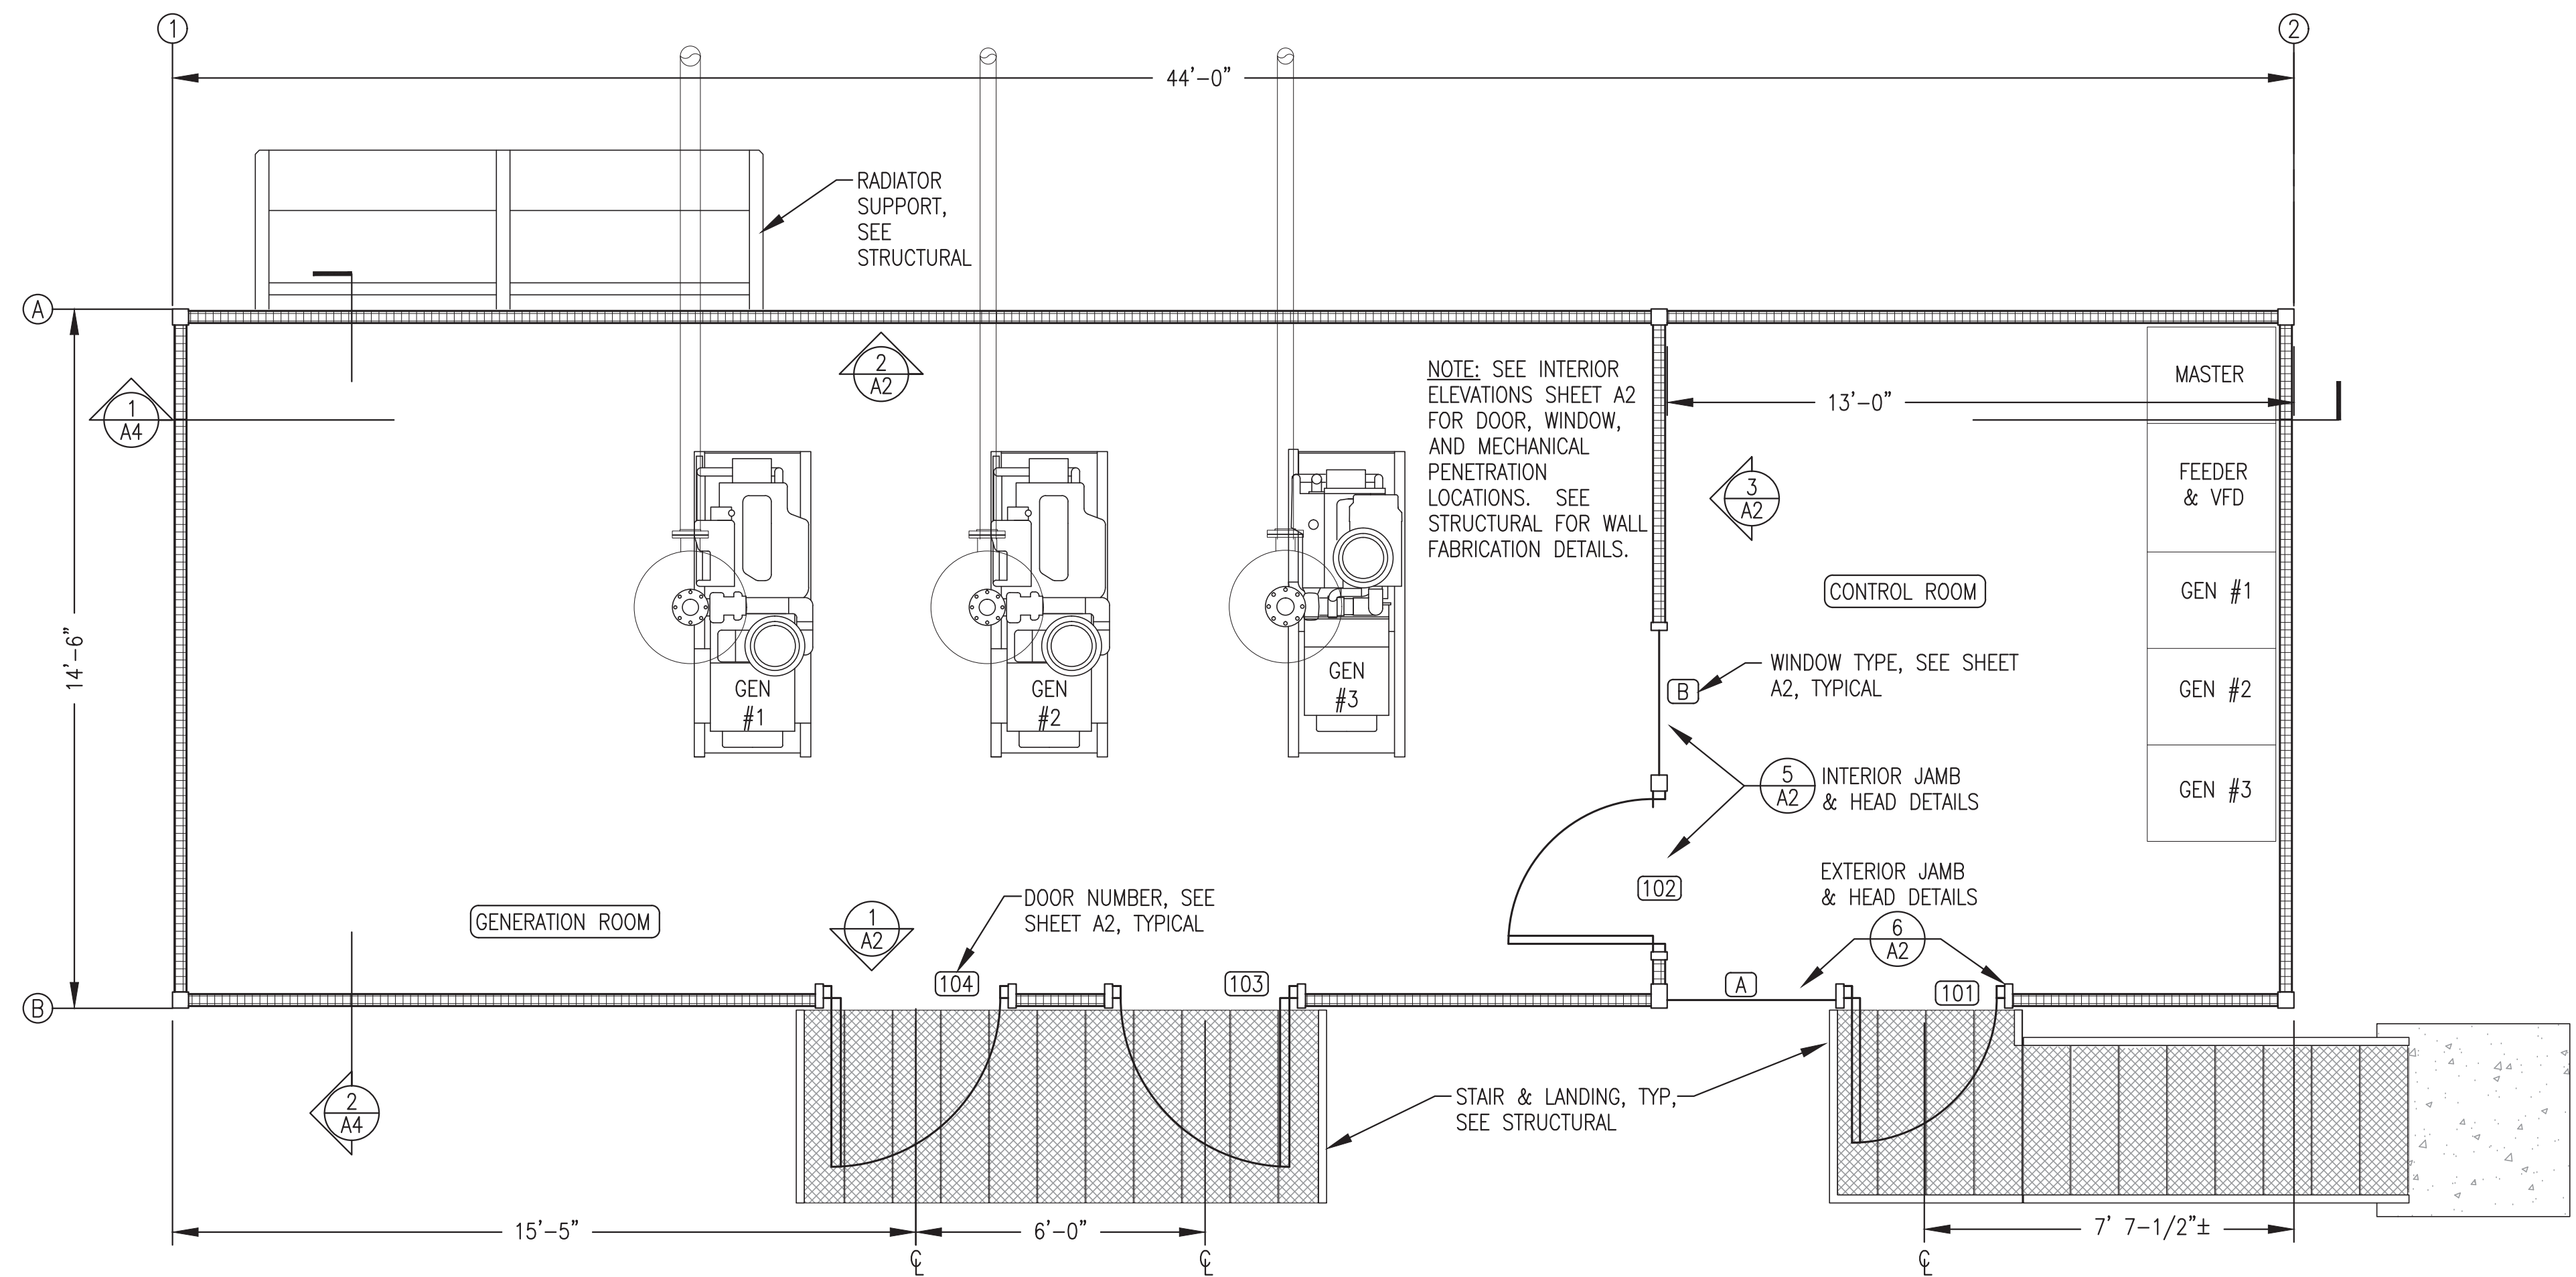

**1 FLOOR PLAN**  
A1  
3/8"=1'-0"

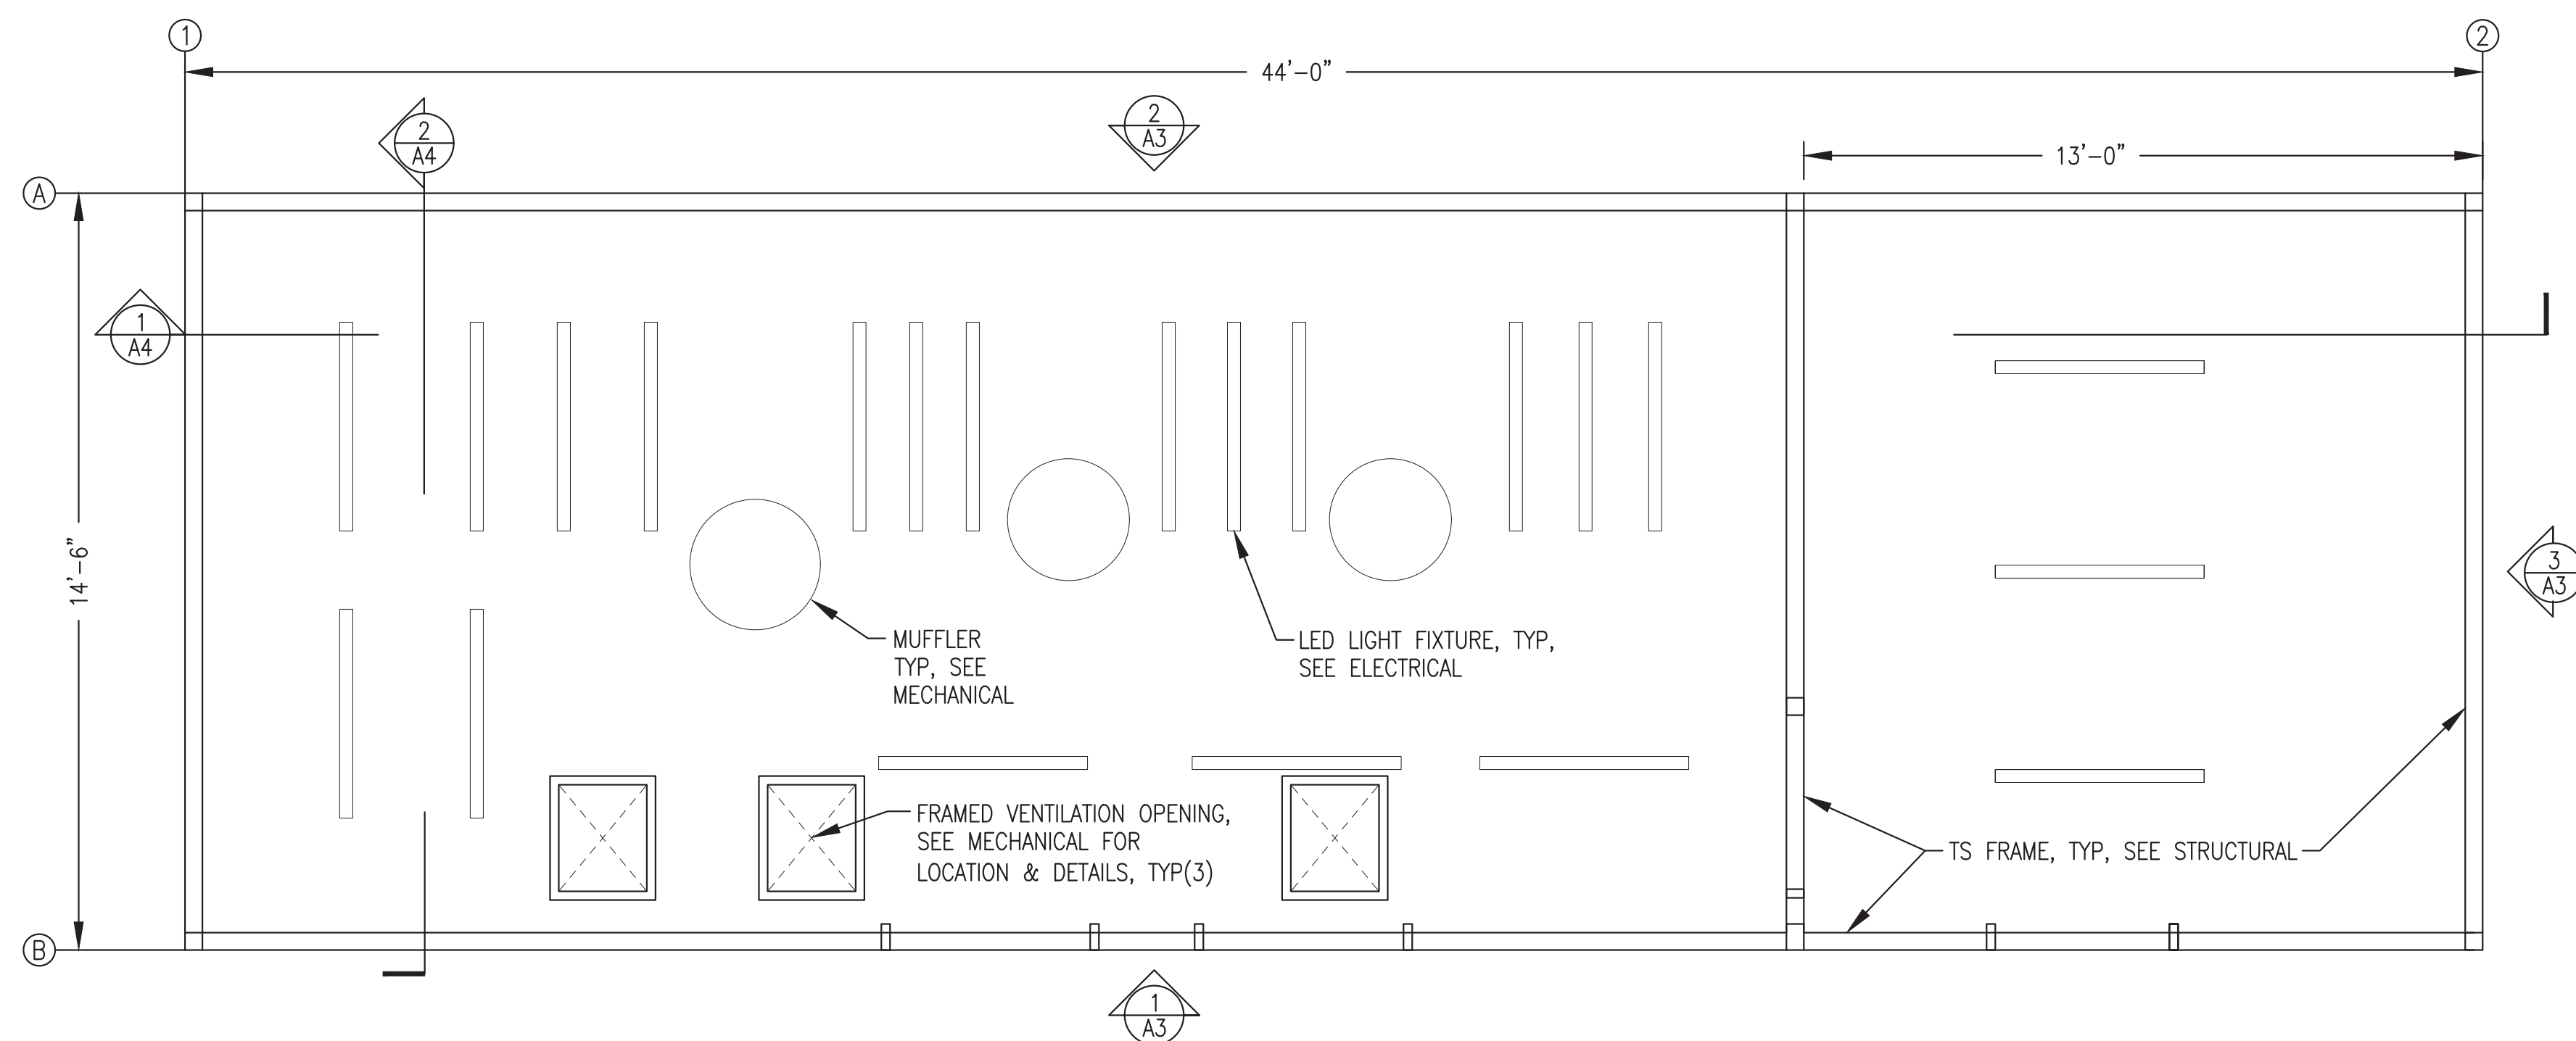

**2 REFLECTED CEILING PLAN**  
A1  
3/8"=1'-0"


CODE ANALYSIS – 2012 EDITION INTERNATIONAL BUILDING CODE	
OCCUPANCY CLASSIFICATION	REF: IBC-2012, SEC. 306.2
GROUP F-1: FACTORY INDUSTRIAL MODERATE HAZARD – ELECTRIC GENERATION PLANT	
TYPE OF CONSTRUCTION	REF: IBC-2012, TABLE 601
TYPE V-B (NON-RATED)	REF: IBC-2012, SEC. 602.5
BUILDING HEIGHTS AND AREAS	REF: IBC-2012, TABLE 503
MAX ALLOWED = 40'-0" 1 STORY 8,500 S.F.	ACTUAL = 16'-0" 1 STORY 720 S.F.
FIRE RESISTANCE RATING REQUIREMENTS FOR BUILDING ELEMENTS	REF: IBC-2012, TABLE 601
STRUCTURAL FRAME: 0 HR BEARING WALLS: 0 HR INTERIOR PARTITIONS: 0 HR FLOOR: 0 HR ROOF: 0 HR	
FIRE RESISTANCE RATING REQUIREMENTS FOR EXTERIOR WALLS	REF: IBC-2012, TABLE 602
EXTERIOR WALLS 10' < X < 30' 0 HR	
FIRE PROTECTION SYSTEM	REF: IBC-2012, SEC. 903.2.4
FIRE PROTECTION NOT REQUIRED. WATER MIST FIRE SUPPRESSION SYSTEM PROVIDED (SEE MECHANICAL).	
OCCUPANT LOAD	REF: IBC-2012, TABLE 1004.1.2
MECHANICAL/STORAGE = 300 S.F./PERSON 610 S.F./300 S.F. PER OCCUPANT = 2 OCCUPANTS	
MEANS OF EGRESS – TRAVEL DISTANCE	REF: IBC-2012, TABLE 1016.2
MAX ALLOWED = 200'	ACTUAL = 40'
COMBUSTIBLE LIQUIDS STORAGE	REF: IBC-2012, TABLE 307.1(1)(i)
MAX ALLOWED = 660 GAL CLASS II LIQUIDS ACTUAL = 200 GAL CLASS II (DIESEL FUEL DAY TANK)	
MAX ALLOWED = 13200 GAL CLASS IIIB LIQUIDS ACTUAL = 110 GAL CLASS IIIB (GLYCOL & LUBE OIL)	
STATIONARY STORAGE BATTERY SYSTEMS	REF: IBC-2012, SEC. 608.1
MAX EXEMPT = 50 GAL (FLOODED LEAD ACID) ACTUAL = 6 GAL (6 BATTERIES AT 1 GAL MAX EACH)	
<b>ARCHITECTURAL GENERAL NOTES:</b>	
1) SEE CIVIL SITE PLAN FOR LOCATION AND LAYOUT. PROVIDE SEPARATION TO PROPERTY BOUNDARIES IN ACCORDANCE WITH CODE ANALYSIS.	
2) PROVIDE A COMPLETE AND OPERATIONAL FACILITY. ALL WORK TO BE IN ACCORDANCE WITH CURRENT APPROVED EDITIONS OF THE IBC, IMC, IFC, AND NEC INCLUDING STATE OF ALASKA AMENDMENTS.	
3) SEE SHEET A2 FOR DOOR AND WINDOW DETAILS AND SCHEDULE. SEE SHEETS A3 AND A4 FOR DESCRIPTION OF FIELD INSTALLED ROOF SYSTEM.	
4) INSULATE ALL WALLS, FLOORS, AND CEILINGS WITH HIGH TEMPERATURE MINERAL FIBER ACOUSTICAL FIRE BATT INSULATION, MIN R VALUE 4 PER INCH, MIN 2000F MELTING TEMP. ROXUL AFB OR EQUAL. FILL ALL PANEL VOIDS OR PROVIDE THICKNESS AS INDICATED ON DRAWINGS. MECHANICALLY FASTEN FLOOR INSULATION TIGHT TO FLOOR.	
5) UPON COMPLETION OF FABRICATION ROUND ALL CORNERS AND GRIND EDGES SMOOTH AND PAINT ALL INTERIOR AND EXTERIOR EXPOSED STEEL. PERFORM ALL PAINTING IN A WARM DRY ENVIRONMENT IN ACCORDANCE WITH MANUFACTURER'S INSTRUCTIONS INCLUDING DRYING TIME TO RE-COAT.	
6) SANDBLAST EXTERIOR SURFACE TO SSPC-SP-10. PRIME WITH ONE COAT OF REINFORCED INORGANIC ZINC PRIMER, DEVOE CATHA-COAT 302 OR APPROVED EQUAL, COLOR GREEN, TO 3 MILS DRY FILM THICKNESS. COVER WITH TWO COATS OF EPOXY, DEVOE BAR-RUST 236 OR APPROVED EQUAL, TO 12 MILS DRY FILM THICKNESS. FIRST COAT COLOR GRAY, SECOND COAT COLOR WHITE.	
7) FINISH EXTERIOR WALLS AND SKIDS (ALL EXPOSED VERTICAL EXTERIOR SURFACES) WITH ONE COAT OF ALIPHATIC URETHANE ENAMEL, DEVOE DEVTHANE 389 OR APPROVED EQUAL, COLOR WHITE, TO 3 MILS DRY FILM THICKNESS.	
8) SANDBLAST INTERIOR SURFACE TO SSPC-SP-6. PRIME AND FINISH WITH TWO COATS OF EPOXY, PPG AMERLOC 2 VOC OR APPROVED EQUAL, TO 8 MILS TOTAL DRY FILM THICKNESS. CEILING COLOR WHITE. WALL AND FLOOR COLOR ANSI 61 GRAY. NOTE THAT FIRST COAT ON WALLS AND FLOOR MAY BE WHITE.	

**THIS DRAWING INCLUDES DETAILS THAT ARE NOT PART OF THE MODULE ASSEMBLY SCOPE AND IS PROVIDED STRICTLY FOR IDENTIFYING LOCATIONS, INSTALLATION DETAILS, AND SPECIFICATIONS FOR DOORS AND WINDOWS.**


ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022




PROJECT: <b>RAMPART POWER SYSTEM UPGRADE</b>	
TITLE: <b>FLOOR PLAN, REFLECTED CEILING PLAN, CODE ANALYSIS, &amp; GENERAL NOTES</b>	
DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: DGT/BCG	DATE: 3/15/22
FILE NAME: RAM PP A1-A4	SHEET: <b>A1</b>
PROJECT NUMBER:	
P.O. 111405, Anchorage, AK 99511 (907)349-0100	

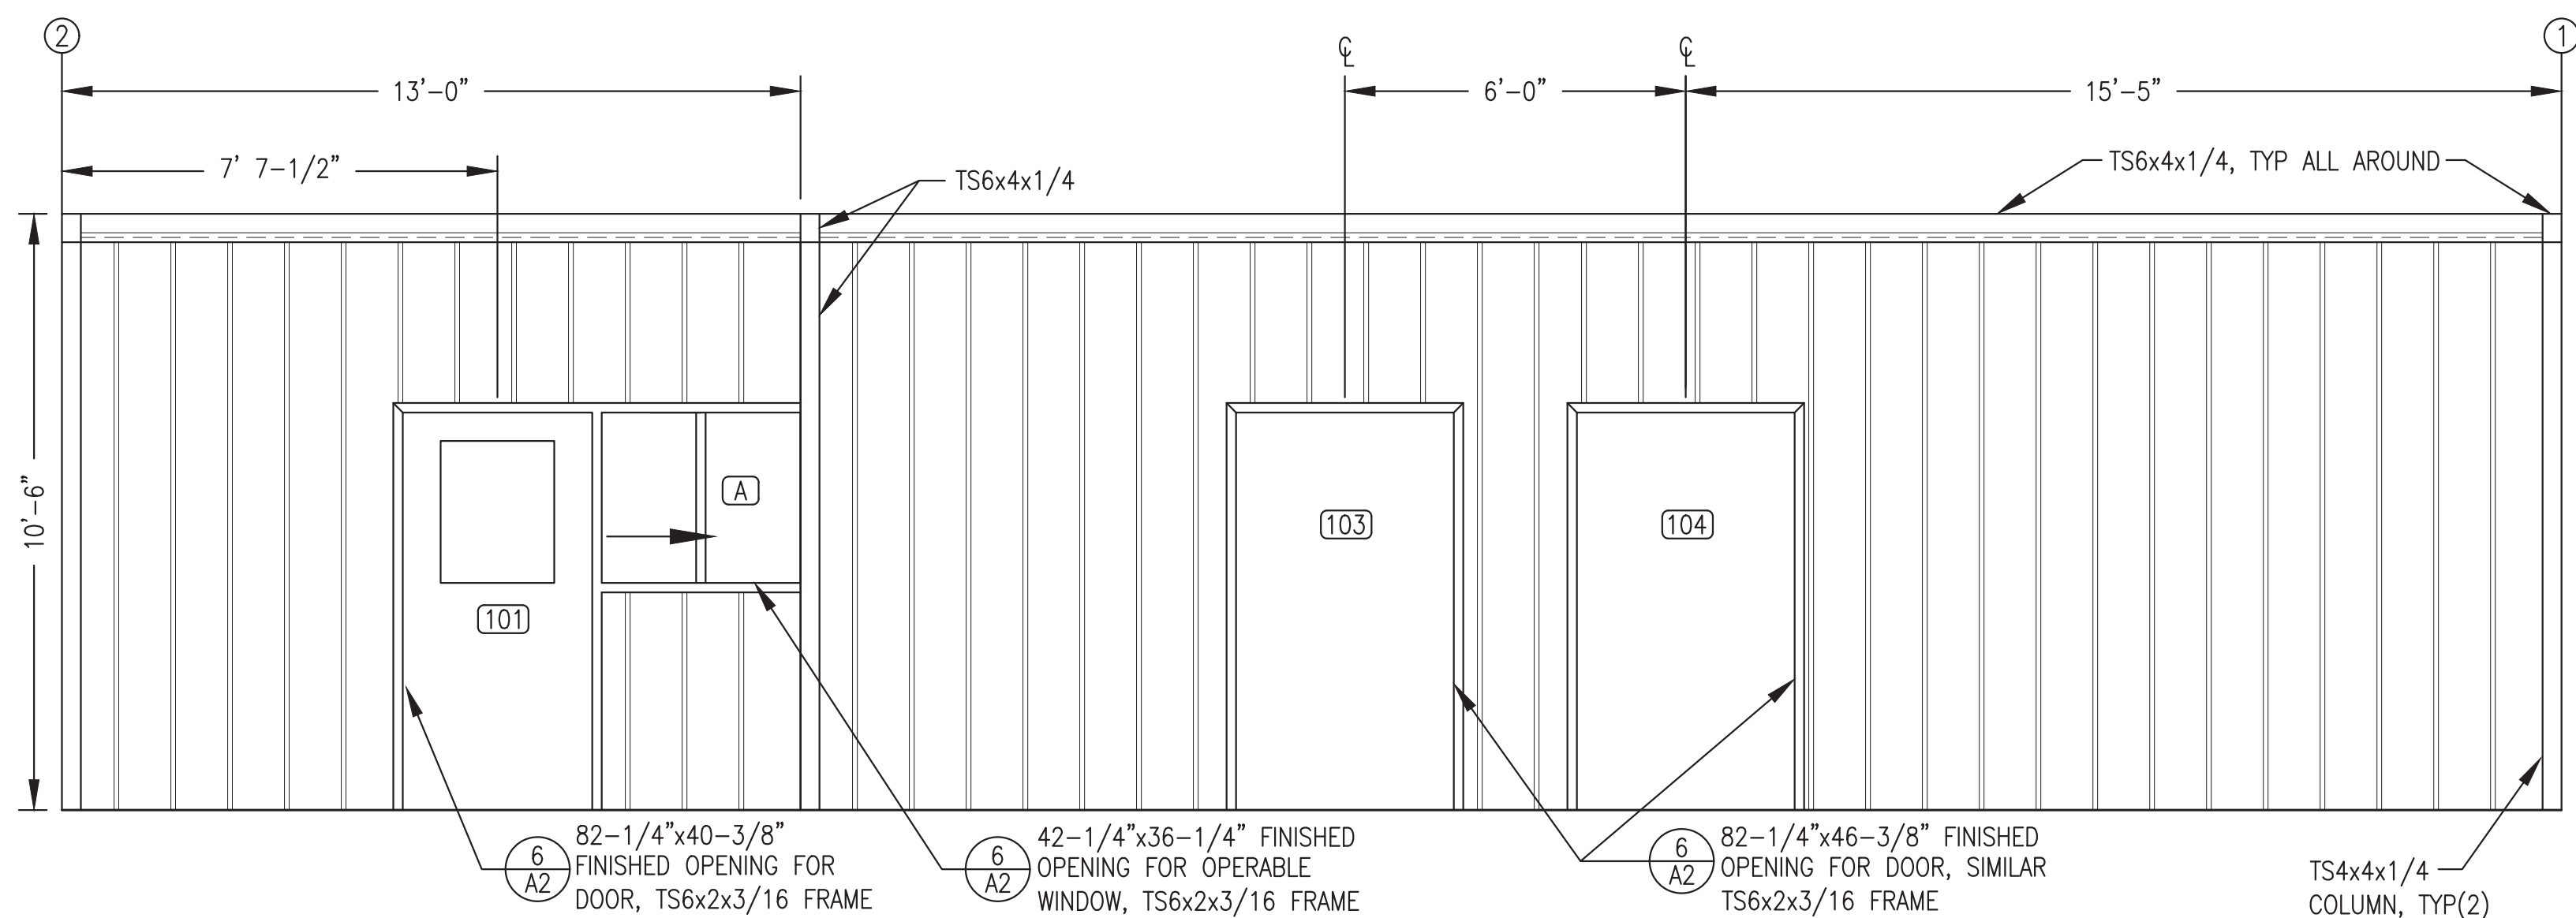


**1 FRONT WALL INTERIOR ELEVATION**  
 A2 3/8"=1'-0"

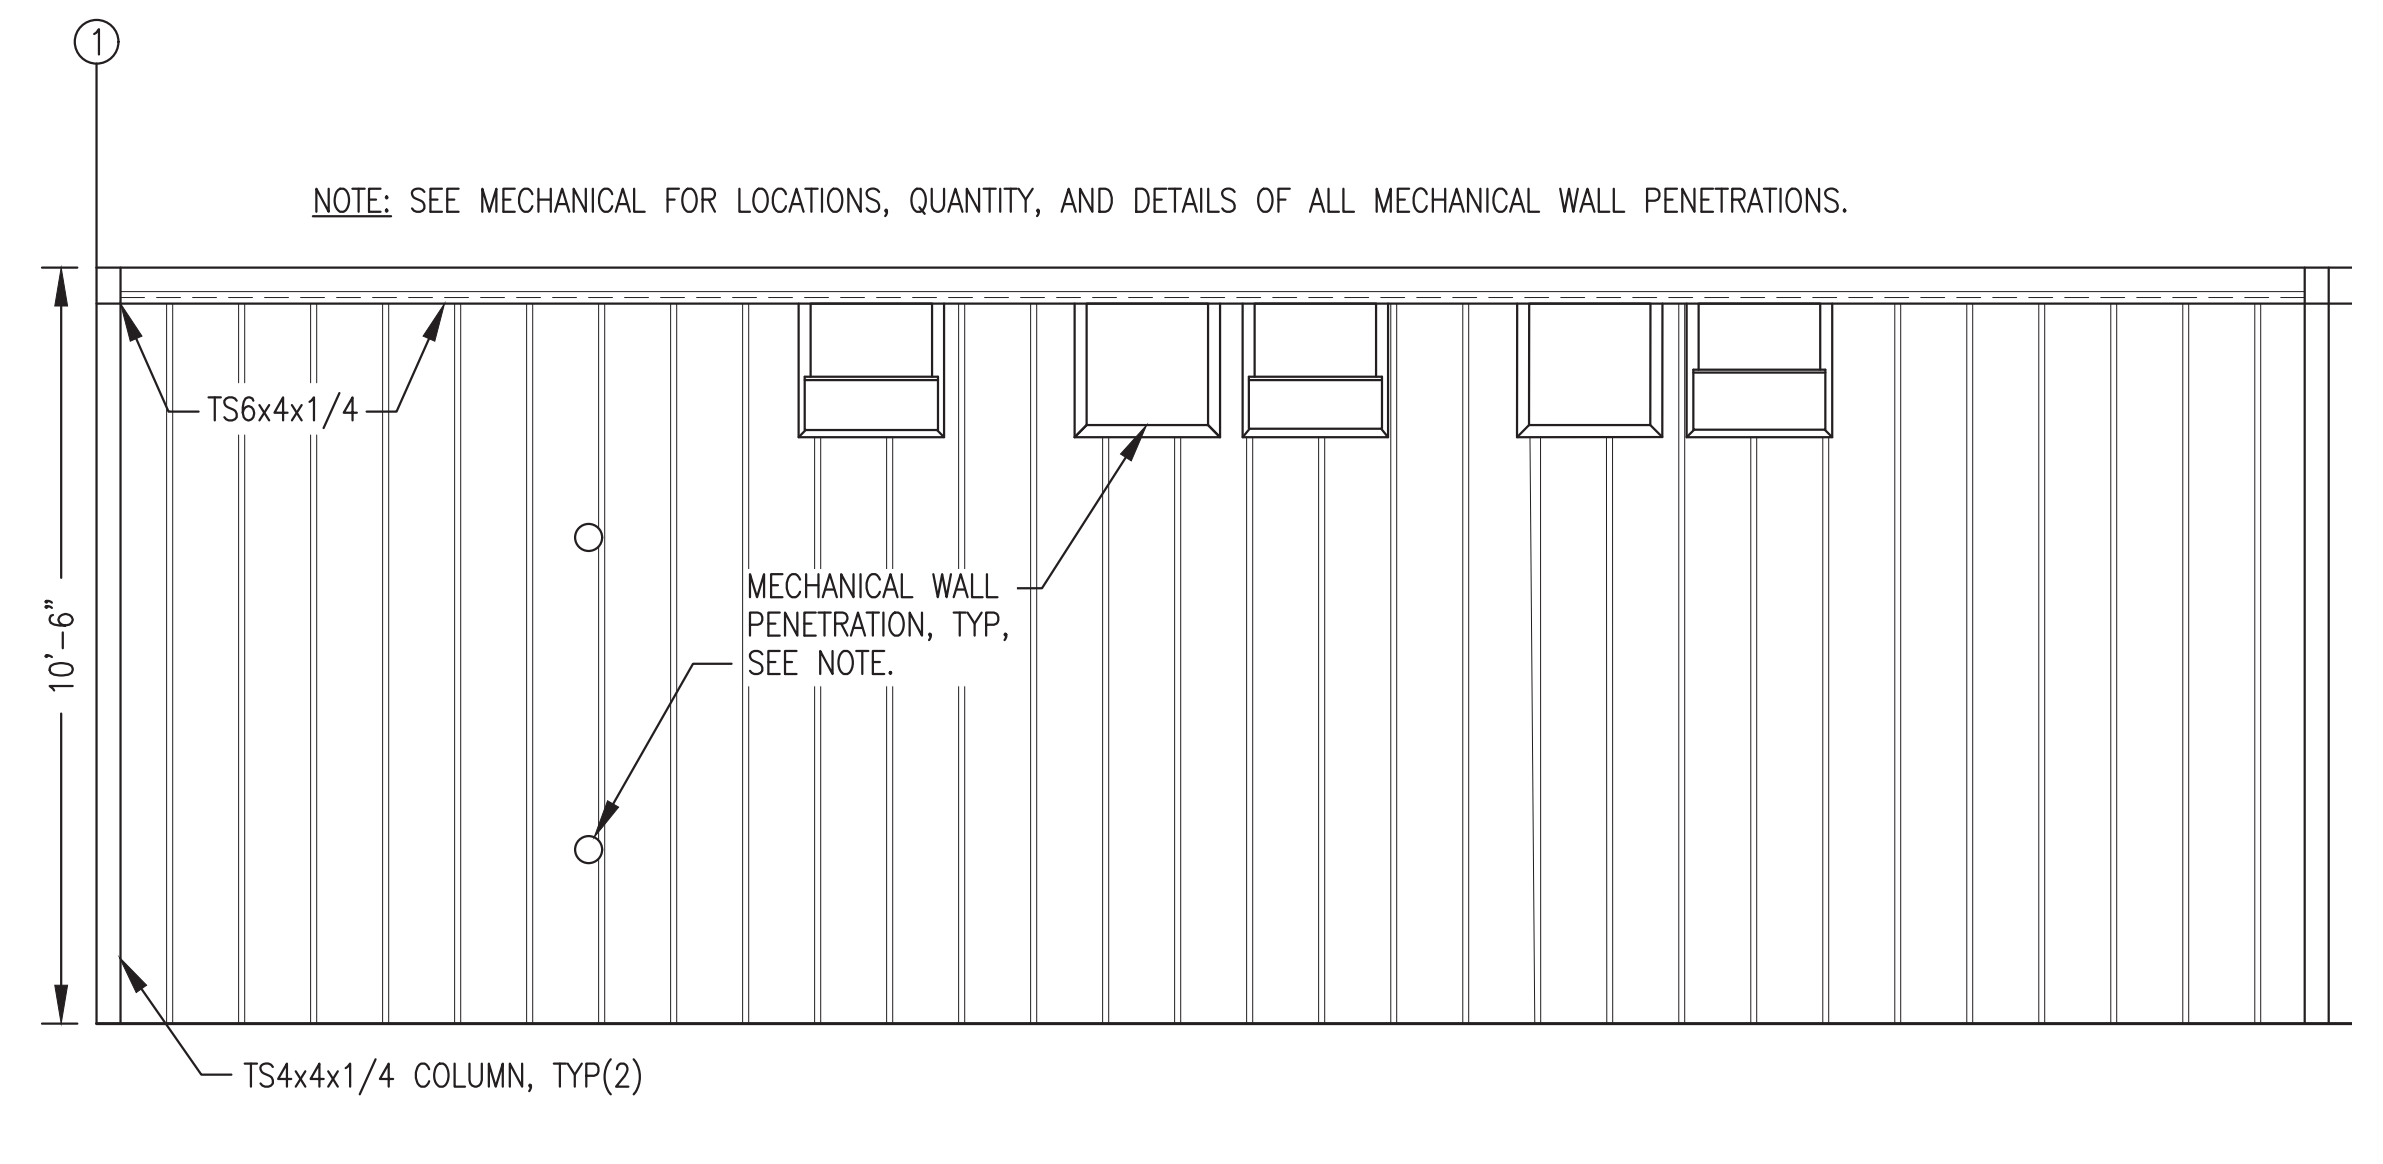

**2 PARTIAL GENERATOR ROOM BACK WALL INTERIOR ELEVATION**  
 A2 3/8"=1'-0"

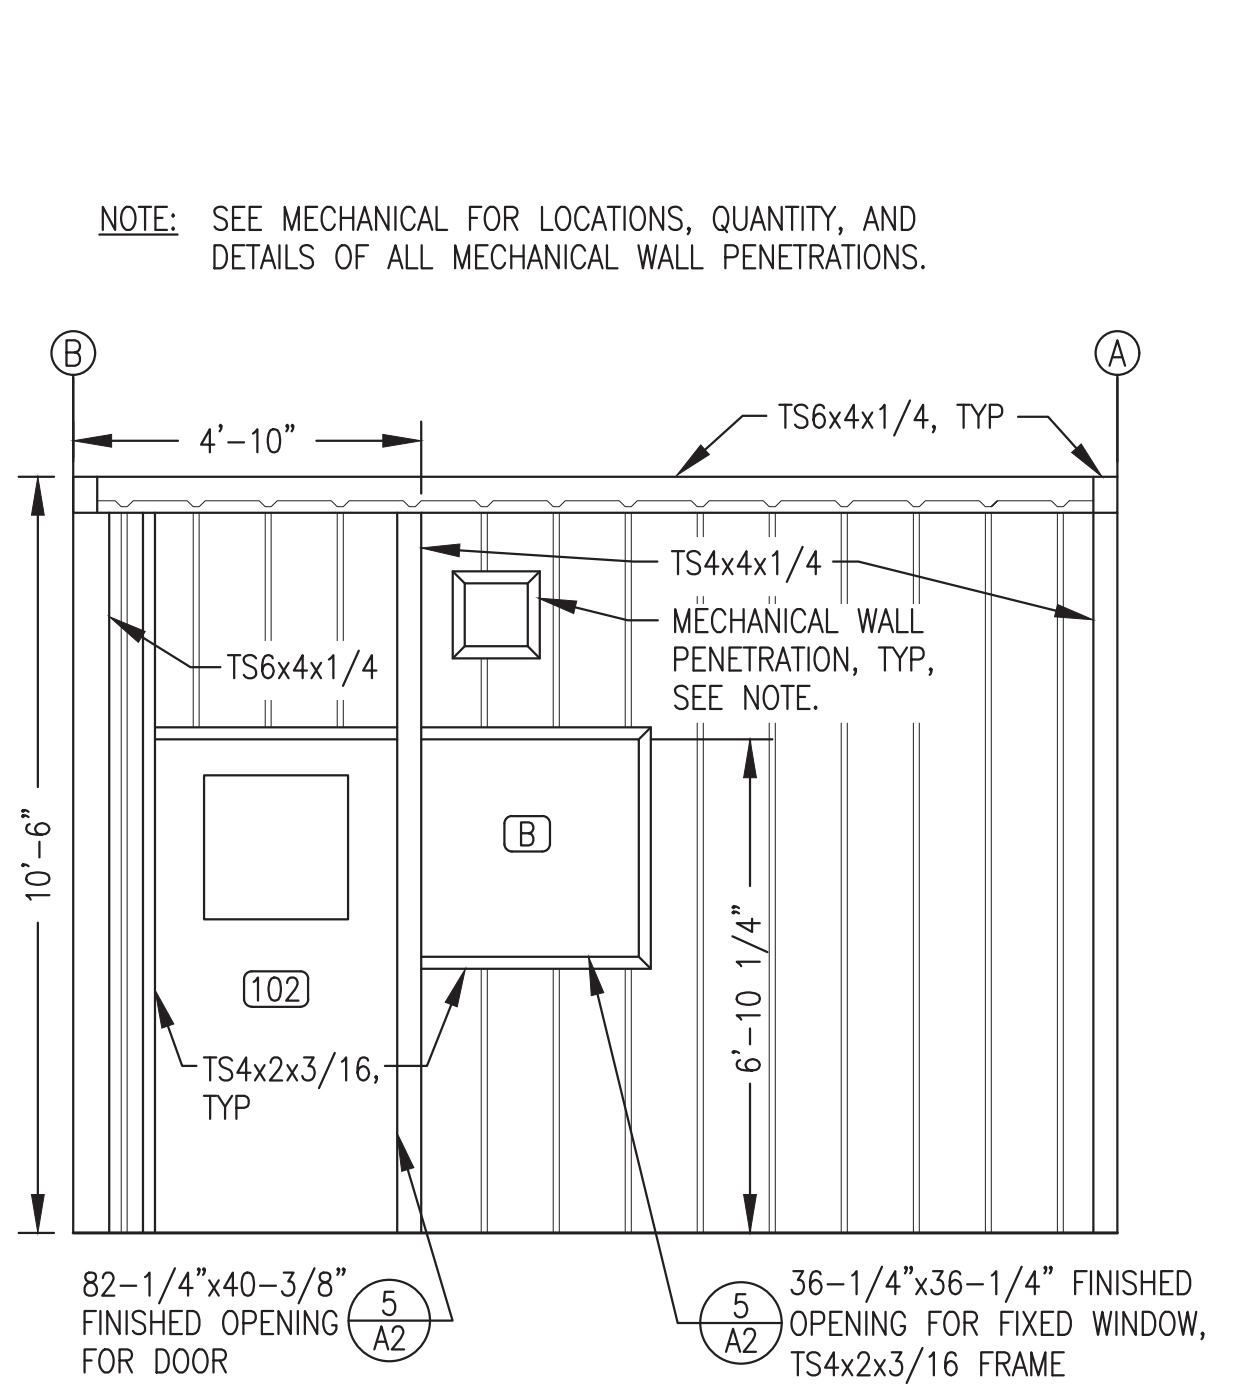


**3 CONTROL ROOM WALL INTERIOR ELEVATION**  
 A2 3/8"=1'-0"

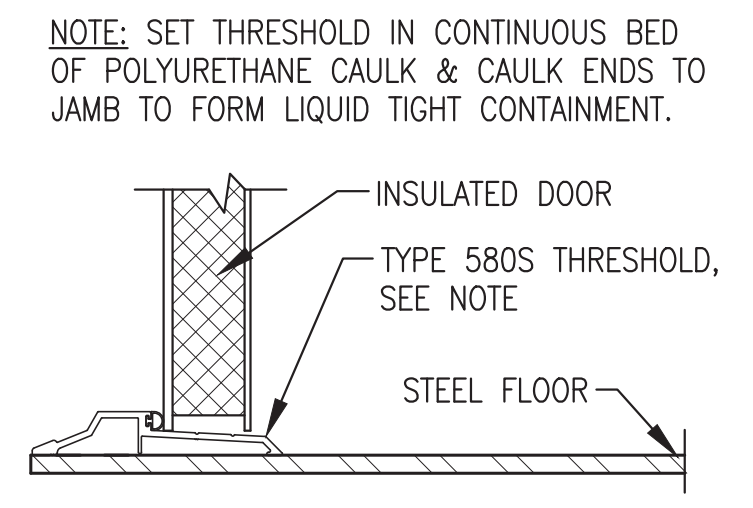


**4 TYPICAL DOOR THRESHOLD**  
 A2 NO SCALE

**FRAMED OPENING NOTES:**


- FABRICATE FRAMED OPENINGS FOR DOORS, WINDOWS, ETC. WITH MITERED CORNERS AND FULL PENETRATION GROOVE WELDS. GRIND OUT INSIDE OF MITERED CORNERS TO PROVIDE FULL CLEAR OPENING.
- FABRICATE TO FINISHED INSIDE (CLEAR) DIMENSIONS INDICATED AND LOCATE TO INSIDE EDGE OR CENTERLINE AS INDICATED.

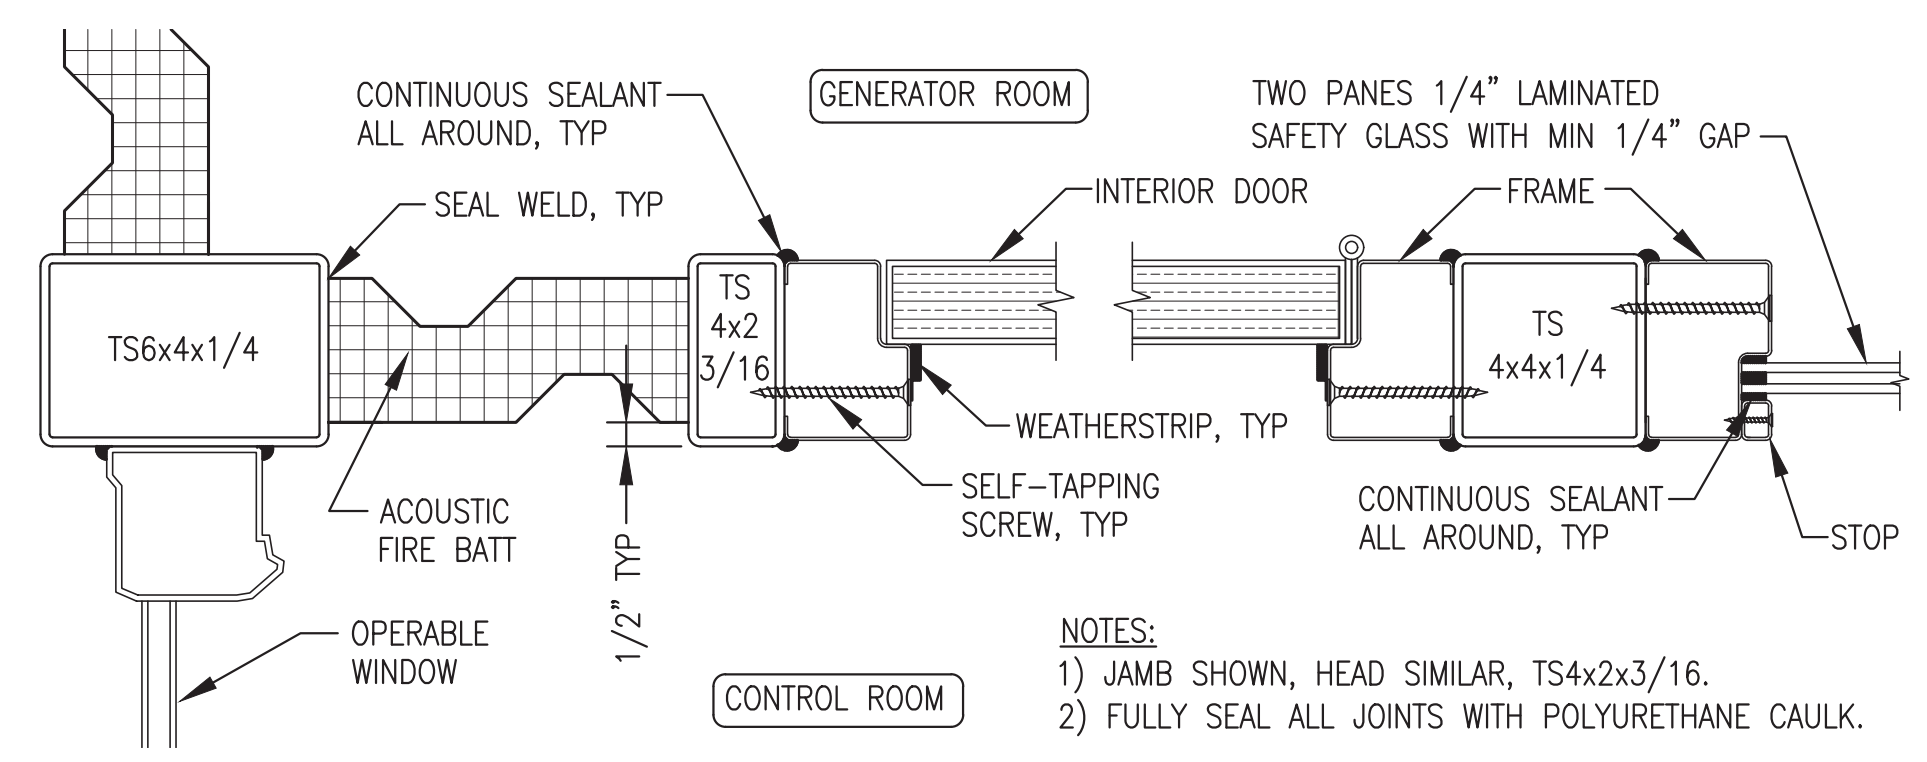

**5 INTERIOR DOOR AND WINDOW JAMB/HEAD**  
 A2 3"=1'-0"

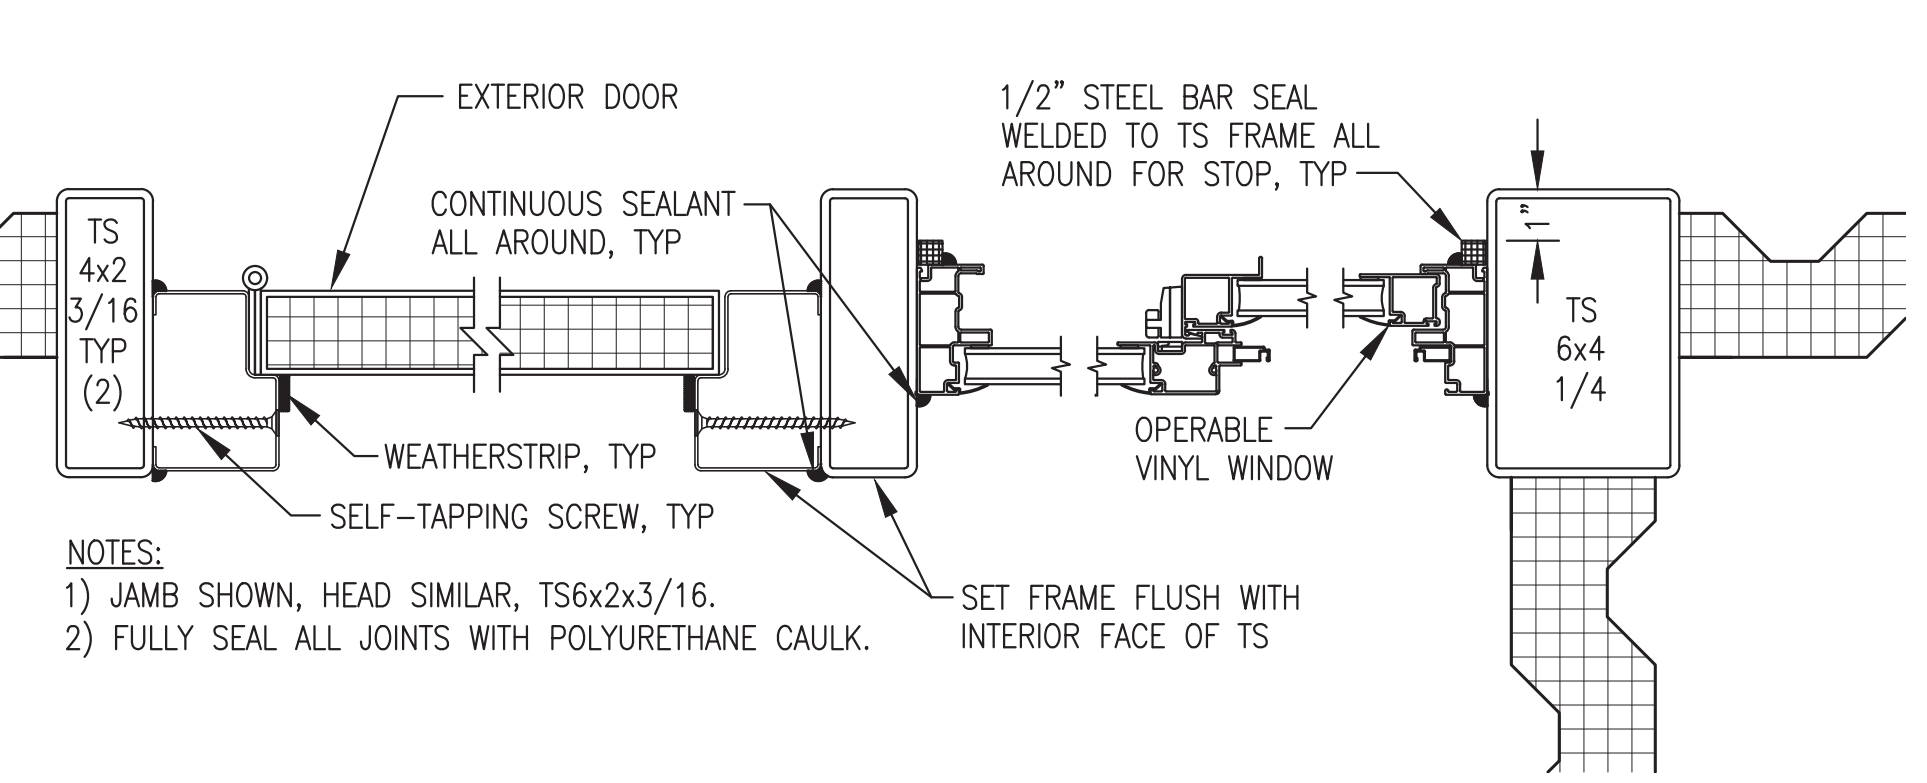

**6 TYPICAL EXTERIOR DOOR AND WINDOW JAMB/HEAD**  
 A2 3"=1'-0"

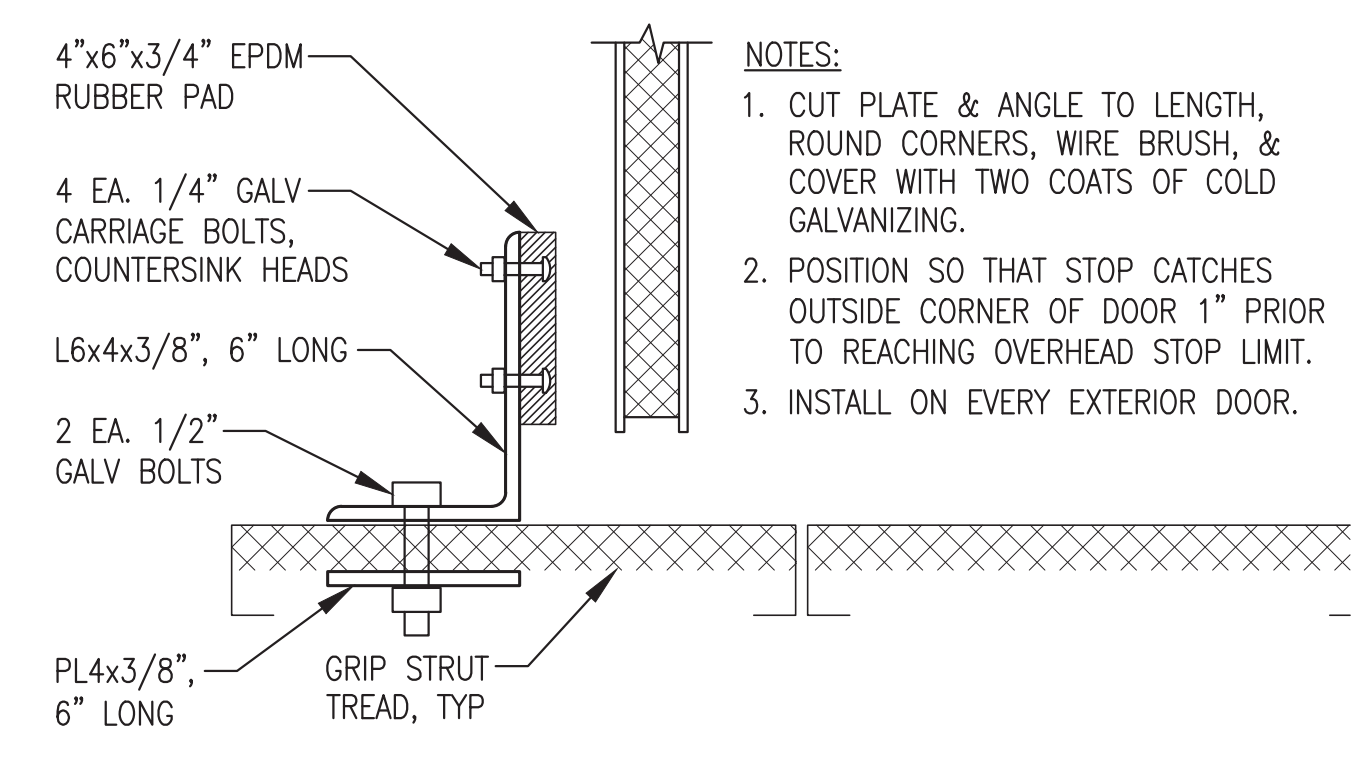

**7 TYPICAL EXTERIOR DOOR BOTTOM STOP**  
 A2 NO SCALE

DOOR CONSTRUCTION							FRAME CONSTRUCTION						
DOOR NO.	WIDTH	HEIGHT	THICK NESS	MATERIAL	CORE	REMARKS	WALL THICK.	MATERIAL	TYPE	PROFILE	PREP.	FIRE RATING	HDWR. GROUP
101	3'-0"	6'-8"	1-3/4"	16 GA. H.M.	POLYURETHANE	24"x24" RE-LIGHT {4}	N/A	16 GA. H.M.	WELDED	SINGLE RABBETED	DIMPLE & PUNCH	NONE	HW-1
102	3'-0"	6'-8"	1-3/4"	16 GA. H.M.	POLYURETHANE	24"x24" RE-LIGHT {4}	N/A	16 GA. H.M.	WELDED	SINGLE RABBETED	DIMPLE & PUNCH	NONE	HW-2
103	3'-6"	6'-8"	1-3/4"	16 GA. H.M.	POLYURETHANE		N/A	16 GA. H.M.	WELDED	SINGLE RABBETED	DIMPLE & PUNCH	NONE	HW-3
104	3'-6"	6'-8"	1-3/4"	16 GA. H.M.	POLYURETHANE		N/A	16 GA. H.M.	WELDED	SINGLE RABBETED	DIMPLE & PUNCH	NONE	HW-3

**DOOR HARDWARE:**

HW	EA	DESCRIPTION	MANUFACTURER	MODEL	SIZE
HW-1	3	HINGES	HAGER	BB1191	4.5 x 4.5NRP x 630
	1	EXIT DEVICE	PRECISION	2108	x 4908AX3 x 630
	1	DOOR CLOSER	BEST	BROWN CONSTRUCTION CORE	
	1	DOOR CLOSER	LCN	4040	x SCUSH x 689
	1	W/SPRING STOP			
	1	KICK PLATE	ROCKWOOD	K1050	10 x 34 x 630
	1	WEATHER STRIP	PEMKO	2891AS	x 36 (HEAD)
	2	WEATHER STRIP	PEMKO	290AS	x 80 (SIDE JAMBS)
	1	THRESHOLD	HAGER	580S	x 36

**DOOR FRAME PROFILE:**

**WINDOW TYPES:**

**NOTES:**


- DOORS AND HOLLOW METAL FRAMES GALVANIZED AND FACTORY PRIMED. ALL FRAMES WELDED CONSTRUCTION, DIMPLED AND PUNCHED.
- DOORS TO HAVE SOLID POLYURETHANE INSULATION CORE WITH TOPS INVERTED AND CAULKED WATER TIGHT.
- FINISH ALL DOORS AND HOLLOW METAL FRAMES WITH TWO COATS OF PAINT IDENTICAL TO INTERIOR WALLS AND FLOORS AS SPECIFIED ON SHEET A1.
- INSTALL INSULATED RE-LIGHT WITH TWO PANES OF 1/4" LAMINATED SAFETY GLASS WITH 1/2" AIR GAP IN EACH DOOR PANEL, 24"x24" OR 24"x18" AS INDICATED.

**THIS DRAWING INCLUDES DETAILS THAT ARE NOT PART OF THE MODULE ASSEMBLY SCOPE AND IS PROVIDED STRICTLY FOR IDENTIFYING LOCATIONS, INSTALLATION DETAILS, AND SPECIFICATIONS FOR DOORS AND WINDOWS.**


ISSUED FOR  
 MODULE  
 CONSTRUCTION  
 MARCH 2022




PROJECT: RAMPART POWER SYSTEM UPGRADE	
TITLE: INTERIOR ELEVATIONS & DOOR/WINDOW DETAILS & SCHEDULE	
DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: DGT/BCG	DATE: 3/15/22
FILE NAME: RAM PP A1-A4	SHEET: A2
PROJECT NUMBER:	
P.O. 111405, Anchorage, AK 99511 (907)349-0100	

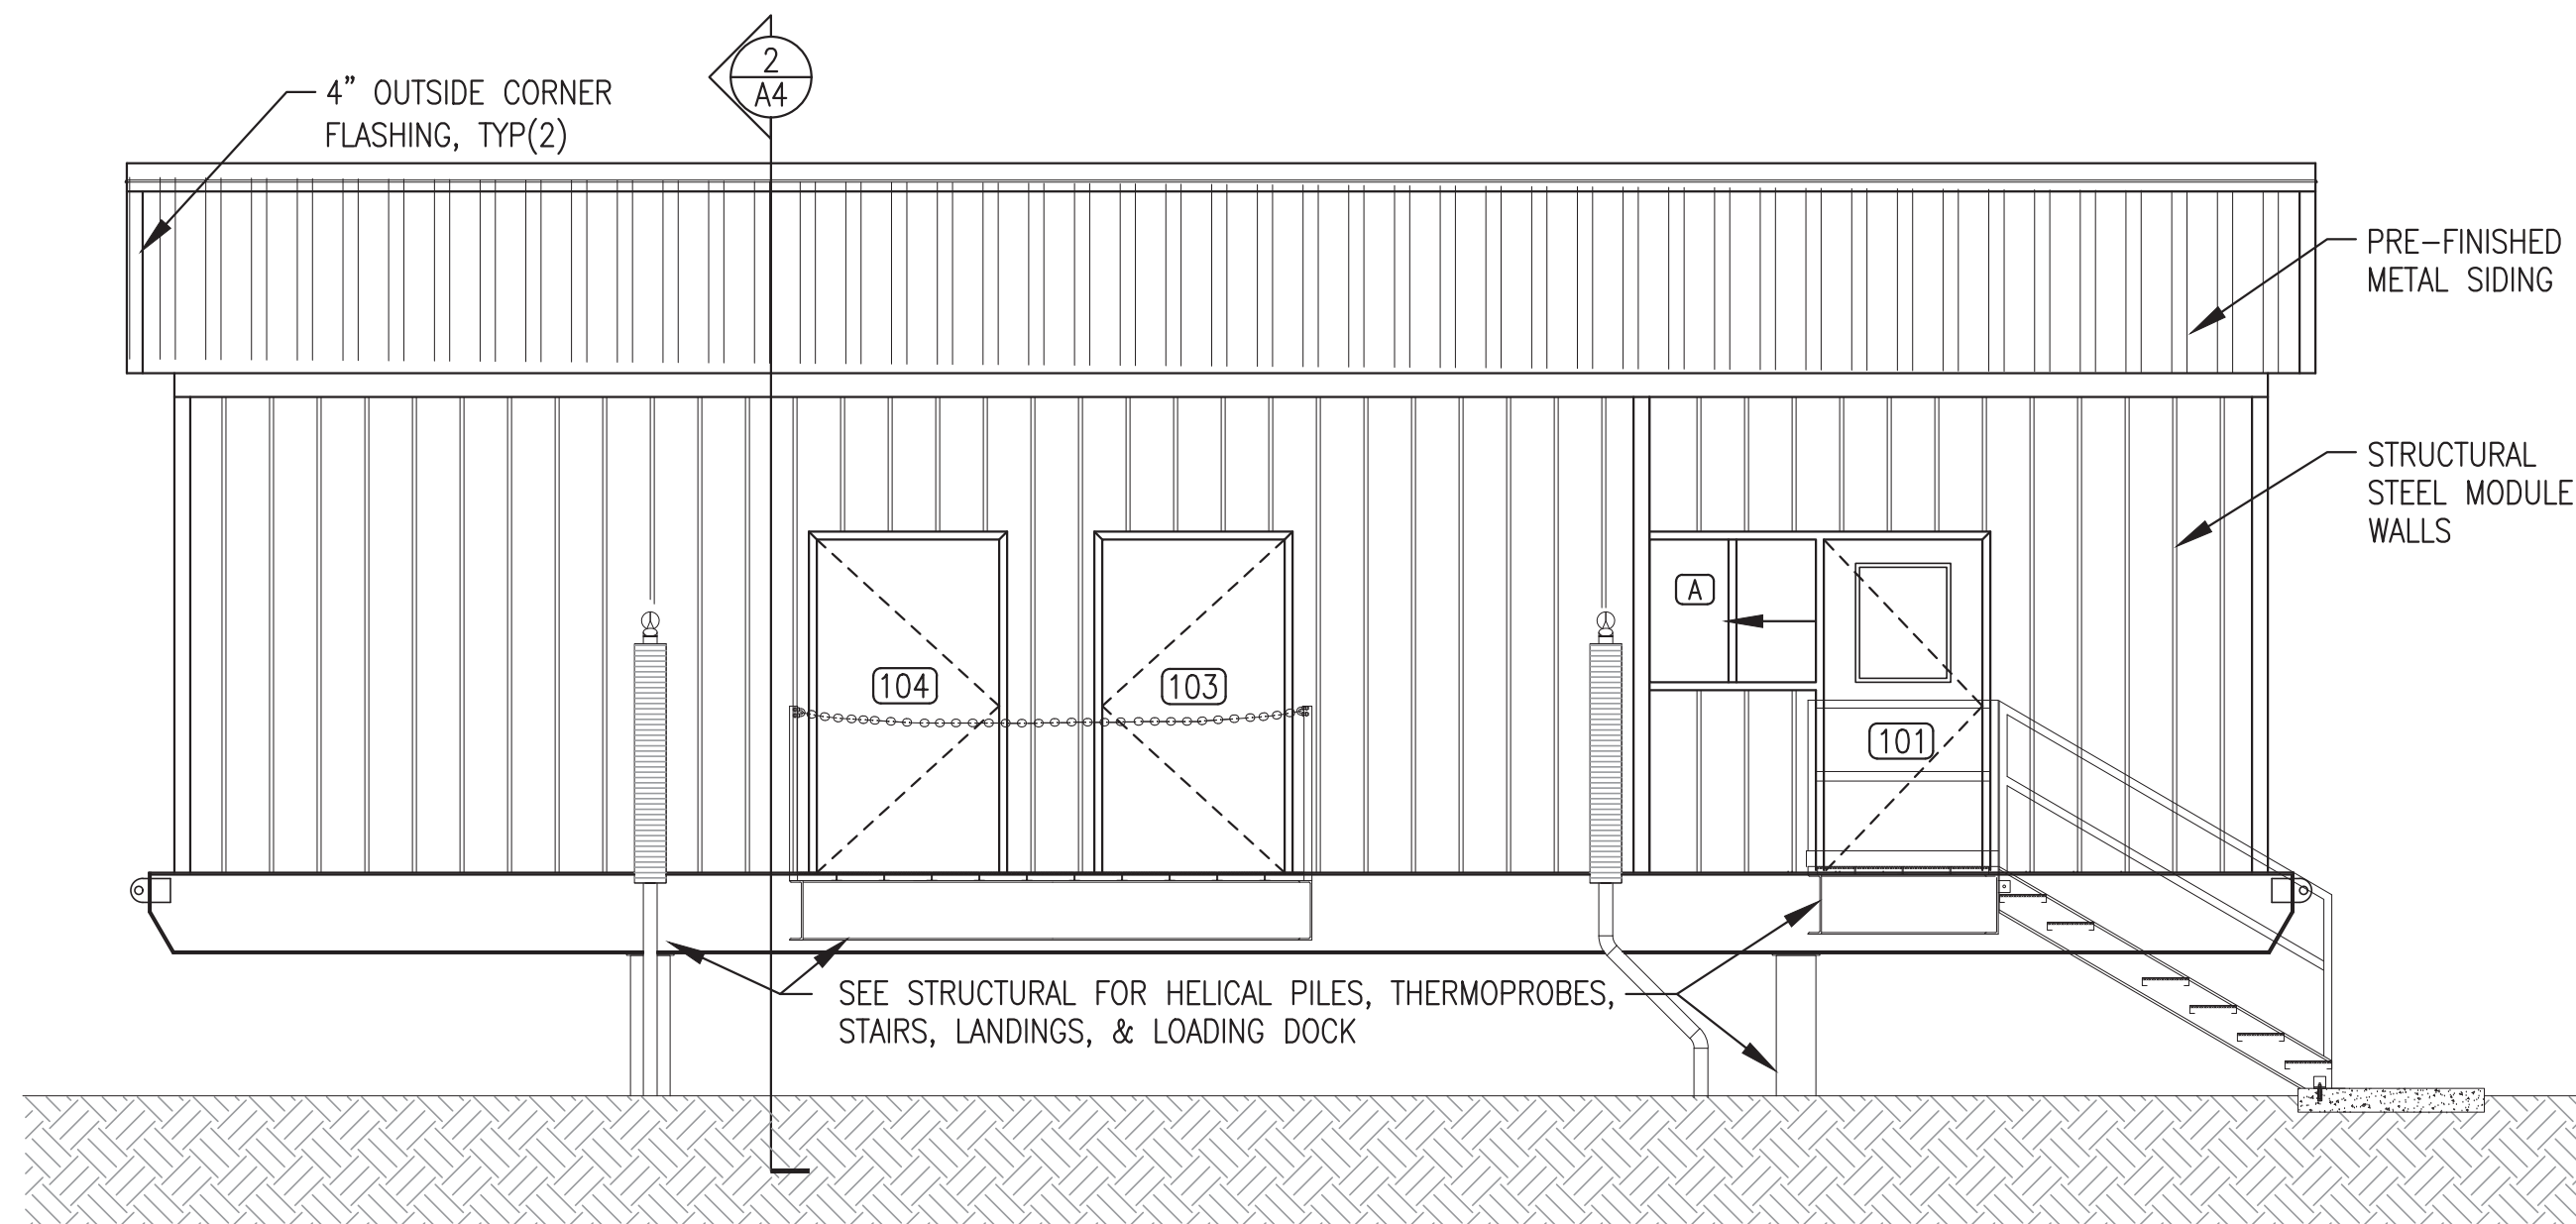

1 FRONT EXTERIOR ELEVATION  
1/4"=1'-0"

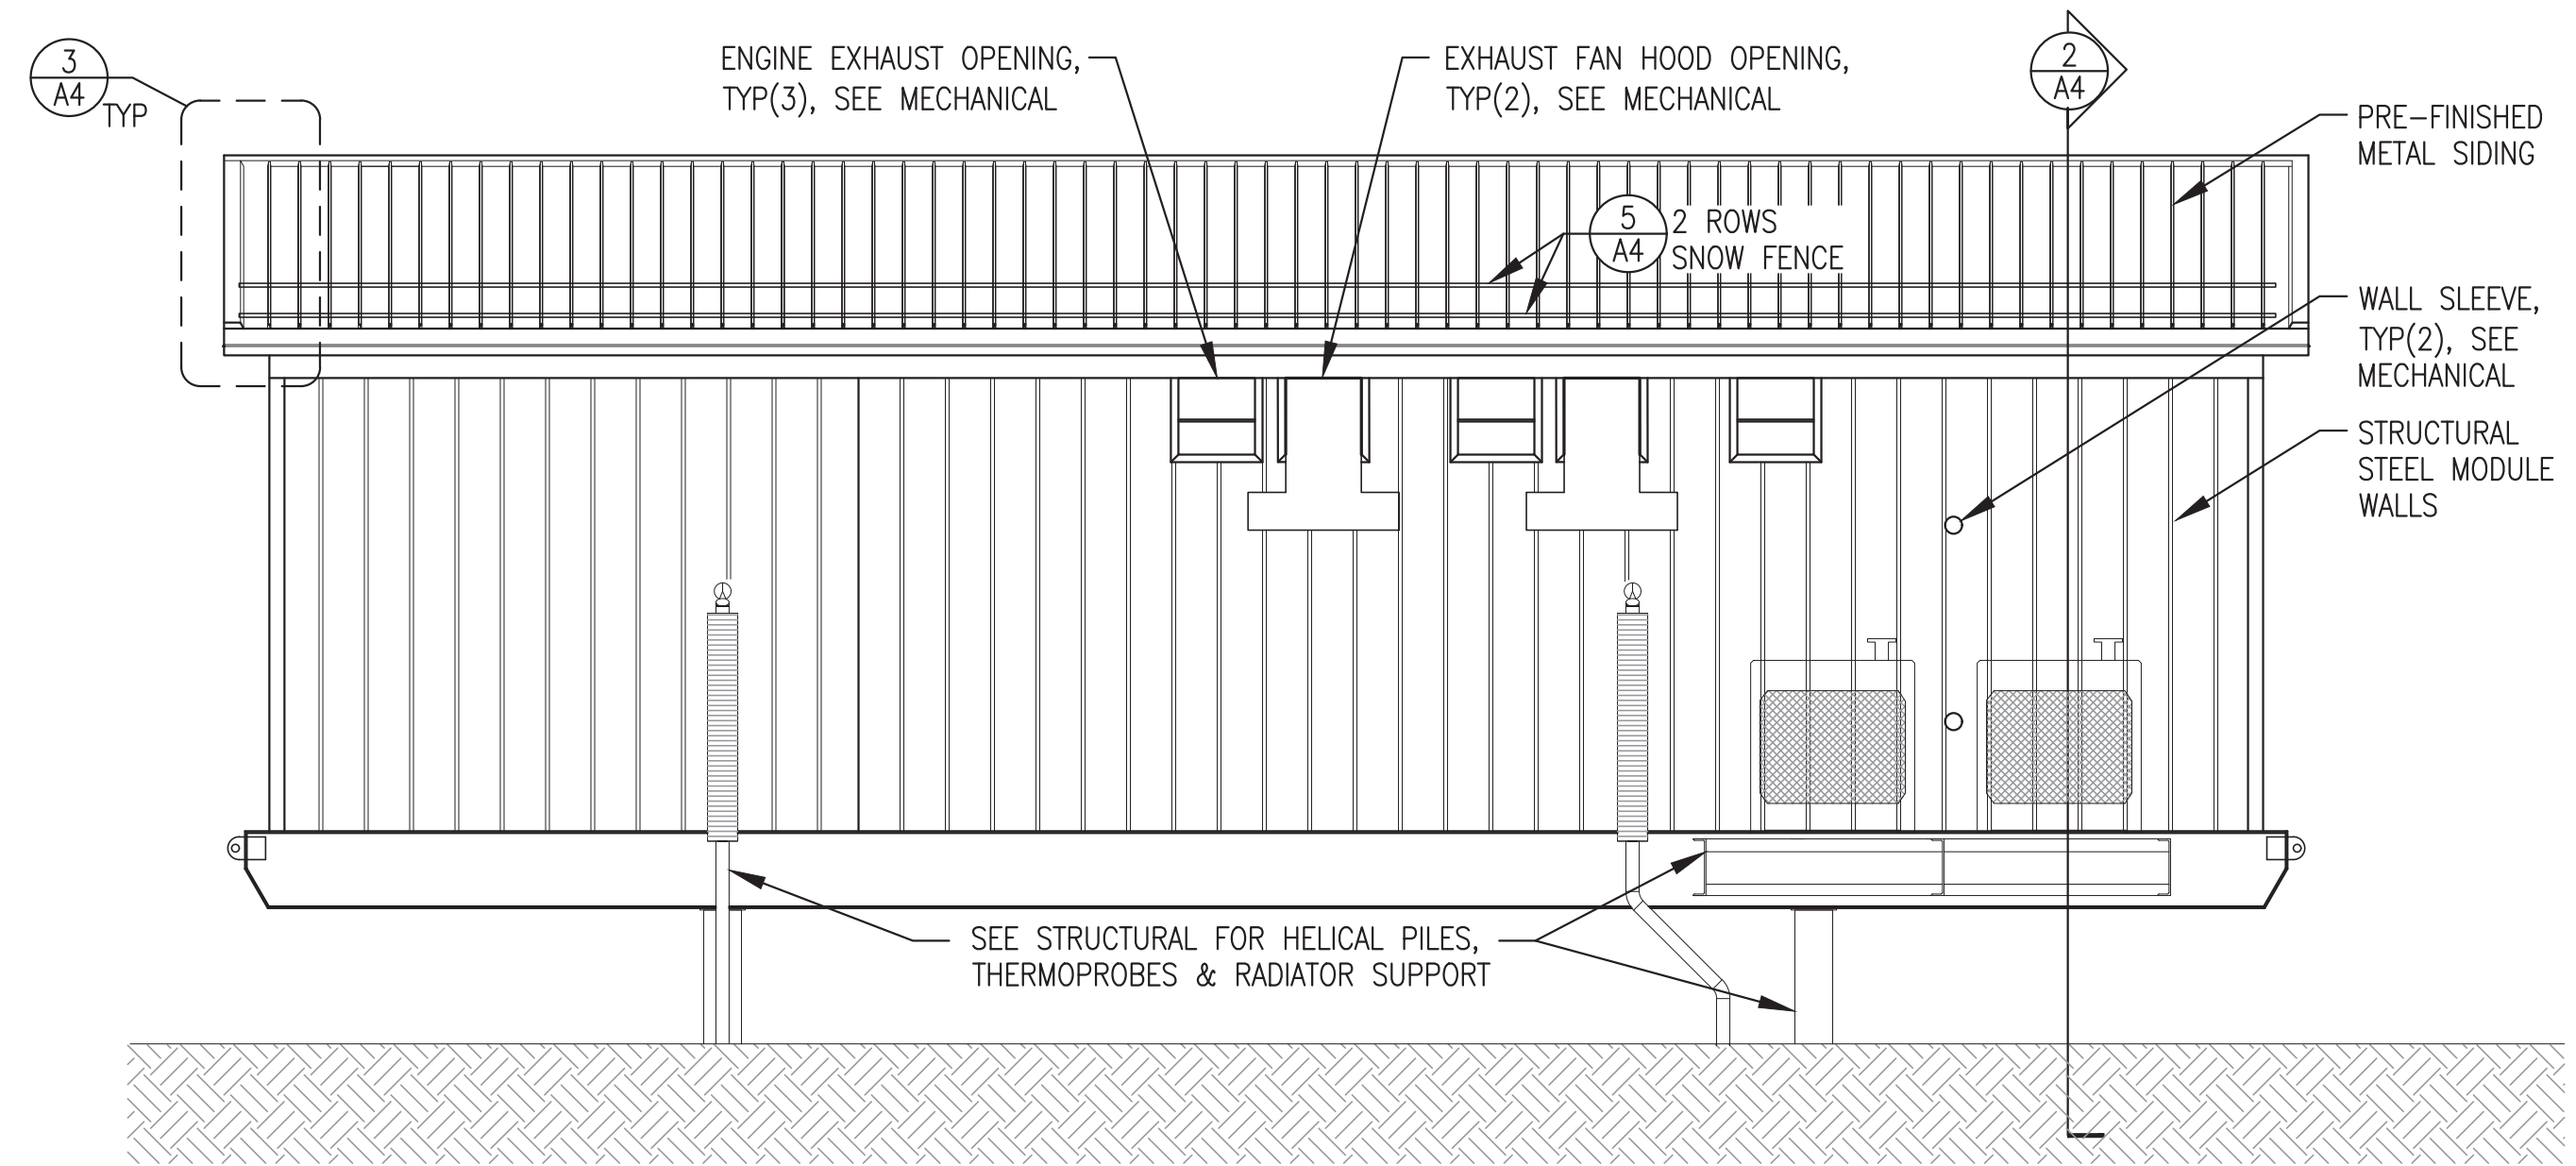

2 BACK EXTERIOR ELEVATION  
1/4"=1'-0"

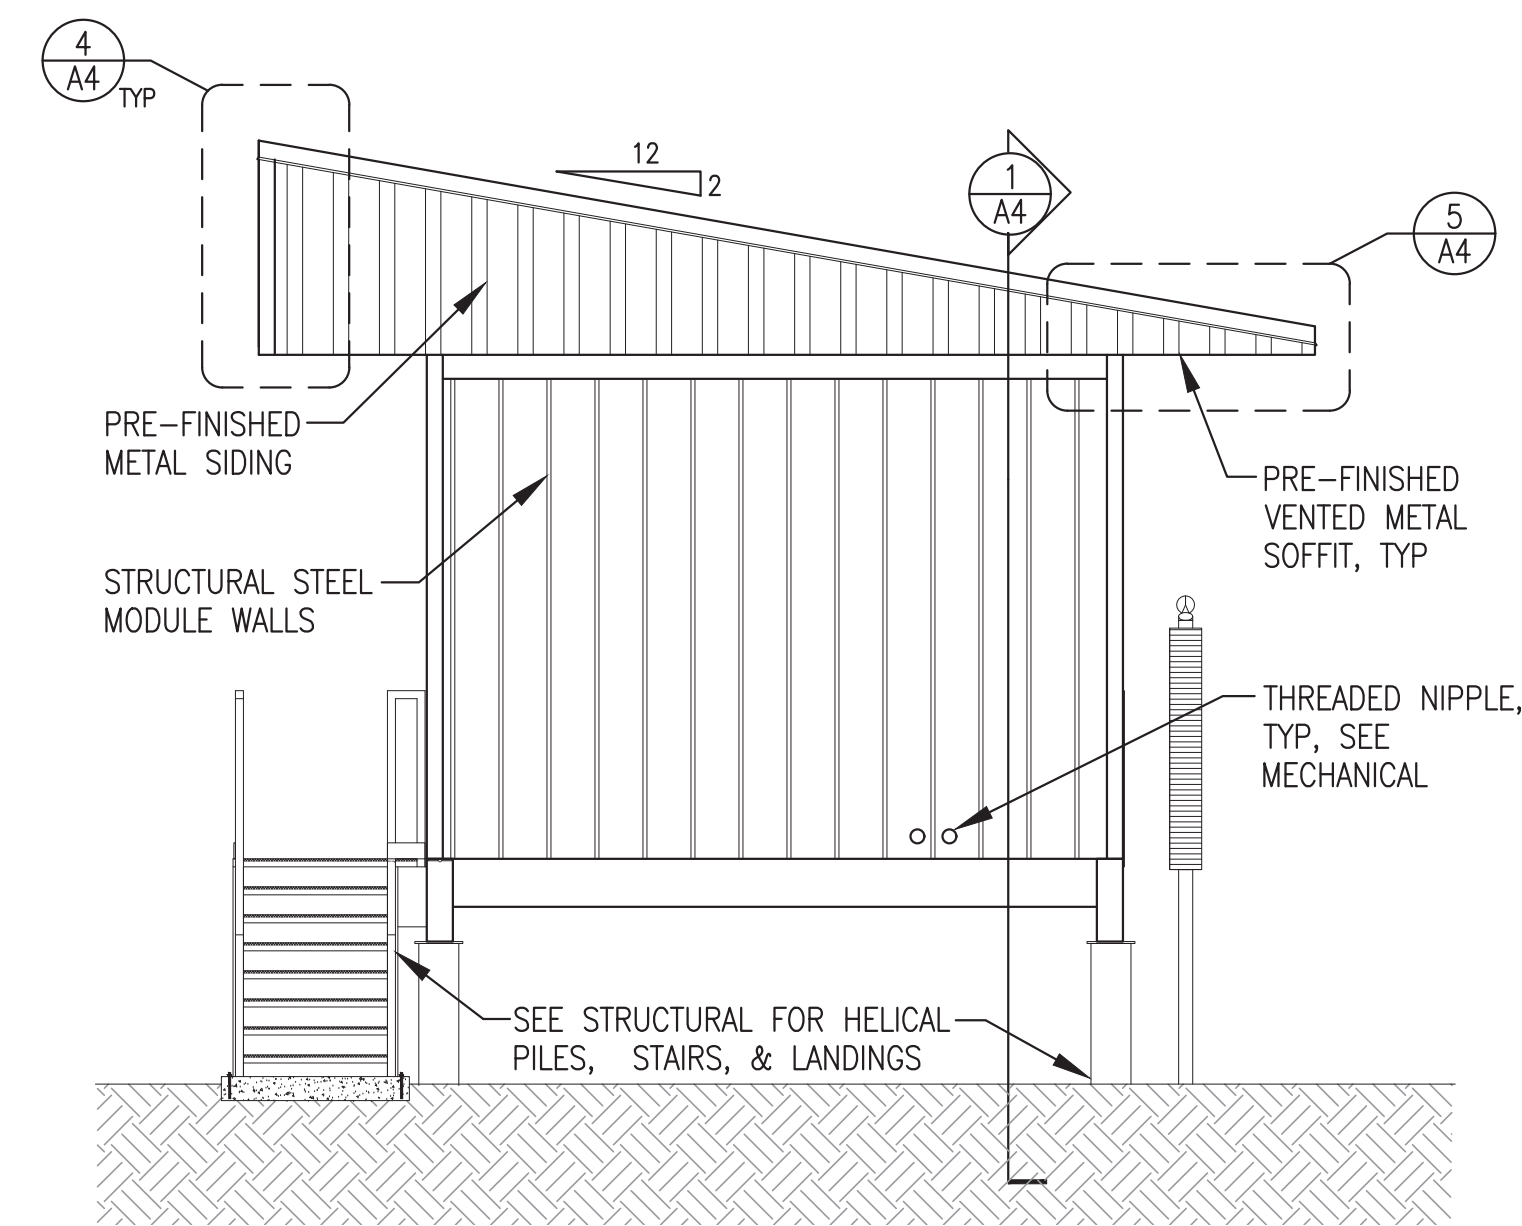


3 END EXTERIOR ELEVATION  
1/4"=1'-0"

ROOFING SYSTEM NOTES:

- 1) FIELD INSTALL TRUSSES TO MODULE STRUCTURE. FIELD INSTALL PLYWOOD SHEATHING, ICE AND WATER SHIELD, AND METAL ROOFING/SIDING AS INDICATED. SEAL AND FLASH ALL SEAMS TO FORM A CONTINUOUS WEATHERPROOF SEAL.
- 2) ALL ROOFING, SIDING, SOFFIT, TRIM, AND FLASHING SHALL BE MIN 24 GAUGE GALVANIZED STEEL WITH KYNAR FINISH, COLOR COLOR COLONIAL RED. ALL FASTENERS SHALL BE CORROSION RESISTANT COATED SCREWS AND RIVETS.
- 3) ROOFING SHALL BE MECHANICAL STANDING SEAM TYPE, 24 GAUGE, 16" NET COVERAGE, 2" HIGH RIBS AT 16" O.C. WITH TWO PENCIL RIBS BETWEEN. AEP SPAN SPAN LOK HP OR EQUAL. FURNISH CLIPS AND FASTENERS AS REQUIRED TO MEET LOAD CONDITIONS INDICATED ON SHEET S1.
- 4) SIDING SHALL BE LOW PROFILE, 24 GAUGE, 36" NET COVERAGE, 1-1/4" HIGH MAJOR RIBS AND 1/4" HIGH MINOR RIBS AT 12" O.C. AEP SPAN SUPER-SPAN OR EQUAL. FURNISH FASTENERS AS REQUIRED TO MEET LOAD CONDITIONS INDICATED ON SHEET S1.1.
- 5) VENTED SOFFIT PANELS SHALL BE 24 GAUGE GALVANIZED STEEL, 12" NET COVERAGE, KYNAR FINISH, 1" STANDOFF FROM SUBSTRATE, CONCEALED FASTENERS, WITH TWO PENCIL RIBS PROVIDING MINIMUM 7.8% NET FREE AREA. AEP SPAN FLUSH PANEL OR EQUAL.
- 6) SEE SHEET A4 FOR ROOF MOUNTED SNOW FENCE.

ROOFING SYSTEM TRIM & FLASHING:

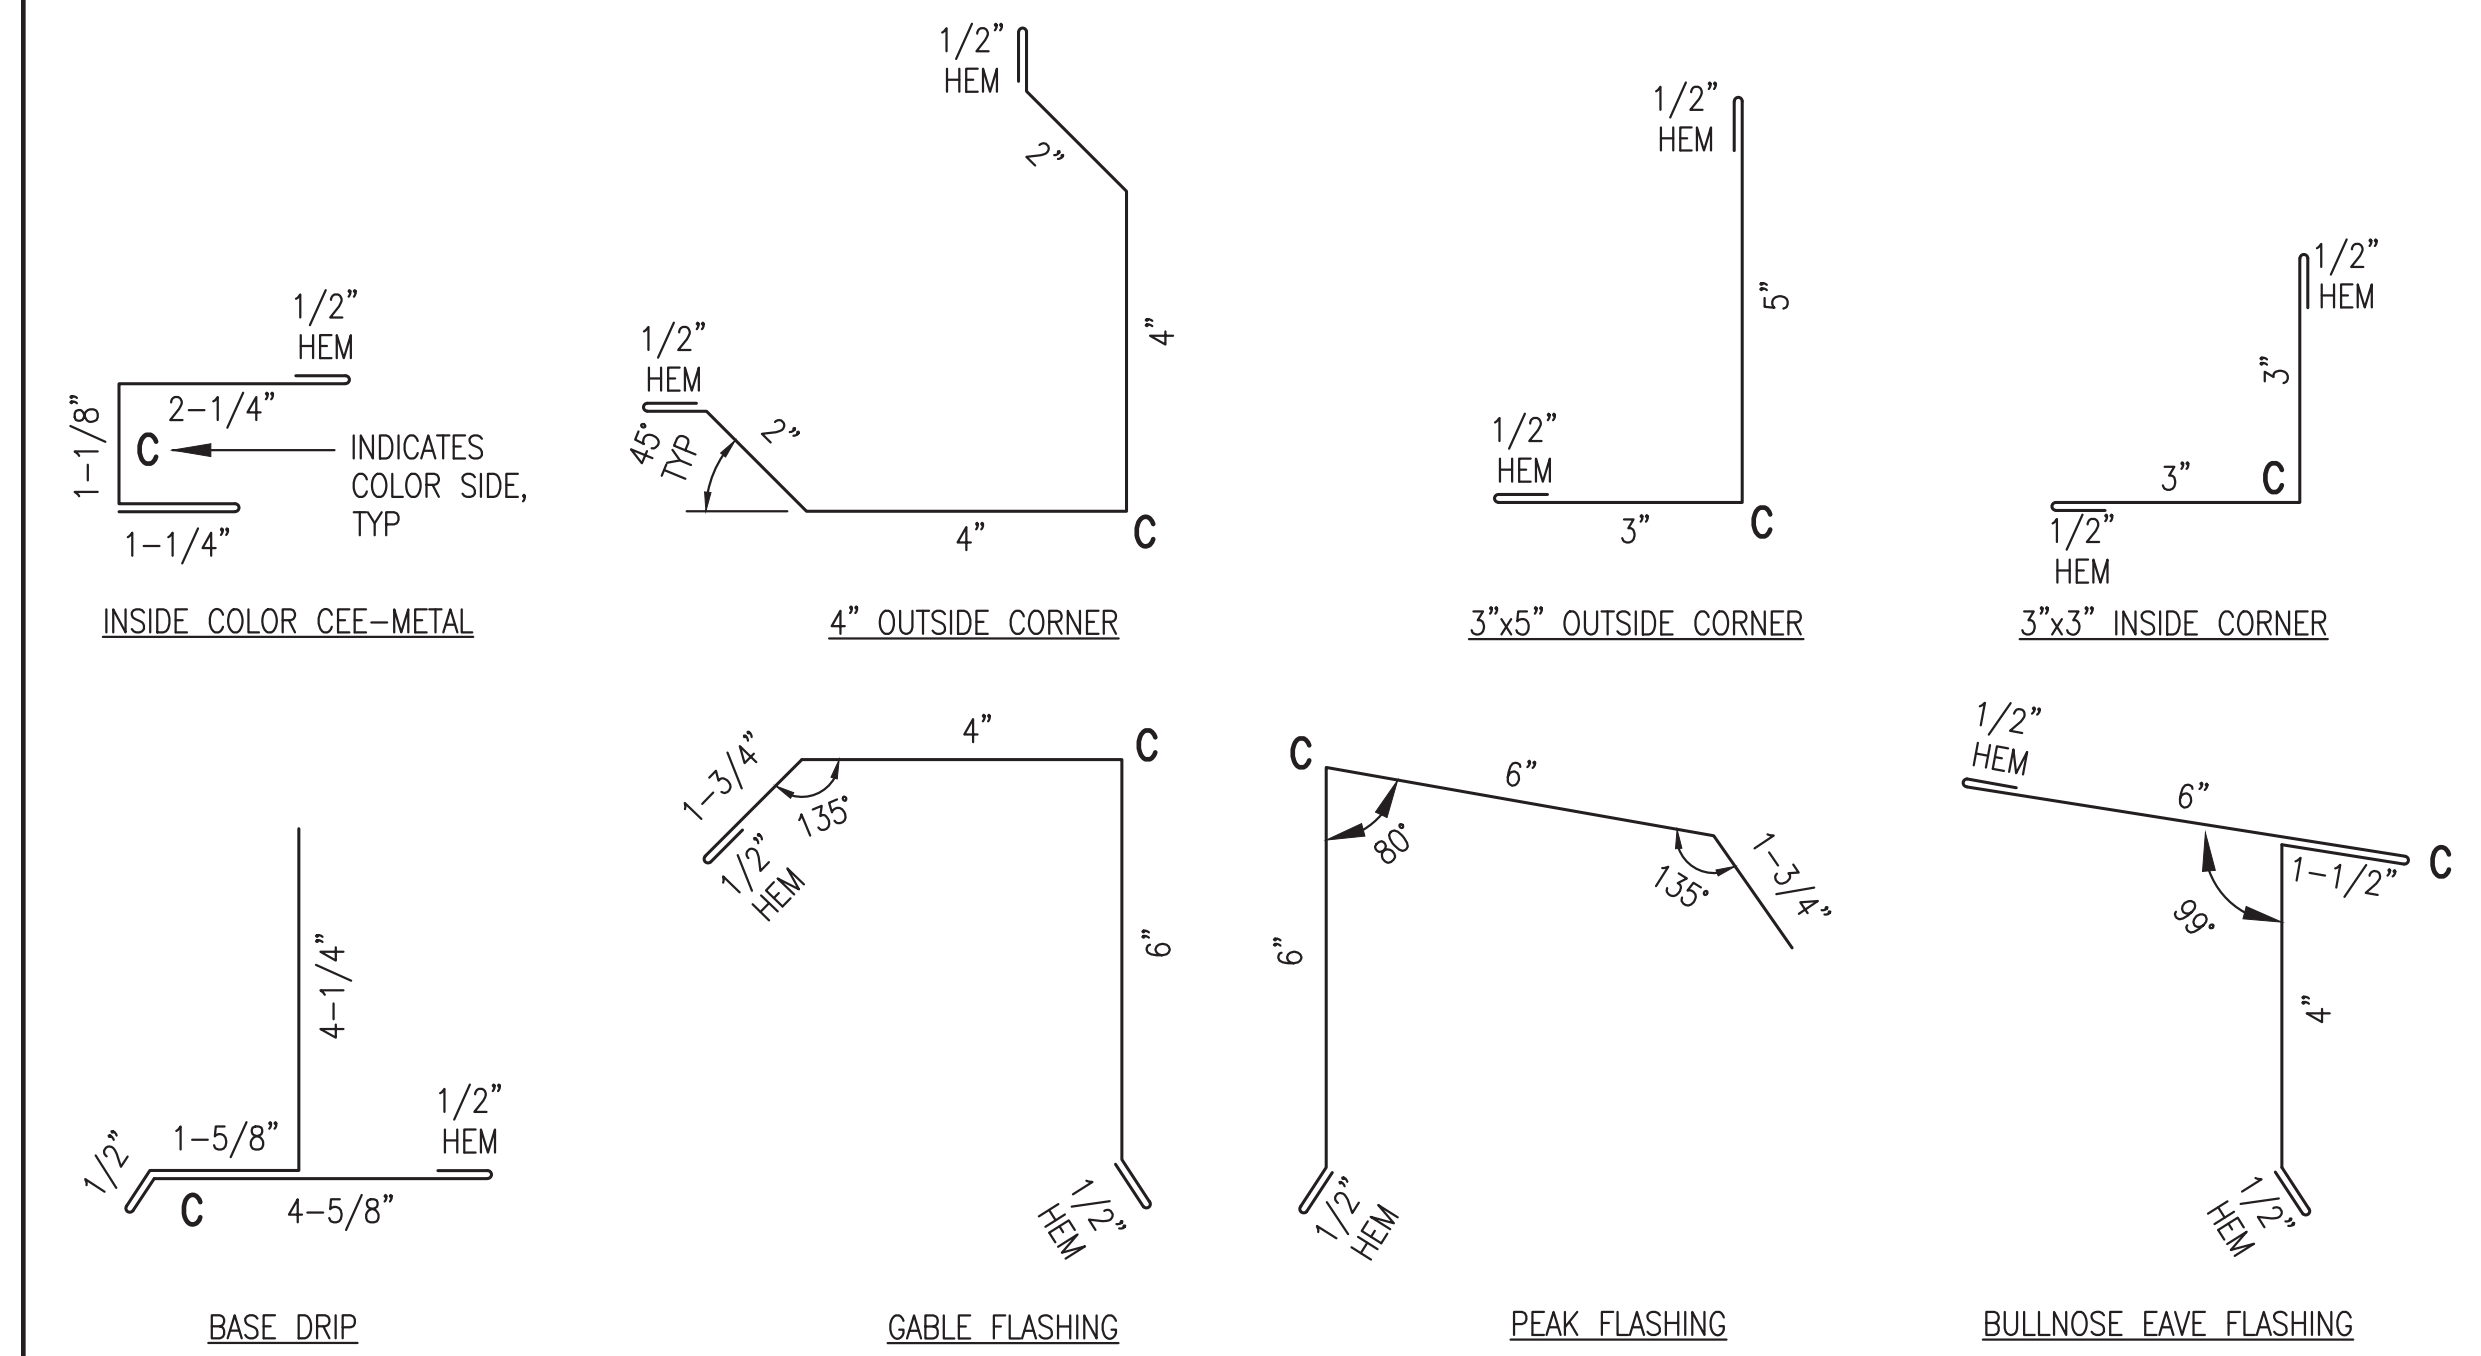


THIS DRAWING SHOWS WORK THAT WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT FOR ON SITE INSTALLATION AND IS PROVIDED HERE FOR REFERENCE ONLY.


REVISION #1  
ISSUED JULY  
2022




1	REVISED FOR ONSITE FOUNDATION DESIGN	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: EXTERIOR ELEVATIONS & ROOFING NOTES & TRIM DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: DGT/BCG		DATE: 3/15/22	
FILE NAME: RAM PP A1-A4		SHEET: A3	
PROJECT NUMBER:			

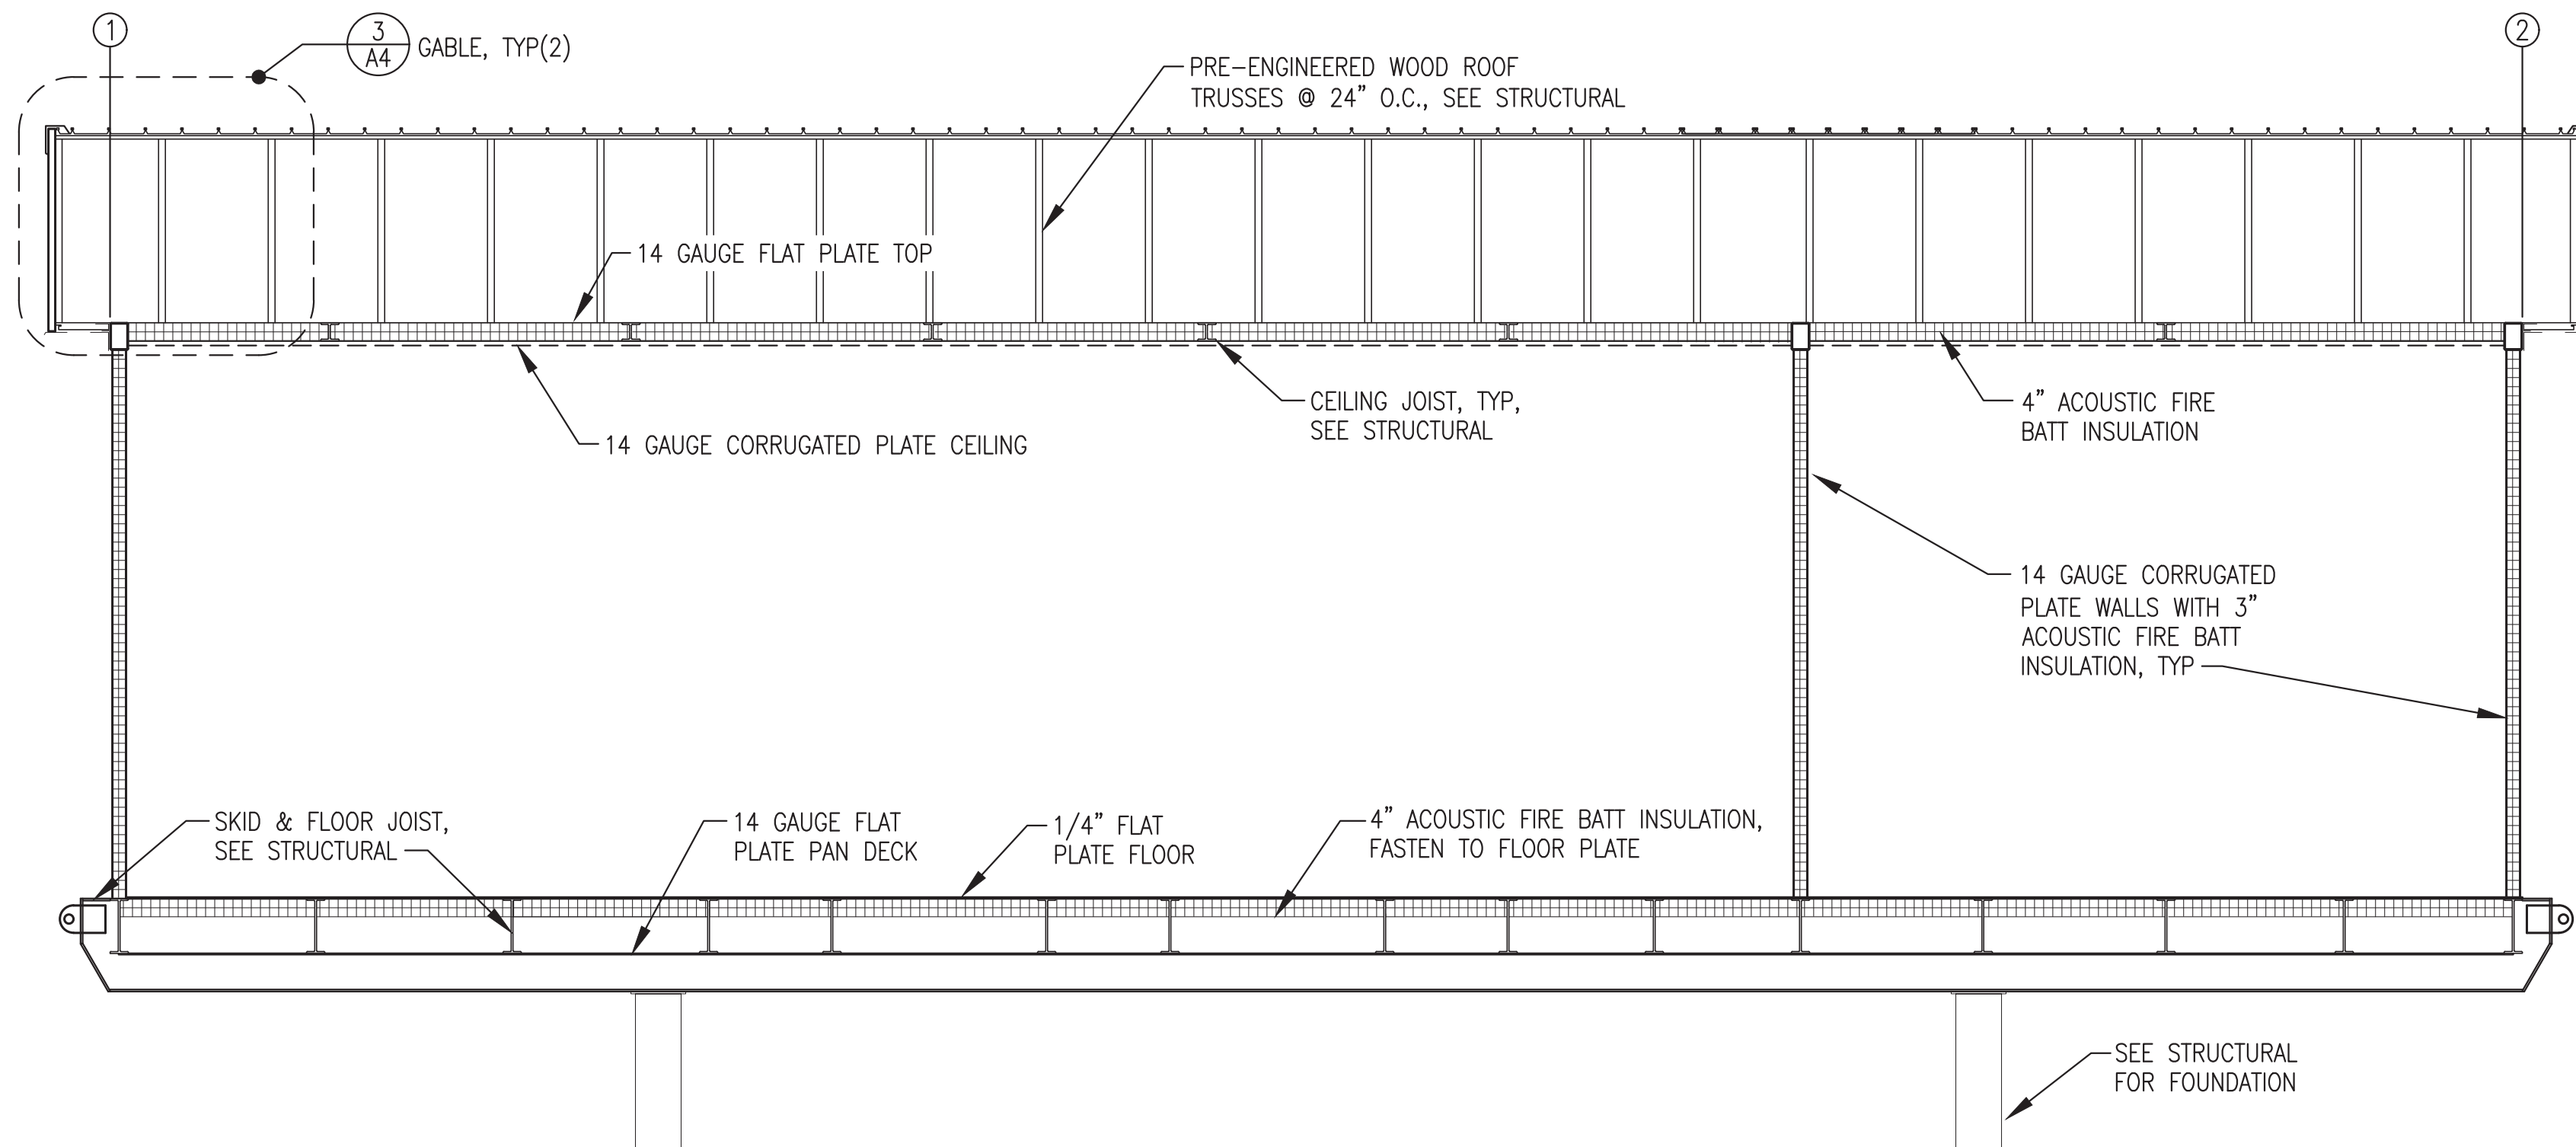


**1** BUILDING SECTION  
A4 3/8"=1'-0"

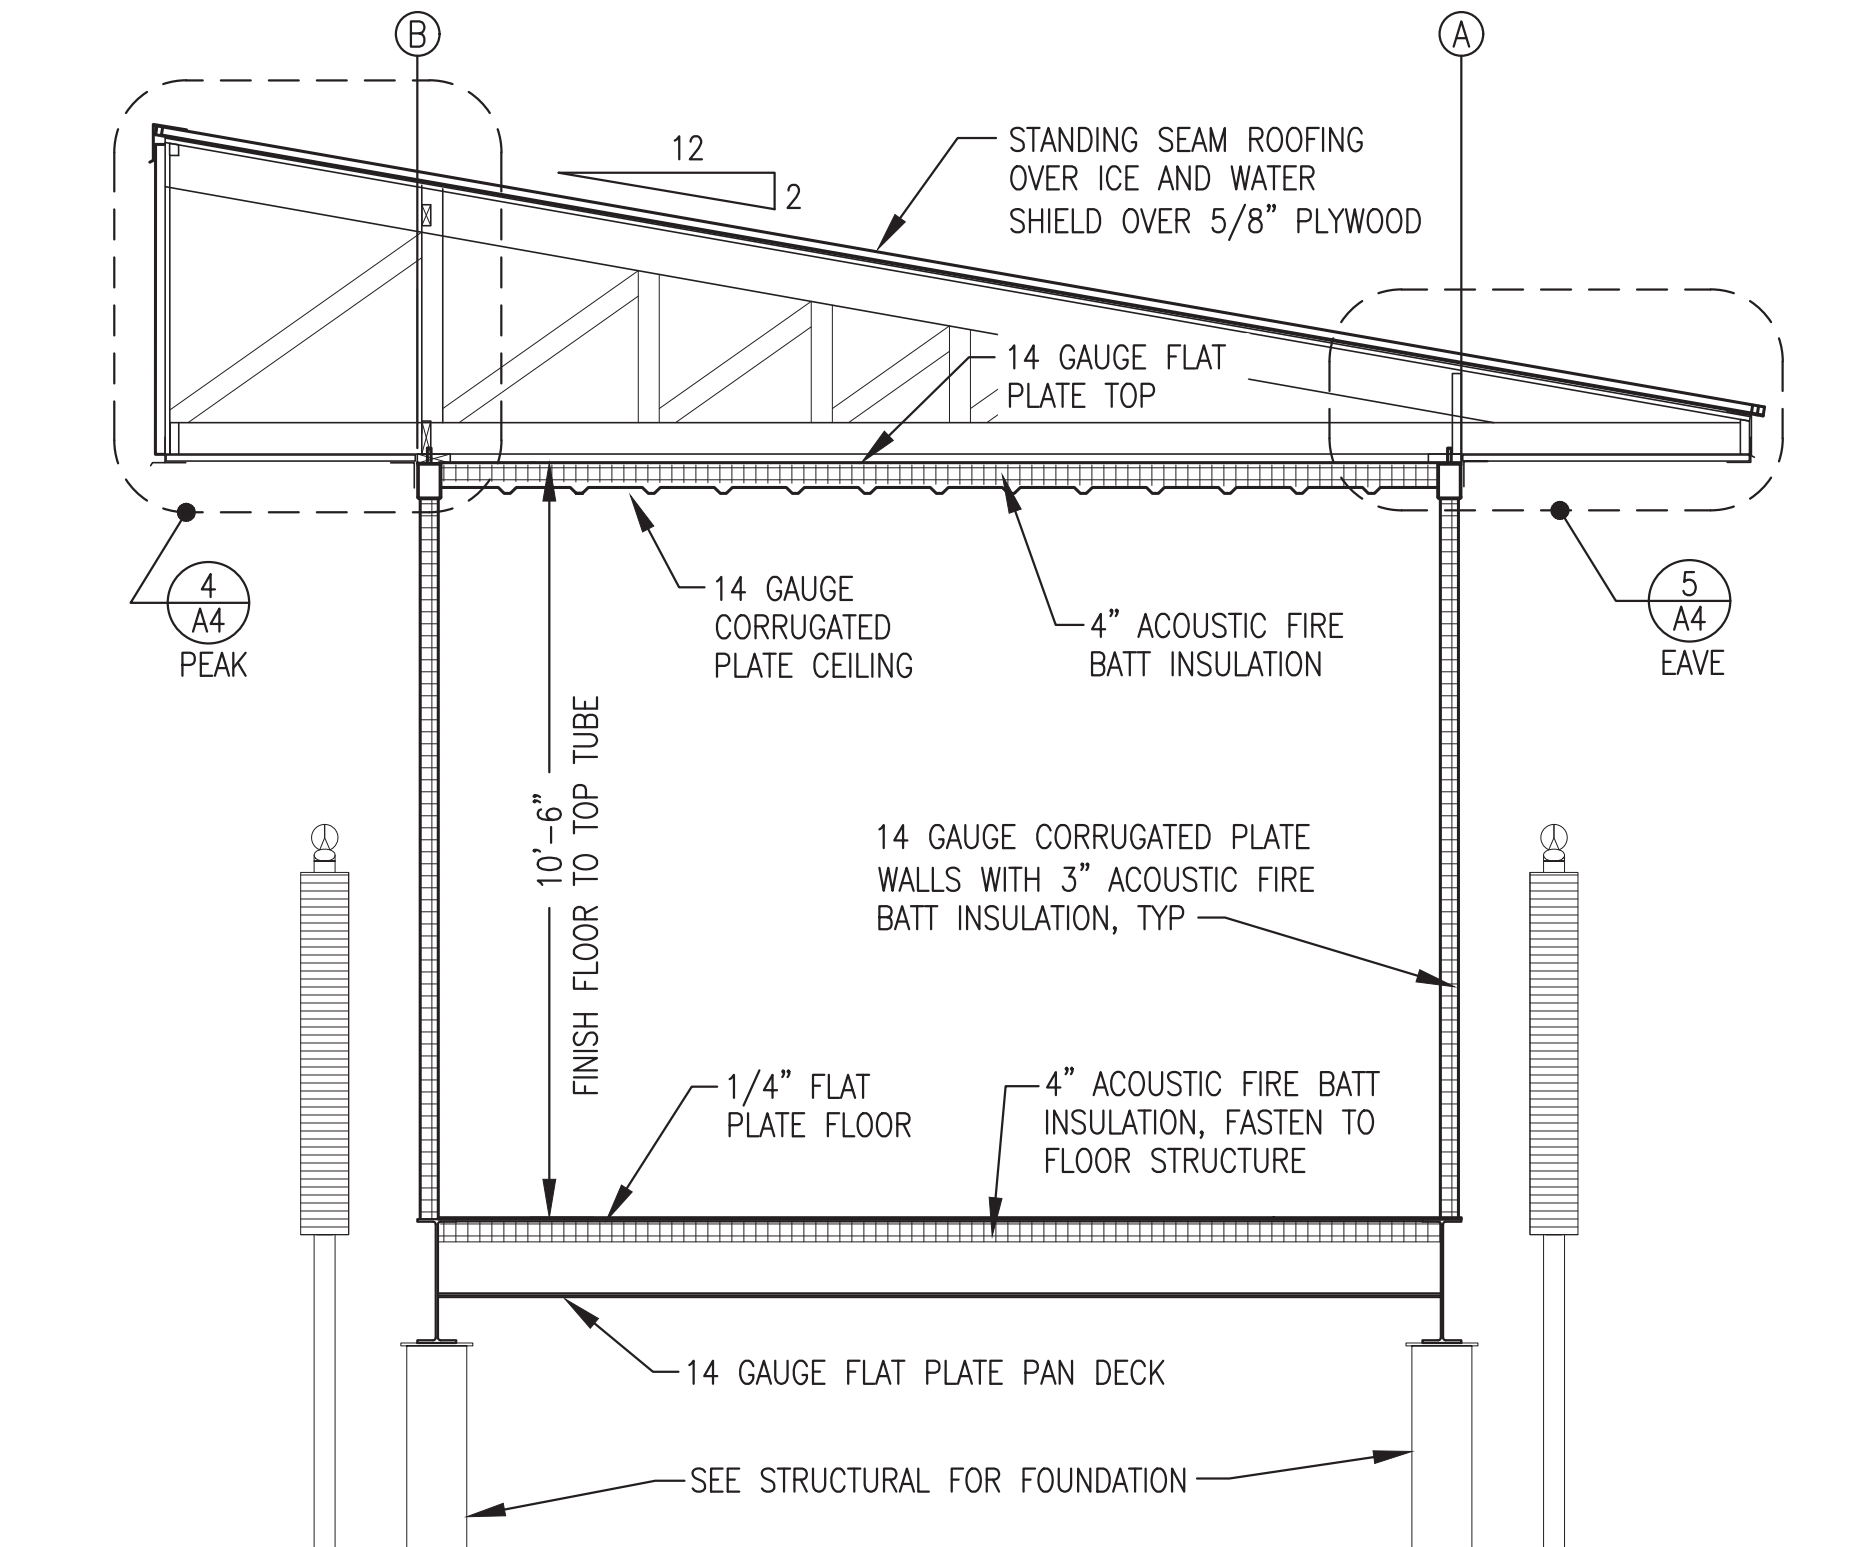


**2** BUILDING SECTION  
A4 3/8"=1'-0"

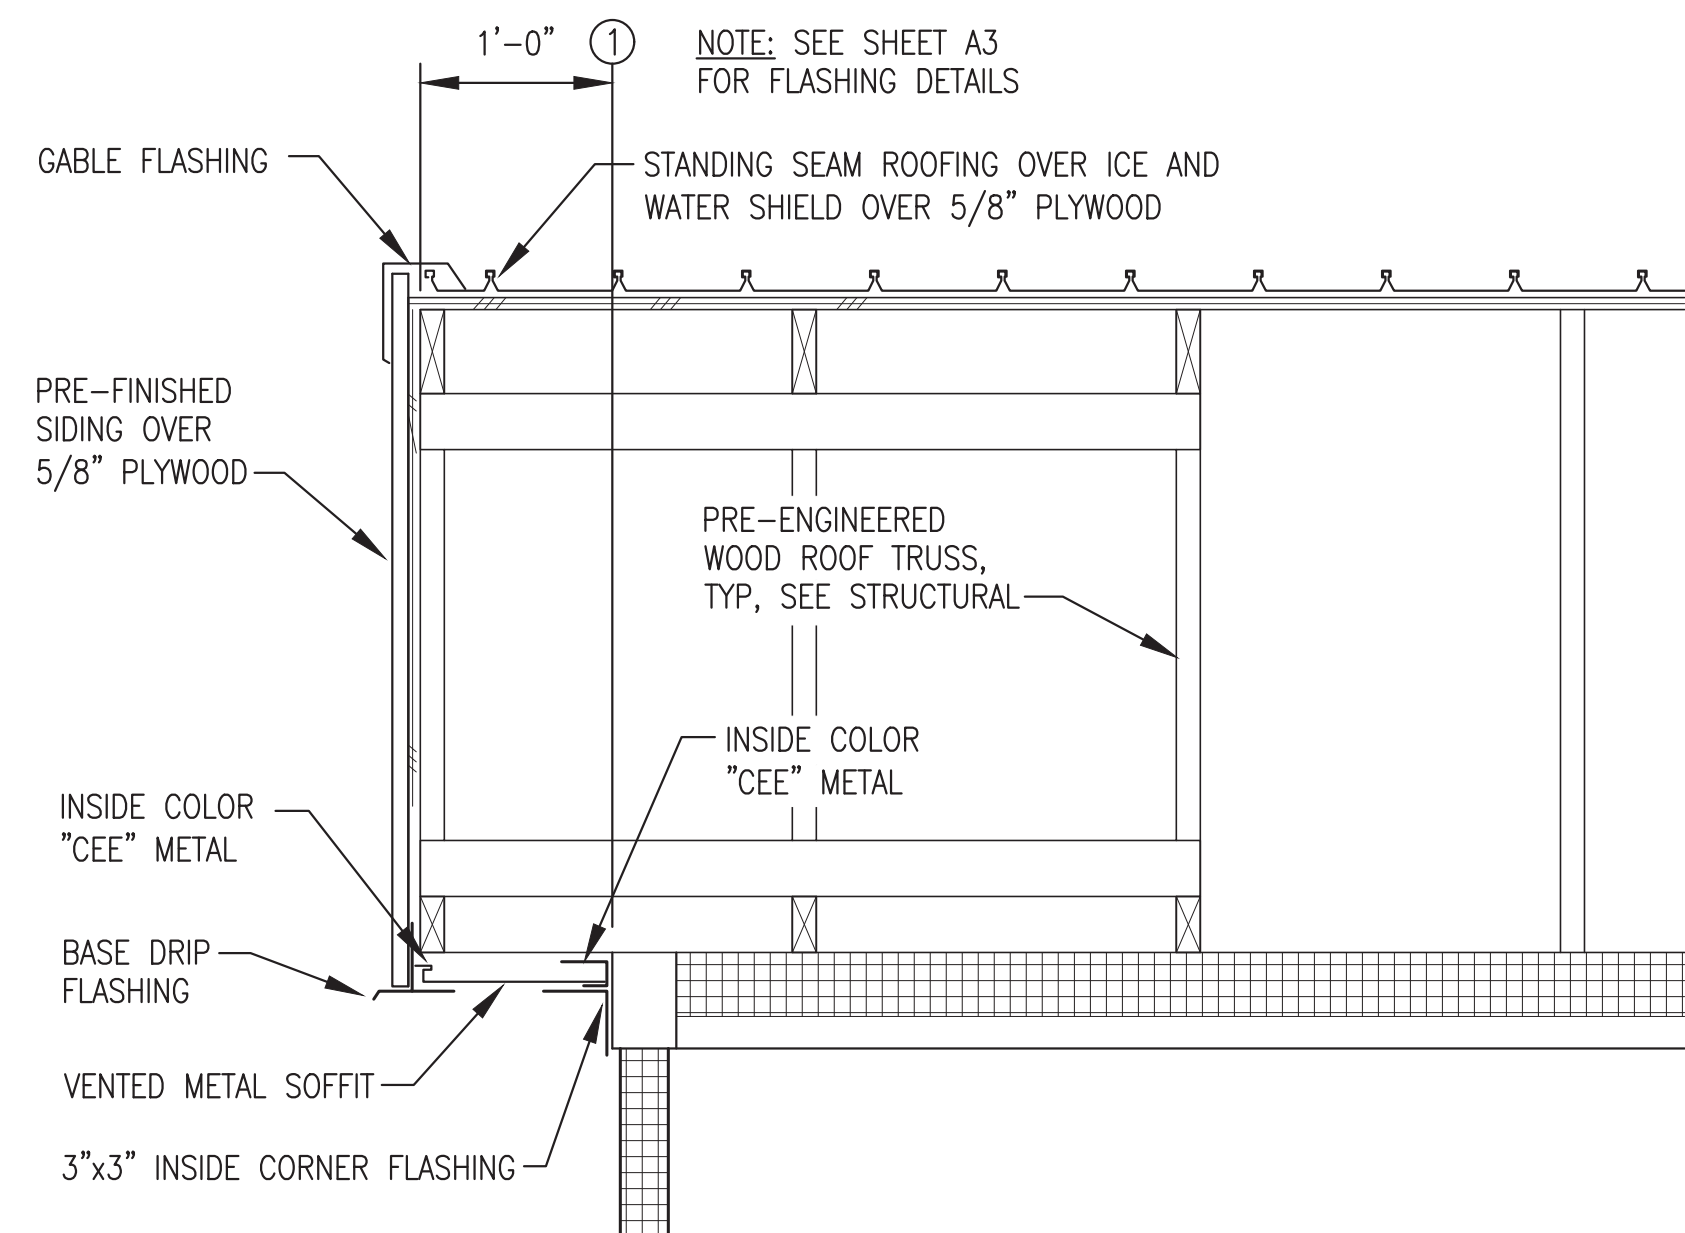

**3** GABLE DETAIL  
A4 1"=1'-0"

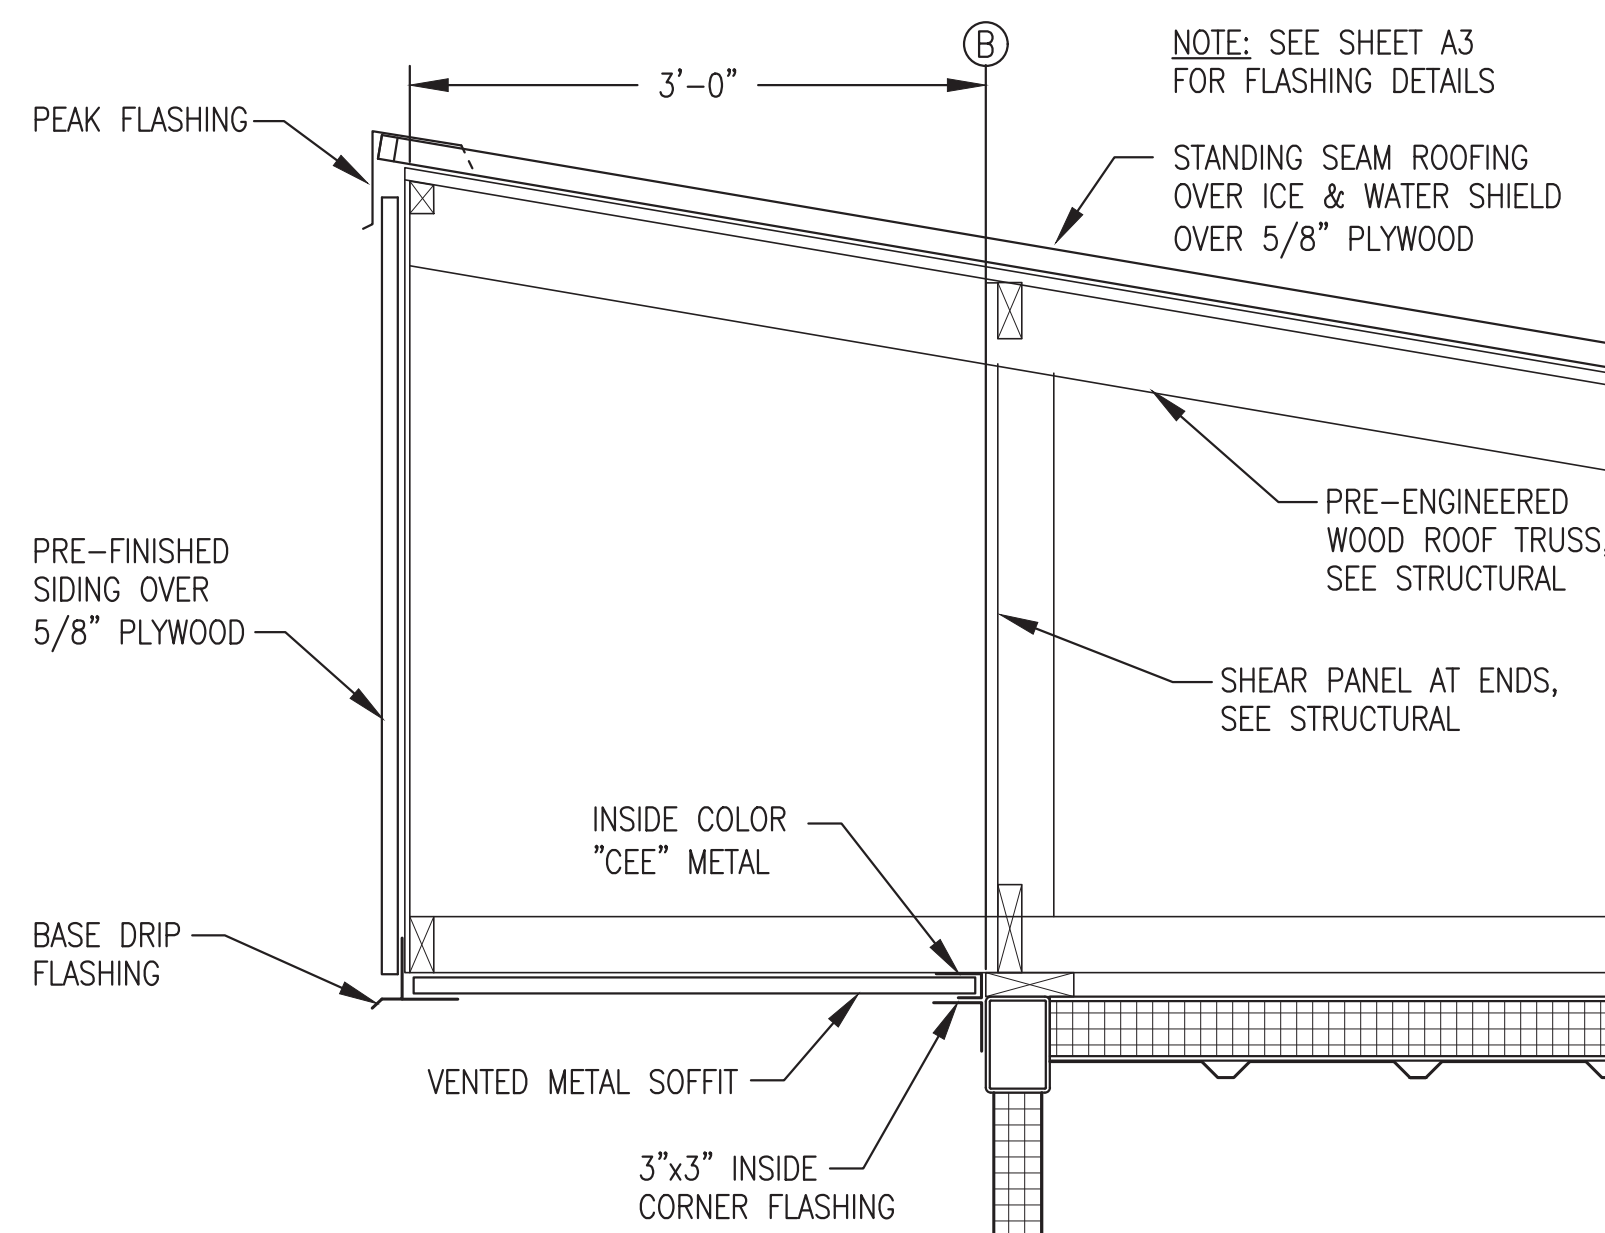

**4** PEAK DETAIL  
A4 1"=1'-0"

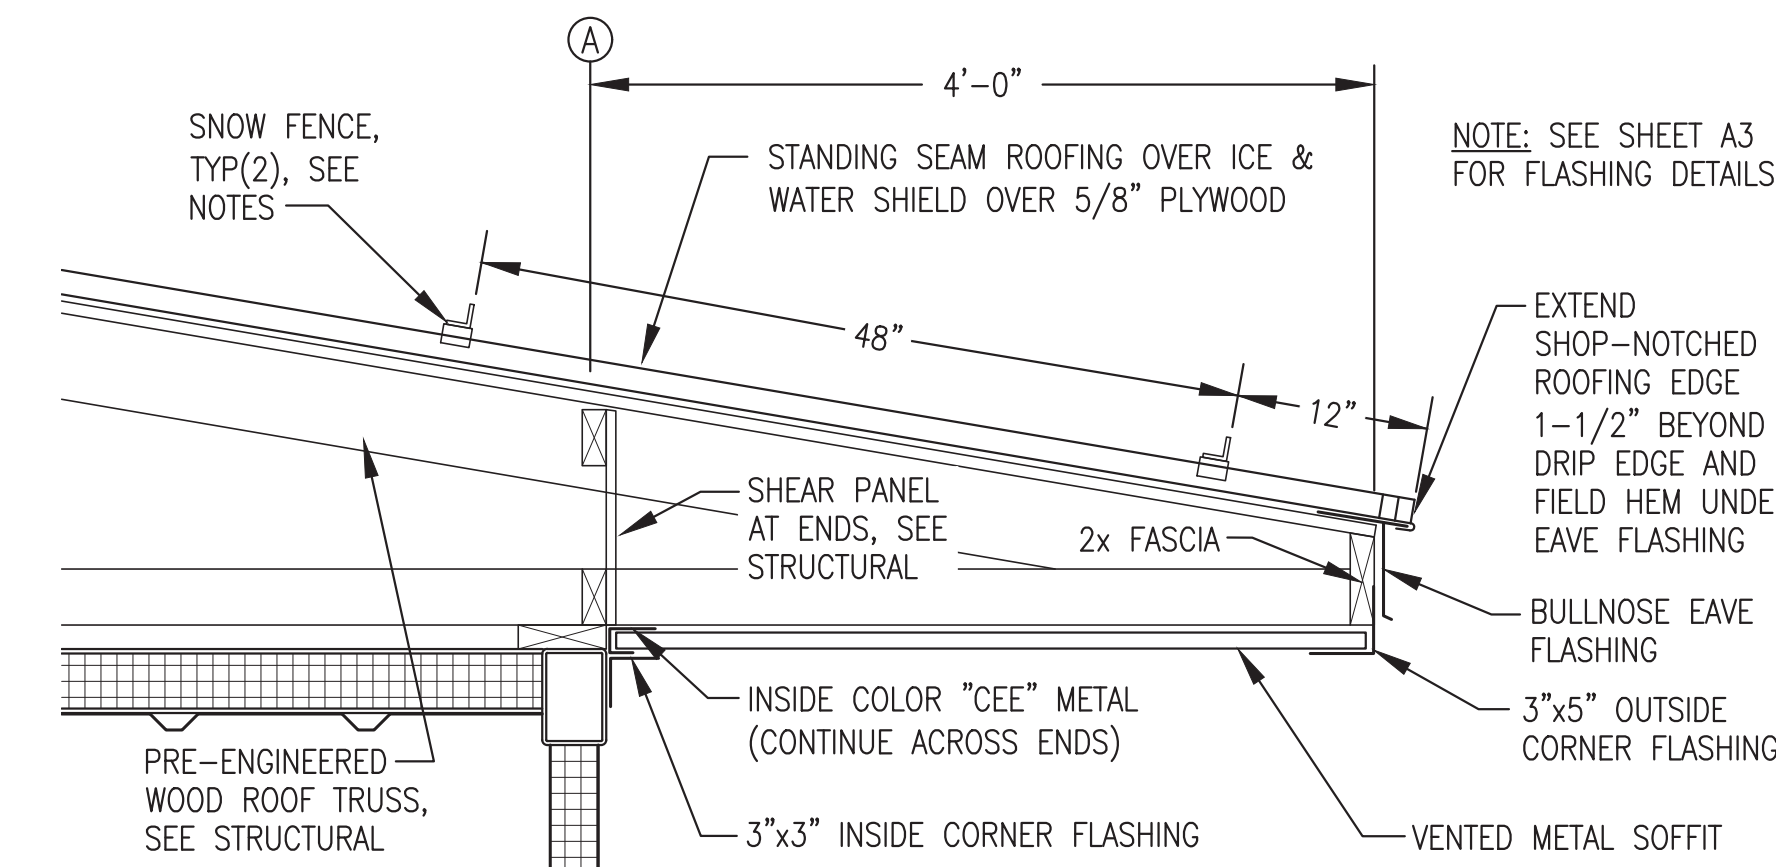

**5** EAVE DETAIL  
A4 1"=1'-0"

**SNOW FENCE NOTES:**


- 1) PROVIDE 2 ROWS OF SNOW RETENTION FENCE AS INDICATED.
- 2) SNOW FENCE SHALL BE L.M. CURBS COLOR GUARD OR APPROVED EQUAL. FURNISH COMPLETE SYSTEM INCLUDING UNPUNCHED COLOR GUARD, SPLICES, VERSA CLIPS, SNO CLIPS III, S5-U CLAMPS, AND ALL REQUIRED FASTENERS.

THIS DRAWING SHOWS WORK THAT WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT FOR ON SITE INSTALLATION AND IS PROVIDED HERE FOR REFERENCE ONLY.

REVISION #1  
ISSUED JULY  
2022



1	REVISED FOR ONSITE FOUNDATION DESIGN	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: BUILDING SECTIONS & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: DGT/BCG		DATE: 3/15/22	
FILE NAME: RAM PP A1-A4		SHEET: A4	
PROJECT NUMBER:			
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

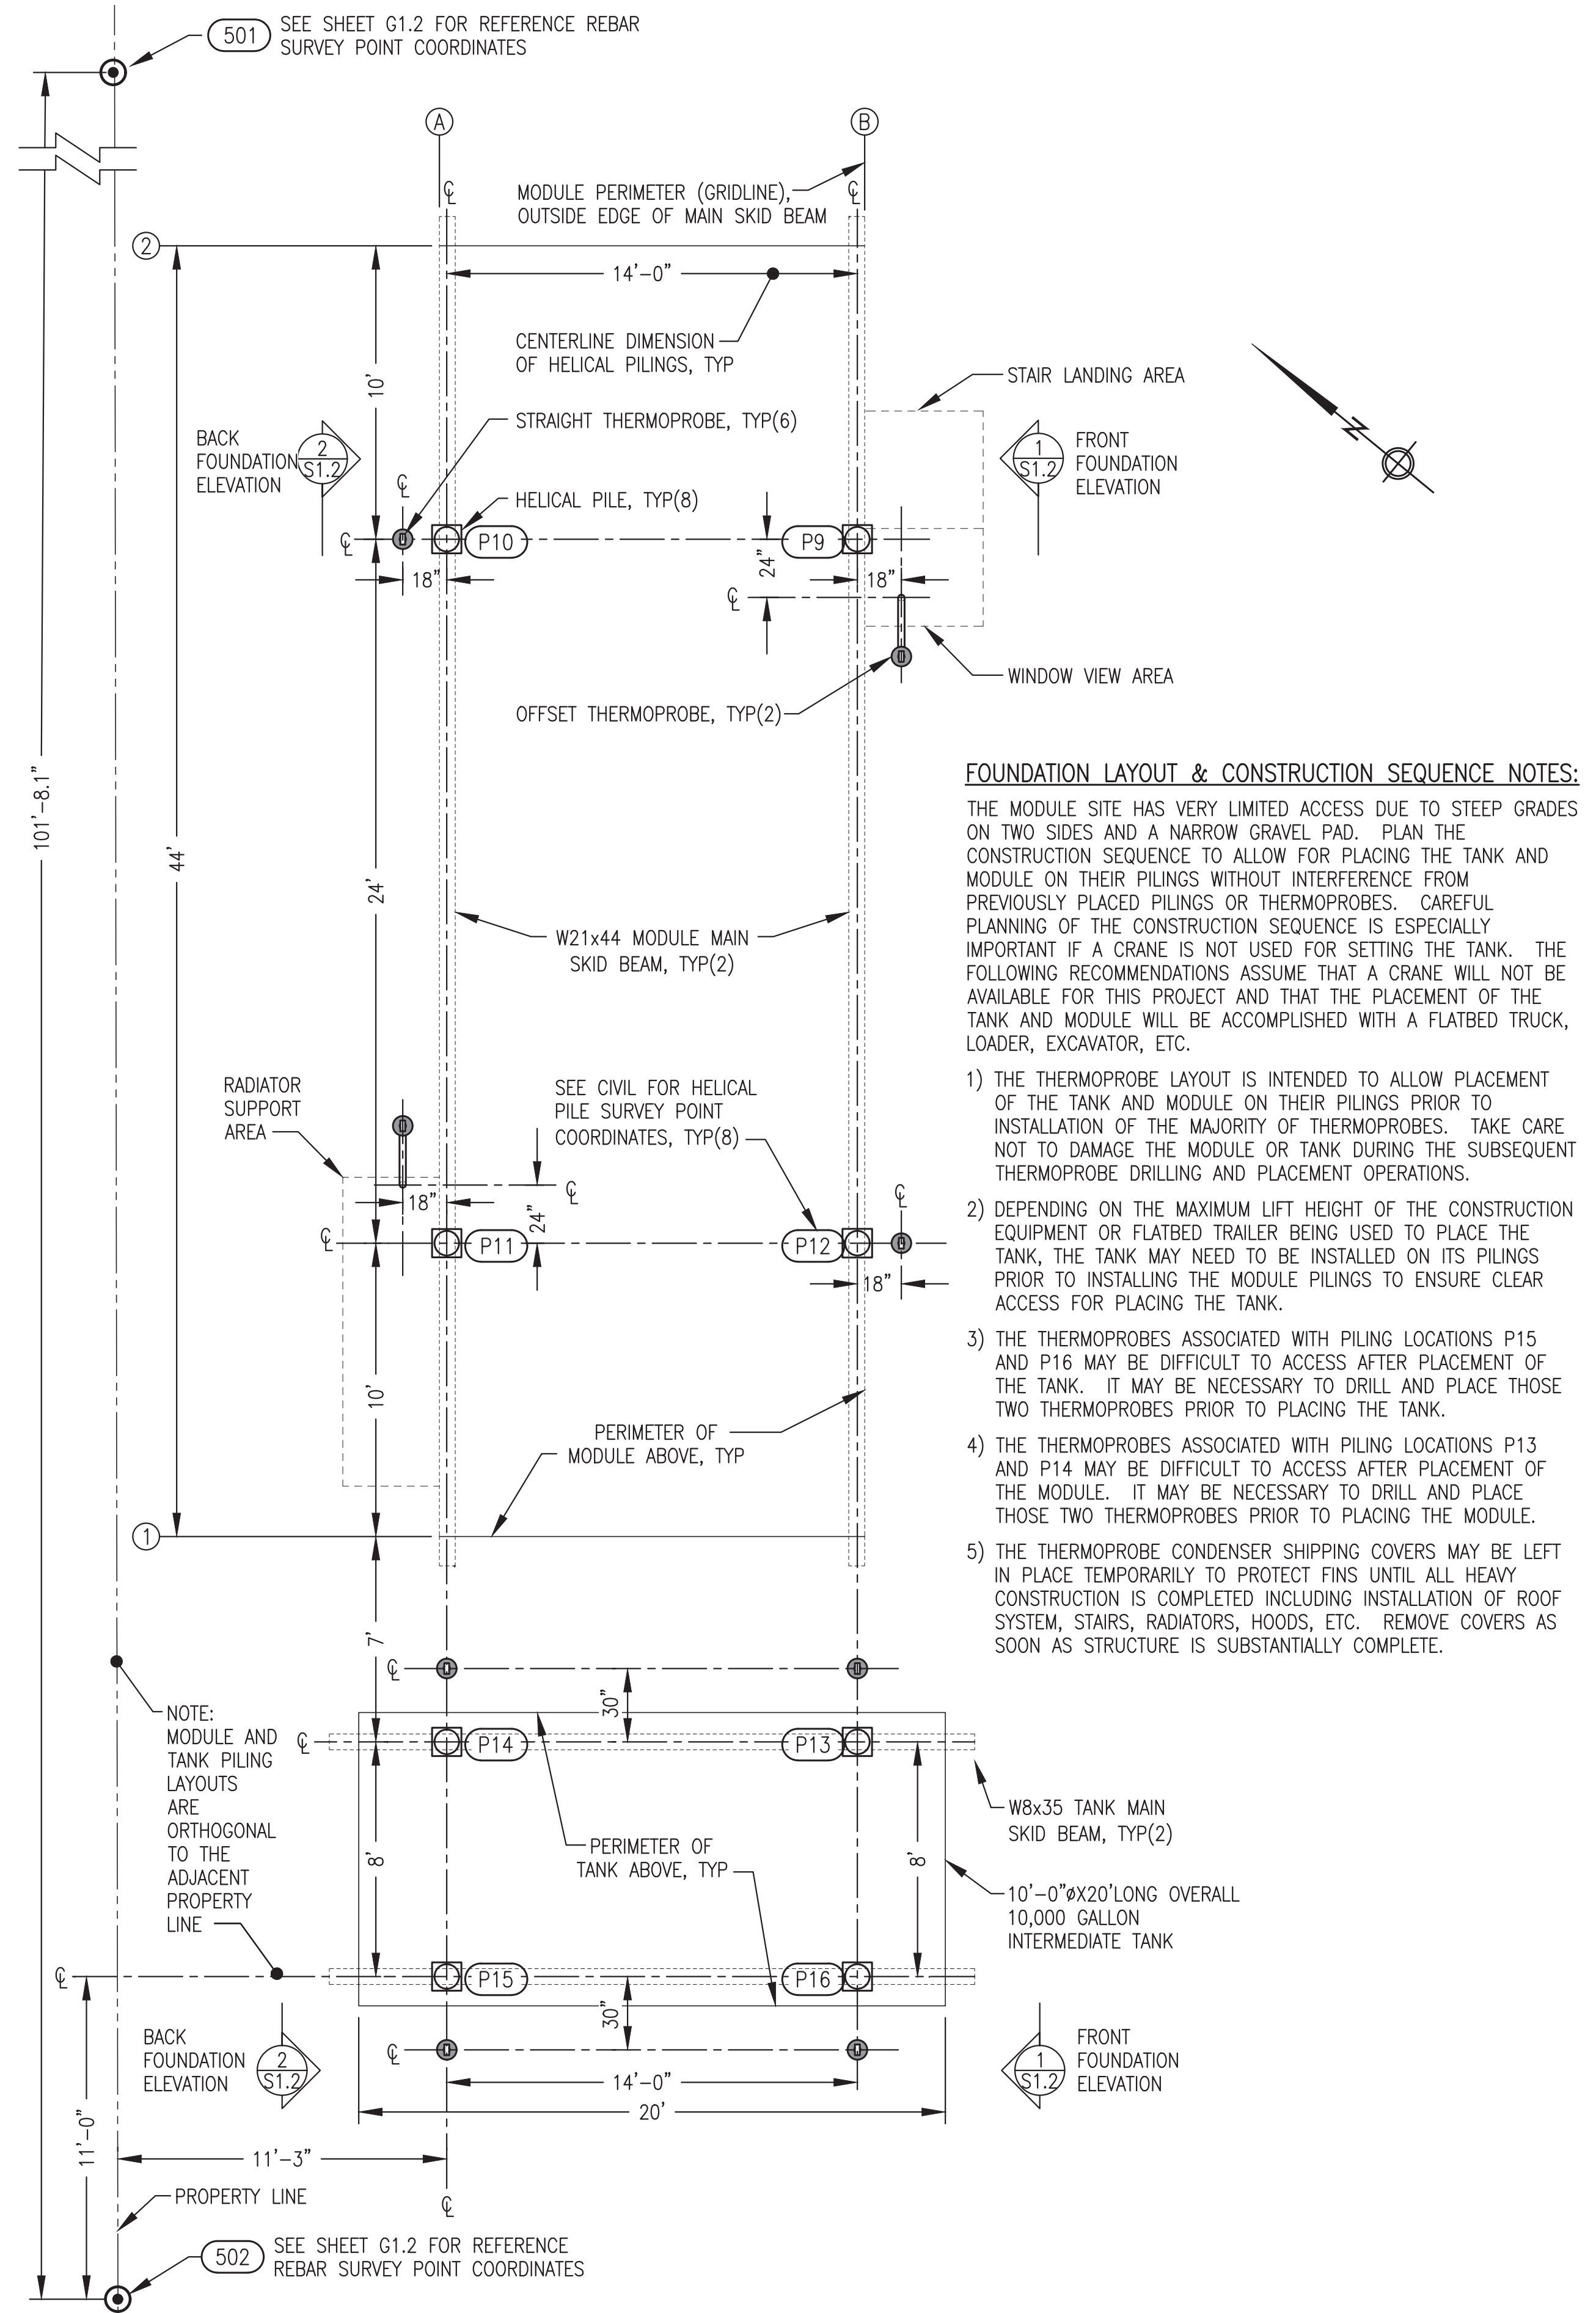

**FOUNDATION LAYOUT & CONSTRUCTION SEQUENCE NOTES:**

THE MODULE SITE HAS VERY LIMITED ACCESS DUE TO STEEP GRADES ON TWO SIDES AND A NARROW GRAVEL PAD. PLAN THE CONSTRUCTION SEQUENCE TO ALLOW FOR PLACING THE TANK AND MODULE ON THEIR PILINGS WITHOUT INTERFERENCE FROM PREVIOUSLY PLACED PILINGS OR THERMOPROBES. CAREFUL PLANNING OF THE CONSTRUCTION SEQUENCE IS ESPECIALLY IMPORTANT IF A CRANE IS NOT USED FOR SETTING THE TANK. THE FOLLOWING RECOMMENDATIONS ASSUME THAT A CRANE WILL NOT BE AVAILABLE FOR THIS PROJECT AND THAT THE PLACEMENT OF THE TANK AND MODULE WILL BE ACCOMPLISHED WITH A FLATBED TRUCK, LOADER, EXCAVATOR, ETC.

- 1) THE THERMOPROBE LAYOUT IS INTENDED TO ALLOW PLACEMENT OF THE TANK AND MODULE ON THEIR PILINGS PRIOR TO INSTALLATION OF THE MAJORITY OF THERMOPROBES. TAKE CARE NOT TO DAMAGE THE MODULE OR TANK DURING THE SUBSEQUENT THERMOPROBE DRILLING AND PLACEMENT OPERATIONS.
- 2) DEPENDING ON THE MAXIMUM LIFT HEIGHT OF THE CONSTRUCTION EQUIPMENT OR FLATBED TRAILER BEING USED TO PLACE THE TANK, THE TANK MAY NEED TO BE INSTALLED ON ITS PILINGS PRIOR TO INSTALLING THE MODULE PILINGS TO ENSURE CLEAR ACCESS FOR PLACING THE TANK.
- 3) THE THERMOPROBES ASSOCIATED WITH PILING LOCATIONS P15 AND P16 MAY BE DIFFICULT TO ACCESS AFTER PLACEMENT OF THE TANK. IT MAY BE NECESSARY TO DRILL AND PLACE THOSE TWO THERMOPROBES PRIOR TO PLACING THE TANK.
- 4) THE THERMOPROBES ASSOCIATED WITH PILING LOCATIONS P13 AND P14 MAY BE DIFFICULT TO ACCESS AFTER PLACEMENT OF THE MODULE. IT MAY BE NECESSARY TO DRILL AND PLACE THOSE TWO THERMOPROBES PRIOR TO PLACING THE MODULE.
- 5) THE THERMOPROBE CONDENSER SHIPPING COVERS MAY BE LEFT IN PLACE TEMPORARILY TO PROTECT FINS UNTIL ALL HEAVY CONSTRUCTION IS COMPLETED INCLUDING INSTALLATION OF ROOF SYSTEM, STAIRS, RADIATORS, HOODS, ETC. REMOVE COVERS AS SOON AS STRUCTURE IS SUBSTANTIALLY COMPLETE.

**STRUCTURAL GENERAL NOTES:**

- 1.0 DESIGN LOADS:**
- A. BUILDING CODE: 2012 INTERNATIONAL BUILDING CODE
  - B. FLOOR LIVE LOADS: (IBC TABLE 1607.1)  
LIGHT STORAGE/MANUFACTURING 125 PSF OR 2000 POUND POINT LOAD  
MAXIMUM GENERATOR UNIT WEIGHT 6,000 POUNDS
  - C. SNOW LOADS: (ASCE 7-10)  
GROUND SNOW LOAD,  $P_g =$  70 PSF  
COEFFICIENT OF EXPOSURE,  $C_e =$  1.0 PARTIALLY EXPOSED  
SNOW IMPORTANCE FACTOR,  $I_s =$  1.2 CATEGORY IV  
THERMAL COEFFICIENT,  $C_t =$  1.2 COLD, VENTILATED ROOF  
ROOF/FLAT SNOW LOAD,  $P_f =$  65 PSF
  - D. WIND LOADS:  
BASIC WIND SPEED = 120 MPH, 3 SECOND GUST  
RISK CATEGORY = CATEGORY IV  
EXPOSURE CLASSIFICATION = EXPOSURE C
  - E. SEISMIC LOADING:  
SEISMIC =  $S_s = 1.03$   $S_1 = 0.33$   
SEISMIC IMPORTANCE FACTOR = 1.50, CATEGORY IV
- SITE CLASS "D" (DEFAULT)  
BASIC SEISMIC FORCE RESISTANCE SYSTEM  
BUILDING = BEARING WALL WITH STEEL SHEAR PANELS  
FOUNDATION = STEEL HELICAL PILES  
SEISMIC RESPONSE COEFFICIENT - BUILDING  $R = 7.0$   
SEISMIC RESPONSE COEFFICIENT - PILING FRAMES  $R = 6.5$

- 4.0 WOOD:**
- A. 5/8" PLYWOOD SHALL HAVE A PANEL SPAN RATING OF 32/16 - MINIMUM NAILING FOR PANELS, UNLESS OTHERWISE NOTED, SHALL EQUAL 10d NAILS AT 4" CENTERS AROUND PLYWOOD PANEL EDGES AND 10d'S @ 12" CENTERS ALONG INTERMEDIATE FRAMING. BLOCK ALL DIAPHRAGM PANEL EDGES WITH 2x4 FLAT BLOCKING. OSB PANELS WILL NOT BE ACCEPTED.
  - B. FRAMING MATERIAL: DOUGLAS FIR OR HEM FIR, NO. 2 OR BETTER MINIMUM FOR JOISTS, STUDS, PANEL JOINTS, WOOD PLATES, BLOCKING, AND HEADERS. MAXIMUM MOISTURE CONTENT SHALL BE 19%. FOR FRAMING SPECIFICALLY INDICATED AS TREATED PROVIDE LUMBER TREATED FOR GROUND CONTACT TO 0.4 RETENTION MINIMUM.
  - C. ALL METAL TO WOOD OR WOOD TO WOOD CONNECTIONS SHALL BE STANDARD OR AS DETAILED ON THE DRAWINGS. ALL FASTENERS SHALL BE GALVANIZED OR STAINLESS STEEL.
  - D. ALL METAL FRAMING ANCHORS AND SPLICE PLATES SHALL BE FABRICATED FROM GALVANIZED STEEL AND SHALL SUPPORT THE LOADS INDICATED ON THE DRAWINGS. ANCHORS INDICATED ON THE DRAWINGS ARE "SIMPSON COMPANY" OR EQUAL.
  - E. MINIMUM NAILING SHALL EQUAL THAT INDICATED IN 2012 IBC TABLE 2304.9.1 UNLESS OTHERWISE INDICATED ON THE DRAWINGS OR ANCHOR MANUFACTURER'S INSTALLATION INSTRUCTIONS. MINIMUM NAILING FOR EXTERIOR PLYWOOD PANELS SHALL EQUAL 10d NAILS AT 4" CENTERS AROUND PLYWOOD PANEL EDGES AND 10d'S @ 12" CENTERS ALONG INTERMEDIATE FRAMING. BLOCK ALL DIAPHRAGM PANEL EDGES WITH 2x4 OR 2x6 BLOCKING. ERECT WOOD FRAMING MEMBERS TRUE TO LINES AND LEVELS. DO NOT DEVIATE FROM TRUE ALIGNMENT MORE THAN 1/4 INCH.
  - F. PREMANUFACTURED ROOF TRUSSES: ALL PRE-MANUFACTURED WOOD TRUSSES SHALL BE "GANG NAIL" OR EQUAL AND SHALL BE FABRICATED WITH GALVANIZED PLATES AND FASTENERS AS INDICATED ABOVE. TRUSSES SHALL BE DESIGNED FOR THE GRAVITY LOADS, WIND & SEISMIC LATERAL & UPLIFT LOADS, AND SUPPORT CONDITIONS AS INDICATED ON THE DRAWINGS. NO DURATION OF LOAD INCREASE IN STRESSES WILL BE ALLOWED FOR SNOW LOADING. UNBALANCED SNOW AND DRIFT LOADING IS REQUIRED. SUBMIT TRUSS DESIGNS STAMPED BY AN ENGINEER LICENSED TO PRACTICE IN THE STATE OF ALASKA. TRUSS DRAWINGS SHALL INDICATE ALL MATERIALS OF CONSTRUCTION.

**2.0 FOUNDATIONS:**

- A. SEE CIVIL FOR SITE PREPARATION AND FOR COORDINATES OF HELICAL PILES.
- B. PROVIDE HELICAL PILE FOUNDATION WITH THERMOPROBES IN ACCORDANCE WITH SPECIFICATIONS AND AS INDICATED ON SHEET S1.2.

**3.0 STRUCTURAL STEEL:**

- A. THE DESIGN, FABRICATION, AND ERECTION OF ALL STRUCTURAL STEEL SHALL COMPLY WITH THE CODE OF STANDARD PRACTICE OF THE AMERICAN INSTITUTE OF STEEL CONSTRUCTION.
- B. ALL STEEL PLATE, SHAPES, AND ROLLED SECTIONS SHALL BE ASTM A36. ALL STEEL TUBING SHALL BE ASTM A500, GRADE B.
- C. ALL METAL TO METAL CONNECTIONS SHALL BE EQUAL TO STANDARD CONNECTION, OR AS DETAILED USING A325 BOLTS (BEARING TYPE CONNECTIONS). TIGHTEN HIGH STRENGTH BOLTS WITH PROPERLY CALIBRATED WRENCHES, BY TURN-OF-THE-NUT METHOD, OR BY LOAD WASHERS. ALL CONNECTIONS UNLESS OTHERWISE DETAILED, SHALL HAVE THE MAXIMUM NUMBER OF 3/4" DIAMETER BOLTS USING STANDARD GAUGES AND CLEARANCES.
- D. ALL WELDING SHALL BE DONE IN ACCORDANCE WITH THE CURRENT CODE OF THE AMERICAN WELDING SOCIETY. USE AWS 5.1 E70XX ELECTRODES. MINIMUM FILLET WELD SHALL BE 3/16" EXCEPT FOR SEAL WELDS TO GAUGE METAL AS INDICATED.
- E. ALL EXPOSED STEEL SURFACES SHALL BE PREPARED AND PAINTED AS INDICATED IN THE ARCHITECTURAL DRAWINGS.

**MODULE PILE LOADS**

MARK	DEAD (K) NOTES 1&2	FLOOR LIVE (K)	SNOW (K)	TOTAL (K)	WIND (K) NOTE 3	SEISMIC (K) NOTE 3
P9						
P10	26.5	6.3	16.4	49.2	2.5 H	4.5 H
P11						
P12						

**TANK PILE LOADS**

NOTE: TANK DEAD LOAD INCLUDES TANK PLUS 95% FUEL CAPACITY.

P13						
P14	26.0	0	1.4	27.4	1.0 H	4.0 H
P15						
P16						

- NOTES:  
1) MODULE DEAD LOAD INCLUDES ALL FIXED EQUIPMENT.  
2) TANK DEAD LOAD INCLUDES FUEL AT CAPACITY.  
3) WIND AND SEISMIC ARE CONSIDERED TRANSIENT LOADS.

**THIS DRAWING SHOWS WORK THAT WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT FOR ON SITE INSTALLATION AND IS PROVIDED HERE FOR REFERENCE ONLY.**

REV.	DESCRIPTION	DATE	BY
1	REVISED TO INCLUDE ONSITE FOUNDATION DESIGN	7/15/22	BCG


ALASKA ENERGY AUTHORITY

PROJECT: RAMPART POWER SYSTEM UPGRADE


TITLE: FOUNDATION PLAN, CODE ANALYSIS, & STRUCTURAL NOTES

DRAWN BY: JTD	SCALE: AS NOTED
DESIGNED BY: DGT/BCG	DATE: 2-18-22
FILE NAME: RAM PP S1-S5	SHEET:
PROJECT NUMBER:	<b>S1.1</b>

P.O. 111405, Anchorage, AK 99511 (907)349-0100






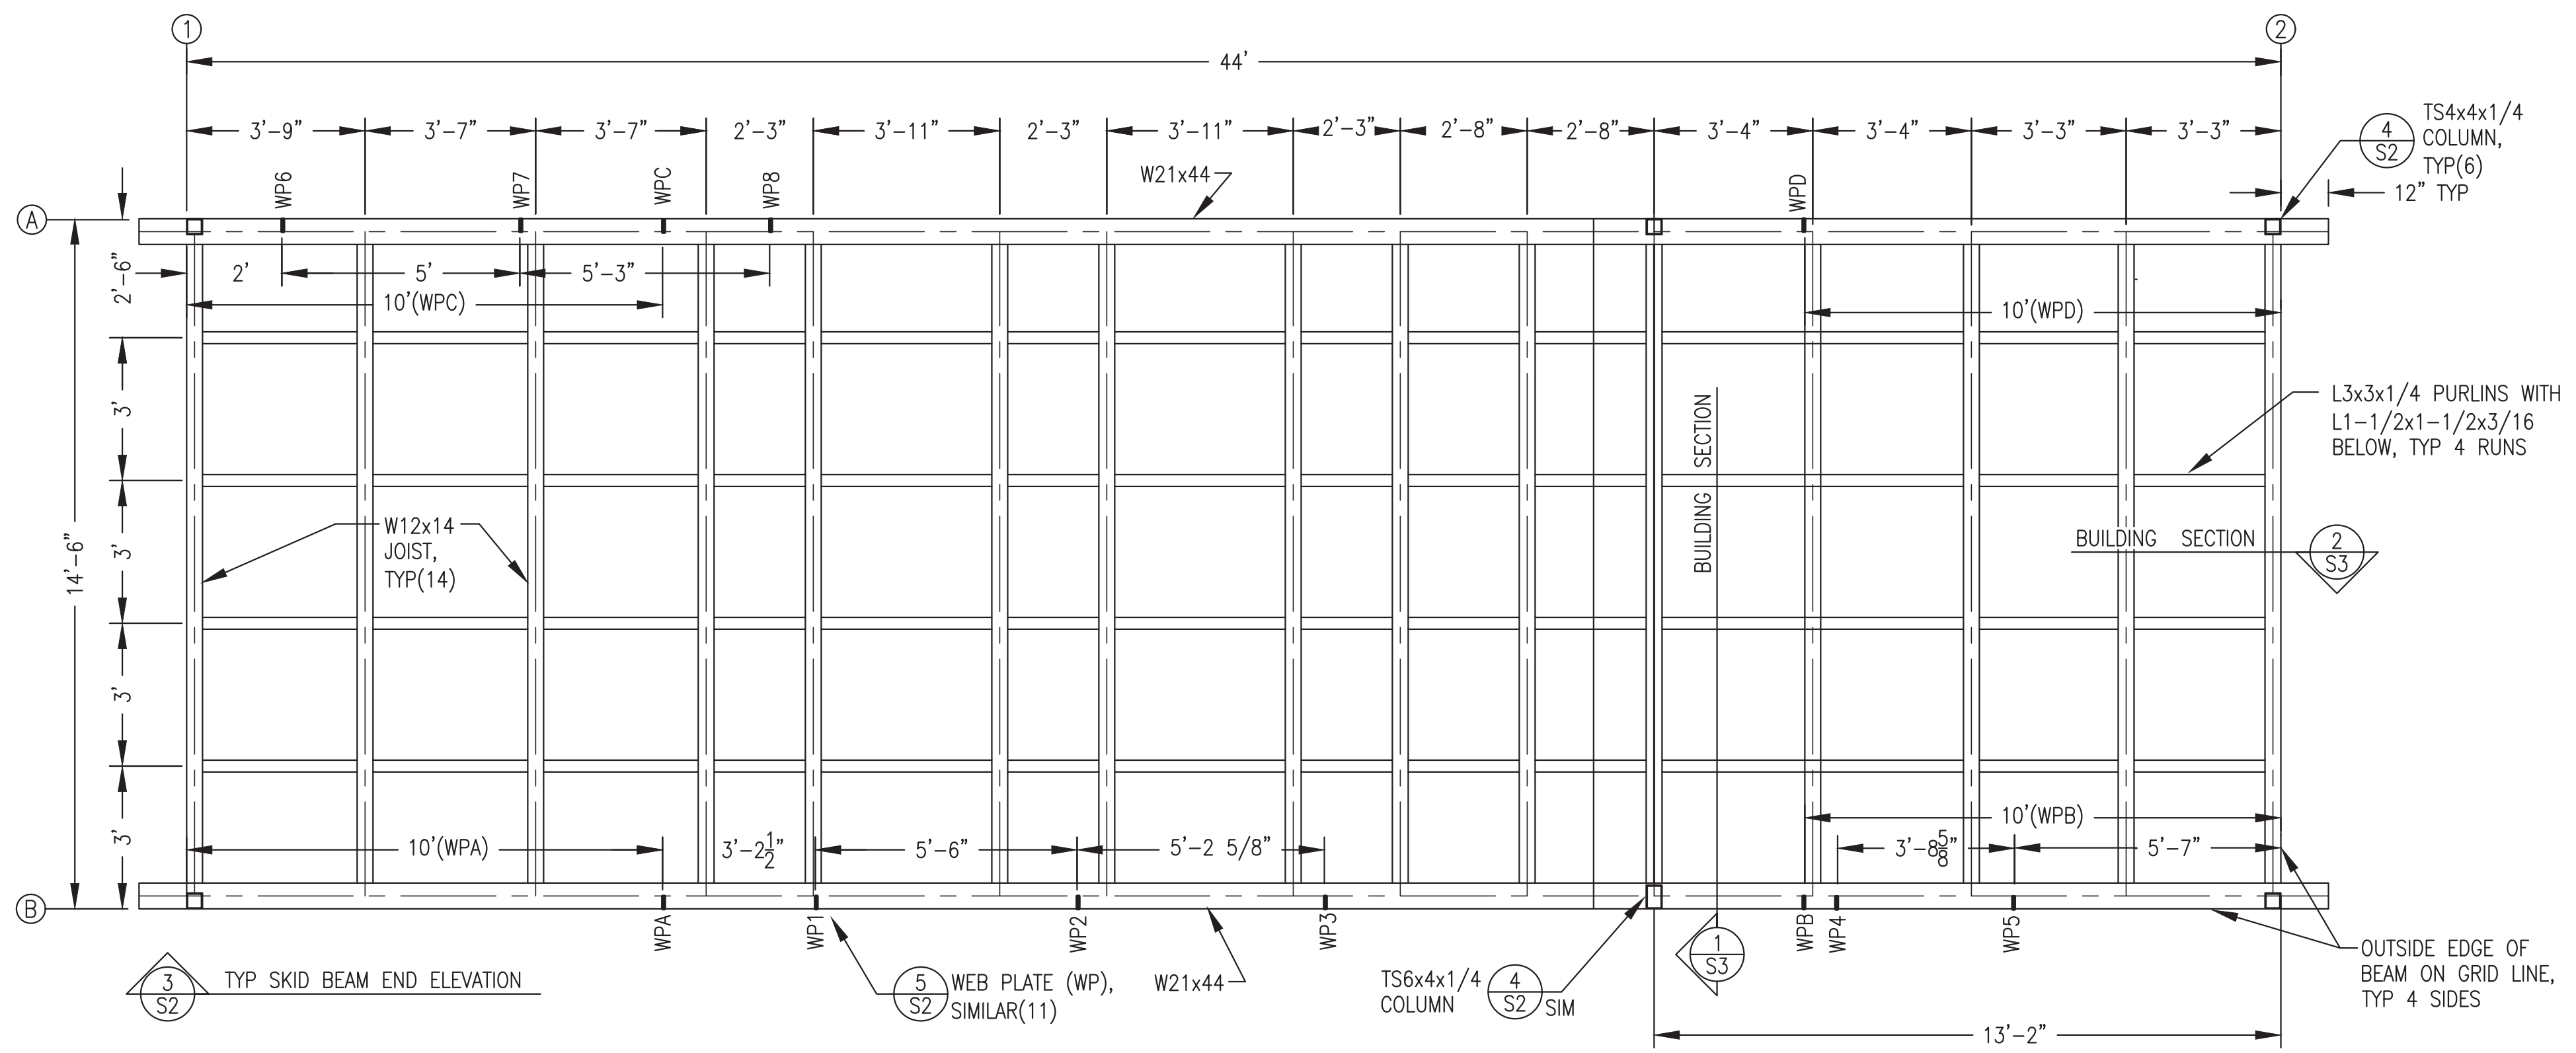


NOTES: 1) FABRICATE FLOOR AND PAN DECKS USING SHEETS CUT SO THAT ALL JOINTS ARE CENTERED ON PURLINS AND/OR JOISTS.  
 2) SEE MECHANICAL SUPPORT PLAN M2.2 FOR GENERATOR SUPPORT PEDESTAL LOCATIONS AND FABRICATION.

**1 FLOOR FRAMING PLAN**  
 S2 3/8"=1'-0"

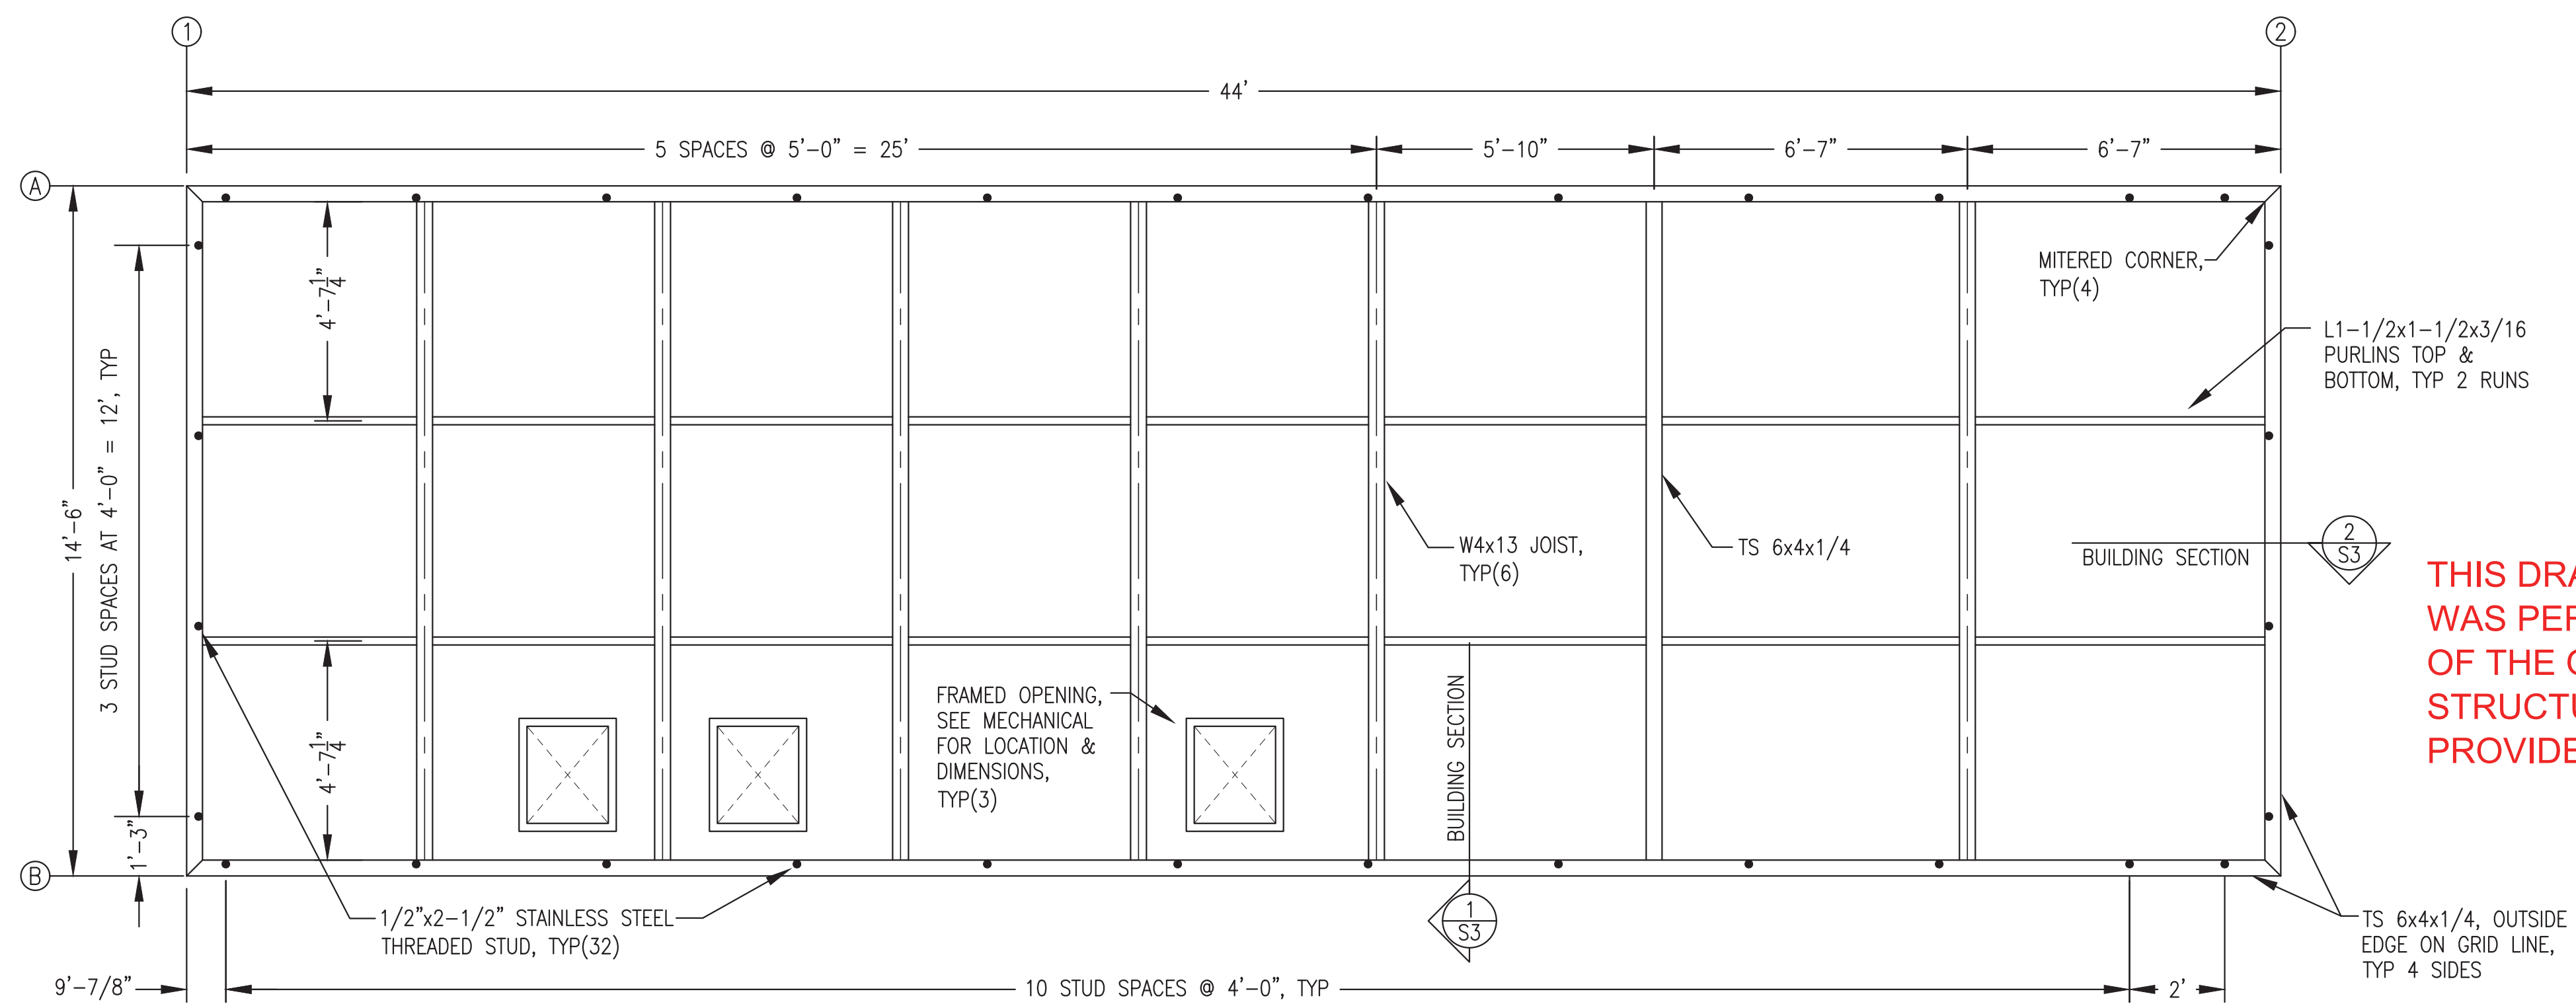


NOTES: 1) FABRICATE CEILING FLAT AND CORRUGATED DECKS USING SHEETS CUT SO THAT ALL JOINTS ARE CENTERED ON PURLINS AND/OR JOISTS.  
 2) SEE MECHANICAL SUPPORT PLAN M2.3 FOR CEILING CORRUGATION LAYOUT AND STRUT SUPPORT LOCATION AND INSTALLATION.  
 3) PROVIDE ADDITIONAL L1-1/2" BOTTOM PURLINS AGAINST PERIMETER TS AS REQUIRED FOR CEILING PLATE SUPPORT.


**2 CEILING FRAMING PLAN**  
 S2 3/8"=1'-0"

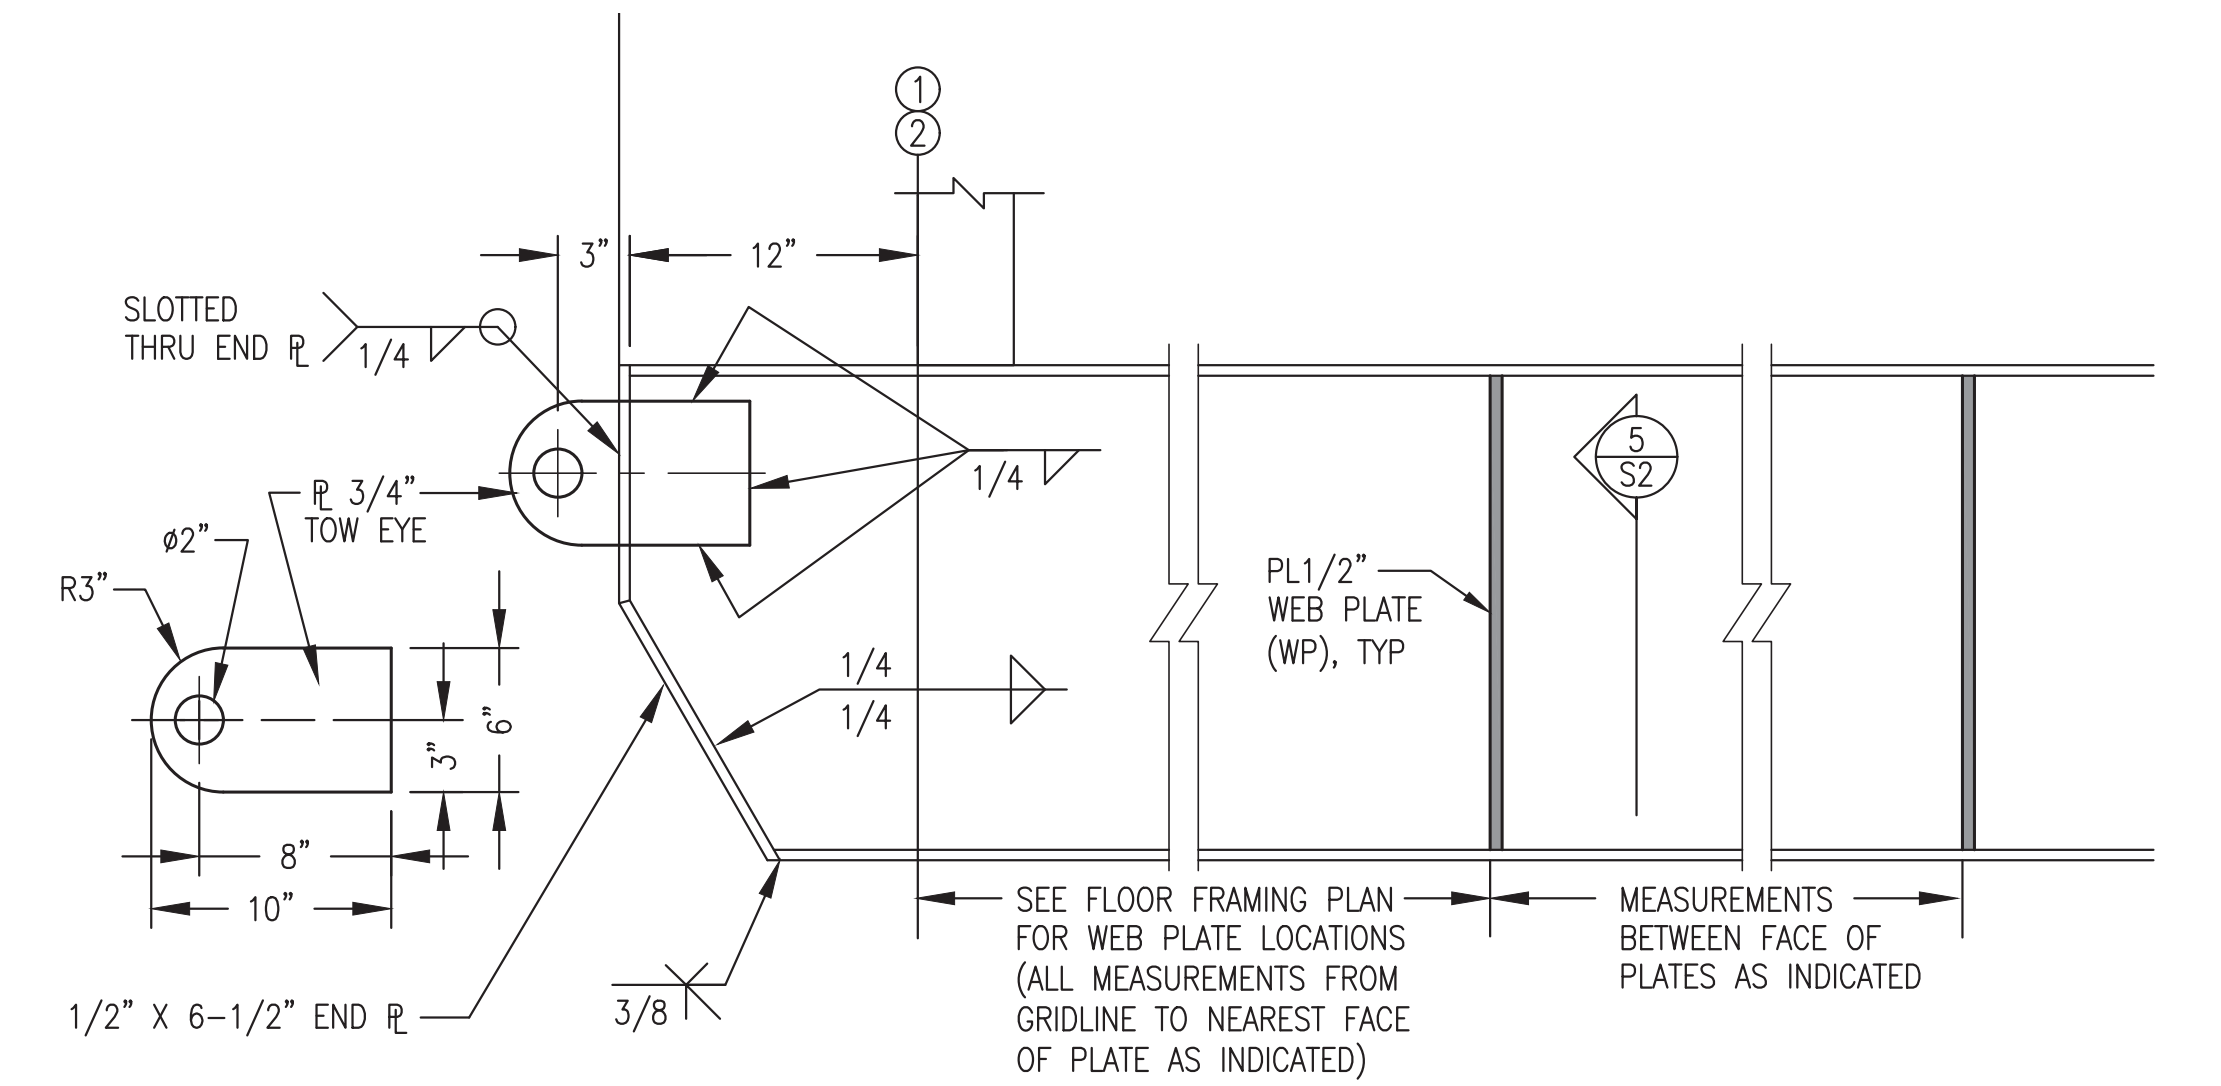

**3 TYPICAL SKID BEAM END ELEVATION**  
 S2 1-1/2"=1'-0"

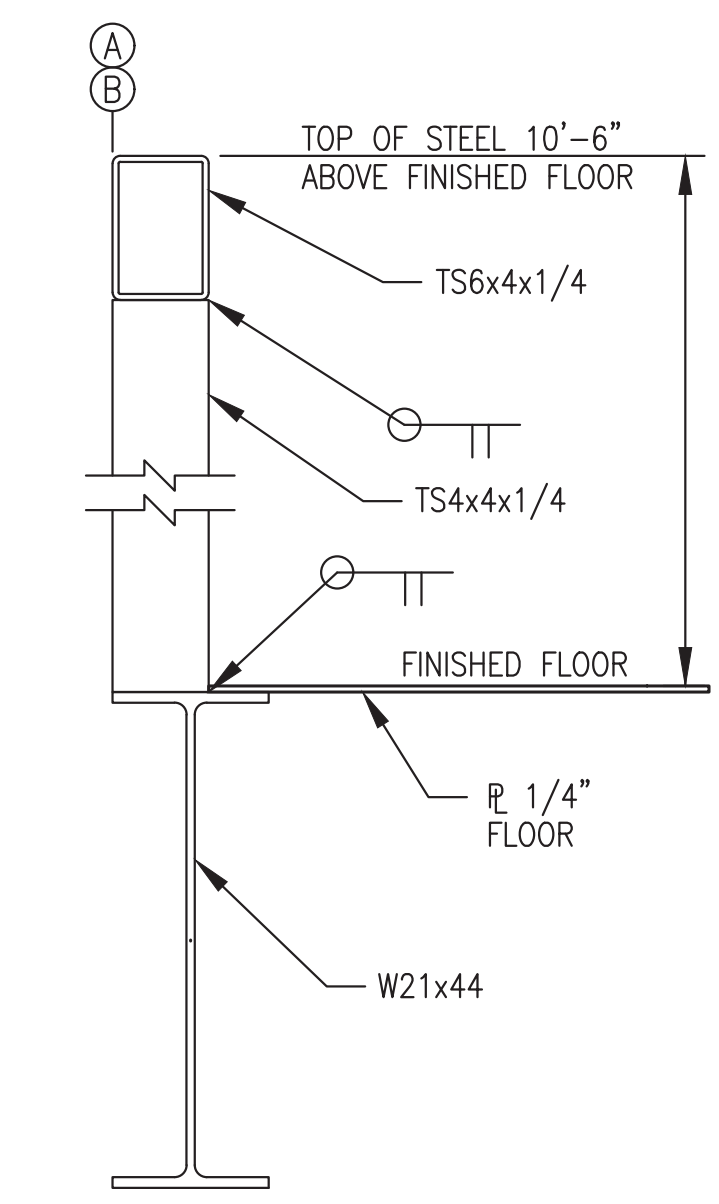


**4 TYP CORNER COLUMN**  
 S2 1-1/2"=1'-0"

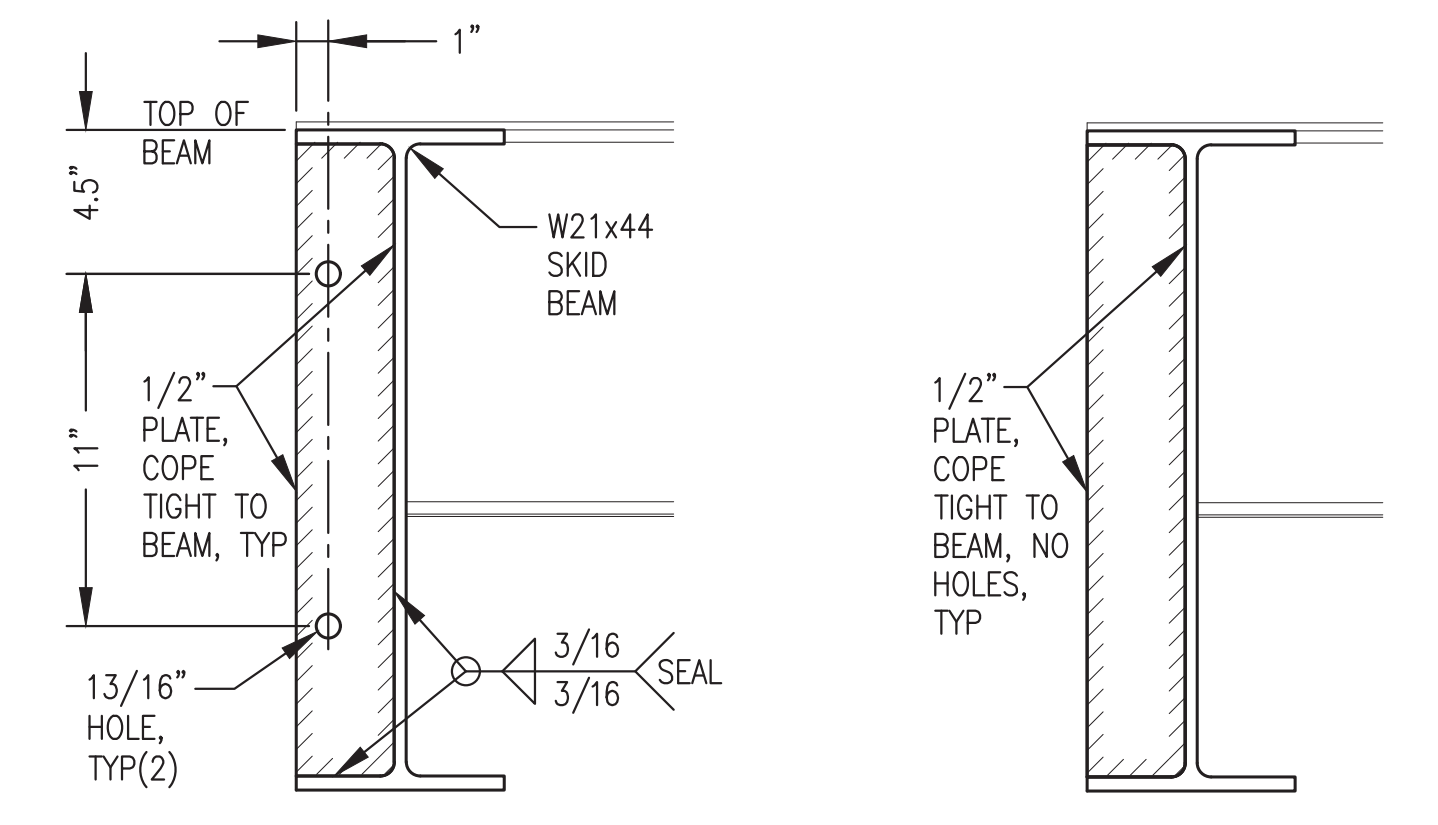


**5 TYPICAL WEB PLATE (WP)**  
 S2 2"=1'-0"

**THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.**

REVISION #1  
 ISSUED JUNE  
 2022




1	MOVED CEILING PURLINS TO MATCH 55" CEILING PANELS PER FABRICATOR REQUEST	6/2/22	BCG
REV.	DESCRIPTION	DATE	BY
 <b>ALASKA ENERGY AUTHORITY</b>			
<b>PROJECT:</b> RAMPART POWER SYSTEM UPGRADE			
<b>TITLE:</b> MODULE FRAMING PLANS & DETAILS			
DRAWN BY: JTD DESIGNED BY: DGT/BCG		SCALE: AS NOTED DATE: 3/15/22	
FILE NAME: RAM_PP_S1-S5 PROJECT NUMBER:		SHEET: <b>S2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

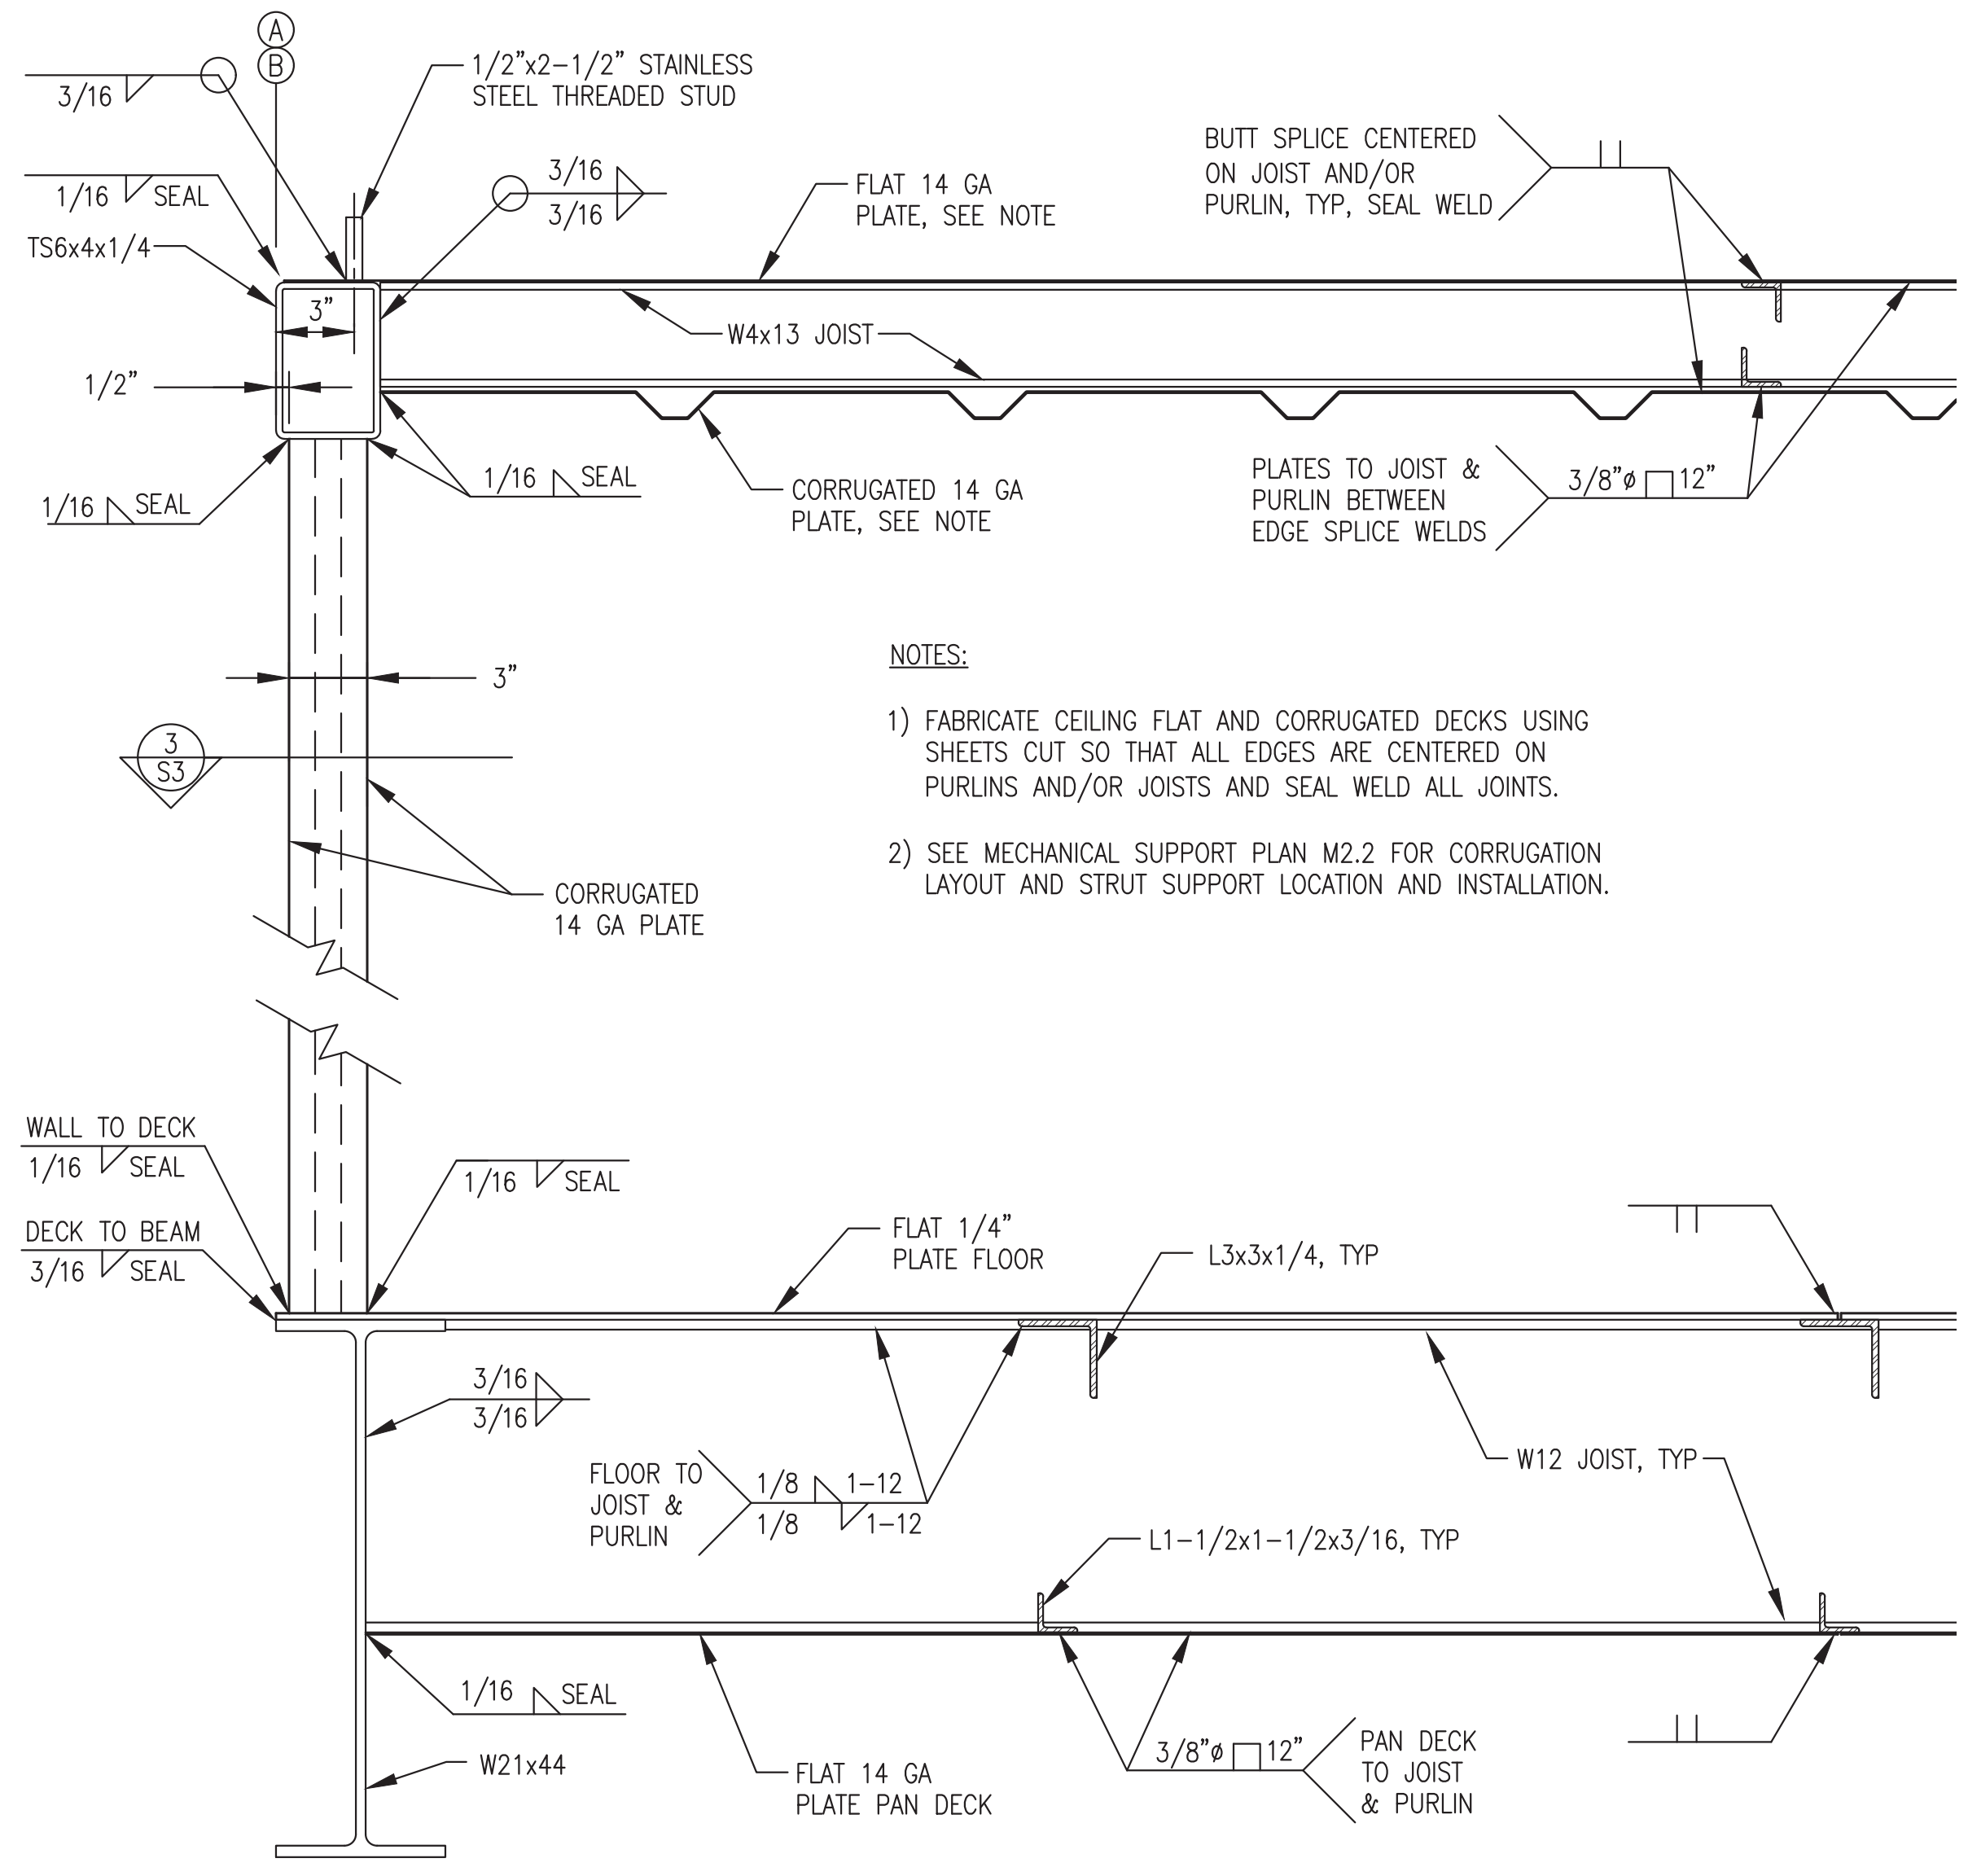


- NOTES:
- 1) FABRICATE CEILING FLAT AND CORRUGATED DECKS USING SHEETS CUT SO THAT ALL EDGES ARE CENTERED ON PURLINS AND/OR JOISTS AND SEAL WELD ALL JOINTS.
  - 2) SEE MECHANICAL SUPPORT PLAN M2.2 FOR CORRUGATION LAYOUT AND STRUT SUPPORT LOCATION AND INSTALLATION.


1 TYPICAL BUILDING SECTION  
S3 2"=1'-0"

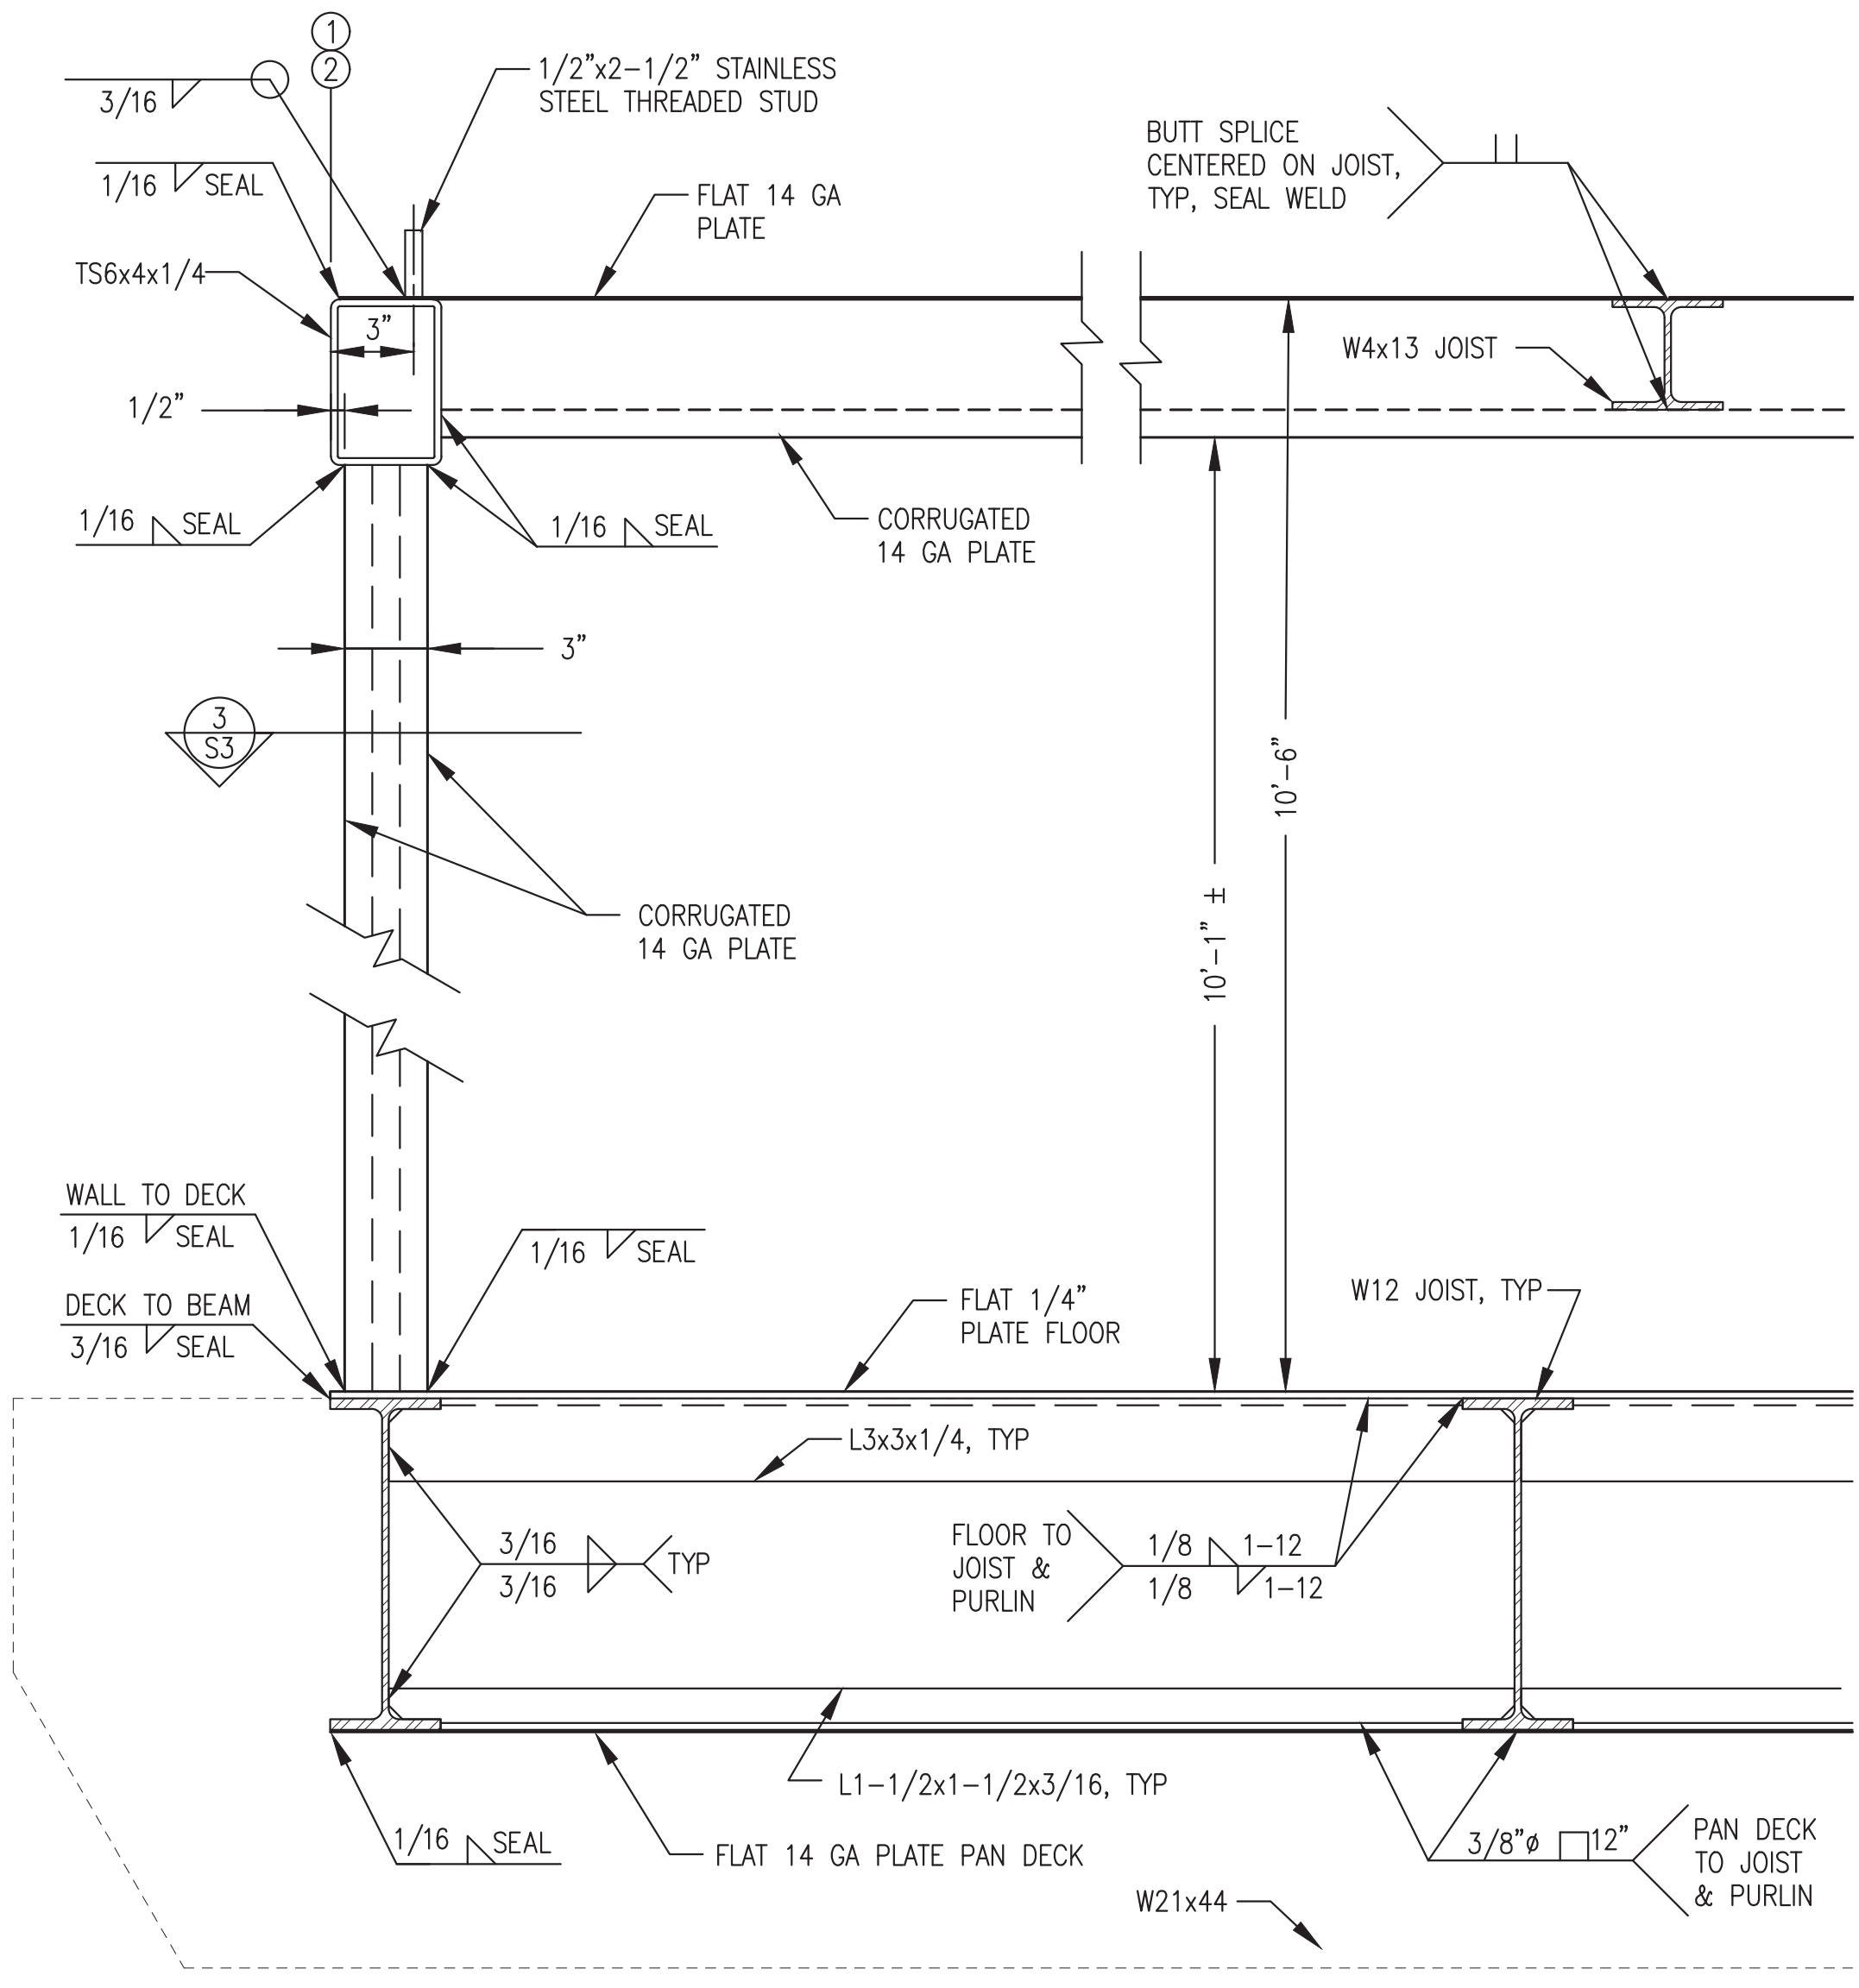

2 TYPICAL BUILDING SECTION  
S3 2"=1'-0"

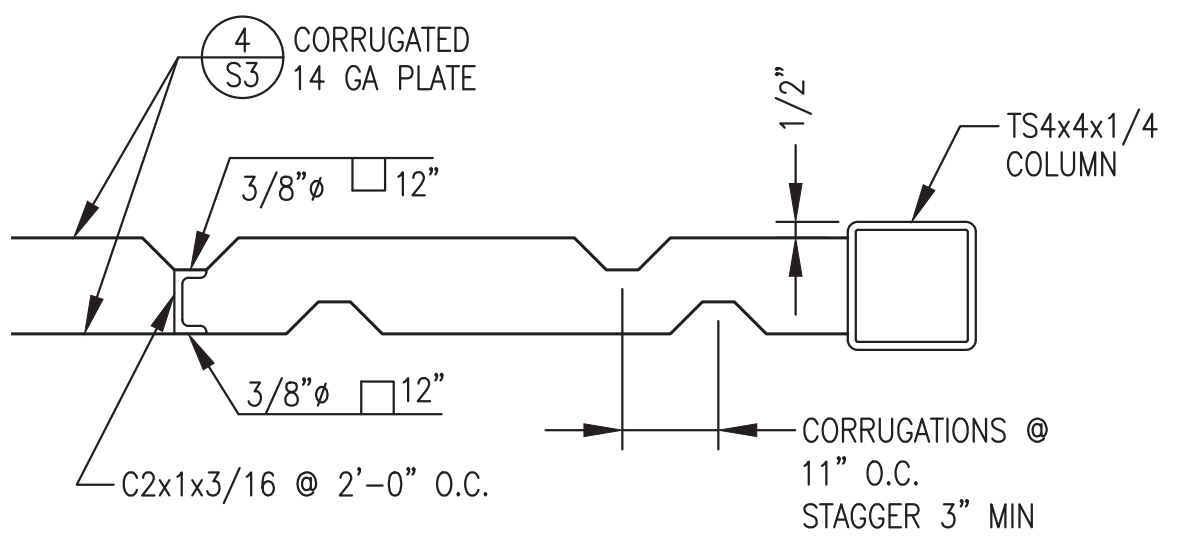


3 TYPICAL EXTERIOR WALL - PLAN VIEW  
S3 2"=1'-0"

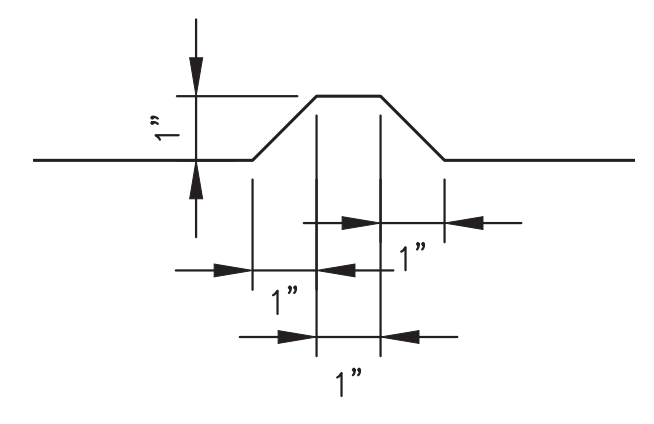


4 TYPICAL CORRUGATION  
S3 4"=1'-0"

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.


REVISION #1  
ISSUED JUNE  
2022




1	CHANGED INTERIOR PLATE CORRUGATIONS TO 11" O.C. PER FABRICATOR REQUEST	6/2/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: MODULE SECTIONS DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: DGT/BCG		DATE: 3/15/22	
FILE NAME: RAM PP S1-S5		SHEET: S3	
PROJECT NUMBER:			
 Gray Stassel Engineering, Inc. P.O. 111405, Anchorage, AK 99511 (907)349-0100			

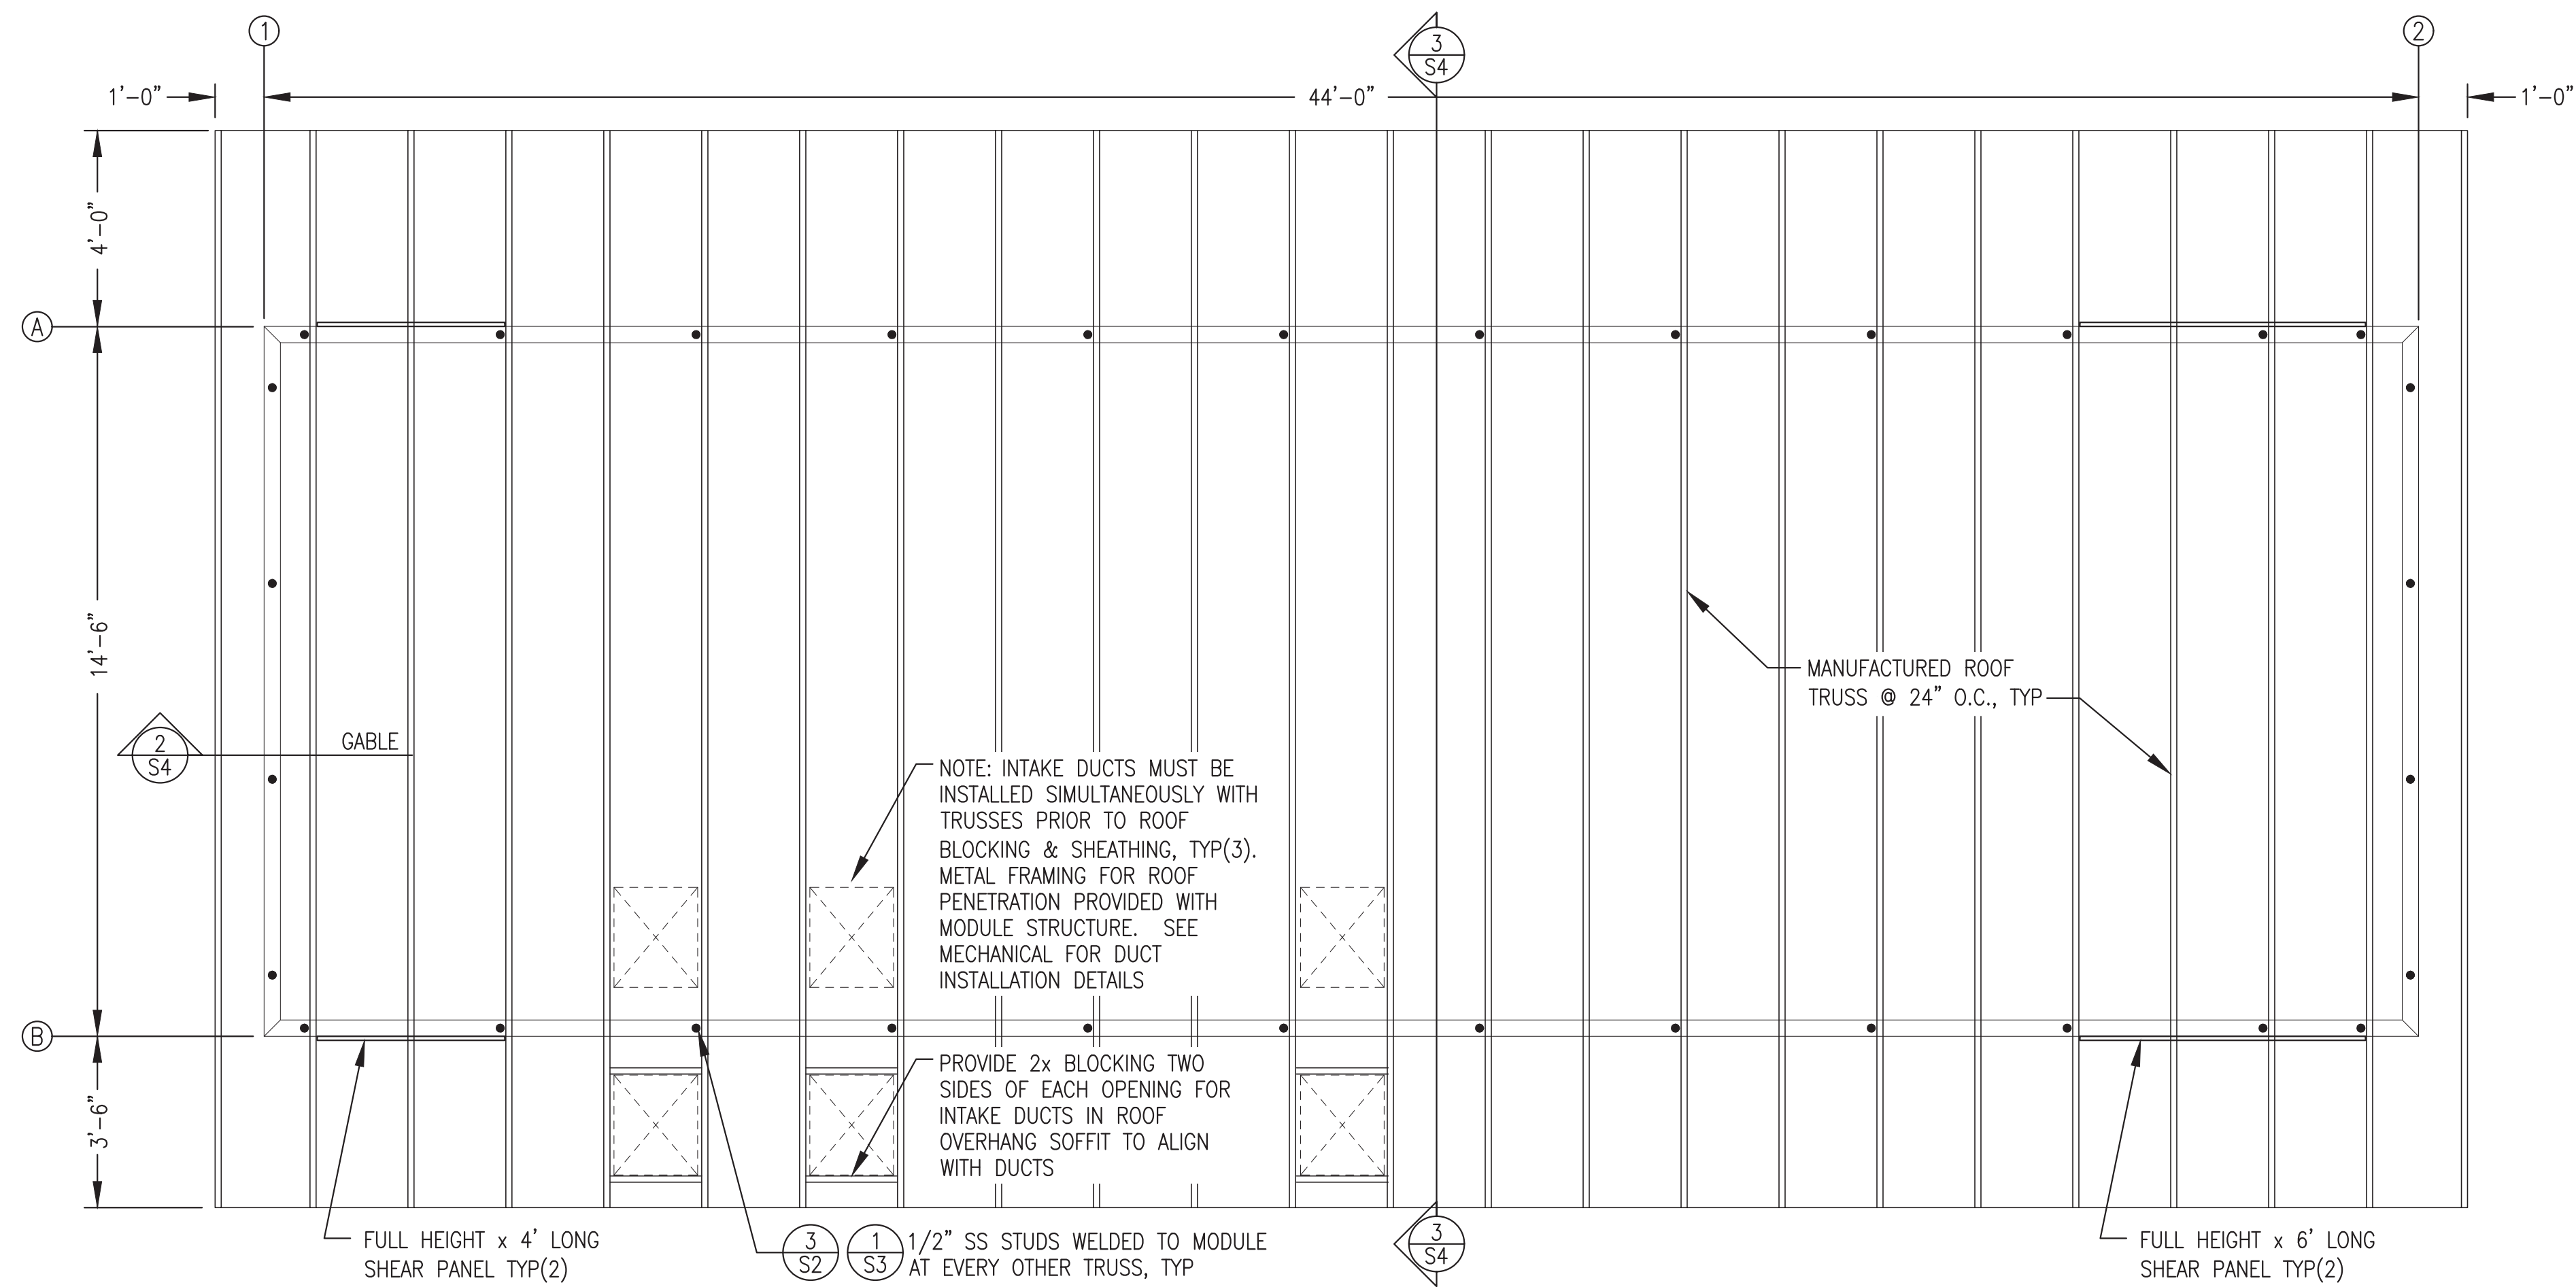

**1**  
S4  
ROOF FRAMING PLAN  
3/8"=1'-0"

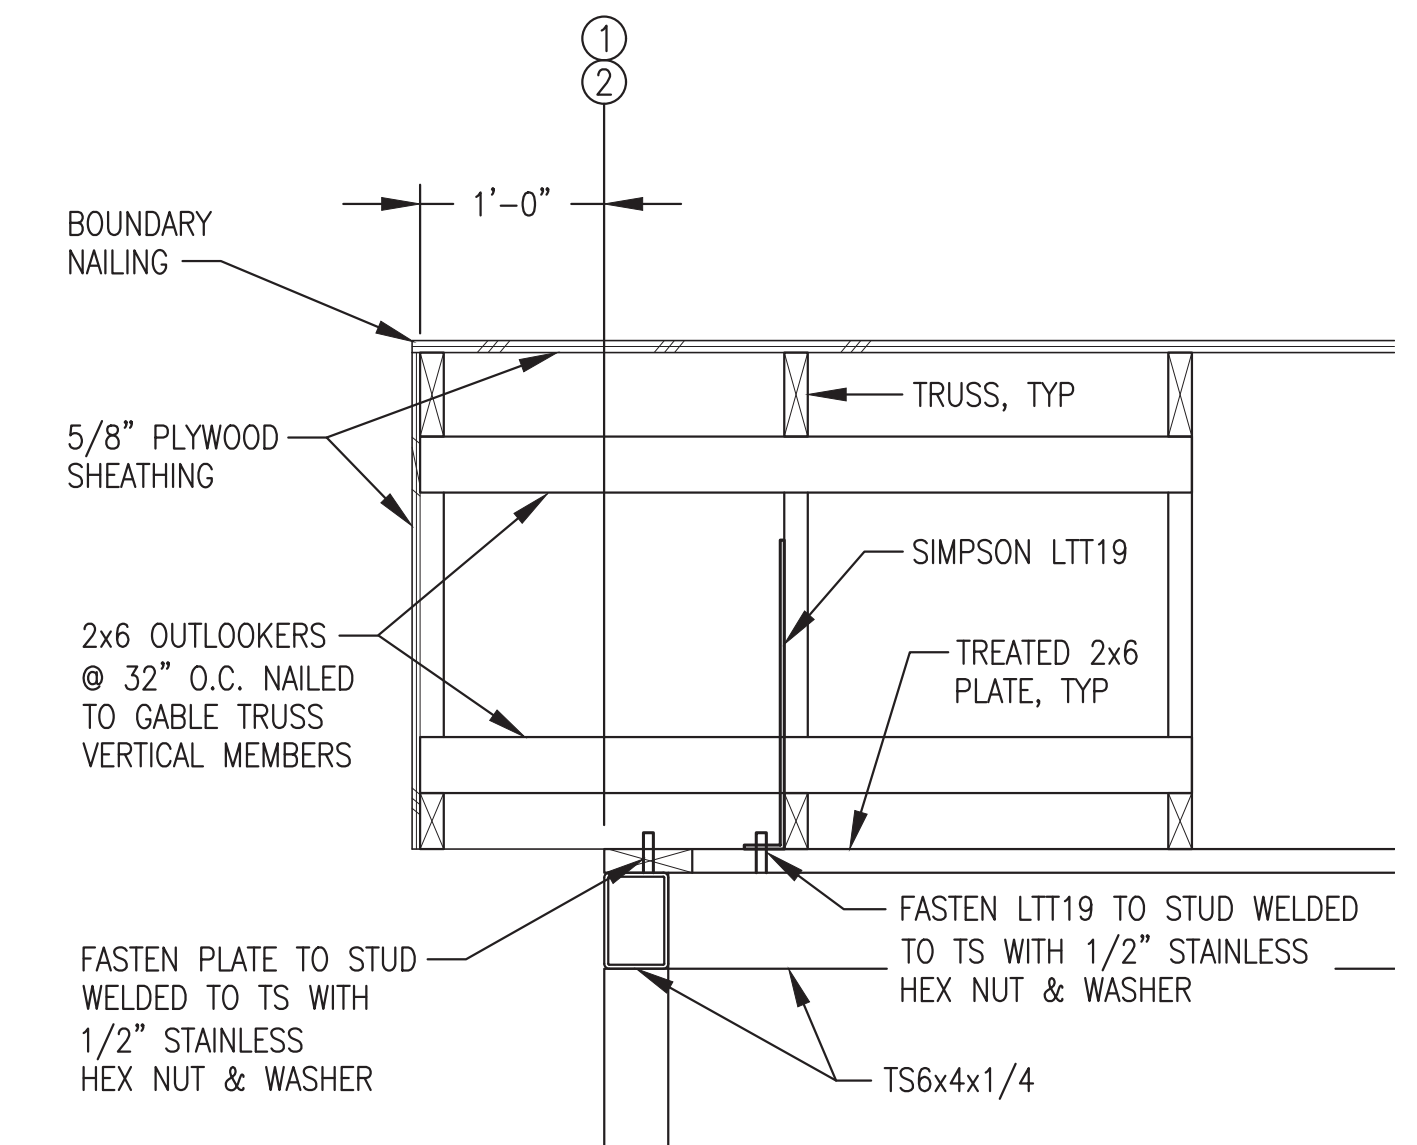


**2**  
S4  
TYPICAL GABLE  
1"=1'-0"

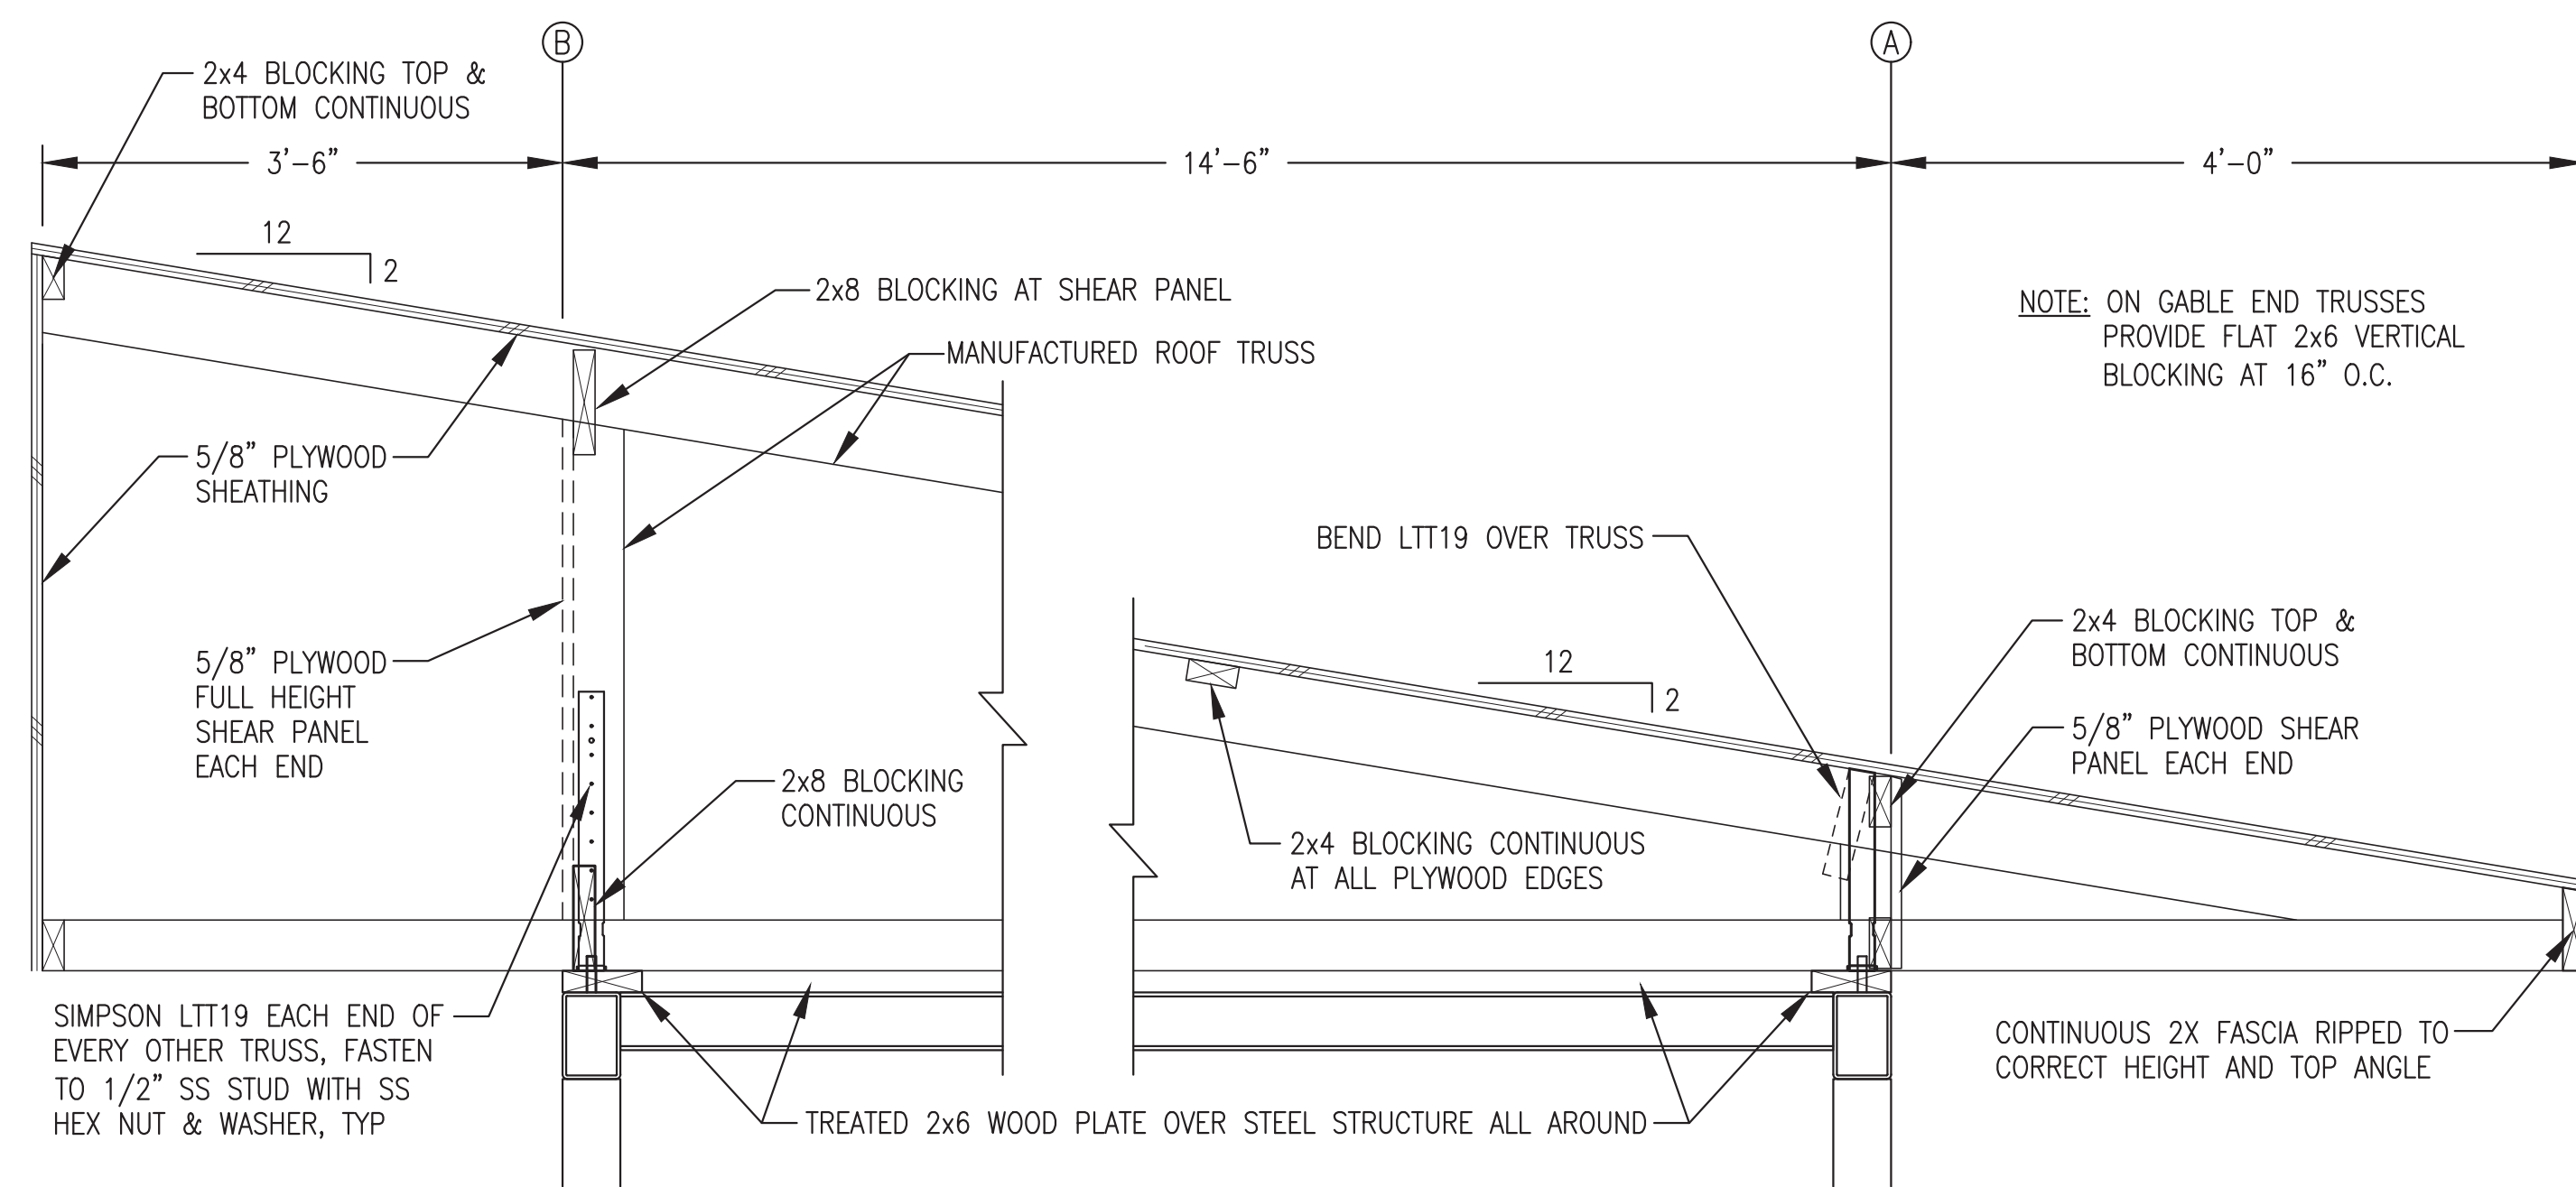


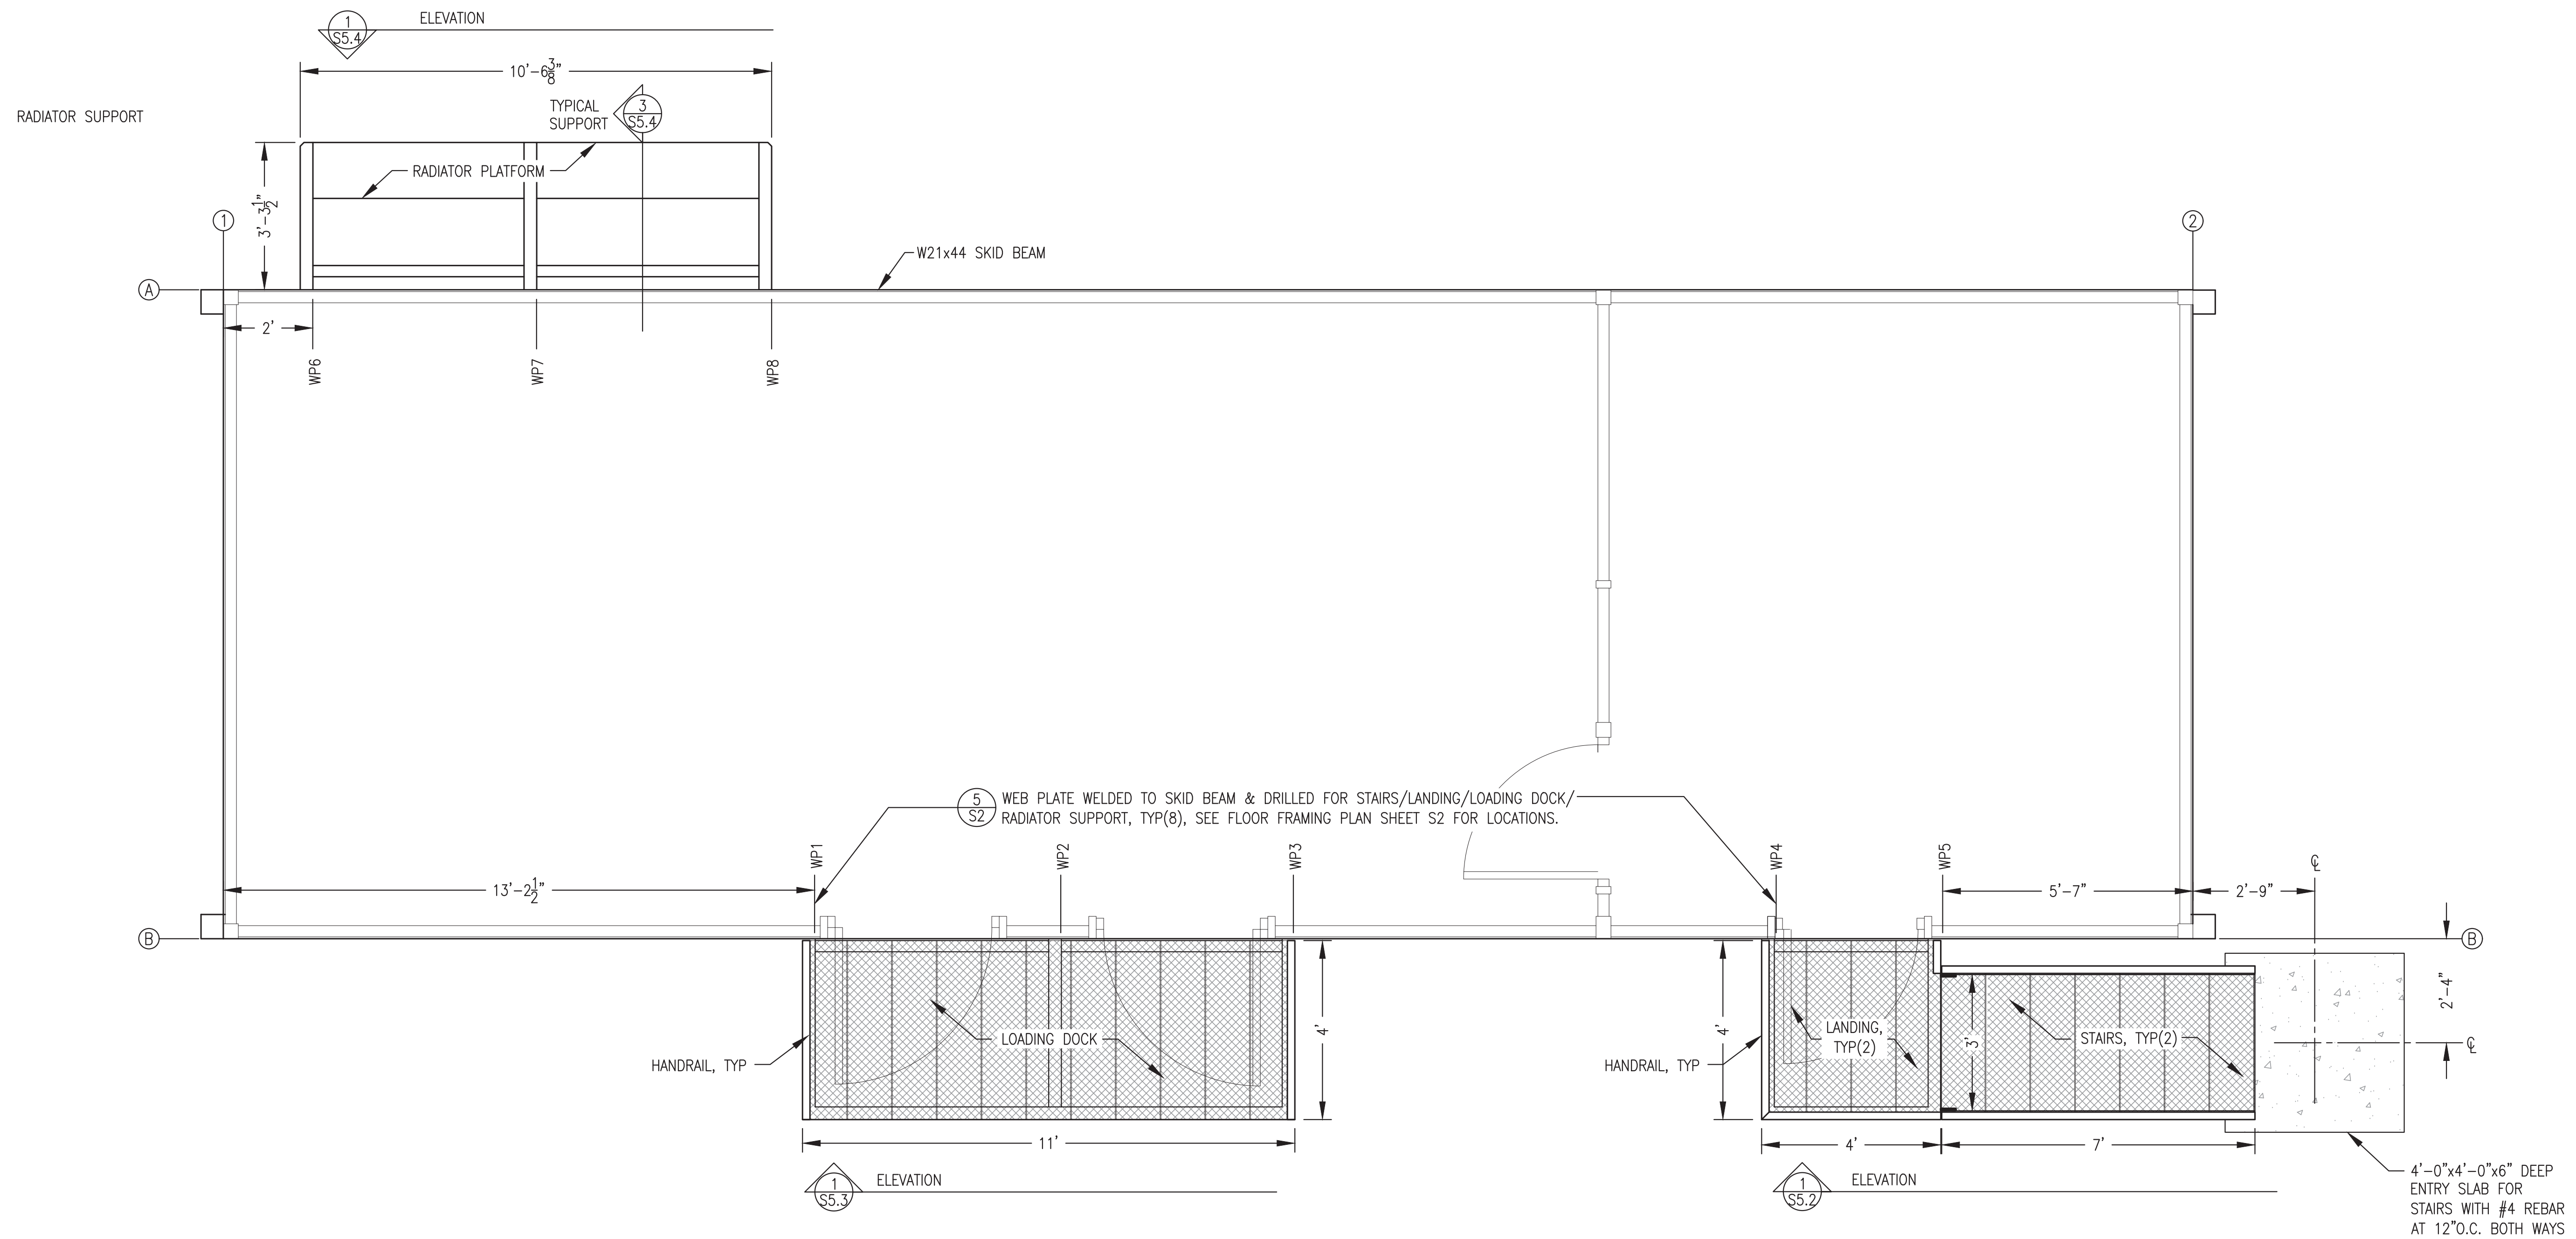
**3**  
S4  
ROOF TRUSS INSTALLATION  
NO SCALE

THIS DRAWING SHOWS WORK THAT WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT FOR ON SITE INSTALLATION AND IS PROVIDED HERE FOR REFERENCE ONLY.

REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022



1	REVISED FOR INTAKE DUCT INSTALLATION NOTES	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: ROOF FRAMING PLAN & DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: DGT/BCG		DATE: 3/15/22	
FILE NAME: RAM PP S1-S5		SHEET:	
PROJECT NUMBER:		<b>S4</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			




1 STAIRS, LANDINGS, LOADING DOCK & RADIATOR SUPPORT PLAN  
 S5.1 1/2"=1'-0"


- EXTERIOR ASSEMBLY FABRICATION GENERAL NOTES:**
- 1) THESE NOTES APPLY TO THE SHOP FABRICATION OF ALL EXTERIOR ASSEMBLIES SHOWN ON THE S5 SHEETS INCLUDING STAIRS, LANDINGS, LOADING DOCK, & RADIATOR SUPPORT.
  - 2) FABRICATE FROM ASTM A-36 STEEL SHAPES AND PLATE. STAIR AND PLATFORM TREADS TO BE PRE-GALVANIZED 2"x11-3/4"x12 GA. GRIP STRUT.
  - 3) RACK ALL SUPPORT BRACKETS LEVEL & PERPENDICULAR TO SKID WITH CONNECTIONS BOLTED TIGHT PRIOR TO WELDING.
  - 4) MAKE ALL JOINTS WITH CONTINUOUS GROOVE OR FILLET WELDS.
  - 5) SANDBLAST OR WIRE BRUSH ENDS OF PRE-GALV TREADS PRIOR TO WELDING TREADS TO STRUCTURE.
  - 6) UPON COMPLETION OF WELDING ROUND CORNERS AND GRIND EDGES SMOOTH.
  - 7) SANDBLAST ALL FABRICATIONS EXCEPT PRE-GALVANIZED GRIP STRUT TO SSPC-SP-6 AND APPLY 3 COATS OF COLD GALVANIZING COMPOUND, ZRC OR EQUAL.
  - 8) FURNISH GALVANIZED STEEL NUTS, BOLTS, AND WASHERS FOR FIELD ASSEMBLY.

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION OR THAT WILL BE PERFORMED BY OTHERS UNDER A SEPARATE FUTURE CONTRACT FOR ON SITE INSTALLATION AND IS PROVIDED HERE FOR REFERENCE ONLY.


ISSUED FOR  
 MODULE  
 CONSTRUCTION  
 MARCH 2022




ALASKA ENERGY AUTHORITY		
PROJECT: RAMPART POWER SYSTEM UPGRADE		
TITLE: STAIRS, LANDINGS, LOADING DOCK, & RADIATOR SUPPORT PLAN		
 Gray Stassel Engineering, Inc. P.O. 111405, Anchorage, AK 99511 (907)349-0100	DRAWN BY: JTD DESIGNED BY: DGT/BCG FILE NAME: RAM PP S1-S5 PROJECT NUMBER:	SCALE: AS NOTED DATE: 3/15/22 SHEET: <b>S5.1</b>

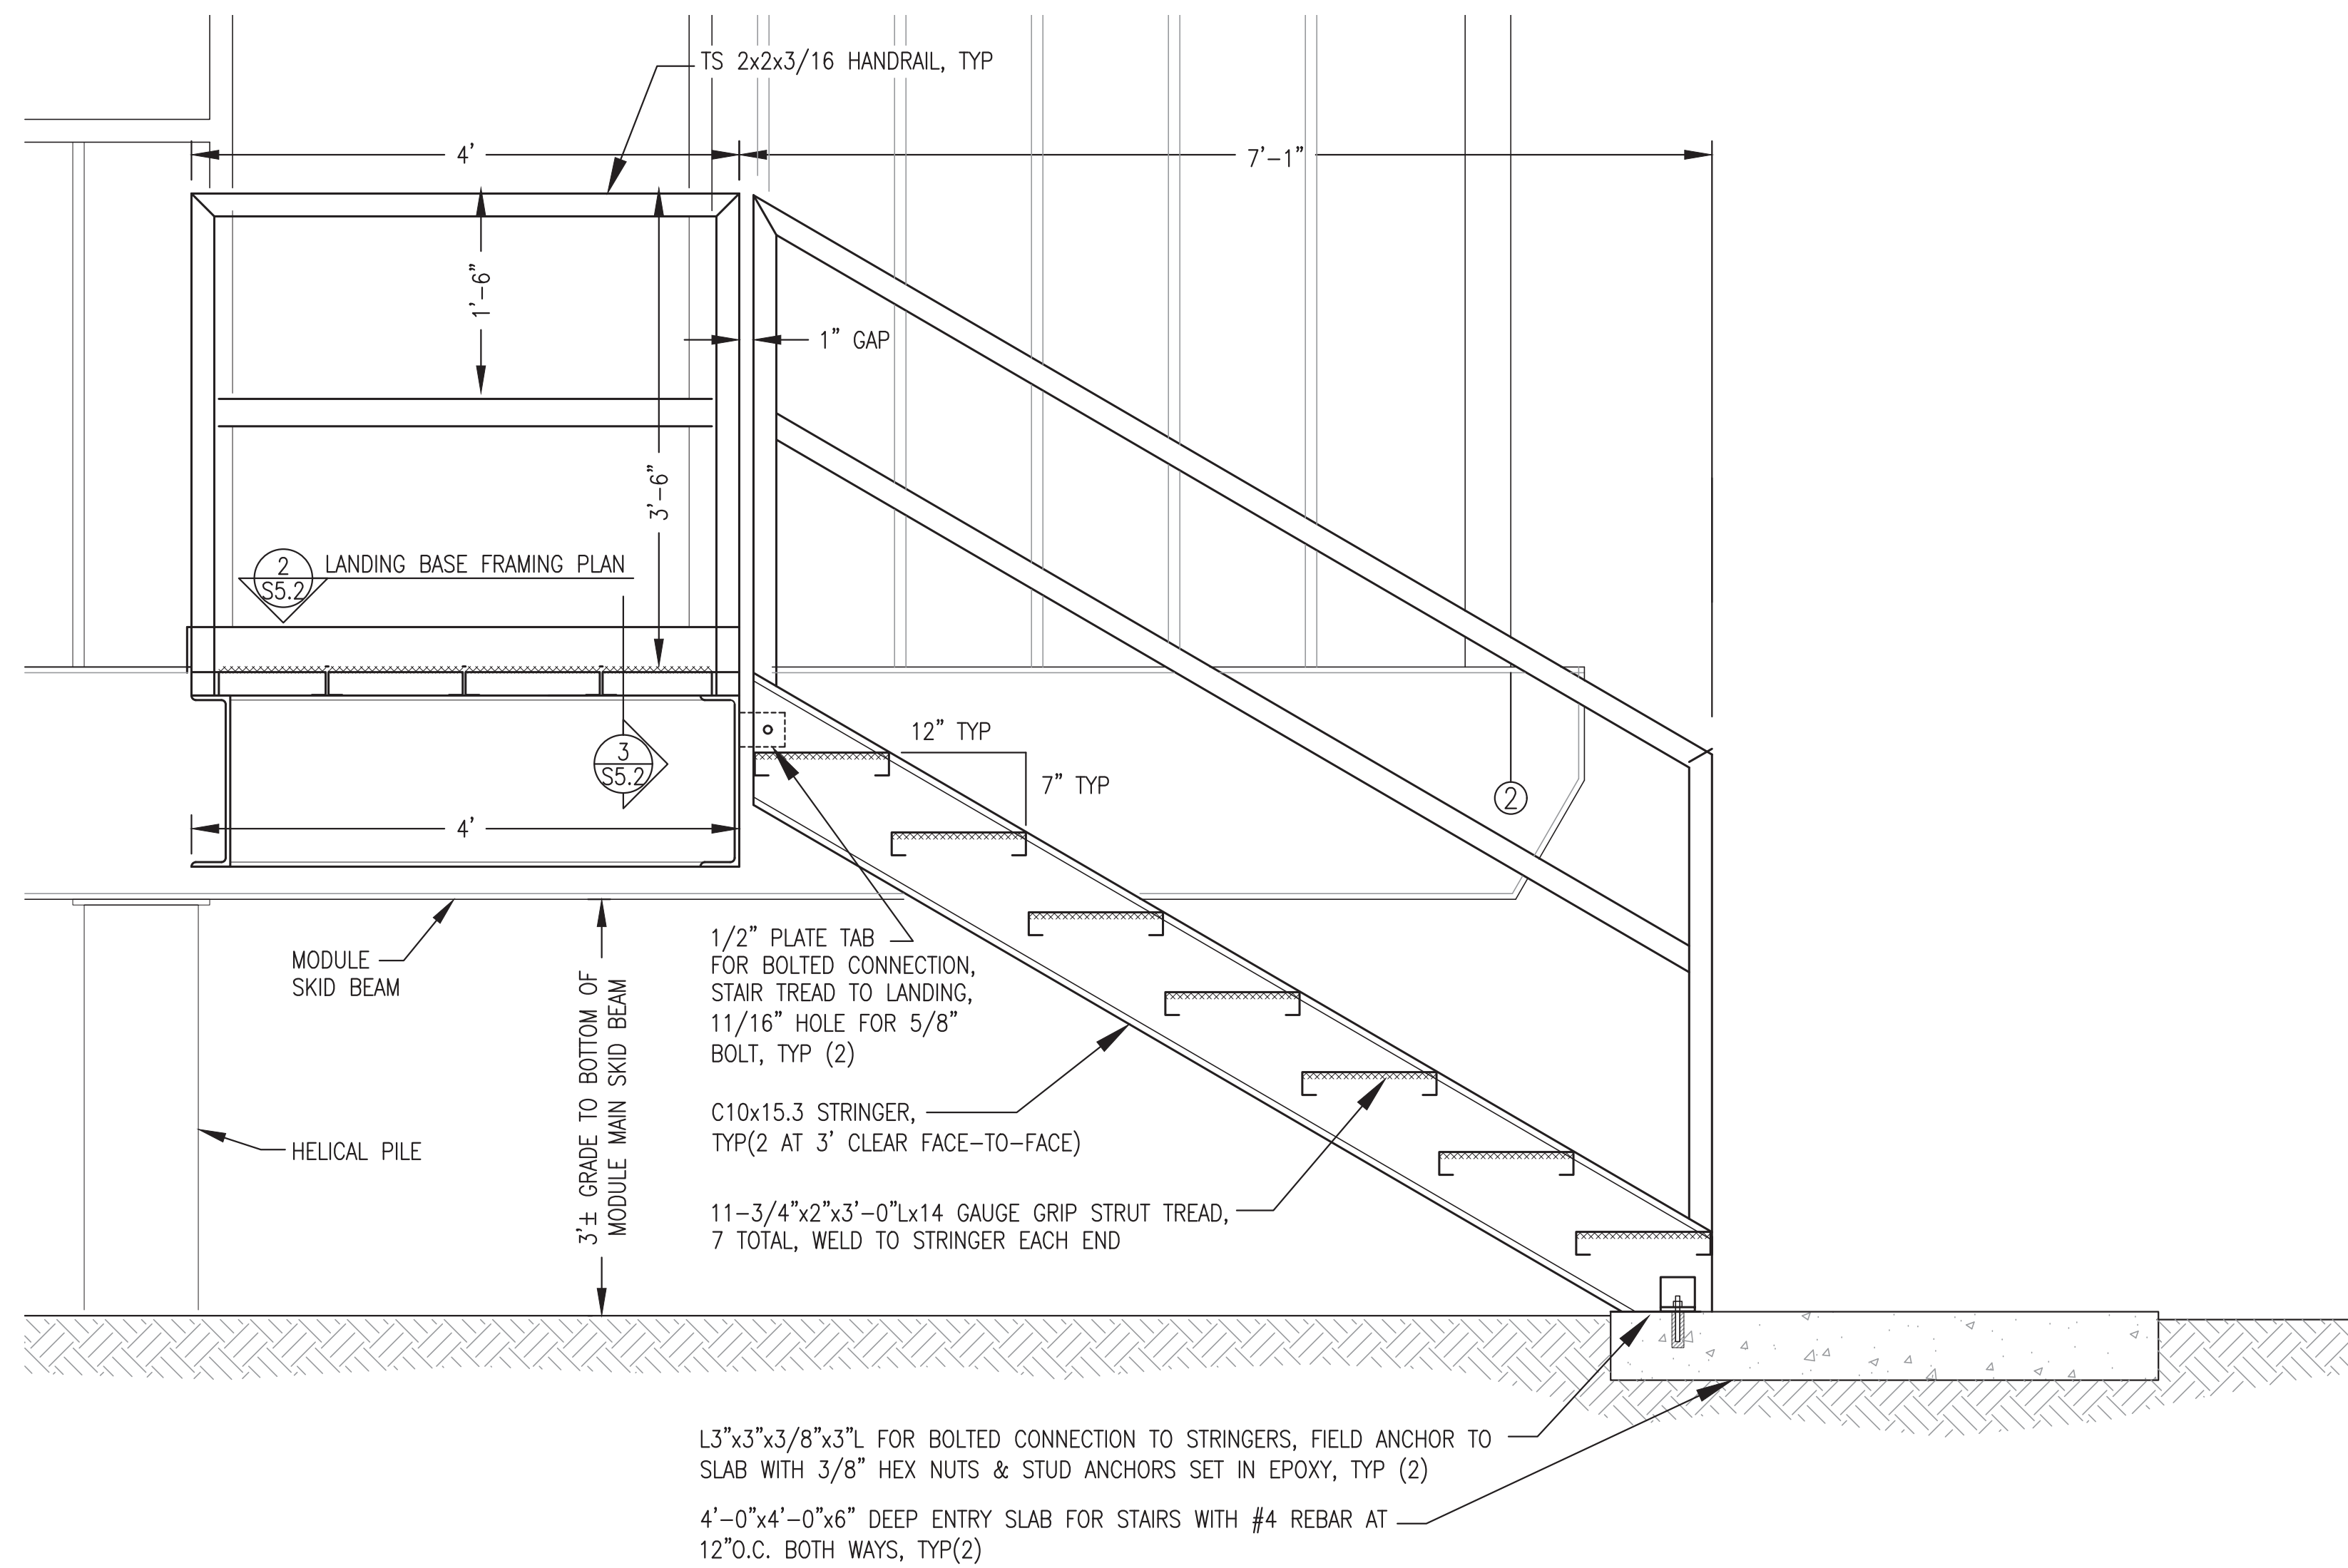

**1** STAIR/LANDING ELEVATION  
S5.2 1"-1'-0"

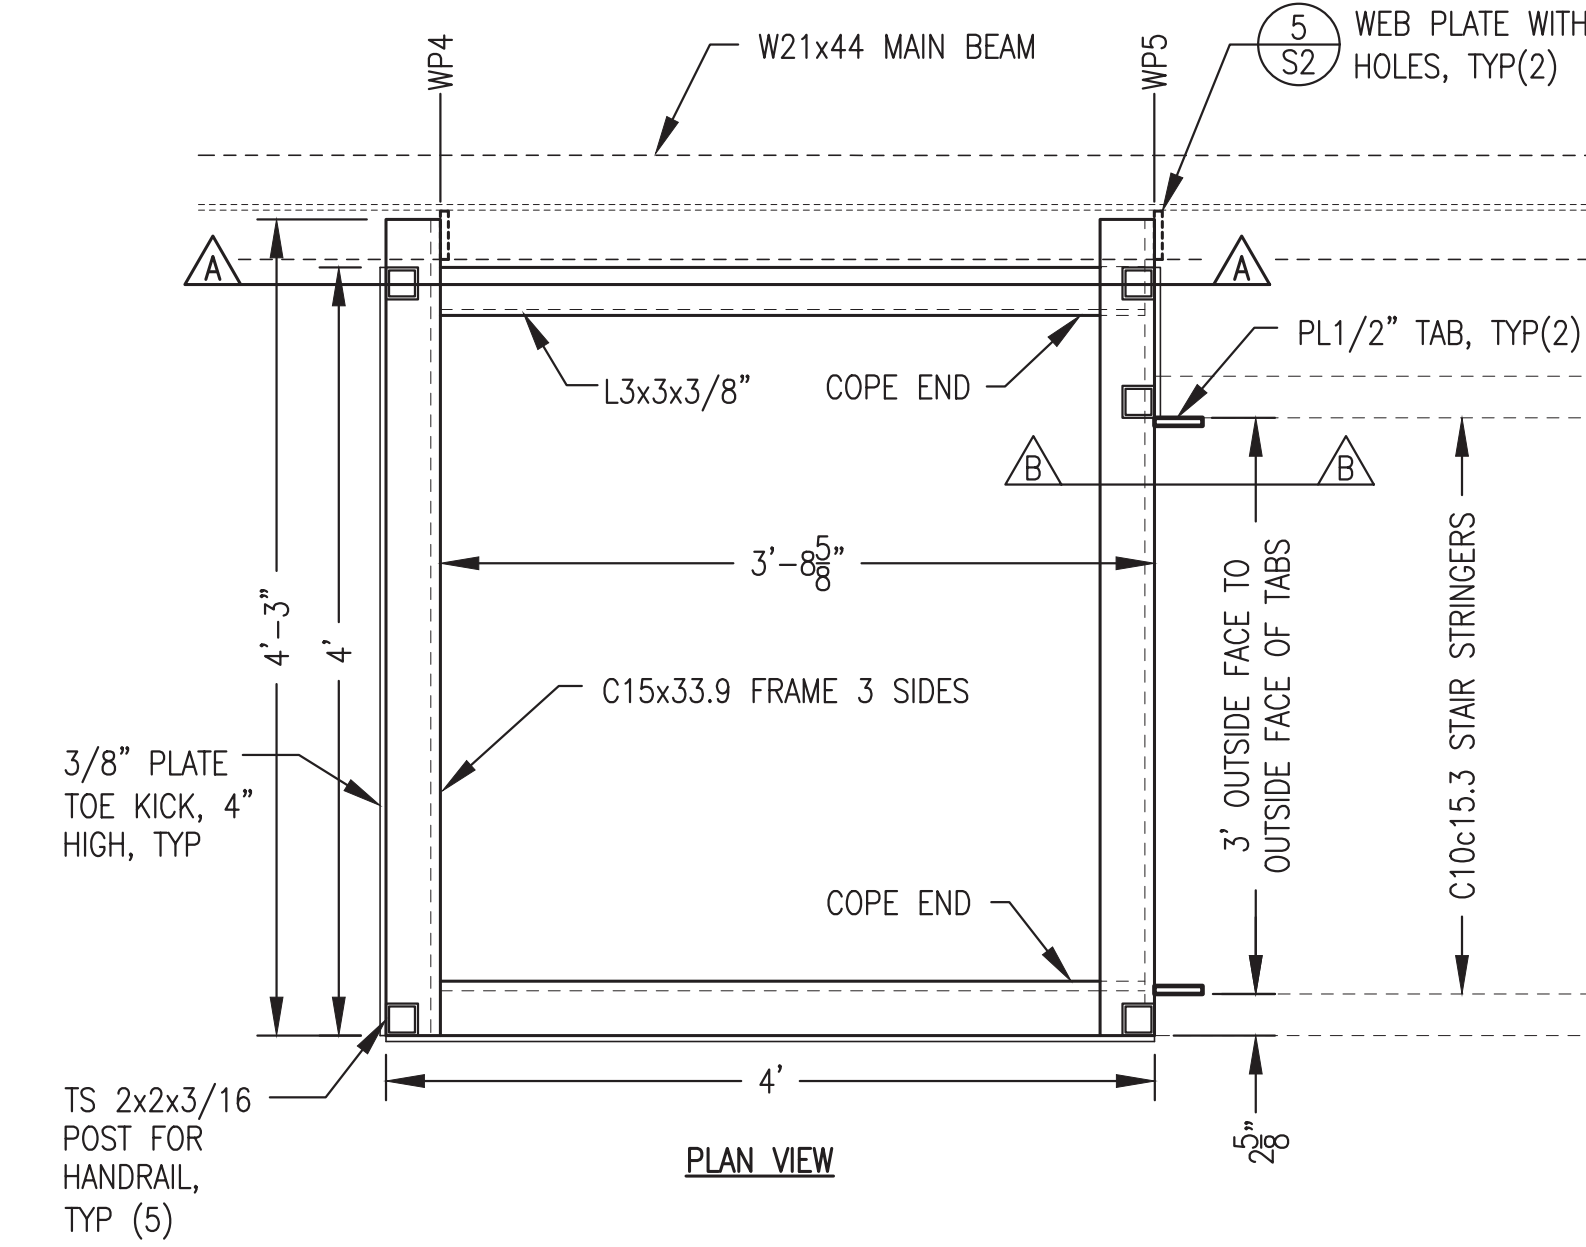

**2** LANDING BASE FRAMING PLAN & SECTIONS  
S5.2 1"-1'-0"

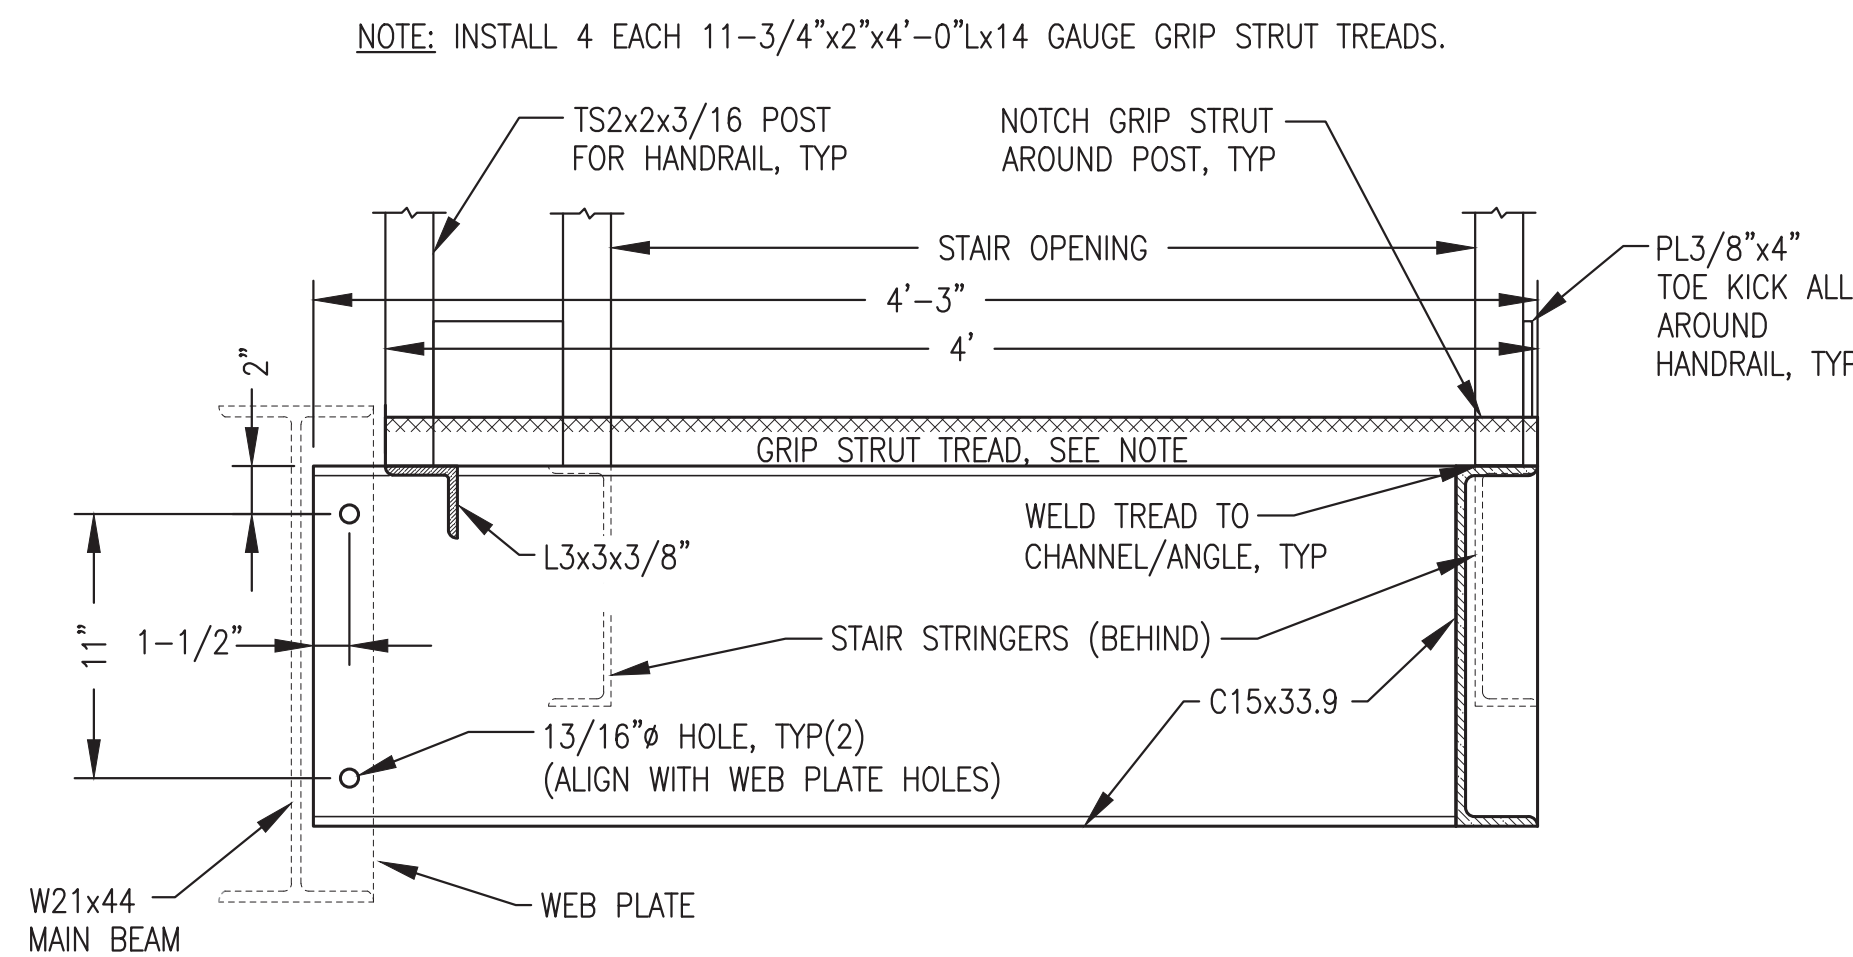


**3** LANDING SECTION & MAIN BEAM CONNECTION DETAIL  
S5.2 1-1/2"=1'-0"

**THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.**


REVISION #1  
ISSUED FOR  
CONSTRUCTION  
JULY 2022




1	REVISED FOR ONSITE FOUNDATION DESIGN	7/15/22	BCG
REV.	DESCRIPTION	DATE	BY
 ALASKA ENERGY AUTHORITY			
PROJECT: RAMPART POWER SYSTEM UPGRADE			
TITLE: STAIRS/LANDINGS FABRICATION DETAILS			
DRAWN BY: JTD		SCALE: AS NOTED	
DESIGNED BY: DGT/BCG		DATE: 3/15/22	
FILE NAME: RAM PP S1-S5		SHEET:	
PROJECT NUMBER:		<b>S5.2</b>	
P.O. 111405, Anchorage, AK 99511 (907)349-0100			

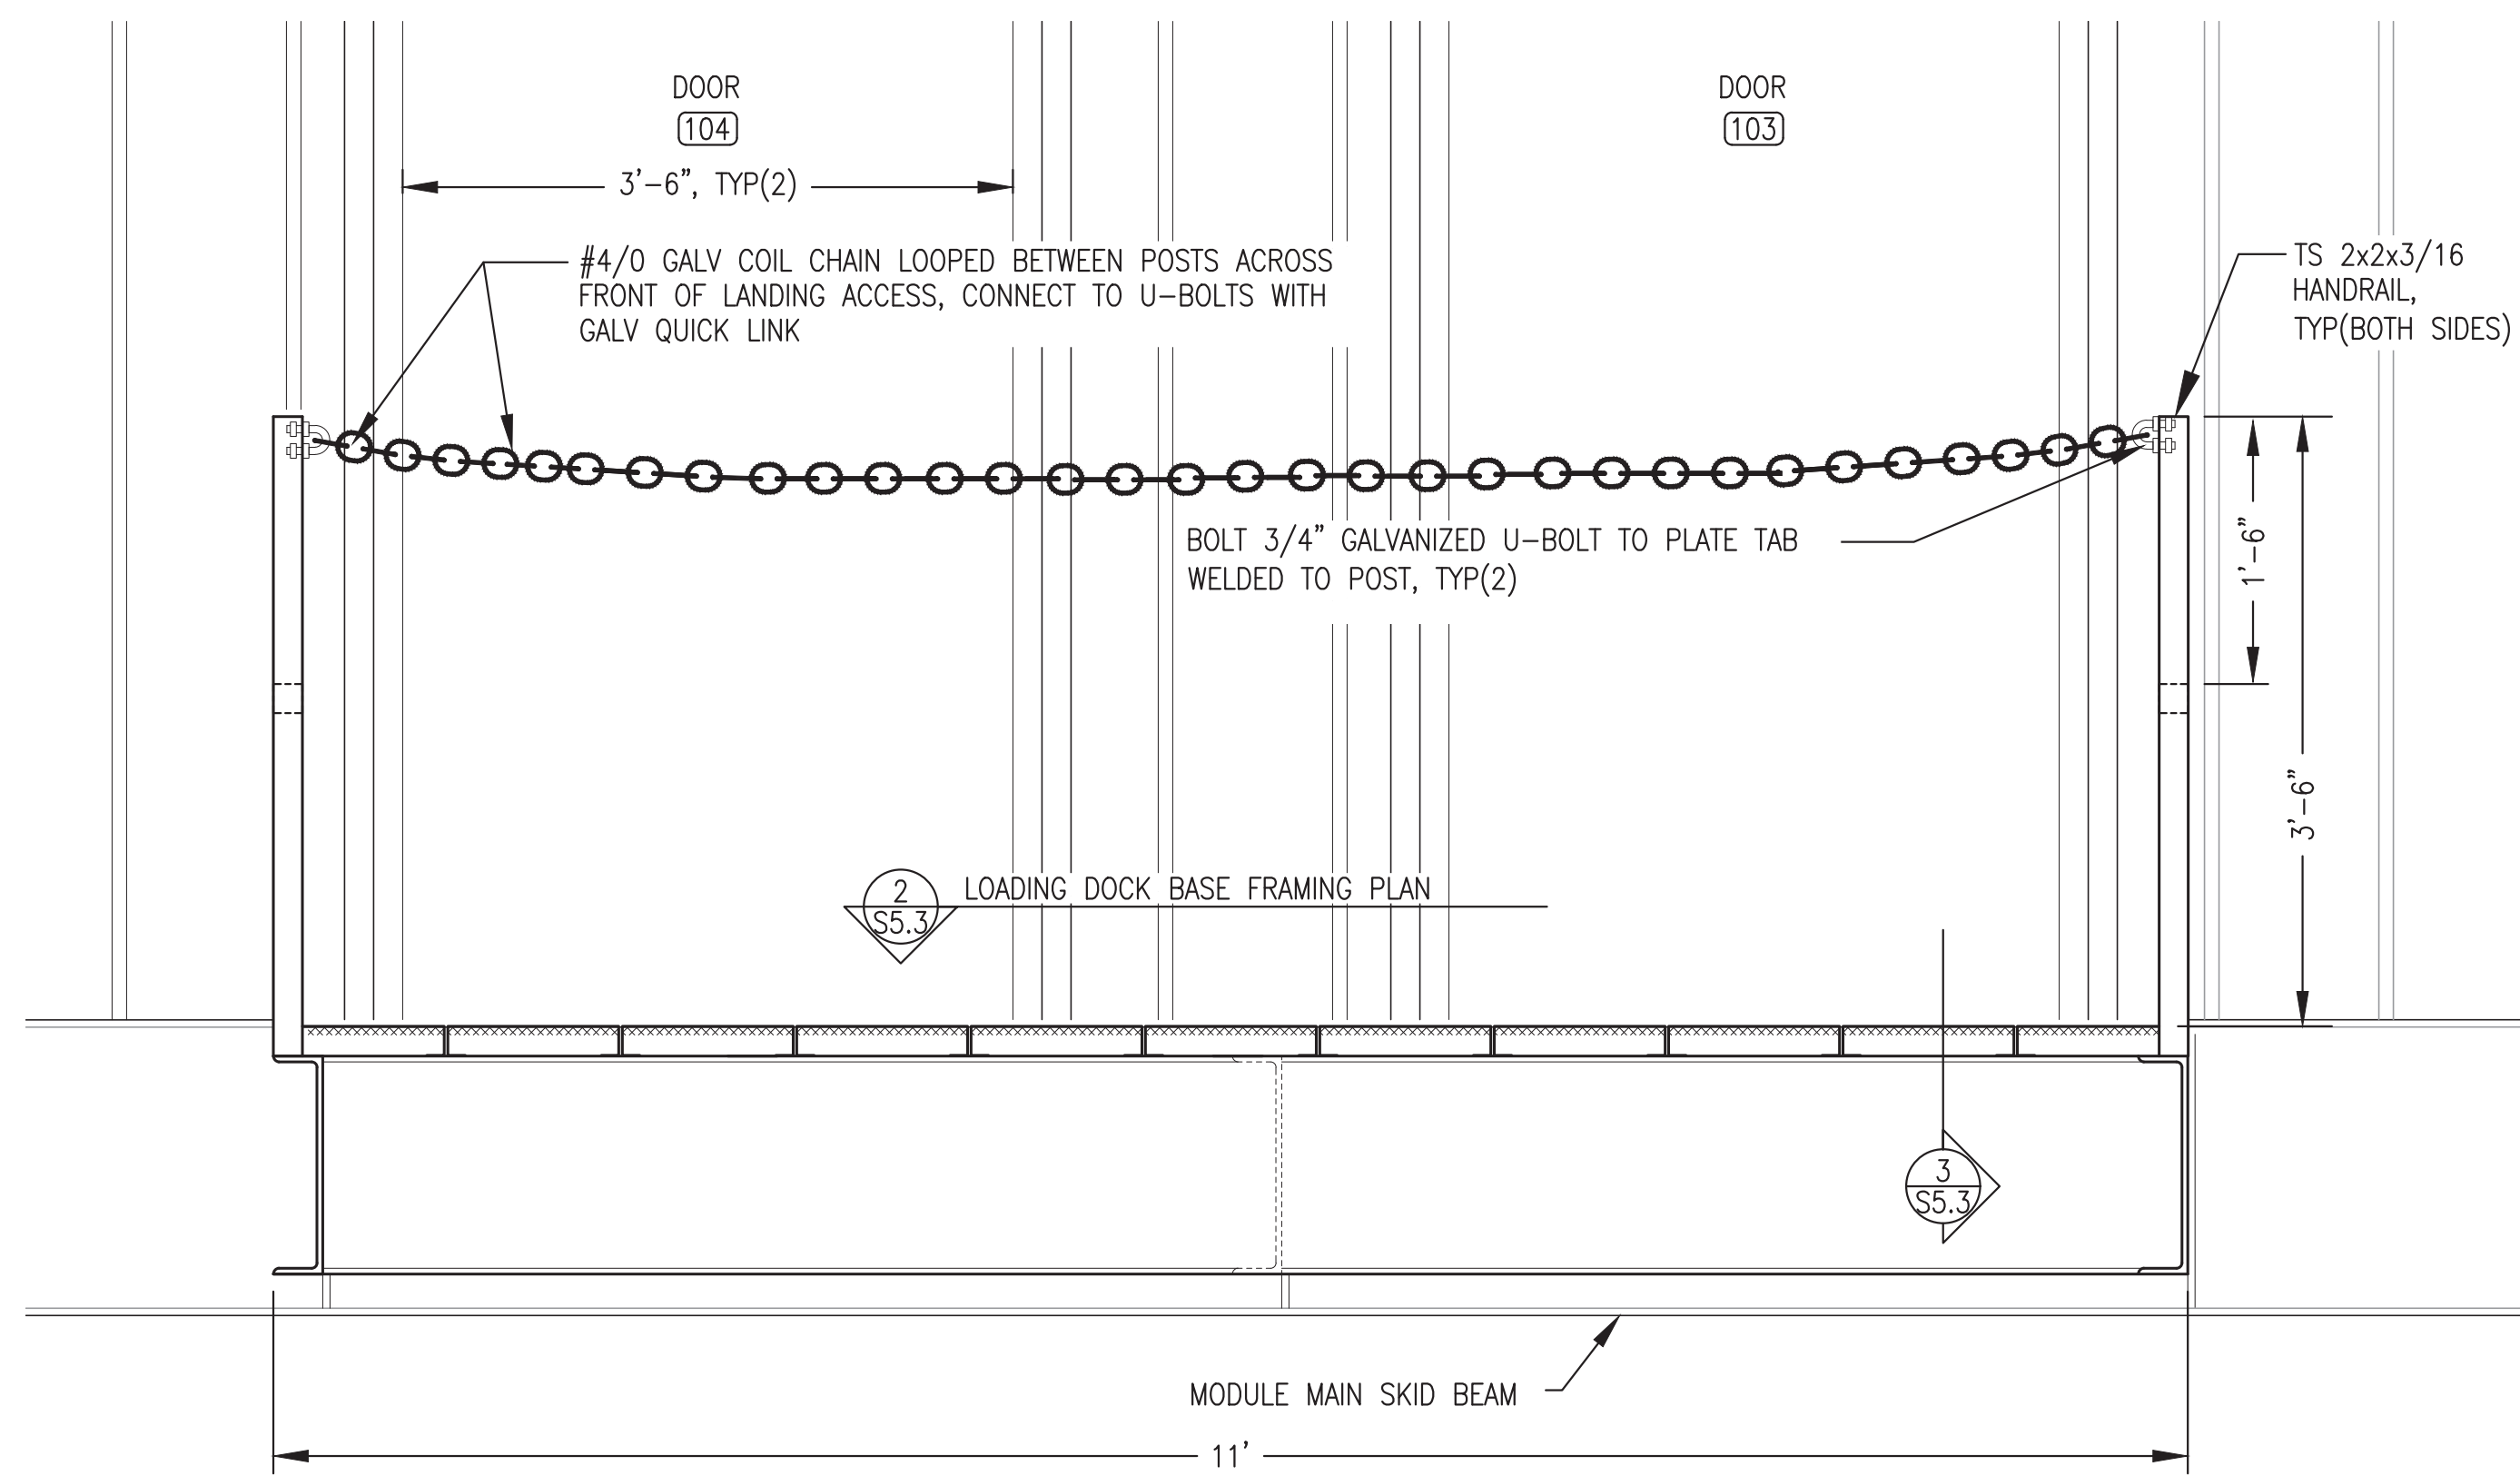

1 **LOADING DOCK ELEVATION**  
S5.3 1"=1'-0"

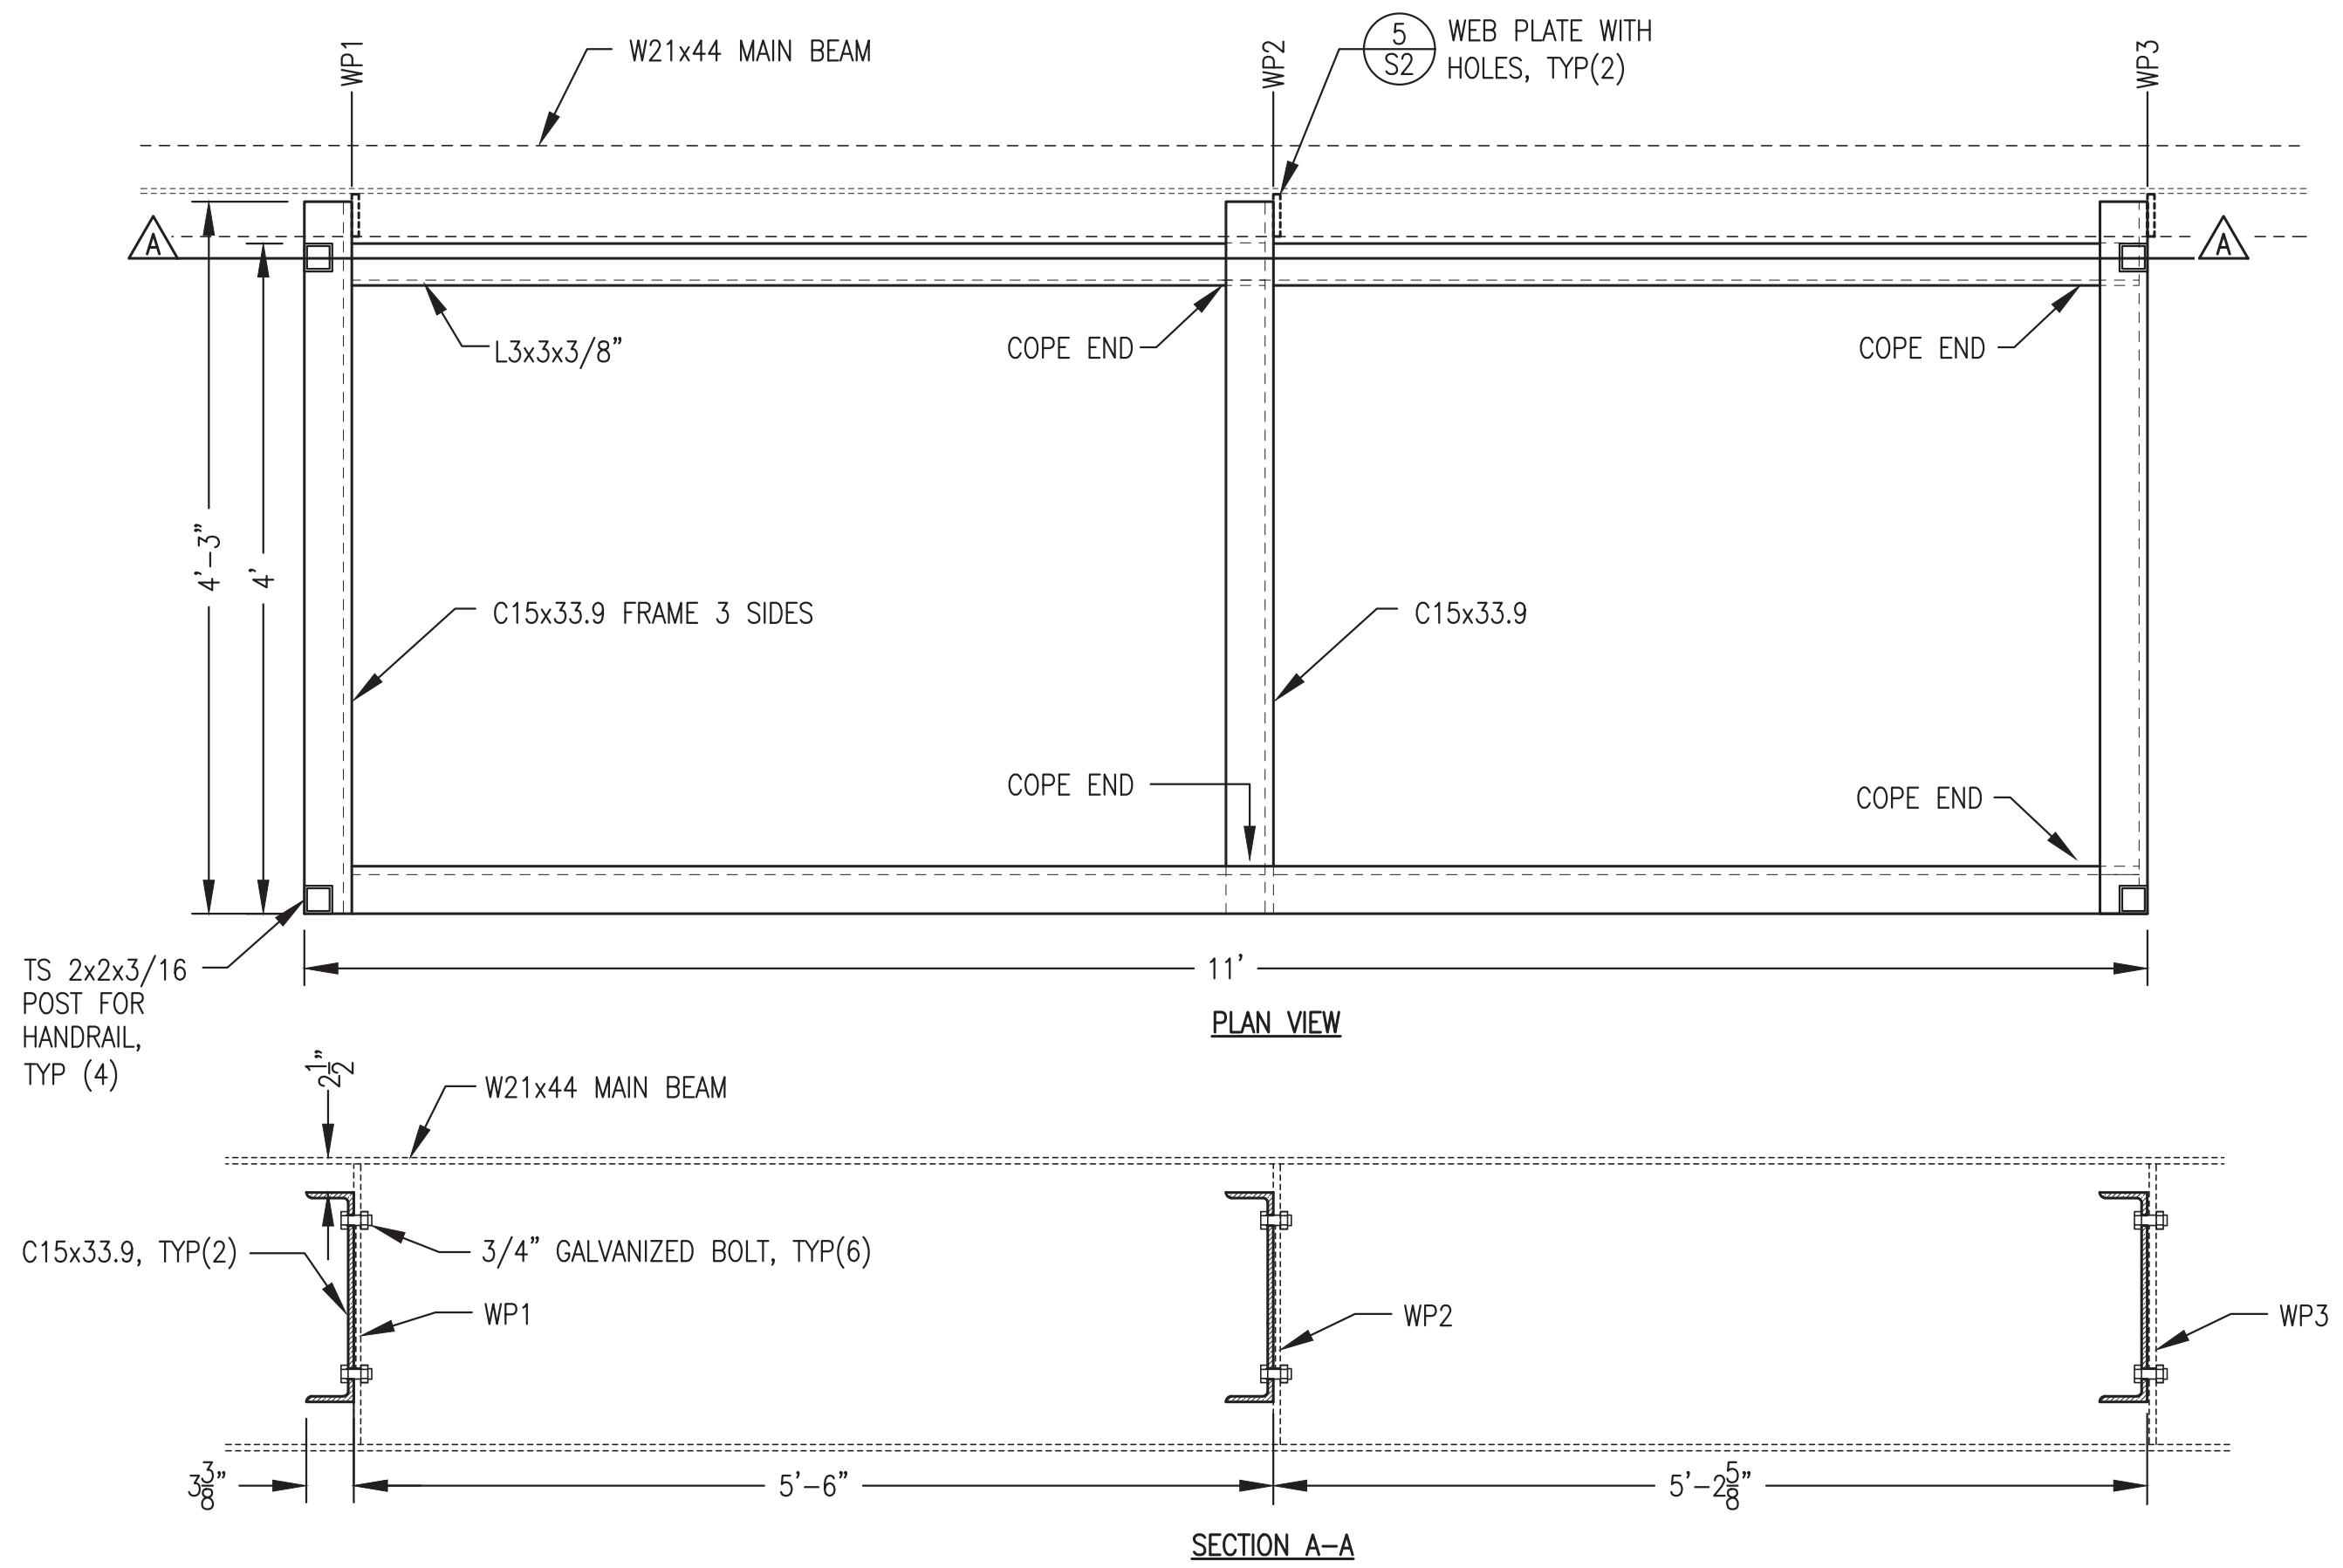


2 **LOADING DOCK BASE FRAMING PLAN & SECTION**  
S5.3 1"=1'-0"

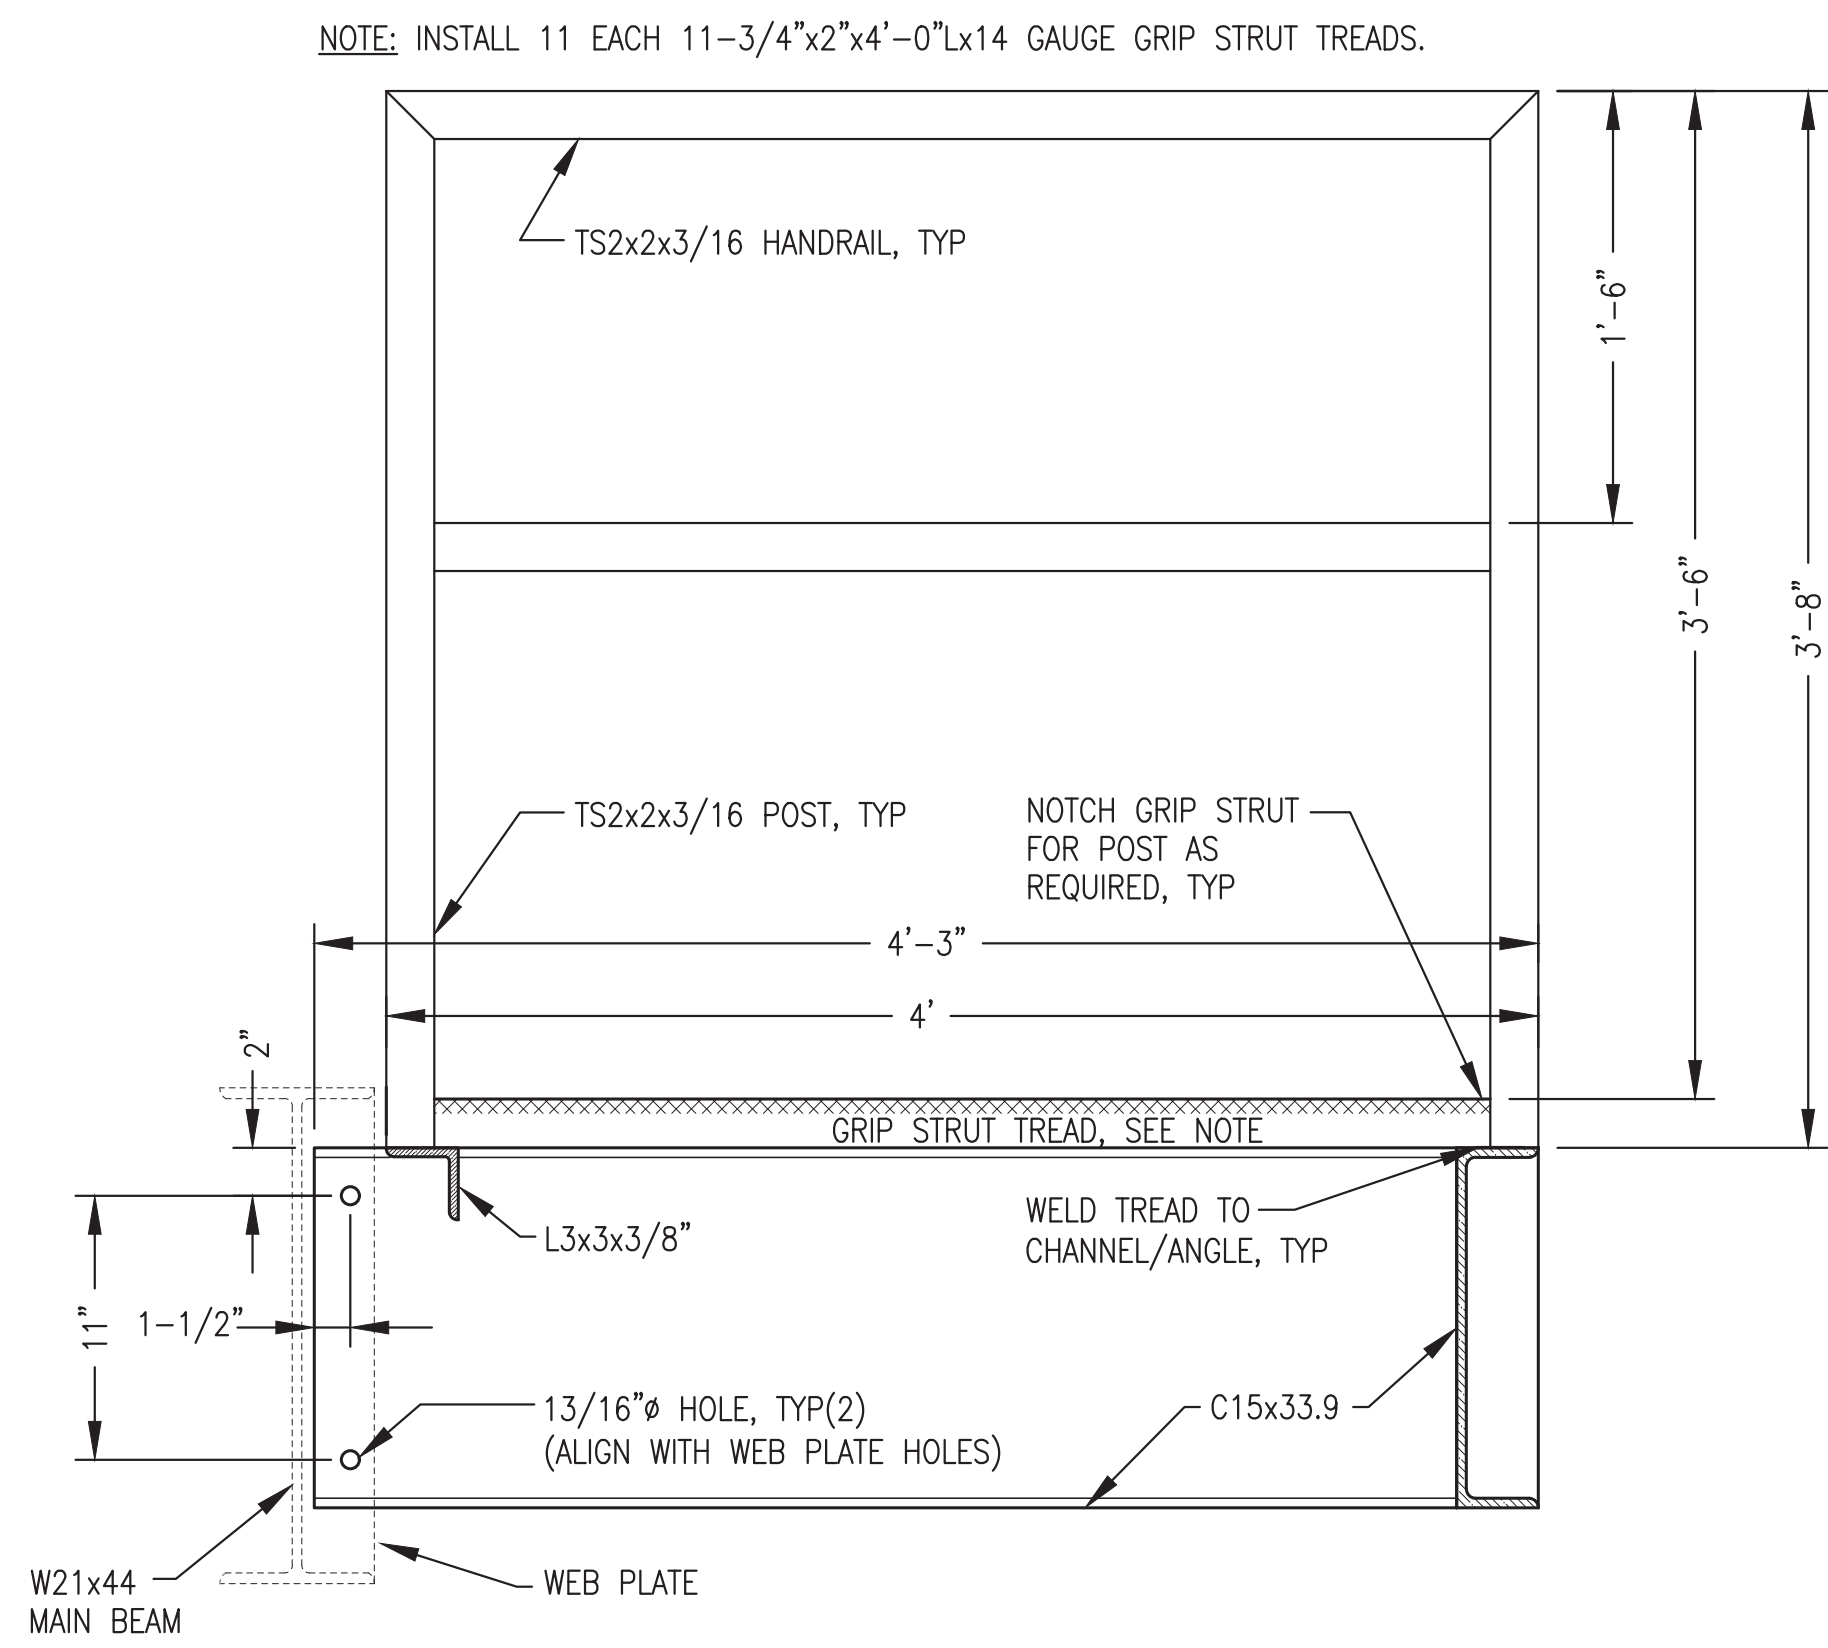

3 **LOADING DOCK SECTION & MAIN BEAM CONNECTION DETAIL**  
S5.3 1-1/2"=1'-0"


THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.

ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022




PROJECT: <b>RAMPART POWER SYSTEM UPGRADE</b>		
TITLE: <b>LOADING DOCK FABRICATION DETAILS</b>		
DRAWN BY: JTD	SCALE: AS NOTED	
DESIGNED BY: DGT/BCG	DATE: 3/15/22	
FILE NAME: RAM PP S1-S5	SHEET:	<b>S5.3</b>
PROJECT NUMBER:		


P.O. 111405, Anchorage, AK 99511 (907)349-0100

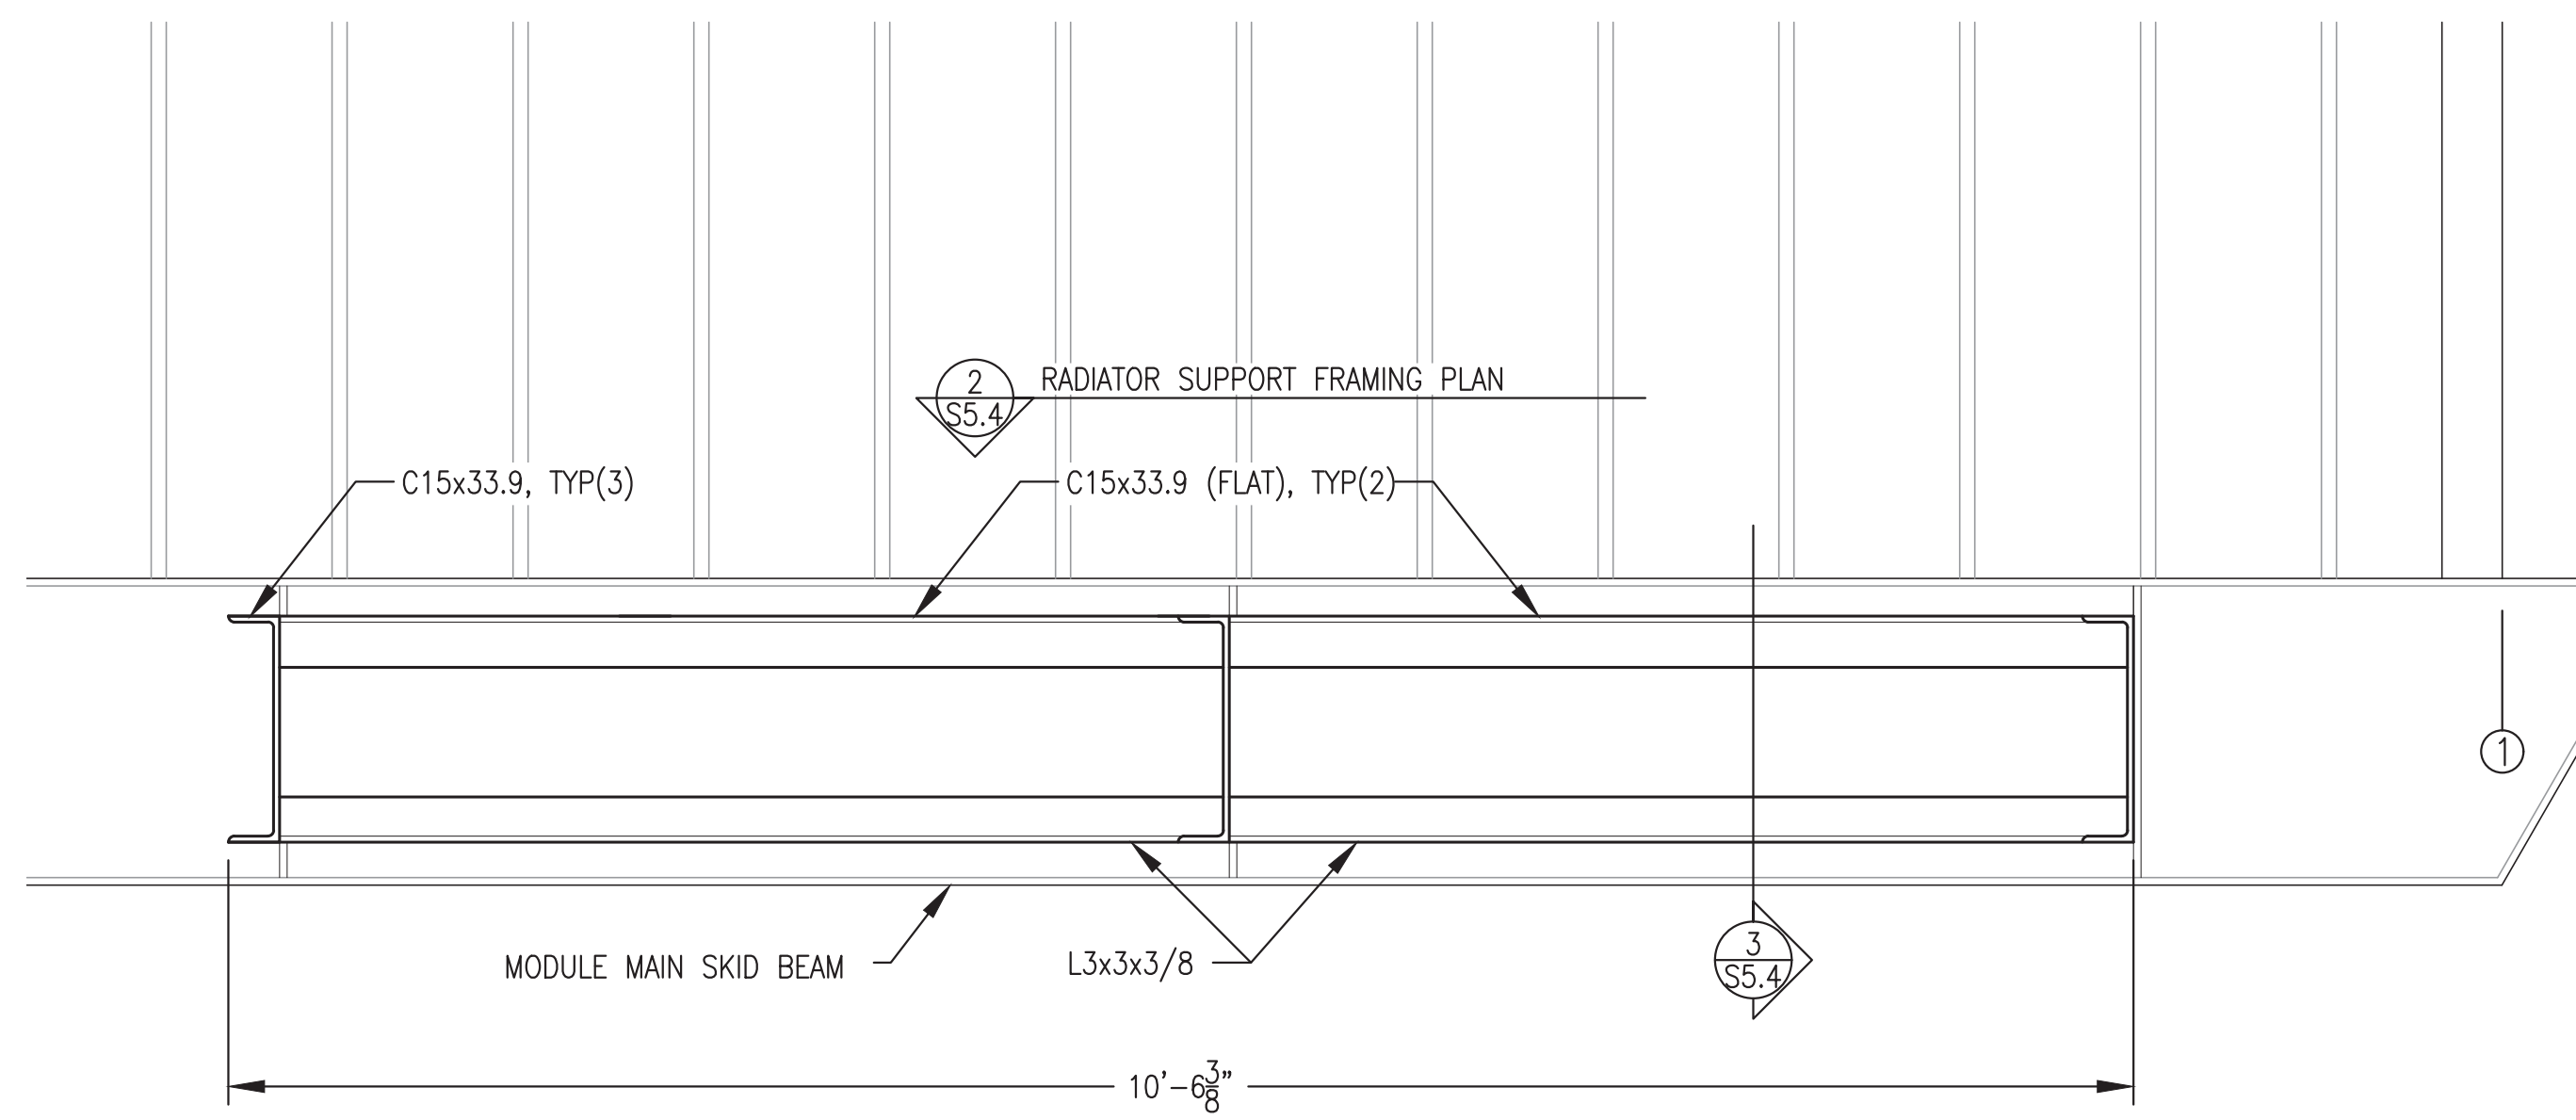

1 RADIATOR SUPPORT ELEVATION  
S5.4 1"=1'-0"

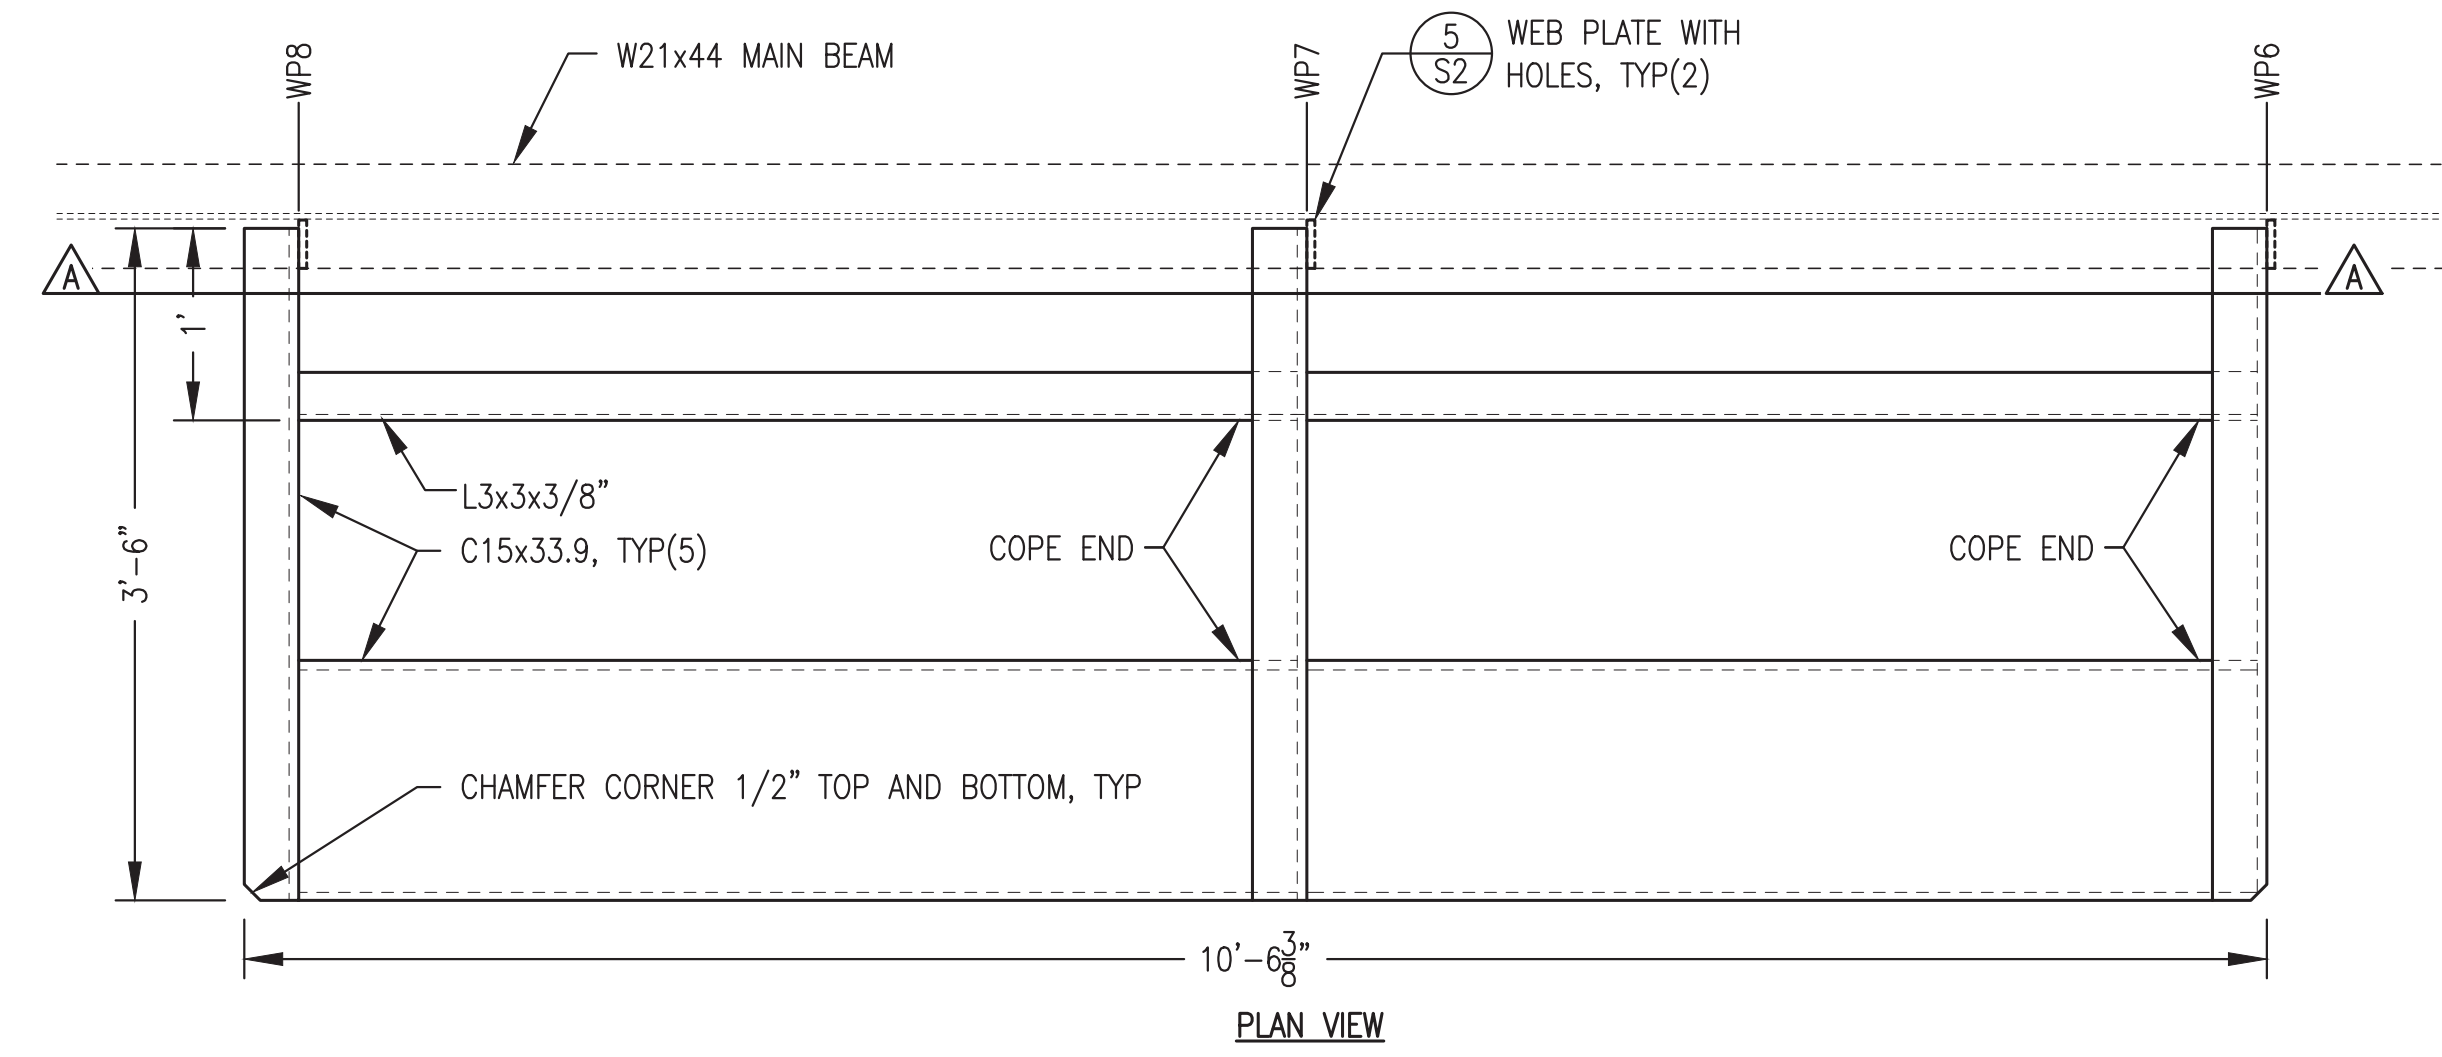


2 RADIATOR SUPPORT FRAMING PLAN & SECTION  
S5.4 1"=1'-0"

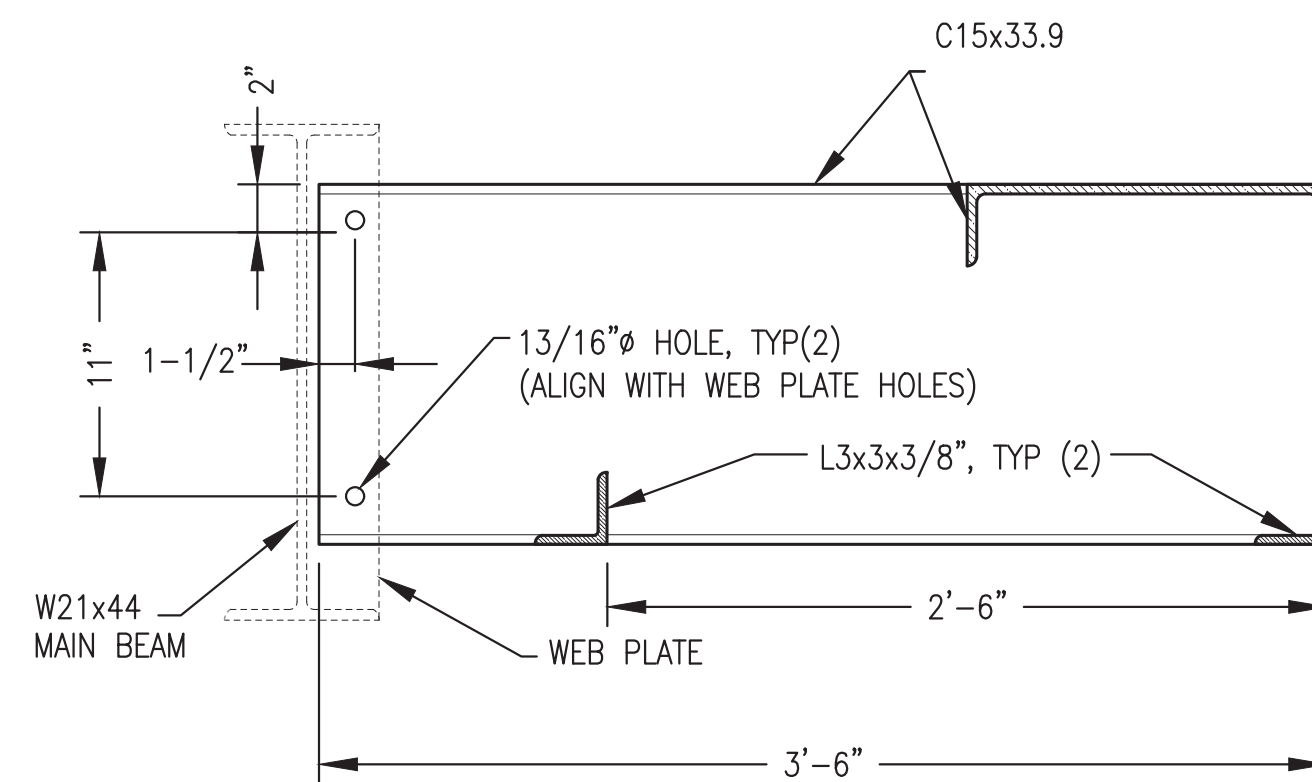

3 RADIATOR SUPPORT SECTION & MAIN BEAM CONNECTION DETAIL  
S5.4 1-1/2"=1'-0"


THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.

ISSUED FOR  
MODULE  
CONSTRUCTION  
MARCH 2022



PROJECT: RAMPART POWER SYSTEM UPGRADE		
TITLE: RADIATOR SUPPORT FABRICATION DETAILS		
DRAWN BY: JTD	SCALE: AS NOTED	DESIGNED BY: DGT/BCG
FILE NAME: RAM PP S1-S5	SHEET:	DATE: 3/15/22
PROJECT NUMBER:		<b>S5.4</b>

**Gray Stassel Engineering, Inc.**  
P.O. 111405, Anchorage, AK 99511 (907)349-0100

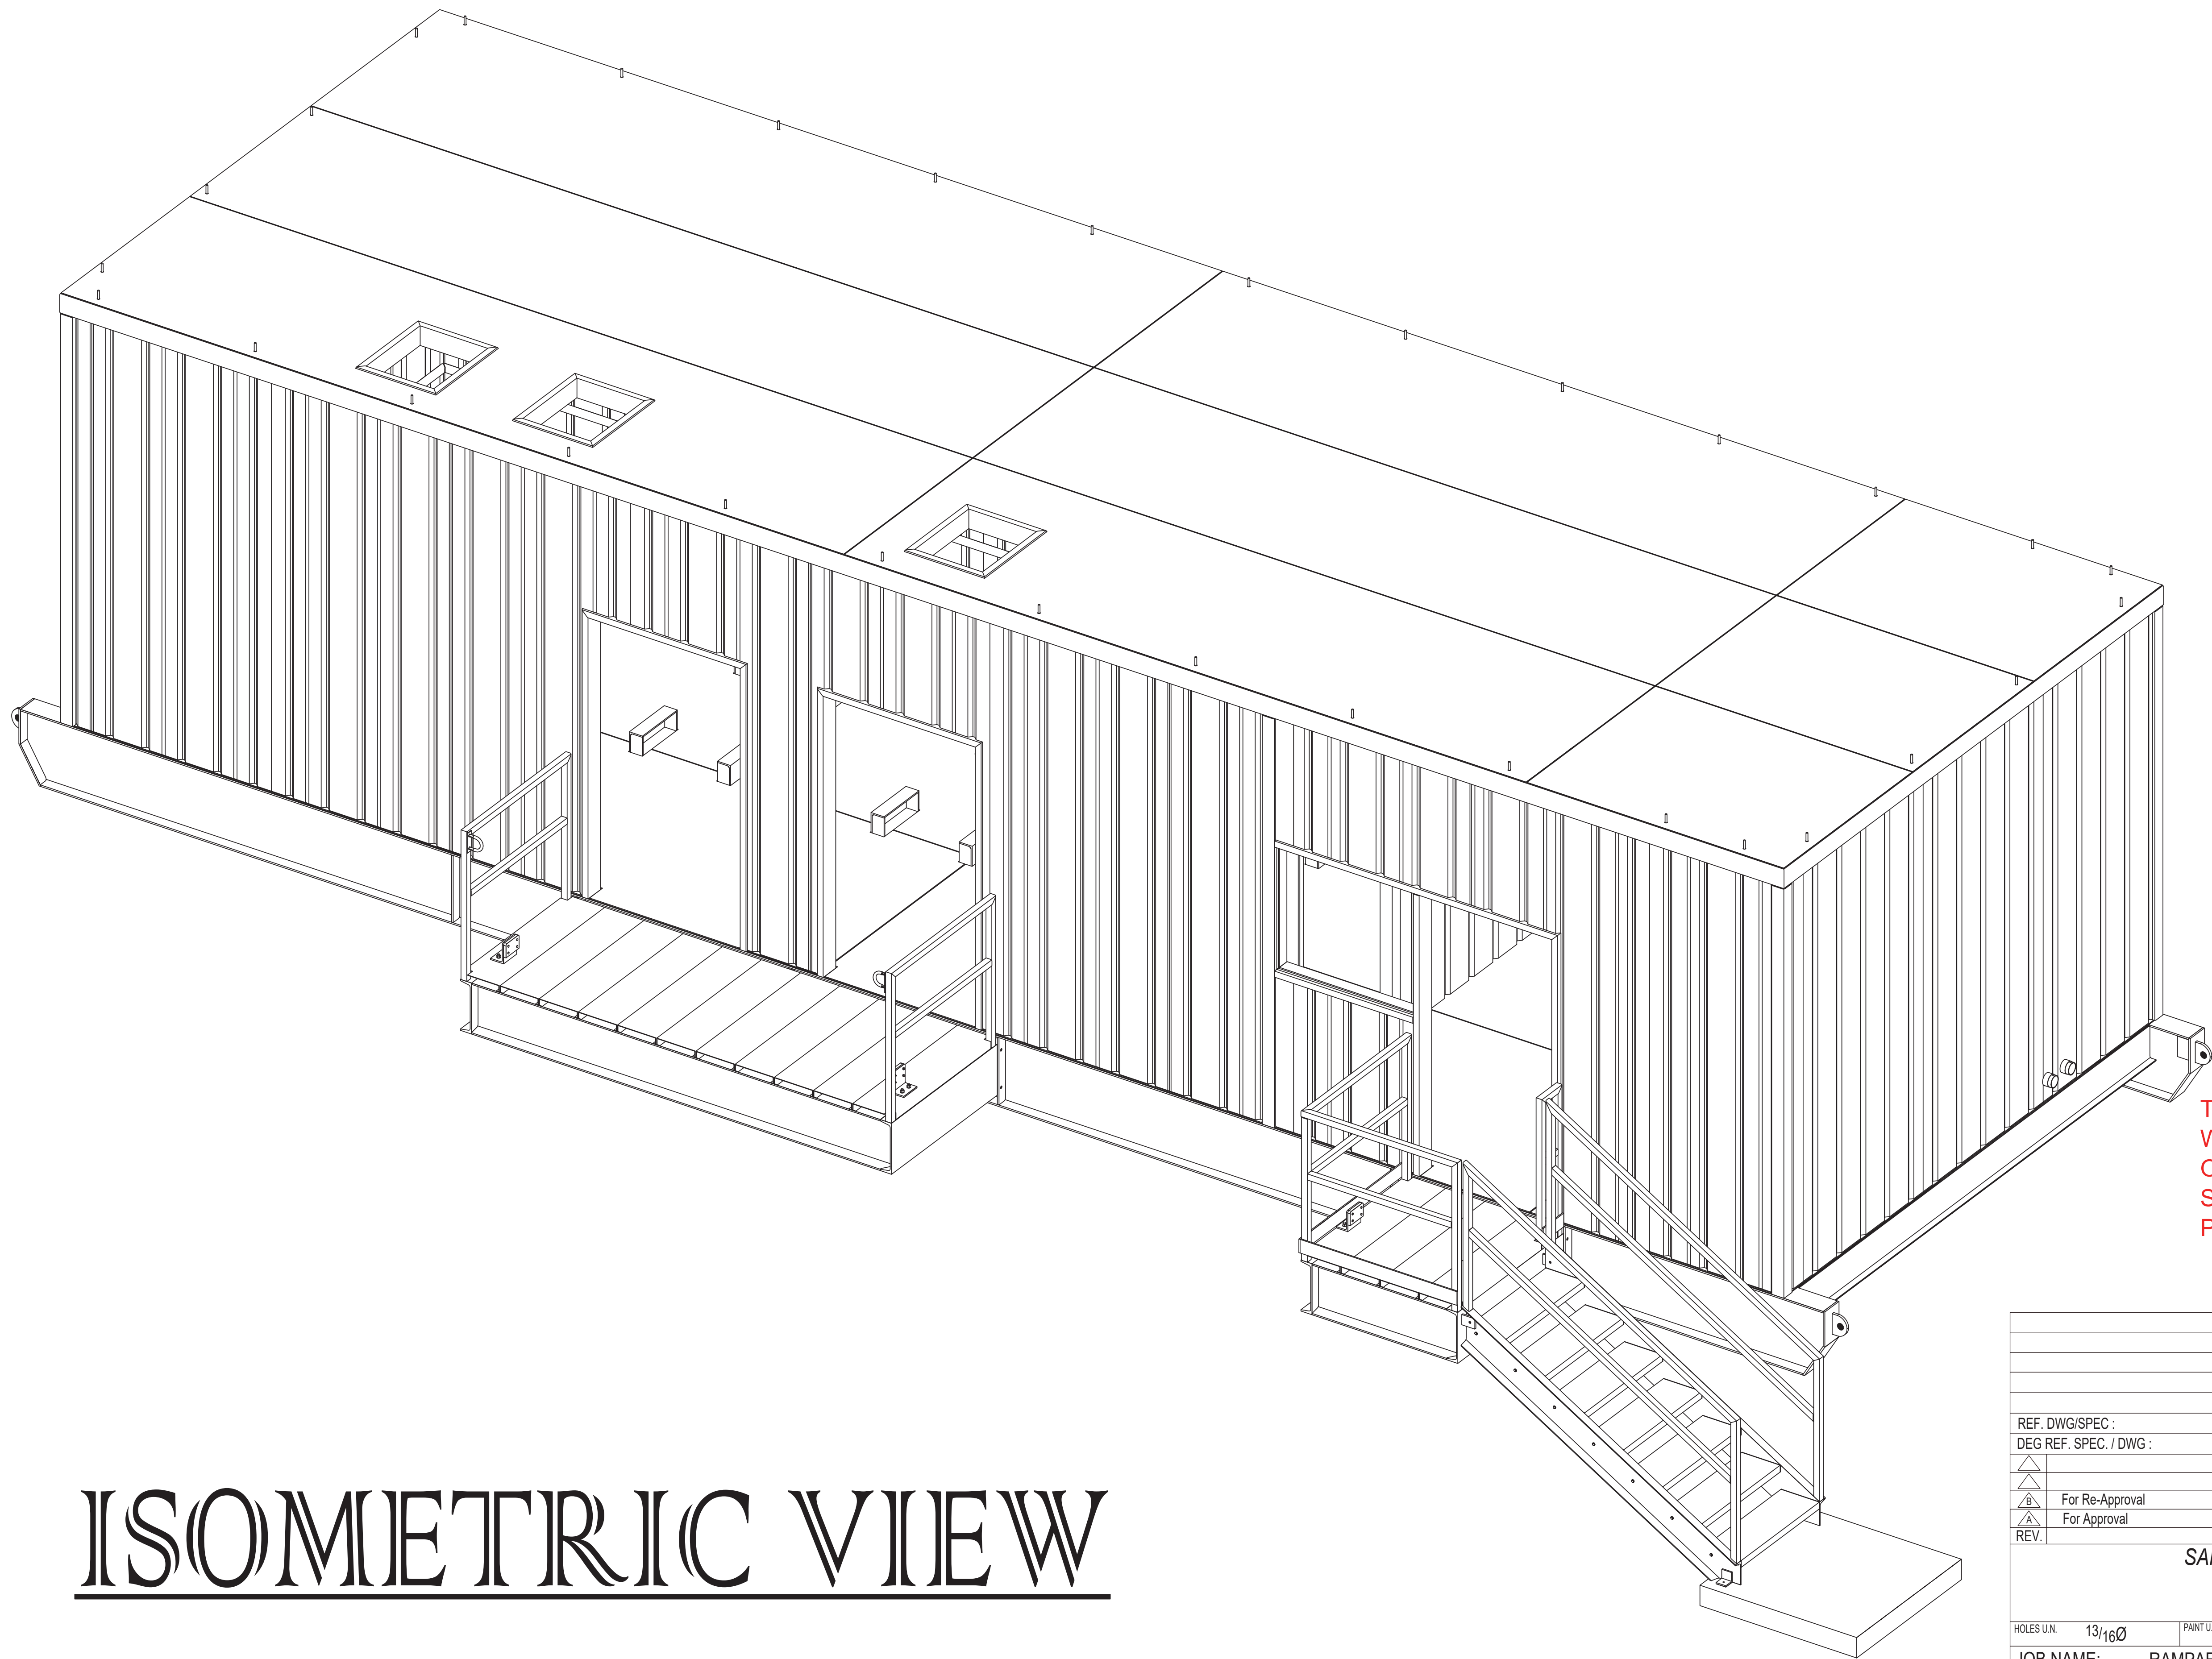


THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.

FOR APPROVAL

**ISOMETRIC VIEW**

FIELD NOTES:			
REF. DWG/SPEC :			
DEG REF. SPEC. / DWG :			
△			
△	For Re-Approval	ALN	07-04-22
△	For Approval	ALN	06-20-22
REV.	DESCRIPTION	BY	DATE
<b>SAMPSON STEEL COMPANY INC.</b>			
1848 POST ROAD ANCHORAGE, ALASKA 99501 PH. ( 907 ) 561-5626 FAX. ( 907 ) 561-5625			
HOLES U.N.	13/16Ø	PAINT U.N.	WELDS E70XX
CLEANING:			
JOB NAME:	RAMPART POWER SYSTEM UPGRADE	DR. BY:	PKM
LOCATION:	ALASKA	CHK. BY:	ALN
CONTRACTOR:	ALASKA ENERGY AUTHORITY	SCALE:	N.A.
DESCRIPTION:	ISOMETRIC VIEW	DATE:	05-26-22
		JOB NUMBER	459
		SHEET NO.	V105
		REV	△



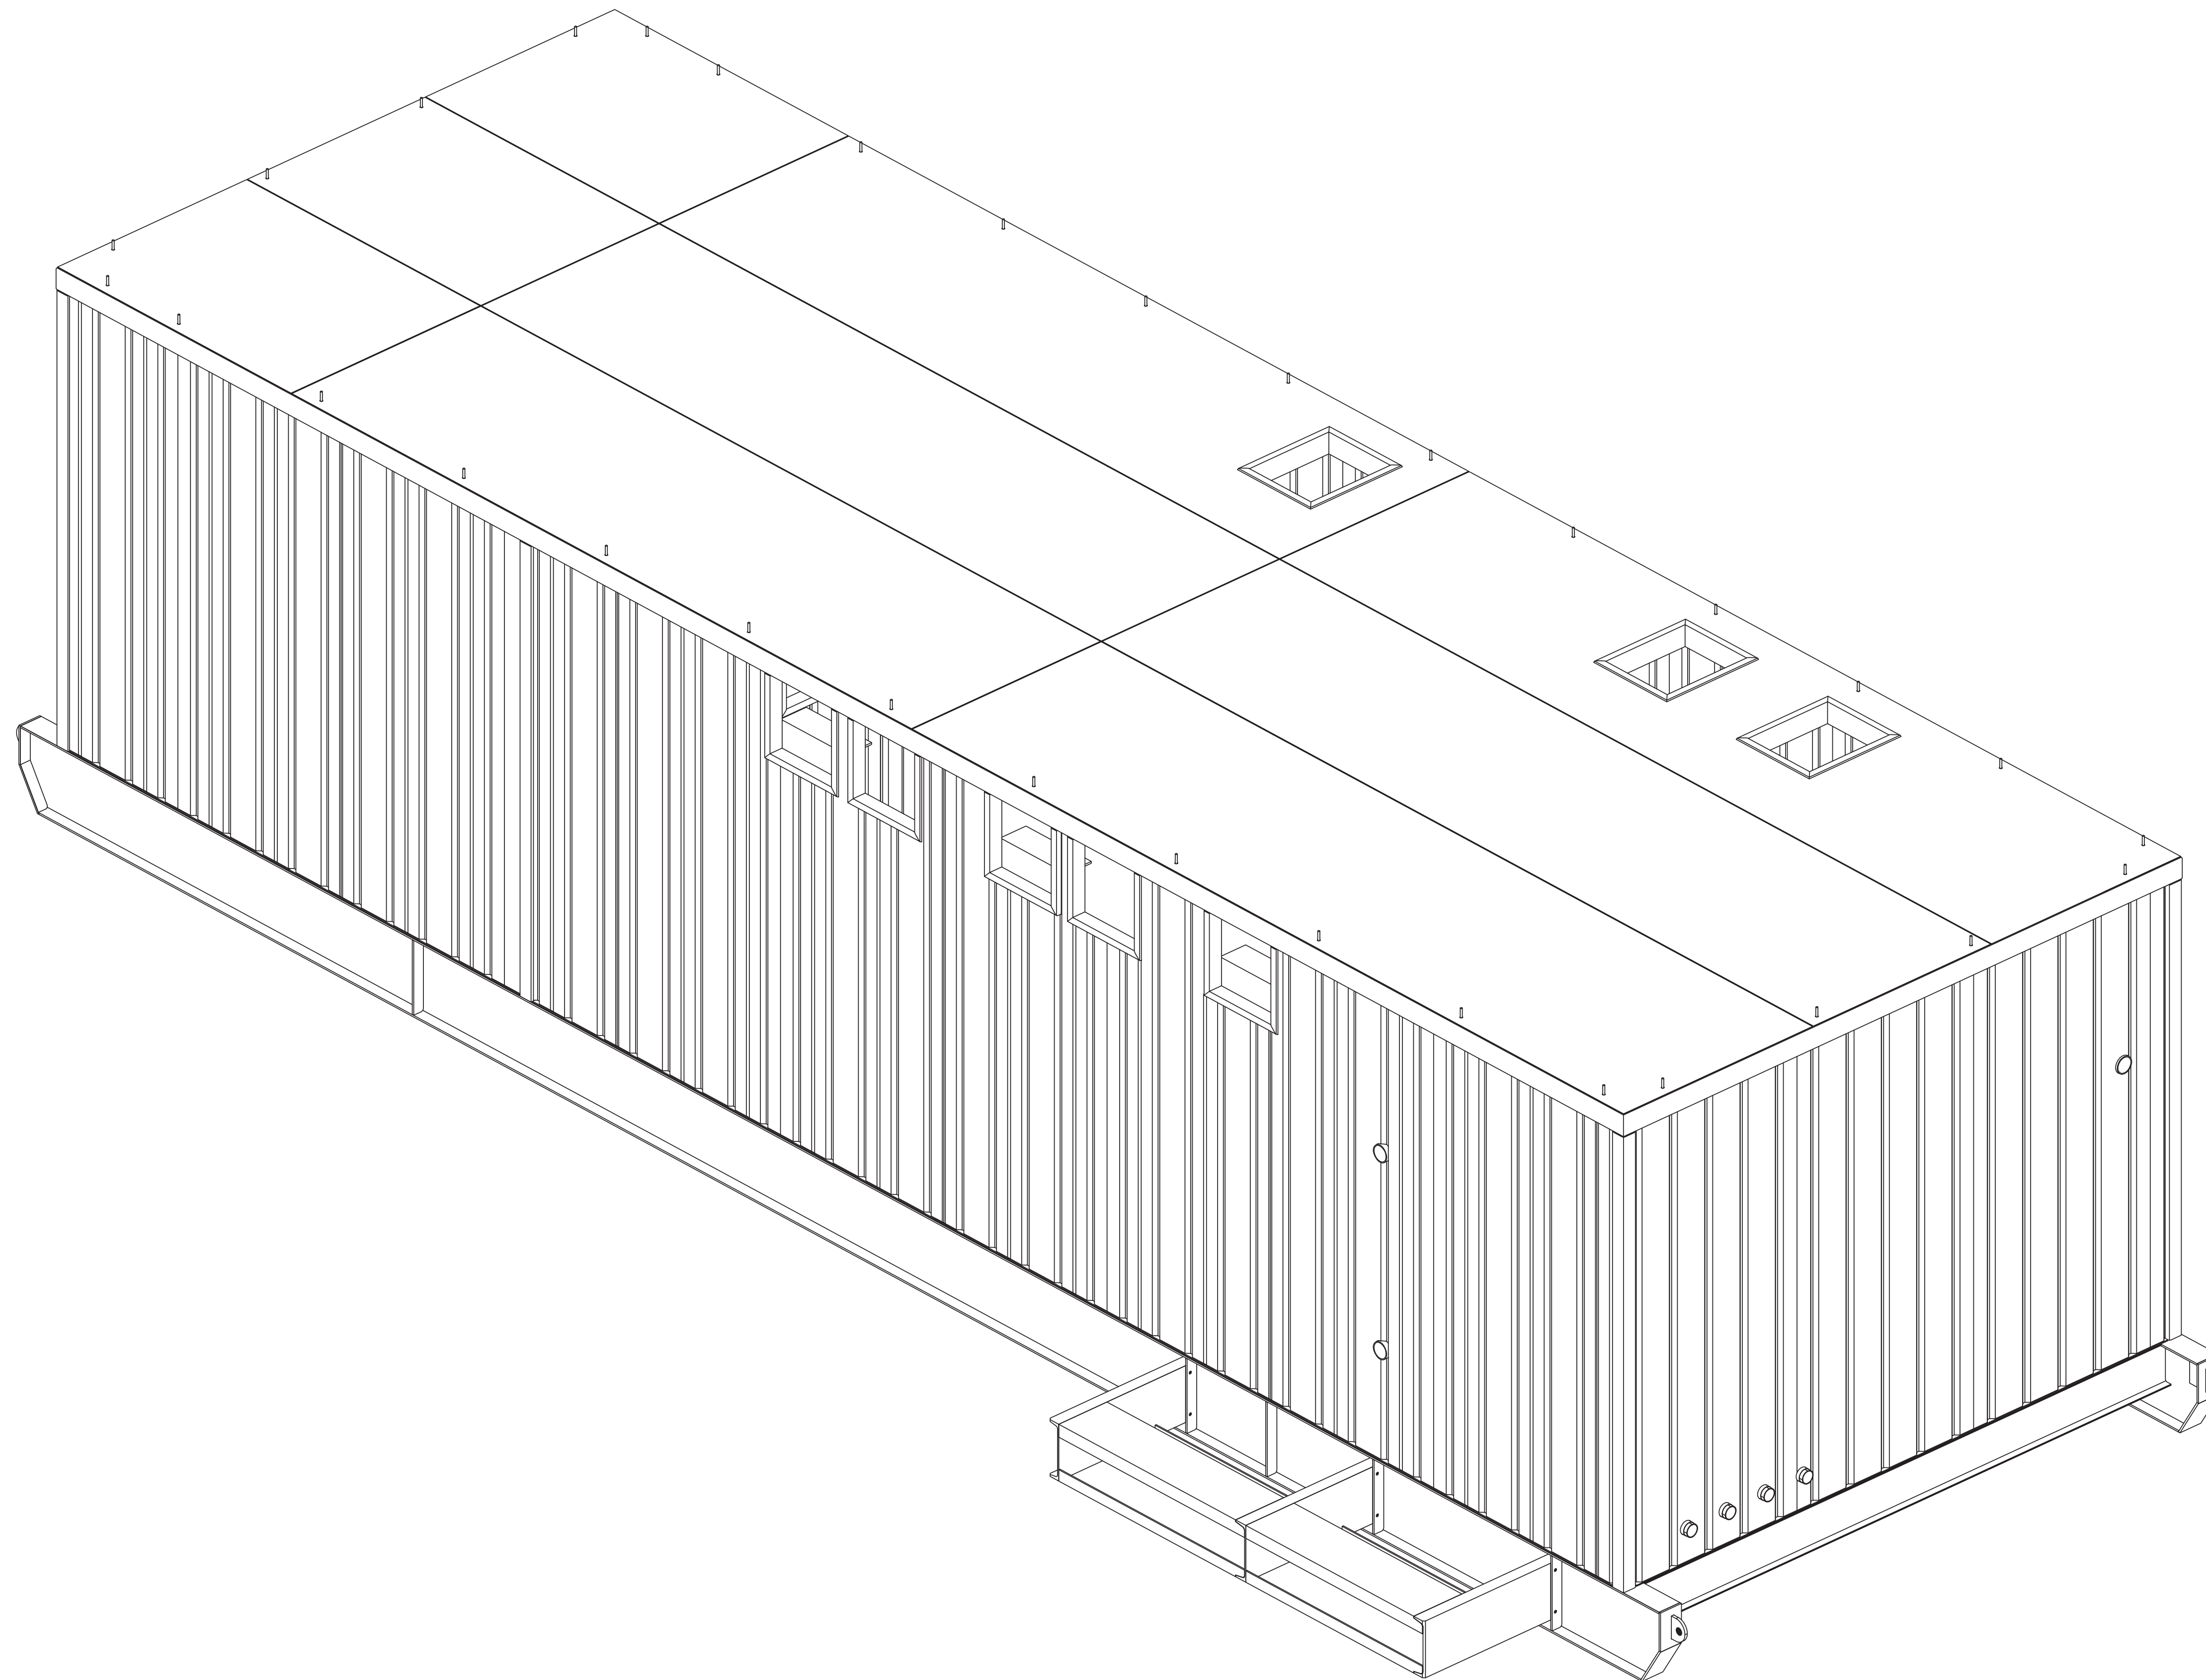

# ISOMETRIC VIEW

THIS DRAWING SHOWS WORK THAT WAS PERFORMED BY OTHERS AS PART OF THE OWNER FURNISHED MODULE STRUCTURE FABRICATION AND IS PROVIDED FOR REFERENCE ONLY.

FOR APPROVAL

FIELD NOTES:

REF. DWG/SPEC :			
DEG REF. SPEC. / DWG :			
△			
△	For Re-Approval	ALN	07-04-22
△	For Approval	ALN	06-20-22
REV.	DESCRIPTION	BY	DATE
<b>SAMPSON STEEL COMPANY INC.</b>			
1848 POST ROAD ANCHORAGE, ALASKA 99501 PH. ( 907 ) 561-5626 FAX. ( 907 ) 561-5625			
HOLES U.N.	13/16Ø	PAINT U.N.	WELDS E70XX
CLEANING:			
JOB NAME:	RAMPART POWER SYSTEM UPGRADE	DR. BY:	PKM
LOCATION:	ALASKA	CHK. BY:	ALN
CONTRACTOR:	ALASKA ENERGY AUTHORITY	SCALE:	N.A.
DESCRIPTION:	ISOMETRIC VIEW	DATE:	05-26-22
		JOB NUMBER	SHEET NO.
		459	V107
		REV	△
